

# EPDP - Temporary Specification for gTLD Registration Data - Phase 2

Fact sheet as of: 7-Feb-2020

## Overview:

Following the adoption by the ICANN Board of a temporary specification on gTLD Registration Data to enable contracted parties to continue to comply with existing ICANN contractual requirements and with community-developed policies as they relate to WHOIS, while also complying with the European Union's General Data Protection Regulation (GDPR), a one-year policy development process was initiated to confirm whether or not the temporary specification should become a consensus policy.


The GNSO Council adopted the Final Report during its Special Council meeting on 4 March 2019 and provided its non-objection to the commencement of Phase 2.

**Wiki Page:** [EPDP Wiki Home Page](#)  
**Email Archive:** <https://mm.icann.org/pipermail/gns0-epdp-team/>  
**EPDP Input Archive:** <https://community.icann.org/x/zlWGBg>


**Chair:** Janis Karklins  
**Vice-Chair(s):** n/a  
**Liaison:** Rafik Dammak

## EPDP Status

**Start Date:** 4-Mar-2019      **EPDP Duration to Date:** **11** Months  
**Expected Completion:** 30-Jun-2020      **Total Expected Duration:** **16** Months



## Section I: Meeting Stats

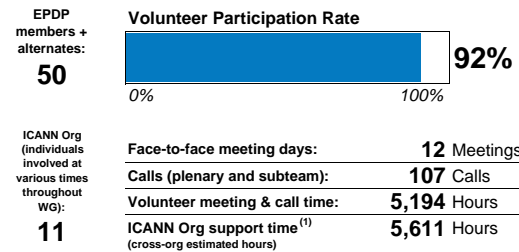

<sup>(1)</sup> Does not include time for Executives, Legal, IT Personnel and Other Organizational Support

## Section II: Financial Resources

| Direct Costs (1)             | FY19,20 Approved Budget | FY19,20 Budget Spent to Date(3) | Committed FY19,20 Services(4) | Remaining FY19,20 Budget | Actual Expenses: WG to Date | Total Spent and Committed to Date |
|------------------------------|-------------------------|---------------------------------|-------------------------------|--------------------------|-----------------------------|-----------------------------------|
| EPDP Professional Services   | \$ 464,764              | \$ 117,930                      | \$ 269,304                    | \$ 77,529                | \$ 117,930                  | \$ 387,235                        |
| N/A                          | \$ -                    | \$ -                            | \$ -                          | \$ -                     | \$ -                        | \$ -                              |
| Travel, Facility, & Catering | \$ 309,680              | \$ 103,773                      | \$ 115,500                    | \$ 90,407                | \$ 103,773                  | \$ 219,273                        |
| <b>Total</b>                 | <b>\$ 774,444</b>       | <b>\$ 221,703</b>               | <b>\$ 384,804</b>             | <b>\$ 167,936</b>        | <b>\$ 221,703</b>           | <b>\$ 606,507</b>                 |


<sup>(1)</sup> Excludes ICANN Organization and overhead allocation.

<sup>(3)</sup> Based on the most recent month end financials (may not include recent expenditures). Represents expenses incurred since inception of work.

<sup>(2)</sup> blank

<sup>(4)</sup> Professional services includes services from signed contracts to be provided or invoiced; travel includes upcoming scheduled meetings.

## Section III: Milestones

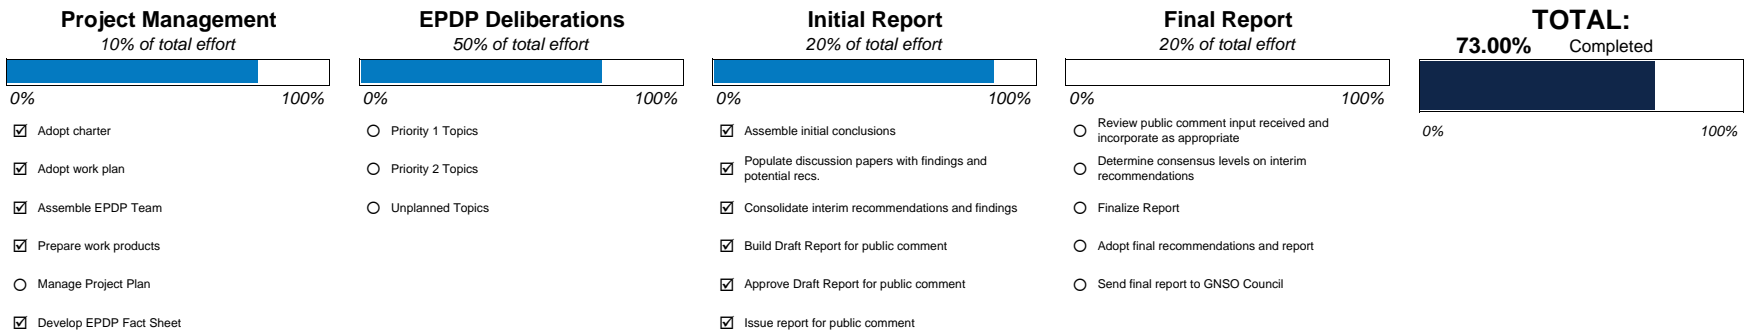

\*\* Please refer to full project plan for detailed tasks and deliverables with their associated duration and assigned dependencies.

Wiki: <https://community.icann.org/x/6BdlBg>
