

EPDP - Temporary Specification for gTLD Registration Data - Phase 2

Fact sheet as of: 29-Feb-2020

Overview:

Following the adoption by the ICANN Board of a temporary specification on gTLD Registration Data to enable contracted parties to continue to comply with existing ICANN contractual requirements and with community-developed policies as they relate to WHOIS, while also complying with the European Union's General Data Protection Regulation (GDPR), a one-year policy development process was initiated to confirm whether or not the temporary specification should become a consensus policy.


The GNSO Council adopted the Final Report during its Special Council meeting on 4 March 2019 and provided its non-objection to the commencement of Phase 2.

Wiki Page: [EPDP Wiki Home Page](#)
Email Archive: <https://mm.icann.org/pipermail/gns0-epdp-team/>
EPDP Input Archive: <https://community.icann.org/x/zlWGBg>


Chair: Janis Karklins
Vice-Chair(s): n/a
Liaison: Rafik Dammak

EPDP Status

Start Date: 4-Mar-2019 **EPDP Duration to Date:** **12** Months
Expected Completion: 30-Jun-2020 **Total Expected Duration:** **16** Months



Section I: Meeting Stats

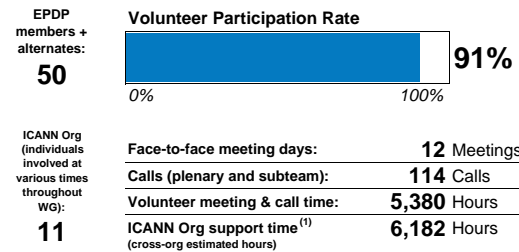

⁽¹⁾ Does not include time for Executives, Legal, IT Personnel and Other Organizational Support

Section II: Financial Resources

Direct Costs (1)	FY19,20 Approved Budget	FY19,20 Budget Spent to Date(3)	Committed FY19,20 Services(4)	Remaining FY19,20 Budget	Actual Expenses: WG to Date	Total Spent and Committed to Date
EPDP Professional Services	\$ 464,764	\$ 134,603	\$ 252,632	\$ 77,529	\$ 134,603	\$ 387,235
N/A	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
Travel, Facility, & Catering	\$ 309,680	\$ 145,879	\$ 10,000	\$ 153,801	\$ 145,879	\$ 155,879
Total	\$ 774,444	\$ 280,482	\$ 262,632	\$ 231,330	\$ 280,482	\$ 543,114

⁽¹⁾ Excludes ICANN Organization and overhead allocation.


⁽³⁾ Based on the most recent month end financials (may not include recent expenditures). Represents expenses incurred since inception of work.

⁽²⁾ blank


⁽⁴⁾ Professional services includes services from signed contracts to be provided or invoiced; travel includes upcoming scheduled meetings.

Section III: Milestones


Project Management 10% of total effort

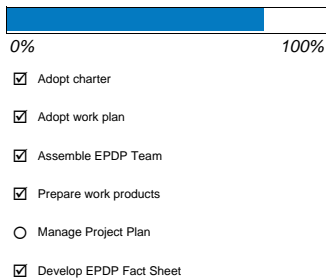


EPDP Deliberations 50% of total effort



Initial Report 20% of total effort

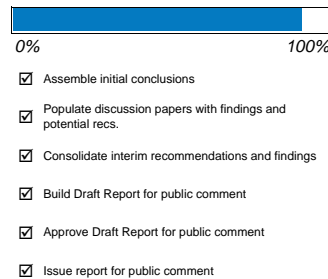

Final Report 20% of total effort



TOTAL: 81.00% Completed



** Please refer to full project plan for detailed tasks and deliverables with their associated duration and assigned dependencies.

Wiki: <https://community.icann.org/x/6BdlBg>
