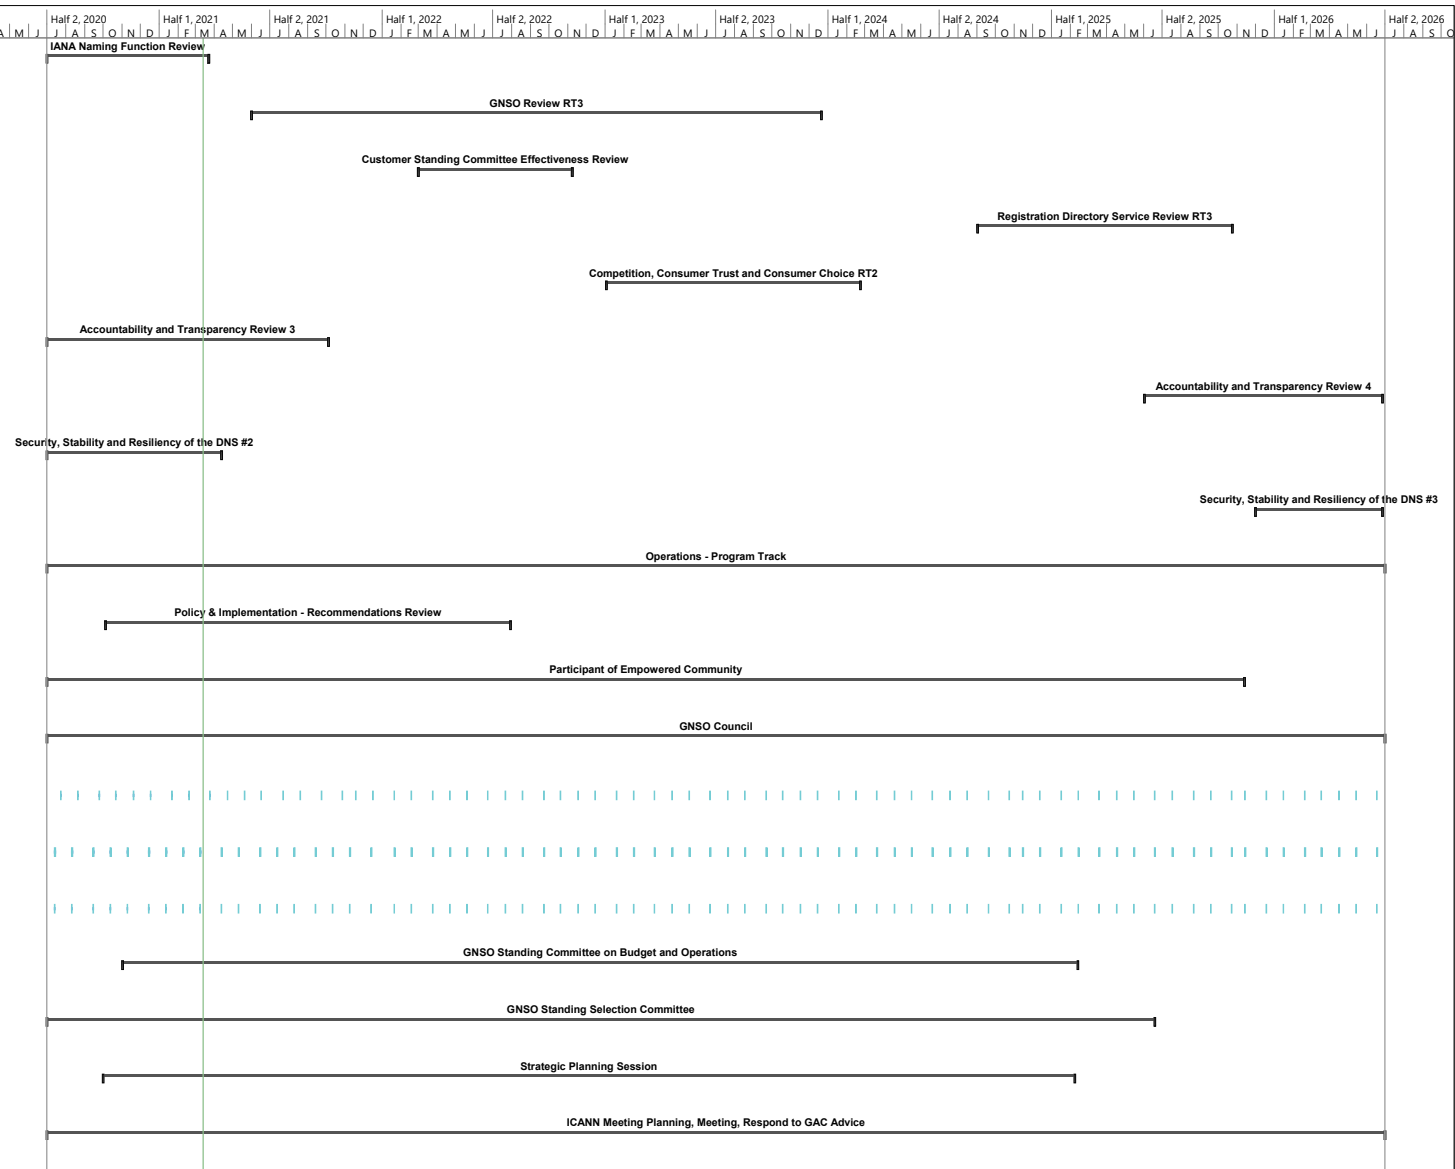


ID	WBS	Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names	GNSO Program Management Planning											
									Half 1, 2020	Half 2, 2020	Half 1, 2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025
1	1	GNSO Program Management Planning	1570 days	Wed 7/1/20	Tue 6/30/26		20%		GNSO Program Management Planning											
2	1.1	RDDS - Program Track	843 days	Wed 7/1/20	Mon 9/18/23		23%		RDDS - Program Track											
3	1.1.1	EPDP: Temporary Specification on gTLD Registration Data - Phase 2	843 days	Wed 7/1/20	Mon 9/18/23		21%		EPDP: Temporary Specification on gTLD Registration Data - Phase 2											
8	1.1.2	Remaining EPDP-P2 Topics (Legal vs. Natural, Unique Contacts, + Accuracy)	760 days	Mon 9/28/20	Mon 8/21/23		20%		Remaining EPDP-P2 Topics (Legal vs. Natural, Unique Contacts, + Accuracy)											
9	1.1.2.1	Remaining EPDP-P2 Topics Track 1 (Legal vs. Natural + Feasibility of Unique Contacts)	513 days	Mon 9/28/20	Mon 9/12/22		23%		Remaining EPDP-P2 Topics Track 1 (Legal vs. Natural + Feasibility of Unique Contacts)											
15	1.1.2.2	Remaining EPDP-P2 Topics Track 2 (Accuracy)	760 days	Mon 9/28/20	Mon 8/21/23		17%		Remaining EPDP-P2 Topics Track 2 (Accuracy)											
26	1.1.3	RDS2 Review Items	578 days	Thu 7/23/20	Thu 10/6/22		94%		RDS2 Review Items											
34	1.1.4	IRT: Temporary Specification on gTLD Registration Data - Phase 1	546 days	Wed 7/1/20	Mon 8/1/22		32%		IRT: Temporary Specification on gTLD Registration Data - Phase 1											
122	1.1.5	Revised ICANN Procedure for Handling Whois Conflicts with Privacy Law	675 days	Fri 7/31/20	Tue 2/28/23		22%		Revised ICANN Procedure for Handling Whois Conflicts with Privacy Law											
135	1.1.6	EPDP-P1 Rec27 Wave 1.5 & Wave 2 Other Policy Impacts	156 days	Mon 3/1/21	Fri 10/1/21		6%		EPDP-P1 Rec27 Wave 1.5 & Wave 2 Other Policy Impacts											
138	1.1.7	IRT: Privacy & Proxy Services Accreditation Issues (on-hold pending EPDP)	270 days	Fri 5/21/21	Wed 6/1/22		0%		IRT: Privacy & Proxy Services Accreditation Issues (on-hold pending EPDP)											
140	1.1.8	IRT: Translation/Transliteration of gTLD Registration Data (on-hold pending EPDP + RDAP)	270 days	Fri 5/21/21	Wed 6/1/22		0%		IRT: Translation/Transliteration of gTLD Registration Data (on-hold pending EPDP + RDAP)											
142	1.2	RPM - Program Track	1205 days	Wed 7/1/20	Tue 2/4/25		20%		RPM - Program Track											
143	1.2.1	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 1 (URS, TMCH, Sunrise, Claims)	520 days	Wed 7/1/20	Fri 6/24/22		47%		PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 1 (URS, TMCH, Sunrise, Claims)											
153	1.2.2	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 2 (UDRP)	1045 days	Wed 2/10/21	Tue 2/4/25		2%		PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 2 (UDRP)											
159	1.3	gTLD - Program Track	815 days	Wed 7/1/20	Wed 8/9/23		22%		gTLD - Program Track											
160	1.3.1	CCWG: New gTLD Auction Proceeds Drafting Team (group completed 31 May 2020)	470 days	Mon 8/3/20	Wed 5/18/22		34%		CCWG: New gTLD Auction Proceeds Drafting Team (group completed 31 May 2020)											
164	1.3.2	PDP: New gTLD Subsequent Procedures PDP	798 days	Wed 7/1/20	Mon 7/17/23		21%		PDP: New gTLD Subsequent Procedures PDP											
169	1.3.3	Internationalized Domain Names	815 days	Wed 7/1/20	Wed 8/9/23		18%		Internationalized Domain Names											
170	1.3.3.1	IDN Operational Track 1 Working Group	280 days	Mon 8/3/20	Thu 8/26/21		29%		IDN Operational Track 1 Working Group											
173	1.3.3.2	IDN Policy Track 2 EPDP Working Group	735 days	Wed 10/21/20	Wed 8/9/23		5%		IDN Policy Track 2 EPDP Working Group											
179	1.3.3.3	IDN Track 3 Council Coordination	375 days	Wed 7/1/20	Fri 12/3/21		35%		IDN Track 3 Council Coordination											
181	1.4	Expiration - Program Track	651 days	Thu 10/1/20	Tue 3/28/23		23%		Expiration - Program Track											
182	1.4.1	Expired Domain Deletion Policy (EDDP) / Expired Registration Recovery Policy (ERRP) Review	651 days	Thu 10/1/20	Tue 3/28/23		23%		Expired Domain Deletion Policy (EDDP) / Expired Registration Recovery Policy (ERRP) Review											
186	1.5	Transfers - Program Track	1107 days	Wed 7/1/20	Fri 9/20/24		17%		Transfers - Program Track											
187	1.5.1	Transfer Policy Review	1107 days	Wed 7/1/20	Fri 9/20/24		17%		Transfer Policy Review											
197	1.6	IGO - Program Track	733 days	Wed 7/1/20	Tue 4/18/23		5%		IGO - Program Track											
198	1.6.1	PDP: RPM - IGO Curative Rights Work Track	733 days	Wed 7/1/20	Tue 4/18/23		11%		PDP: RPM - IGO Curative Rights Work Track											
205	1.6.2	PDP: Curative Rights Protections for IGO/INGOs	330 days	Thu 1/13/22	Tue 4/18/23		0%		PDP: Curative Rights Protections for IGO/INGOs											
208	1.6.3	PDP: Protection of International Organization Names in All gTLDs	270 days	Thu 4/7/22	Tue 4/18/23		0%		PDP: Protection of International Organization Names in All gTLDs											
210	1.7	Accountability - Program Track	1000 days	Wed 7/1/20	Wed 4/24/24		32%		Accountability - Program Track											
211	1.7.1	Independent Review Process - Implementation Oversight Team	100 days	Wed 7/1/20	Tue 11/17/20		100%		Independent Review Process - Implementation Oversight Team											
213	1.7.2	Cross Community Working Group on Enhancing ICANN Accountability - WS2	440 days	Wed 7/1/20	Fri 3/4/22		41%		Cross Community Working Group on Enhancing ICANN Accountability - WS2											
216	1.7.3	Multistakeholder Model Evolution	1000 days	Wed 7/1/20	Wed 4/24/24		18%		Multistakeholder Model Evolution											
218	1.7.4	Geo Regions Review	380 days	Wed 7/1/20	Fri 12/10/21		40%		Geo Regions Review											
220	1.8	Reviews - Program Track	1568 days	Wed 7/1/20	Fri 6/26/26		23%		Reviews - Program Track											

ID	WBS	Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names	Half 1, 2020	Half 2, 2020	Half 1, 2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026	
221	1.8.1	IANA Naming Function Review	190 days	Wed 7/1/20	Mon 3/22/21		100%		J	F	M	A	M	J	F	M	A	M	J	F	M	A	M
224	1.8.2	GNSO Review RT3	670 days	Tue 6/1/21	Wed 12/20/23		0%																
230	1.8.3	Customer Standing Committee Effectiveness Review	180 days	Tue 3/1/22	Mon 11/7/22		0%																
233	1.8.4	Registration Directory Service Review RT3	300 days	Mon 9/2/24	Thu 10/23/25		0%																
236	1.8.5	Competition, Consumer Trust and Consumer Choice RT2	300 days	Tue 1/3/23	Thu 2/22/24		0%																
239	1.8.6	Accountability and Transparency Review 3	330 days	Wed 7/1/20	Mon 10/4/21		63%																
242	1.8.7	Accountability and Transparency Review 4	280 days	Mon 6/2/25	Fri 6/26/26		0%																
245	1.8.8	Security, Stability and Resiliency of the DNS #2	205 days	Wed 7/1/20	Mon 4/12/21		89%																
248	1.8.9	Security, Stability and Resiliency of the DNS #3	150 days	Mon 12/1/25	Fri 6/26/26		0%																
251	1.9	Operations - Program Track	1570 days	Wed 7/1/20	Tue 6/30/26		13%																
252	1.9.1	Policy & Implementation - Recommendations Review	477 days	Mon 10/5/20	Fri 7/29/22		20%																
257	1.9.2	Participant of Empowered Community	1406 days	Wed 7/1/20	Wed 11/12/25		13%																
269	1.9.3	GNSO Council	1570 days	Wed 7/1/20	Tue 6/30/26		13%																
270	1.9.3.1	GNSO Council - Monthly Meetings	1545 days	Thu 7/23/20	Wed 6/17/26		13%																
343	1.9.3.2	GNSO Council - Leadership Meetings	1554 days	Mon 7/13/20	Thu 6/18/26		13%																
416	1.9.3.3	GNSO Council - Action Items	1553 days	Mon 7/13/20	Wed 6/17/26		13%																
489	1.9.3.4	GNSO Standing Committee on Budget and Operations	1123 days	Mon 11/2/20	Wed 2/12/25		20%																
510	1.9.3.5	GNSO Standing Selection Committee	1301 days	Wed 7/1/20	Wed 6/18/25		14%																
512	1.9.3.6	Strategic Planning Session	1142 days	Thu 10/1/20	Fri 2/7/25		8%																
538	1.9.3.7	ICANN Meeting Planning, Meeting, Respond to GAC Advice	1570 days	Wed 7/1/20	Tue 6/30/26		11%																



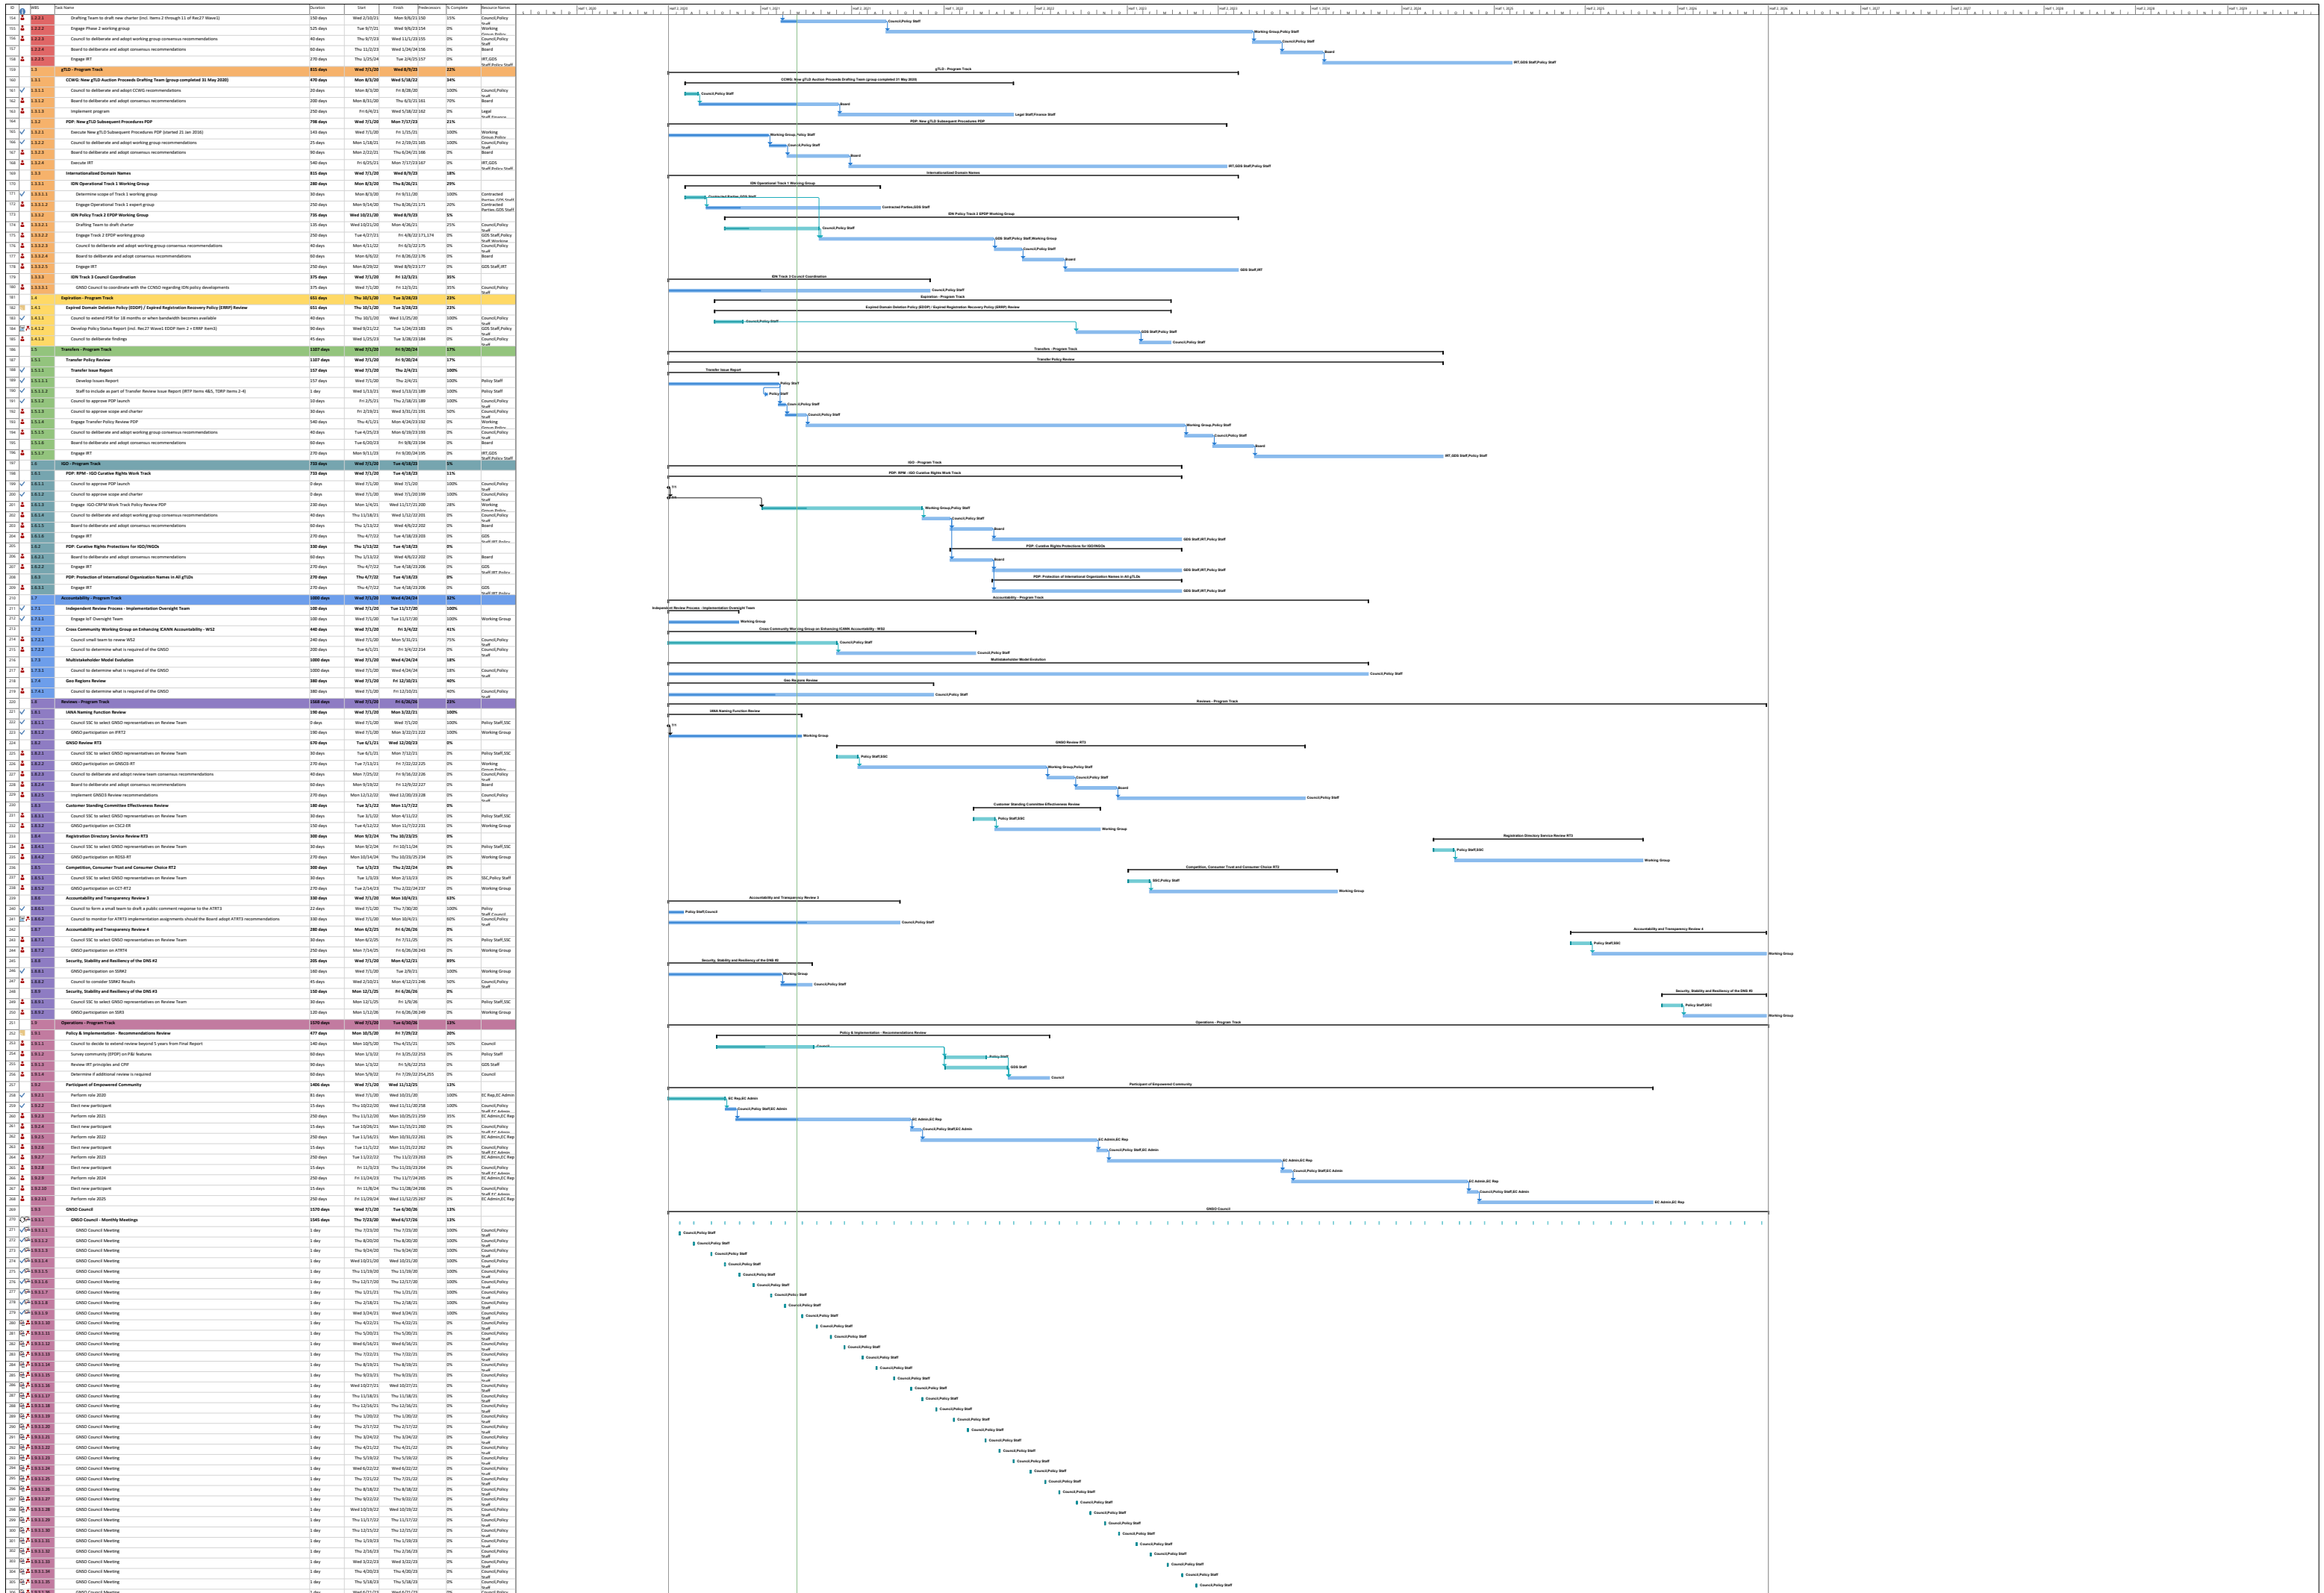


Table with columns: ID, Name, Date, Duration, Start, End, Status, Resource Name, etc. Contains task details for 'GMSD Council - Action Items' and 'GMSD Strategic Committee on Budget and Operations'.

