


ID	WBS	Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names	Timeline											
									Half 1, 2020	Half 2, 2020	Half 1, 2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025
1	1	GNSO Program Management Planning	1570 days	Wed 7/1/20	Tue 6/30/26		16%		GNSO Program Management Planning											
2	1.1	RDDS - Program Track	823 days	Wed 7/1/20	Mon 8/21/23		20%		RDDS - Program Track											
3	1.1.1	EPDP: Temporary Specification on gTLD Registration Data - Phase 2	733 days	Wed 7/1/20	Tue 4/18/23		10%		EPDP: Temporary Specification on gTLD Registration Data - Phase 2											
8	1.1.2	Remaining EPDP-P2 Topics (Legal vs. Natural, Unique Contacts, + Accuracy)	760 days	Mon 9/28/20	Mon 8/21/23		7%		Remaining EPDP-P2 Topics (Legal vs. Natural, Unique Contacts, + Accuracy)											
9	1.1.2.1	Remaining EPDP-P2 Topics Track 1 (Legal vs. Natural + Feasibility of Unique Contacts)	473 days	Mon 9/28/20	Mon 7/18/22		15%		Remaining EPDP-P2 Topics Track 1 (Legal vs. Natural + Feasibility of Unique Contacts)											
15	1.1.2.2	Remaining EPDP-P2 Topics Track 2 (Accuracy)	760 days	Mon 9/28/20	Mon 8/21/23		3%		Remaining EPDP-P2 Topics Track 2 (Accuracy)											
26	1.1.3	RDS2 Review Items	578 days	Thu 7/23/20	Thu 10/6/22		94%		RDS2 Review Items											
34	1.1.4	IRT: Temporary Specification on gTLD Registration Data - Phase 1	546 days	Wed 7/1/20	Mon 8/1/22		37%		IRT: Temporary Specification on gTLD Registration Data - Phase 1											
122	1.1.5	Revised ICANN Procedure for Handling Whois Conflicts with Privacy Law	635 days	Fri 7/31/20	Tue 1/3/23		16%		Revised ICANN Procedure for Handling Whois Conflicts with Privacy Law											
135	1.1.6	EPDP-P1 Rec27 Wave 1.5 & Wave 2 Other Policy Impacts (pending delivery)	165 days	Thu 12/17/20	Tue 8/3/21		0%		EPDP-P1 Rec27 Wave 1.5 & Wave 2 Other Policy Impacts (pending delivery)											
138	1.1.7	IRT: Privacy & Proxy Services Accreditation Issues (on-hold pending EPDP)	270 days	Fri 1/22/21	Tue 2/1/22		0%		IRT: Privacy & Proxy Services Accreditation Issues (on-hold pending EPDP)											
140	1.1.8	IRT: Translation/Transliteration of gTLD Registration Data (on-hold pending EPDP + RDAP)	270 days	Fri 1/22/21	Tue 2/1/22		0%		IRT: Translation/Transliteration of gTLD Registration Data (on-hold pending EPDP + RDAP)											
142	1.2	RPM - Program Track	1175 days	Wed 7/1/20	Tue 12/24/24		18%		RPM - Program Track											
143	1.2.1	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 1 (URS, TMCH, Sunrise, Claims)	490 days	Wed 7/1/20	Fri 5/13/22		46%		PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 1 (URS, TMCH, Sunrise, Claims)											
153	1.2.2	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 2 (UDRP)	1015 days	Wed 2/10/21	Tue 12/24/24		0%		PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 2 (UDRP)											
159	1.3	gTLD - Program Track	815 days	Wed 7/1/20	Wed 8/9/23		14%		gTLD - Program Track											
160	1.3.1	CCWG: New gTLD Auction Proceeds Drafting Team (group completed 31 May 2020)	390 days	Mon 8/3/20	Wed 1/26/22		6%		CCWG: New gTLD Auction Proceeds Drafting Team (group completed 31 May 2020)											
164	1.3.2	PDP: New gTLD Subsequent Procedures PDP	814 days	Wed 7/1/20	Tue 8/8/23		13%		PDP: New gTLD Subsequent Procedures PDP											
169	1.3.3	Internationalized Domain Names	815 days	Wed 7/1/20	Wed 8/9/23		18%		Internationalized Domain Names											
170	1.3.3.1	IDN Operational Track 1 Working Group	280 days	Mon 8/3/20	Thu 8/26/21		29%		IDN Operational Track 1 Working Group											
173	1.3.3.2	IDN Policy Track 2 EPDP Working Group	735 days	Wed 10/21/20	Wed 8/9/23		5%		IDN Policy Track 2 EPDP Working Group											
179	1.3.3.3	IDN Track 3 Council Coordination	375 days	Wed 7/1/20	Fri 12/3/21		35%		IDN Track 3 Council Coordination											
181	1.4	Expiration - Program Track	651 days	Thu 10/1/20	Tue 3/28/23		23%		Expiration - Program Track											
182	1.4.1	Expired Domain Deletion Policy (EDDP) / Expired Registration Recovery Policy (ERRP) Review	651 days	Thu 10/1/20	Tue 3/28/23		23%		Expired Domain Deletion Policy (EDDP) / Expired Registration Recovery Policy (ERRP) Review											
186	1.5	Transfers - Program Track	1125 days	Wed 7/1/20	Wed 10/16/24		15%		Transfers - Program Track											
187	1.5.1	Transfer Policy Review	1125 days	Wed 7/1/20	Wed 10/16/24		15%		Transfer Policy Review											
197	1.6	IGO - Program Track	773 days	Wed 7/1/20	Tue 6/13/23		1%		IGO - Program Track											
198	1.6.1	PDP: RPM - IGO Curative Rights Work Track	773 days	Wed 7/1/20	Tue 6/13/23		1%		PDP: RPM - IGO Curative Rights Work Track											
205	1.6.2	PDP: Curative Rights Protections for IGO/INGOs	330 days	Thu 3/10/22	Tue 6/13/23		0%		PDP: Curative Rights Protections for IGO/INGOs											
208	1.6.3	PDP: Protection of International Organization Names in All gTLDs	270 days	Thu 6/2/22	Tue 6/13/23		0%		PDP: Protection of International Organization Names in All gTLDs											
210	1.7	Accountability - Program Track	400 days	Wed 7/1/20	Fri 1/7/22		43%		Accountability - Program Track											
211	1.7.1	Independent Review Process - Implementation Oversight Team	100 days	Wed 7/1/20	Tue 11/17/20		100%		Independent Review Process - Implementation Oversight Team											
213	1.7.2	Cross Community Working Group on Enhancing ICANN Accountability - WS2	400 days	Wed 7/1/20	Fri 1/7/22		35%		Cross Community Working Group on Enhancing ICANN Accountability - WS2											
216	1.7.3	Multistakeholder Model Evolution	380 days	Wed 7/1/20	Fri 12/10/21		40%		Multistakeholder Model Evolution											
218	1.7.4	Geo Regions Review	380 days	Wed 7/1/20	Fri 12/10/21		40%		Geo Regions Review											
220	1.8	Reviews - Program Track	1568 days	Wed 7/1/20	Fri 6/26/26		16%		Reviews - Program Track											

ID	WBS	Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names	Half 1, 2020	Half 2, 2020	Half 1, 2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023	Half 1, 2024	Half 2, 2024	Half 1, 2025	Half 2, 2025	Half 1, 2026	Half 2, 2026
221	1.8.1	IANA Naming Function Review	190 days	Wed 7/1/20	Mon 3/22/21		75%															
224	1.8.2	GNSO Review RT3	670 days	Tue 6/1/21	Wed 12/20/23		0%															
230	1.8.3	Customer Standing Committee Effectiveness Review	180 days	Tue 3/1/22	Mon 11/7/22		0%															
233	1.8.4	Registration Directory Service Review RT3	300 days	Mon 9/2/24	Thu 10/23/25		0%															
236	1.8.5	Competition, Consumer Trust and Consumer Choice RT2	300 days	Tue 1/3/23	Thu 2/22/24		0%															
239	1.8.6	Accountability and Transparency Review 3	330 days	Wed 7/1/20	Mon 10/4/21		44%															
242	1.8.7	Accountability and Transparency Review 4	280 days	Mon 6/2/25	Fri 6/26/26		0%															
245	1.8.8	Security, Stability and Resiliency of the DNS #2	205 days	Wed 7/1/20	Mon 4/12/21		62%															
248	1.8.9	Security, Stability and Resiliency of the DNS #3	150 days	Mon 12/1/25	Fri 6/26/26		0%															
251	1.9	Operations - Program Track	1570 days	Wed 7/1/20	Tue 6/30/26		10%															
252	1.9.1	Policy & Implementation - Recommendations Review	477 days	Mon 10/5/20	Fri 7/29/22		23%															
257	1.9.2	Participant of Empowered Community	1406 days	Wed 7/1/20	Wed 11/12/25		9%															
269	1.9.3	GNSO Council	1570 days	Wed 7/1/20	Tue 6/30/26		9%															
270	1.9.3.1	GNSO Council - Monthly Meetings	1545 days	Thu 7/23/20	Wed 6/17/26		10%															
343	1.9.3.2	GNSO Council - Leadership Meetings	1554 days	Mon 7/13/20	Thu 6/18/26		10%															
416	1.9.3.3	GNSO Council - Action Items	1553 days	Mon 7/13/20	Wed 6/17/26		10%															
489	1.9.3.4	GNSO Standing Committee on Budget and Operations	1123 days	Mon 11/2/20	Wed 2/12/25		13%															
510	1.9.3.5	GNSO Standing Selection Committee	1301 days	Wed 7/1/20	Wed 6/18/25		12%															
512	1.9.3.6	Strategic Planning Session	1142 days	Thu 10/1/20	Fri 2/7/25		8%															
538	1.9.3.7	ICANN Meeting Planning, Meeting, Respond to GAC Advice	1570 days	Wed 7/1/20	Tue 6/30/26		6%															

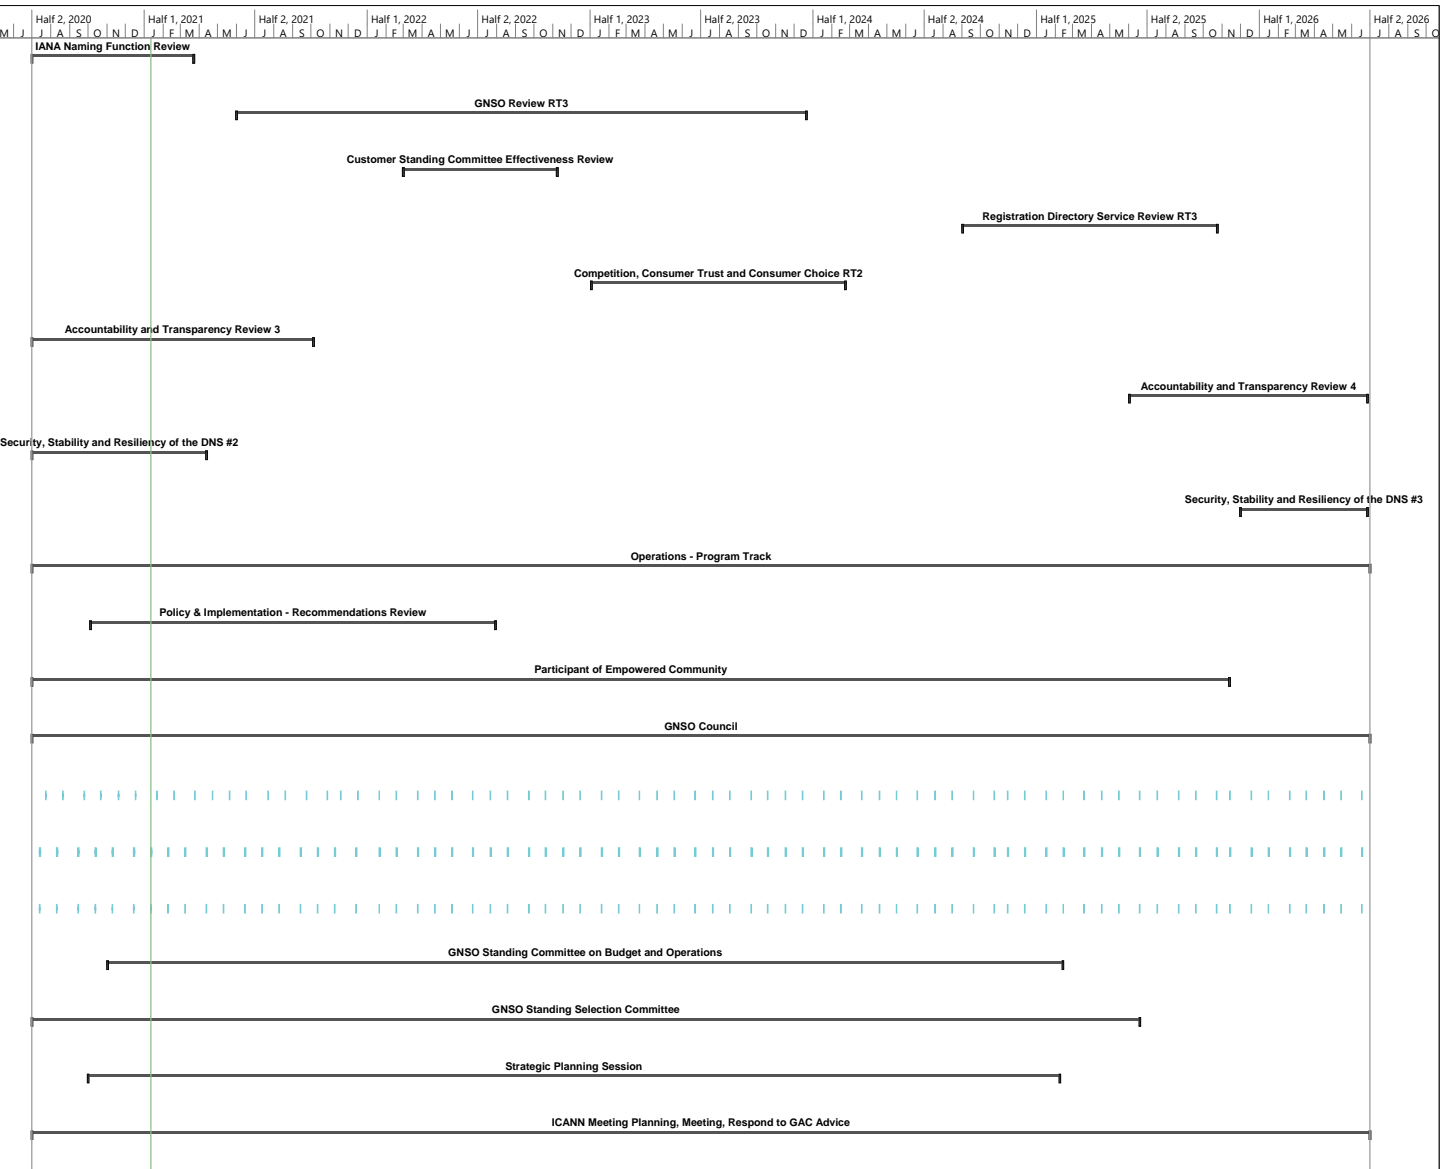

ID	WBS	Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names
1	1	GNDO Program Management Planning	1570 days	Wed 7/1/20	Tue 6/30/26		16%	
2	1.1	RDS5 - Program Track	823 days	Wed 7/1/20	Mon 8/21/23		20%	
3	1.1.1	EPDP: Temporary Specification on gTLD Registration Data - Phase 2	733 days	Wed 7/1/20	Tue 4/18/23		10%	
4	1.1.1.1	Engage EPDP: Temporary Specification on gTLD Registration Data - Phase 2	23 days	Wed 7/1/20	Fri 7/31/20		100%	Policy Staff, Working Group
5	1.1.1.2	Council to deliberate and adopt working group consensus recommendations	40 days	Mon 8/3/20	Fri 9/25/20		100%	Council, Policy Staff
6	1.1.1.3	Board to deliberate and adopt consensus recommendations	150 days	Mon 9/28/20	Thu 4/22/21		5%	Board
7	1.1.1.4	Engage IRT: Temporary Specification on gTLD Registration Data - Phase 2	520 days	Fri 4/23/21	Tue 4/18/23		0%	GDS Staff, IRT, Policy Staff
8	1.1.2	Remaining EPDP-P2 Topics (Legal vs. Natural, Unique Contacts, + Accuracy)	760 days	Mon 9/28/20	Mon 8/21/23		7%	
9	1.1.2.1	Remaining EPDP-P2 Topics Track 1 (Legal vs. Natural + Feasibility of Unique Contacts)	473 days	Mon 9/28/20	Mon 7/18/22		15%	
10	1.1.2.1.1	Reset EPDP-P2A and elect new Chair	58 days	Mon 9/28/20	Wed 12/16/20		100%	Council, Policy Staff
11	1.1.2.1.2	Engage EPDP-P2A to address remaining topics	140 days	Thu 12/17/20	Tue 6/29/21		9%	Working Group
12	1.1.2.1.3	Council to deliberate and adopt working group consensus recommendations	45 days	Wed 6/30/21	Tue 8/31/21		0%	Council, Policy Staff
13	1.1.2.1.4	Board to deliberate and adopt consensus recommendations	50 days	Wed 9/1/21	Mon 11/8/21		0%	Board
14	1.1.2.1.5	Engage IRT	180 days	Tue 11/9/21	Mon 7/18/22		0%	GDS Staff, IRT, Policy Staff
15	1.1.2.2	Remaining EPDP-P2 Topics Track 2 (Accuracy)	760 days	Mon 9/28/20	Mon 8/21/23		3%	
16	1.1.2.2.1	Staff to produce Briefing Document on Accuracy	130 days	Mon 9/28/20	Thu 3/25/21		15%	GDS Staff
17	1.1.2.2.2	Council to form Accuracy Scoping Team	60 days	Fri 3/26/21	Thu 6/17/21		0%	Council, Policy Staff
18	1.1.2.2.3	Deliberate scope and decide to request Issues Report	30 days	Fri 6/18/21	Thu 7/29/21		0%	Council, Policy Staff
19	1.1.2.2.4	Issues Report	60 days	Fri 7/30/21	Thu 10/21/21		0%	Policy Staff
20	1.1.2.2.5	Council to approve PDP launch	20 days	Fri 10/22/21	Wed 11/17/21		0%	Council, Policy Staff
21	1.1.2.2.6	Council to approve scope and charter	40 days	Thu 11/18/21	Wed 1/12/22		0%	Council, Policy Staff
22	1.1.2.2.7	Engage RDS Accuracy PDP	150 days	Thu 1/13/22	Wed 8/10/22		0%	Working Group
23	1.1.2.2.8	Council to deliberate and adopt working group consensus recommendations	40 days	Thu 8/11/22	Wed 10/5/22		0%	Council, Policy Staff
24	1.1.2.2.9	Board to deliberate and adopt consensus recommendations	50 days	Thu 10/6/22	Wed 12/14/22		0%	Board
25	1.1.2.2.10	Engage IRT	180 days	Thu 12/15/22	Mon 8/21/23		0%	GDS Staff, IRT, Policy Staff
26	1.1.3	RDS2 Review Items	578 days	Thu 7/23/20	Thu 10/6/22		94%	
27	1.1.3.1	RDS2 Review - Recommendation CC.1 (suspension of domain due to incorrect RDS)	578 days	Thu 7/23/20	Thu 10/6/22		83%	
28	1.1.3.1.1	Reply to Board on proposed action	10 days	Thu 7/23/20	Wed 8/5/20		100%	Council, Policy Staff
29	1.1.3.1.2	Determine if CC.1 can be coupled with remaining EPDP-P2 Topics (Accuracy)	1 day	Fri 10/22/21	Fri 10/22/21		0%	Council, Policy Staff
30	1.1.3.1.3	CC.1 Implemented	1 day	Thu 10/6/22	Thu 10/6/22		0%	Council, Policy Staff
31	1.1.3.2	RDS2 Review - Recommendation CC.4 (measure, audit, etc. of RDS Policies)	10 days	Thu 7/23/20	Wed 8/5/20		100%	
32	1.1.3.2.1	Reply to Board on proposed action	10 days	Thu 7/23/20	Wed 8/5/20		100%	Council, Policy Staff
33	1.1.3.2.2	Council will take no action as operating procedures already allow for this	10 days	Thu 7/23/20	Wed 8/5/20		100%	Council, Policy Staff
34	1.1.4	IRT: Temporary Specification on gTLD Registration Data - Phase 1	546 days	Wed 7/1/20	Mon 8/1/22		37%	
35	1.1.4.1	Engage IRT: Temporary Specification on gTLD Registration Data - Phase 1	545 days	Wed 7/1/20	Mon 8/1/22		55%	GDS Staff, IRT, Policy Staff
36	1.1.4.2	EPDP-P1 Rec27 Wave 1 Other Policy Impacts	344 days	Wed 7/1/20	Fri 10/22/21		31%	
37	1.1.4.2.1	Add Grace Period (AGP) Limits Policy [LOW]	1 day	Wed 7/1/20	Wed 7/1/20		100%	
38	1.1.4.2.1.1	No impacts as a result of Registration Data Services Policy implementation	1 day	Wed 7/1/20	Wed 7/1/20		100%	GDS Staff
39	1.1.4.2.2	Additional Whois Information Policy (AWIP) [LOW]	110 days	Thu 9/4/20	Thu 2/4/21		41%	
40	1.1.4.2.2.1	Produce redlines of consensus policy provisions (assumes step 2 accomplished here)	45 days	Fri 9/4/20	Thu 11/5/20		100%	GDS Staff
41	1.1.4.2.2.2	Review and confirm redlines for final changes	30 days	Fri 11/6/20	Thu 12/17/20		0%	GDS Staff, IRT, Policy Staff
42	1.1.4.2.2.3	Conduct public comment of changes	30 days	Fri 12/18/20	Thu 1/28/21		0%	GDS Staff, IRT, Policy Staff
43	1.1.4.2.2.4	Post updated consensus policy	5 days	Fri 1/29/21	Thu 2/4/21		0%	GDS Staff
44	1.1.4.2.3	Expired Domain Deletion Policy (EDDP) [MEDIUM]	120 days	Thu 9/4/20	Thu 2/18/21		38%	
45	1.1.4.2.3.1	Produce redlines of consensus policy provisions	45 days	Fri 9/4/20	Thu 11/5/20		100%	GDS Staff
46	1.1.4.2.3.2	Review and confirm redlines for final changes	40 days	Fri 11/6/20	Thu 12/31/20		0%	GDS Staff, IRT, Policy Staff
47	1.1.4.2.3.3	Conduct public comment of changes	30 days	Fri 1/1/21	Thu 2/11/21		0%	GDS Staff, IRT, Policy Staff
48	1.1.4.2.3.4	Post updated consensus policy	5 days	Fri 2/12/21	Thu 2/18/21		0%	GDS Staff
49	1.1.4.2.4	Expired Registration Recovery Policy (ERRP) [LOW]	120 days	Thu 9/4/20	Thu 2/18/21		38%	
50	1.1.4.2.4.1	Produce redlines of consensus policy provisions	45 days	Fri 9/4/20	Thu 11/5/20		100%	GDS Staff
51	1.1.4.2.4.2	Review and confirm redlines for final changes	40 days	Fri 11/6/20	Thu 12/31/20		0%	GDS Staff, IRT, Policy Staff
52	1.1.4.2.4.3	Conduct public comment of changes	30 days	Fri 1/1/21	Thu 2/11/21		0%	GDS Staff, IRT, Policy Staff
53	1.1.4.2.4.4	Post updated consensus policy	5 days	Fri 2/12/21	Thu 2/18/21		0%	GDS Staff
54	1.1.4.2.5	Protection of IGO / INGO Identifiers in All gTLDs Policy [LOW]	1 day	Wed 7/1/20	Wed 7/1/20		100%	
55	1.1.4.2.5.1	No impacts as a result of Registration Data Services Policy implementation	1 day	Wed 7/1/20	Wed 7/1/20		100%	GDS Staff
56	1.1.4.2.6	Registry Registration Data Directory Services Consistent Labeling and Display Policy (CL&D) [HIGH]	90 days	Mon 8/3/20	Fri 12/4/20		0%	
57	1.1.4.2.6.1	Council to determine next steps based on EPDP-P1-IRT + Rec27 findings	60 days	Fri 9/4/20	Thu 11/26/20		0%	Council, Policy Staff
58	1.1.4.2.6.2	Produce redlines of consensus policy provisions	45 days	Mon 8/3/20	Fri 10/2/20		0%	GDS Staff
59	1.1.4.2.6.3	Review and confirm redlines for final changes	10 days	Mon 10/5/20	Fri 10/16/20		0%	GDS Staff, IRT, Policy Staff
60	1.1.4.2.6.4	Conduct public comment of changes	30 days	Mon 10/19/20	Fri 11/27/20		0%	GDS Staff, IRT, Policy Staff
61	1.1.4.2.6.5	Post updated consensus policy	5 days	Mon 11/30/20	Fri 12/4/20		0%	GDS Staff
62	1.1.4.2.7	Registry Services Evaluation Policy [LOW]	1 day	Wed 7/1/20	Wed 7/1/20		100%	
63	1.1.4.2.7.1	No impacts as a result of Registration Data Services Policy implementation	1 day	Wed 7/1/20	Wed 7/1/20		100%	GDS Staff
64	1.1.4.2.8	Restored Names Accuracy Policy (RNAP) [LOW]	297 days	Fri 9/4/20	Fri 10/22/21		37%	
65	1.1.4.2.8.1	Track 1 - Item 1	120 days	Thu 9/4/20	Thu 2/18/21		38%	
66	1.1.4.2.8.1.1	Produce redlines of consensus policy provisions	45 days	Fri 9/4/20	Thu 11/5/20		100%	GDS Staff
67	1.1.4.2.8.1.2	Review and confirm redlines for final changes	40 days	Fri 11/6/20	Thu 12/31/20		0%	GDS Staff, IRT, Policy Staff
68	1.1.4.2.8.1.3	Conduct public comment of changes	30 days	Fri 1/1/21	Thu 2/11/21		0%	GDS Staff, IRT, Policy Staff
69	1.1.4.2.8.1.4	Post updated consensus policy	5 days	Fri 2/12/21	Thu 2/18/21		0%	GDS Staff
70	1.1.4.2.8.2	Track 2 - Item 2	1 day	Fri 10/22/21	Fri 10/22/21		0%	
71	1.1.4.2.8.2.1	Migrated to Remaining EPDP-P2 Topics Track 2 (Accuracy)	1 day	Fri 10/22/21	Fri 10/22/21		0%	Council, Policy Staff
72	1.1.4.2.9	Revised ICANN Procedure for Handling Whois Conflicts with Privacy Law [LOW]	120 days	Fri 9/4/20	Thu 2/18/21		38%	
73	1.1.4.2.9.1	Track 1 - Items 1 to 3	120 days	Thu 9/4/20	Thu 2/18/21		38%	
74	1.1.4.2.9.1.1	Produce redlines of consensus policy provisions	45 days	Fri 9/4/20	Thu 11/5/20		100%	GDS Staff
75	1.1.4.2.9.1.2	Review and confirm redlines for final changes	40 days	Fri 11/6/20	Thu 12/31/20		0%	GDS Staff, IRT, Policy Staff
76	1.1.4.2.9.1.3	Conduct public comment of changes	30 days	Fri 1/1/21	Thu 2/11/21		0%	GDS Staff, IRT, Policy Staff
77	1.1.4.2.9.1.4	Post updated consensus policy	5 days	Fri 2/12/21	Thu 2/18/21		0%	GDS Staff
78	1.1.4.2.10	Thick Whois Transition Policy for .COM, .NET, .JOBS [HIGH]	90 days	Fri 9/4/20	Thu 1/7/21		0%	
79	1.1.4.2.10.1	Council to determine next steps based on EPDP-P1-IRT + Rec27 findings	60 days	Fri 9/4/20	Thu 11/26/20		0%	Council, Policy Staff
80	1.1.4.2.10.2	Produce redlines of consensus policy provisions	45 days	Fri 9/4/20	Thu 11/5/20		0%	GDS Staff
81	1.1.4.2.10.3	Review and confirm redlines for final changes	10 days	Fri 11/6/20	Thu 11/19/20		0%	GDS Staff, IRT, Policy Staff
82	1.1.4.2.10.4	Conduct public comment of changes	30 days	Fri 11/20/20	Thu 12/31/20		0%	GDS Staff, IRT, Policy Staff
83	1.1.4.2.10.5	Post updated consensus policy	5 days	Fri 1/1/21	Thu 1/7/21		0%	GDS Staff
84	1.1.4.2.11	Transfer Policy [HIGH]	120 days	Fri 9/4/20	Thu 2/18/21		38%	
85	1.1.4.2.11.1	Produce redlines of consensus policy provisions (Items 1,2,3 & 6)	45 days	Fri 9/4/20	Thu 11/5/20		100%	GDS Staff
86	1.1.4.2.11.2	Review and confirm redlines for final changes	40 days	Fri 11/6/20	Thu 12/31/20		0%	GDS Staff, IRT, Policy Staff
87	1.1.4.2.11.3	Conduct public comment of changes	30 days	Fri 1/1/21	Thu 2/11/21		0%	GDS Staff, IRT, Policy Staff
88	1.1.4.2.11.4	Post updated consensus policy	5 days	Fri 2/12/21	Thu 2/18/21		0%	GDS Staff
89	1.1.4.2.12	Transfer Dispute Resolution Policy (TDRP) [HIGH]	120 days	Fri 9/4/20	Thu 2/18/21		38%	
90	1.1.4.2.12.1	Produce redlines of consensus policy provisions	45 days	Fri 9/4/20	Thu 11/5/20		100%	GDS Staff
91	1.1.4.2.12.2	Review and confirm redlines for final changes	40 days	Fri 11/6/20	Thu 12/31/20		0%	GDS Staff, IRT, Policy Staff
92	1.1.4.2.12.3	Conduct public comment of changes	30 days	Fri 1/1/21	Thu 2/11/21		0%	GDS Staff, IRT, Policy Staff
93	1.1.4.2.12.4	Post updated consensus policy	5 days	Fri 2/12/21	Thu 2/18/21		0%	GDS Staff
94	1.1.4.2.13	Rules for Uniform Domain Name Dispute Resolution Policy (UDRP Rules) [HIGH]	120 days	Mon 8/3/20	Fri 1/15/21		38%	
95	1.1.4.2.13.1	Produce redlines of consensus policy provisions (Item 1)	45 days	Mon 8/3/20	Fri 10/2/20		100%	GDS Staff
96	1.1.4.2.13.2	Review and confirm redlines for final changes	40 days	Mon 10/5/20	Fri 11/27/20		0%	GDS Staff, IRT, Policy Staff
97	1.1.4.2.13.3	Conduct public comment of changes	30 days	Mon 11/30/20	Fri 1/8/21		0%	GDS Staff, IRT, Policy Staff
98	1.1.4.2.13.4	Post updated consensus policy	5 days	Mon 1/11/21	Fri 1/15/21		0%	GDS Staff
99	1.1.4.2.14	Uniform Rapid Suspension System Procedure (URSS) [HIGH]	120 days	Wed 5/5/21	Tue 10/19/21		38%	

ID	WBS	Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names	
100	1.1.4.2.14.2	Produce redlines of consensus policy provisions (Items 1.2 & 8)	45 days	Wed 5/5/21	Tue 7/6/21	151	100%	GDS Staff	
101	1.1.4.2.14.2	Review and confirm redlines for final changes	40 days	Wed 7/7/21	Tue 8/31/21	100	0%	GDS Staff,IRT,Policy Staff	
102	1.1.4.2.14.3	Conduct public comment of changes	30 days	Wed 9/1/21	Tue 10/12/21	101	0%	GDS Staff,IRT	
103	1.1.4.2.14.4	Post updated consensus policy	5 days	Wed 10/13/21	Tue 10/19/21	102	0%	GDS Staff	
104	1.1.4.2.15	Uniform Rapid Suspension System Rules (URS Rules) [HIGH]	120 days	Wed 5/5/21	Tue 10/19/21		38%		
105	1.1.4.2.15.1	Produce redlines of consensus policy provisions (Items 1&3)	45 days	Wed 5/5/21	Tue 7/6/21	151	100%	GDS Staff	
106	1.1.4.2.15.2	Review and confirm redlines for final changes	40 days	Wed 7/7/21	Tue 8/31/21	100	0%	GDS Staff,IRT,Policy Staff	
107	1.1.4.2.15.3	Conduct public comment of changes	30 days	Wed 9/1/21	Tue 10/12/21	106	0%	GDS Staff,IRT	
108	1.1.4.2.15.4	Post updated consensus policy	5 days	Wed 10/13/21	Tue 10/19/21	107	0%	GDS Staff	
109	1.1.4.2.16	Whois Data Reminder Policy (WDRP) [MEDIUM]	297 days	Fri 9/4/20	Fri 10/22/21		37%		
110	1.1.4.2.16.1	Track 1 - Item 1	120 days	Fri 9/4/20	Thu 2/18/21		38%		
111	1.1.4.2.16.1	Produce redlines of consensus policy provisions	45 days	Fri 9/4/20	Thu 11/5/20	100	100%	GDS Staff	
112	1.1.4.2.16.1	Review and confirm redlines for final changes	40 days	Fri 11/6/20	Thu 12/31/20	111	0%	GDS Staff,IRT,Policy Staff	
113	1.1.4.2.16.1	Conduct public comment of changes	30 days	Fri 1/1/21	Thu 2/11/21	112	0%	GDS Staff,IRT	
114	1.1.4.2.16.1	Post updated consensus policy	5 days	Fri 2/12/21	Thu 2/18/21	113	0%	GDS Staff	
115	1.1.4.2.16.2	Track 2 - Items 2 through 6	1 day	Fri 10/22/21	Fri 10/22/21		0%		
116	1.1.4.2.16.2	Migrated to Remaining EPDP-#2 Topics Track 2 (Accuracy)	1 day	Fri 10/22/21	Fri 10/22/21	115	0%	Policy Staff,Council	
117	1.1.4.2.17	Whois Marketing Restriction Policy [LOW]	120 days	Fri 9/4/20	Thu 2/18/21		38%		
118	1.1.4.2.17.1	Produce redlines of consensus policy provisions	45 days	Fri 9/4/20	Thu 11/5/20	100	100%	GDS Staff	
119	1.1.4.2.17.2	Review and confirm redlines for final changes	40 days	Fri 11/6/20	Thu 12/31/20	118	0%	GDS Staff,IRT,Policy Staff	
120	1.1.4.2.17.3	Conduct public comment of changes	30 days	Fri 1/1/21	Thu 2/11/21	119	0%	GDS Staff,IRT	
121	1.1.4.2.17.4	Post updated consensus policy	5 days	Fri 2/12/21	Thu 2/18/21	120	0%	GDS Staff	
122	1.1.5	Revised ICANN Procedure for Handling Whois Conflicts with Privacy Law	635 days	Fri 7/31/20	Tue 1/3/23		16%		
123	1.1.5.1	Council small scoping team to determine next steps and Council consideration	60 days	Fri 7/31/20	Thu 10/22/20	100	100%	Council,Policy Staff	
124	1.1.5.2	Request ICANN org to develop revised proposal for Invoking Procedure	120 days	Fri 10/23/20	Wed 4/7/21	123	35%	GDS Staff,Policy Staff	
125	1.1.5.3	Council to deliberate findings and determine appropriate path	45 days	Thu 4/8/21	Wed 6/9/21	124	0%	Council,Policy Staff	
126	1.1.5.4	If required, review WPIAG Charter to determine if it's fit for purpose	30 days	Thu 6/10/21	Wed 7/21/21	125	0%	Council,Policy Staff	
127	1.1.5.5	If required, Council to approve charter and launch WPIAG	105 days	Thu 7/22/21	Tue 12/14/21		0%		
128	1.1.5.5.1	Engage WPIAG	60 days	Thu 7/22/21	Wed 10/13/21	126	0%	Policy Staff,Working Group	
129	1.1.5.5.2	Council to deliberate findings and determine appropriate path	45 days	Thu 10/14/21	Tue 12/14/21	128	0%	Council,Policy Staff	
130	1.1.5.6	If required, Council to approve launch of EPDP	275 days	Wed 12/15/21	Tue 1/3/23		0%		
131	1.1.5.6.1	Engage EPDP: Temporary Specification on gTLD Registration Data - Phase 2	90 days	Wed 12/15/21	Tue 4/19/22	129	0%	Policy Staff,Working Group	
132	1.1.5.6.2	Council to deliberate and adopt working group consensus recommendations	45 days	Wed 4/20/22	Tue 6/21/22	131	0%	Council,Policy Staff	
133	1.1.5.6.3	Board to deliberate and adopt consensus recommendations	50 days	Wed 6/22/22	Tue 8/30/22	132	0%	Board	
134	1.1.5.6.4	Engage IRT: Temporary Specification on gTLD Registration Data - Phase 2	90 days	Wed 8/31/22	Tue 1/3/23	133	0%	GDS Staff,Policy Staff	
135	1.1.6	EPDP-P1 Rec27 Wave 1.5 & Wave 2 Other Policy Impacts (pending delivery)	165 days	Thu 12/17/20	Tue 8/3/21		0%		
136	1.1.6.1	Council to consider Wave 1.5 report and determine next steps	90 days	Thu 12/17/20	Tue 4/20/21	100	0%	GDS Staff,Council,Policy Staff	
137	1.1.6.2	Council to consider Wave 2 report and determine next steps	90 days	Wed 3/31/21	Tue 8/3/21	100	0%	GDS Staff,Council,Policy Staff	
138	1.1.7	IRT: Privacy & Proxy Services Accreditation Issues (on-hold pending EPDP)	270 days	Fri 1/22/21	Tue 2/1/22		0%		
139	1.1.7.1	Engage IRT: Privacy & Proxy Services Accreditation Issues	270 days	Fri 1/22/21	Tue 2/1/22	100	0%	GDS Staff,IRT,Policy Staff	
140	1.1.8	IRT: Translation/Transliteration of gTLD Registration Data (on-hold pending EPDP + RDAF)	270 days	Fri 1/22/21	Tue 2/1/22		0%		
141	1.1.8.1	Engage IRT: Translation/Transliteration of gTLD Registration Data	270 days	Fri 1/22/21	Tue 2/1/22	100	0%	GDS Staff,IRT,Policy Staff	
142	1.2	RPM - Program Track	1175 days	Wed 7/1/20	Tue 12/24/24		38%		
143	1.2.1	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 1 (URS, TMCH, Sunrise, Claims)	490 days	Wed 7/1/20	Fri 5/13/22		46%		
144	1.2.1.1	Engage Phase 1 working group (started 4 Mar 2016)	120 days	Wed 7/1/20	Tue 12/15/20	100	100%	Working Group,Policy Staff	
145	1.2.1.2	EPDP-P1 Rec27 Wave 1 Other Policy Impacts	77 days	Wed 7/1/20	Thu 10/15/20		100%		
146	1.2.1.2.1	Track 2 - URS - Items 3 through 7	77 days	Wed 7/1/20	Thu 10/15/20		100%		
147	1.2.1.2.1.1	Determine if or easily can be addressed, else report back to Council	77 days	Wed 7/1/20	Thu 10/15/20	100	100%	Policy Staff,Working Group	
148	1.2.1.2.2	Track 2 - URS Rules - Items 2, 4 through 8	77 days	Wed 7/1/20	Thu 10/15/20		100%		
149	1.2.1.2.2.1	Determine if or easily can be addressed, else report back to Council	77 days	Wed 7/1/20	Thu 10/15/20	100	100%	Policy Staff,Working Group	
150	1.2.1.3	Council to deliberate and adopt working group consensus recommendations	40 days	Wed 12/16/20	Tue 2/9/21	144,147,149	50%	Council,Policy Staff	
151	1.2.1.4	Board to deliberate and adopt consensus recommendations	60 days	Wed 2/10/21	Mon 5/3/21	150	0%	Board	
152	1.2.1.5	Engage IRT	270 days	Tue 5/4/21	Fri 5/13/22	151	0%	IRT,GDS Staff,Policy Staff	
153	1.2.2	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 2 (URRP)	1015 days	Wed 2/10/21	Tue 12/24/24		0%		
154	1.2.2.1	Drafting Team to draft new charter (incl. Items 2 through 11 of Rec27 Wave1)	120 days	Wed 2/10/21	Mon 7/26/21	150	0%	Council,Policy Staff	
155	1.2.2.2	Engage Phase 2 working group	525 days	Tue 7/27/21	Wed 7/26/23	154	0%	Working Group,Policy Staff	
156	1.2.2.3	Council to deliberate and adopt working group consensus recommendations	40 days	Thu 7/27/23	Wed 9/20/23	155	0%	Council,Policy Staff	
157	1.2.2.4	Board to deliberate and adopt consensus recommendations	60 days	Thu 9/21/23	Wed 12/13/23	156	0%	Board	
158	1.2.2.5	Engage IRT	270 days	Thu 12/14/23	Tue 12/24/24	157	0%	IRT,GDS Staff,Policy Staff	
159	1.3	gTLD - Program Track	815 days	Wed 7/1/20	Wed 8/9/23		14%		
160	1.3.1	CCWG: New gTLD Auction Proceeds Drafting Team (group completed 31 May 2020)	390 days	Mon 8/3/20	Wed 1/26/22		6%		
161	1.3.1.1	Council to deliberate and adopt CCWG recommendations	20 days	Mon 8/3/20	Fri 8/28/20	100	100%	Council,Policy Staff	
162	1.3.1.2	Board to deliberate and adopt consensus recommendations	120 days	Mon 8/31/20	Fri 2/12/21	161	4%	Board	
163	1.3.1.3	Implement program	250 days	Mon 2/15/21	Wed 1/26/22	162	0%	Legal Staff,Finance Staff	
164	1.3.2	PDP: New gTLD Subsequent Procedures PDP	814 days	Wed 7/1/20	Tue 8/8/23		13%		
165	1.3.2.1	Execute New gTLD Subsequent Procedures PDP (started 21 Jan 2016)	124 days	Wed 7/1/20	Mon 12/21/20	100	85%	Working Group,Policy Staff	
166	1.3.2.2	Council to deliberate and adopt working group recommendations	60 days	Tue 12/22/20	Mon 3/15/21	165	0%	Council,Policy Staff	
167	1.3.2.3	Board to deliberate and adopt consensus recommendations	90 days	Tue 3/16/21	Fri 7/16/21	166	0%	Board	
168	1.3.2.4	Execute IRT	540 days	Mon 7/19/21	Tue 8/8/23	167	0%	IRT,GDS Staff,Policy Staff	
169	1.3.3	Internationalized Domain Names	815 days	Wed 7/1/20	Wed 8/9/23		18%		
170	1.3.3.1	IDN Operational Track 1 Working Group	280 days	Mon 8/3/20	Thu 8/26/21		29%		
171	1.3.3.1.1	Determine scope of Track 1 working group	30 days	Mon 8/3/20	Fri 9/11/20	100	100%	Contracted Parties,GDS Staff	
172	1.3.3.1.2	Engage Operational Track 1 expert group	250 days	Mon 9/14/20	Thu 8/26/21	171	20%	Contracted Parties,GDS Staff	
173	1.3.3.2	IDN Policy Track 2 EPDP Working Group	785 days	Wed 10/21/20	Wed 8/9/23		5%		
174	1.3.3.2.1	Drafting Team to draft charter	135 days	Wed 10/21/20	Mon 4/26/21	100	25%	Council,Policy Staff	
175	1.3.3.2.2	Engage Track 2 EPDP working group	250 days	Tue 4/27/21	Fri 4/8/22	174	0%	GDS Staff,Policy Staff,Working Group	
176	1.3.3.2.3	Council to deliberate and adopt working group consensus recommendations	40 days	Mon 4/11/22	Fri 6/3/22	175	0%	Council,Policy Staff	
177	1.3.3.2.4	Board to deliberate and adopt consensus recommendations	60 days	Mon 6/6/22	Fri 8/26/22	176	0%	Board	
178	1.3.3.2.5	Engage IRT	250 days	Mon 8/29/22	Wed 8/9/23	177	0%	GDS Staff,IRT	
179	1.3.3.3	IDN Track 3 Council Coordination	375 days	Wed 7/1/20	Fri 12/3/21		35%		
180	1.3.3.3.1	GNSO Council to coordinate with the CCNSO regarding IDN policy developments	375 days	Wed 7/1/20	Fri 12/3/21	100	35%	Council,Policy Staff	
181	1.4	Expiration - Program Track	651 days	Thu 10/1/20	Tue 3/28/23		23%		
182	1.4.1	Expired Domain Deletion Policy (EDDP) / Expired Registration Recovery Policy (ERRP) Review	651 days	Thu 10/1/20	Tue 3/28/23		23%		
183	1.4.1.1	Council to extend PDR for 18 months or when bandwidth becomes available	40 days	Thu 10/1/20	Wed 11/25/20	100	100%	Council,Policy Staff	
184	1.4.1.2	Develop Policy Status Report (incl. Rec27 Wave1 EDDP Item 2 + ERRP Item3)	90 days	Wed 9/21/22	Tue 1/24/23	183	0%	GDS Staff,Policy Staff	
185	1.4.1.3	Council to deliberate findings	45 days	Wed 1/25/23	Tue 3/28/23	184	0%	Council,Policy Staff	
186	1.5	Transfers - Program Track	1125 days	Wed 7/1/20	Wed 10/16/24		15%		
187	1.5.1	Transfer Policy Review	1125 days	Wed 7/1/20	Wed 10/16/24		15%		
188	1.5.1.1	Transfer Issue Report	170 days	Wed 7/1/20	Tue 2/23/21		100%		
189	1.5.1.1.1	Develop Issues Report	170 days	Wed 7/1/20	Tue 2/23/21	100	100%	Policy Staff	
190	1.5.1.1.2	Staff to include as part of Transfer Review Issue Report (IRTP Items 4&5, TDRP Items 2-4)	1 day	Wed 1/13/21	Wed 1/13/21	189	100%	Policy Staff	
191	1.5.1.2	Council to approve PDP launch	10 days	Wed 2/24/21	Tue 3/9/21	189	0%	Council,Policy Staff	
192	1.5.1.3	Council to approve scope and charter	35 days	Wed 3/10/21	Mon 4/26/21	191	0%	Council,Policy Staff	
193	1.5.1.4	Engage Transfer Policy Review PDP	540 days	Tue 4/27/21	Thu 5/18/23	192	0%	Working Group,Policy Staff	
194	1.5.1.5	Council to deliberate and adopt working group consensus recommendations	40 days	Fri 5/19/23	Wed 7/12/23	193	0%	Council,Policy Staff	
195	1.5.1.6	Board to deliberate and adopt consensus recommendations	60 days	Thu 7/13/23	Wed 10/4/23	194	0%	Board	
196	1.5.1.7	Engage IRT	270 days	Thu 10/5/23	Wed 10/16/24	195	0%	IRT,GDS Staff,Policy Staff	
197	1.6	IGO - Program Track	773 days	Wed 7/1/20	Tue 6/13/23		1%		
198	1.6.1	PDP: RPM - IGO Curative Rights Work Track	773 days	Wed 7/1/20	Tue 6/13/23		1%		

ID	WBS	Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names
199	1.6.1.1	Council to approve PDP launch	0 days	Wed 7/1/20	Wed 7/1/20		100%	Council,Policy Staff
200	1.6.1.2	Council to approve scope and charter	0 days	Wed 7/1/20	Wed 7/1/20	199	100%	Council,Policy Staff
201	1.6.1.3	Engage IGO-CRPM Work Track Policy Review PDP	270 days	Mon 1/4/21	Wed 1/12/22	200	3%	Working Group,Policy Staff
202	1.6.1.4	Council to deliberate and adopt working group consensus recommendations	40 days	Thu 1/13/22	Wed 3/9/22	201	0%	Working Group,Policy Staff
203	1.6.1.5	Board to deliberate and adopt consensus recommendations	60 days	Thu 3/10/22	Wed 6/1/22	202	0%	Board
204	1.6.1.6	Engage IRT	270 days	Thu 6/2/22	Tue 6/13/23	203	0%	GDS Staff,IRT,Policy Staff
205	1.6.2	PDP: Curative Rights Protections for IGO/INGOs	330 days	Thu 3/10/22	Tue 6/13/23		0%	GDS Staff,IRT,Policy Staff
206	1.6.2.1	Board to deliberate and adopt consensus recommendations	60 days	Thu 3/10/22	Wed 6/1/22	205	0%	Board
207	1.6.2.2	Engage IRT	270 days	Thu 6/2/22	Tue 6/13/23	206	0%	GDS Staff,IRT,Policy Staff
208	1.6.3	PDP: Protection of International Organization Names in All gTLDs	270 days	Thu 6/2/22	Tue 6/13/23		0%	GDS Staff,IRT,Policy Staff
209	1.6.3.1	Engage IRT	270 days	Thu 6/2/22	Tue 6/13/23	208	0%	GDS Staff,IRT,Policy Staff
210	1.7	Accountability - Program Track	400 days	Wed 7/1/20	Fri 12/17/20		43%	
211	1.7.1	Independent Review Process - Implementation Oversight Team	100 days	Wed 7/1/20	Tue 11/17/20		100%	
212	1.7.1.1	Engage IoT Oversight Team	100 days	Wed 7/1/20	Tue 11/17/20		100%	Working Group
213	1.7.2	Cross Community Working Group on Enhancing ICANN Accountability - WS2	400 days	Wed 7/1/20	Fri 12/17/20		35%	
214	1.7.2.1	Council small team to review WS2	200 days	Wed 7/1/20	Mon 4/5/21		70%	Council,Policy Staff
215	1.7.2.2	Council to determine what is required of the GNSO	200 days	Tue 4/6/21	Fri 1/7/22	214	0%	Council,Policy Staff
216	1.7.3	Multistakeholder Model Evolution	380 days	Wed 7/1/20	Fri 12/10/21		40%	
217	1.7.3.1	Council to determine what is required of the GNSO	380 days	Wed 7/1/20	Fri 12/10/21		40%	Council,Policy Staff
218	1.7.4	Geo Regions Review	380 days	Wed 7/1/20	Fri 12/10/21		40%	
219	1.7.4.1	Council to determine what is required of the GNSO	380 days	Wed 7/1/20	Fri 12/10/21		40%	Council,Policy Staff
220	1.8	Reviews - Program Track	1568 days	Wed 7/1/20	Fri 6/26/26		16%	
221	1.8.1	IANA Naming Function Review	190 days	Wed 7/1/20	Mon 3/22/21		75%	
222	1.8.1.1	Council SSC to select GNSO representatives on Review Team	0 days	Wed 7/1/20	Wed 7/1/20		100%	Policy Staff,SSC
223	1.8.1.2	GNSO participation on IRT2	190 days	Wed 7/1/20	Mon 3/22/21	222	75%	Working Group
224	1.8.2	GNSO Review RT3	670 days	Tue 6/1/21	Wed 12/20/23		0%	
225	1.8.2.1	Council SSC to select GNSO representatives on Review Team	30 days	Tue 6/1/21	Mon 7/12/21		0%	Policy Staff,SSC
226	1.8.2.2	GNSO participation on GNSO3-RT	270 days	Tue 7/13/21	Fri 7/22/22	225	0%	Working Group,Policy Staff
227	1.8.2.3	Council to deliberate and adopt review team consensus recommendations	40 days	Mon 7/25/22	Fri 9/16/22	226	0%	Working Group,Policy Staff
228	1.8.2.4	Board to deliberate and adopt consensus recommendations	60 days	Mon 9/19/22	Fri 12/9/22	227	0%	Board
229	1.8.2.5	Implement GNSO3 Review recommendations	270 days	Mon 12/12/22	Wed 12/20/23	228	0%	Council,Policy Staff
230	1.8.3	Customer Standing Committee Effectiveness Review	180 days	Tue 3/1/22	Mon 11/7/22		0%	
231	1.8.3.1	Council SSC to select GNSO representatives on Review Team	30 days	Tue 3/1/22	Mon 4/11/22		0%	Policy Staff,SSC
232	1.8.3.2	GNSO participation on CSC2-ER	150 days	Tue 4/12/22	Mon 11/7/22	231	0%	Working Group
233	1.8.4	Registration Directory Service Review RT3	300 days	Mon 9/2/24	Thu 10/23/25		0%	
234	1.8.4.1	Council SSC to select GNSO representatives on Review Team	30 days	Mon 9/2/24	Fri 10/11/24		0%	Policy Staff,SSC
235	1.8.4.2	GNSO participation on RDS3-RT	270 days	Mon 10/14/24	Thu 10/23/25	234	0%	Working Group
236	1.8.5	Competition, Consumer Trust and Consumer Choice RT2	300 days	Tue 1/3/23	Thu 2/22/24		0%	
237	1.8.5.1	Council SSC to select GNSO representatives on Review Team	30 days	Tue 1/3/23	Mon 2/13/23		0%	SSC,Policy Staff
238	1.8.5.2	GNSO participation on CCT-RT2	270 days	Tue 2/14/23	Thu 2/22/24	237	0%	Working Group
239	1.8.6	Accountability and Transparency Review 3	330 days	Wed 7/1/20	Mon 10/4/21		44%	
240	1.8.6.1	Council to form a small team to draft a public comment response to the ATRT3	22 days	Wed 7/1/20	Thu 7/30/20		100%	Policy Staff,Council
241	1.8.6.2	Council to monitor for ATRT3 implementation assignments should the Board adopt ATRT3 recommendations	330 days	Wed 7/1/20	Mon 10/4/21		40%	Council,Policy Staff
242	1.8.7	Accountability and Transparency Review 4	280 days	Mon 6/2/25	Fri 6/26/26		0%	
243	1.8.7.1	Council SSC to select GNSO representatives on Review Team	30 days	Mon 6/2/25	Fri 7/11/25		0%	Policy Staff,SSC
244	1.8.7.2	GNSO participation on ATRT4	250 days	Mon 7/14/25	Fri 6/26/26	243	0%	Working Group
245	1.8.8	Security, Stability and Resiliency of the DNS #2	205 days	Wed 7/1/20	Mon 4/12/21		62%	
246	1.8.8.1	GNSO participation on SSR#2	160 days	Wed 7/1/20	Tue 2/9/21		80%	Working Group
247	1.8.8.2	Council to consider SSR#2 Results	45 days	Wed 2/10/21	Mon 4/12/21	246	0%	Council,Policy Staff
248	1.8.9	Security, Stability and Resiliency of the DNS #3	150 days	Mon 12/1/25	Fri 6/26/26		0%	
249	1.8.9.1	Council SSC to select GNSO representatives on Review Team	30 days	Mon 12/1/25	Fri 1/9/26		0%	Policy Staff,SSC
250	1.8.9.2	GNSO participation on SSR3	120 days	Mon 1/12/26	Fri 6/26/26	249	0%	Working Group
251	1.9	Operations - Program Track	1570 days	Wed 7/1/20	Tue 6/30/26		10%	
252	1.9.1	Policy & Implementation - Recommendations Review	477 days	Mon 10/5/20	Fri 7/29/22		23%	
253	1.9.1.1	Council to decide to extend review beyond 5 years from Final Report	100 days	Mon 10/5/20	Fri 2/19/21		70%	Council
254	1.9.1.2	Survey community (EPDF) on P&I features	60 days	Mon 1/3/22	Fri 3/25/22	253	0%	Policy Staff
255	1.9.1.3	Review IRT principles and CPF	90 days	Mon 1/3/22	Fri 5/6/22	254	0%	GDS Staff
256	1.9.1.4	Determine if additional review is required	60 days	Mon 5/9/22	Fri 7/29/22	255	0%	Council
257	1.9.2	Participant of Empowered Community	1406 days	Wed 7/1/20	Wed 11/12/25		9%	
258	1.9.2.1	Perform role 2020	81 days	Wed 7/1/20	Wed 10/21/20		100%	EC Rep,EC Admin
259	1.9.2.2	Elect new participant	15 days	Thu 10/22/20	Wed 11/10/20	258	100%	Council,Policy Staff,EC Admin
260	1.9.2.3	Perform role 2021	250 days	Thu 11/12/20	Mon 10/25/21	259	15%	EC Admin,EC Rep
261	1.9.2.4	Elect new participant	15 days	Tue 10/26/21	Mon 11/15/21	260	0%	Council,Policy Staff,EC Admin
262	1.9.2.5	Perform role 2022	250 days	Tue 11/16/21	Mon 10/31/22	261	0%	EC Admin,EC Rep
263	1.9.2.6	Elect new participant	15 days	Tue 11/1/22	Mon 11/21/22	262	0%	Council,Policy Staff,EC Admin
264	1.9.2.7	Perform role 2023	250 days	Tue 11/22/22	Thu 11/23/23	263	0%	EC Admin,EC Rep
265	1.9.2.8	Elect new participant	15 days	Fri 11/3/23	Thu 11/23/23	264	0%	Council,Policy Staff,EC Admin
266	1.9.2.9	Perform role 2024	250 days	Fri 11/24/23	Thu 11/7/24	265	0%	EC Admin,EC Rep
267	1.9.2.10	Elect new participant	15 days	Fri 11/8/24	Thu 11/28/24	266	0%	Council,Policy Staff,EC Admin
268	1.9.2.11	Perform role 2025	250 days	Fri 11/29/24	Wed 11/12/25	267	0%	EC Admin,EC Rep
269	1.9.3	GNSO Council	1570 days	Wed 7/1/20	Tue 6/30/26		9%	
270	1.9.3.1	GNSO Council - Monthly Meetings	1545 days	Thu 7/23/20	Wed 6/17/26		10%	
343	1.9.3.2	GNSO Council - Leadership Meetings	1554 days	Mon 7/13/20	Thu 6/18/26		10%	
416	1.9.3.3	GNSO Council - Action Items	1553 days	Mon 7/13/20	Wed 6/17/26		10%	
489	1.9.3.4	GNSO Standing Committee on Budget and Operations	1123 days	Mon 11/2/20	Wed 2/12/25		13%	
490	1.9.3.4.1	2020-2021	76 days	Mon 11/2/20	Mon 2/15/21		66%	
491	1.9.3.4.1.1	Refresh roster and confirm Chair	15 days	Mon 11/2/20	Fri 11/20/20		100%	Policy Staff,Council
492	1.9.3.4.1.2	Evaluate fiscal year budget and planning documents	50 days	Mon 11/23/20	Fri 1/29/21	491	70%	Council,Policy Staff
493	1.9.3.4.1.3	Complete draft of comments for Council consideration and submit	11 days	Mon 2/1/21	Mon 2/15/21	492	0%	Council,Policy Staff
494	1.9.3.4.2	2021-2022	75 days	Mon 11/1/21	Fri 2/11/22		0%	
495	1.9.3.4.2.1	Refresh roster and confirm Chair	15 days	Mon 11/1/21	Fri 11/19/21		0%	Policy Staff,Council
496	1.9.3.4.2.2	Evaluate fiscal year budget and planning documents	50 days	Mon 11/22/21	Fri 1/28/22	495	0%	Council,Policy Staff
497	1.9.3.4.2.3	Complete draft of comments for Council consideration and submit	10 days	Mon 1/31/22	Fri 2/11/22	496	0%	Council,Policy Staff
498	1.9.3.4.3	2022-2023	75 days	Tue 11/1/22	Mon 2/13/23		0%	
499	1.9.3.4.3.1	Refresh roster and confirm Chair	15 days	Tue 11/1/22	Mon 11/21/22		0%	Policy Staff,Council
500	1.9.3.4.3.2	Evaluate fiscal year budget and planning documents	50 days	Tue 11/22/22	Mon 1/30/23	499	0%	Council,Policy Staff
501	1.9.3.4.3.3	Complete draft of comments for Council consideration and submit	10 days	Tue 1/31/23	Mon 2/13/23	500	0%	Council,Policy Staff
502	1.9.3.4.4	2023-2024	75 days	Wed 11/1/23	Tue 2/13/24		0%	
503	1.9.3.4.4.1	Refresh roster and confirm Chair	15 days	Wed 11/1/23	Tue 11/21/23		0%	Policy Staff,Council
504	1.9.3.4.4.2	Evaluate fiscal year budget and planning documents	50 days	Wed 11/22/23	Tue 1/30/24	503	0%	Council,Policy Staff
505	1.9.3.4.4.3	Complete draft of comments for Council consideration and submit	10 days	Wed 1/31/24	Tue 2/13/24	504	0%	Council,Policy Staff
506	1.9.3.4.5	2024-2025	75 days	Fri 11/1/24	Wed 2/12/25		0%	
507	1.9.3.4.5.1	Refresh roster and confirm Chair	15 days	Fri 11/1/24	Thu 11/21/24		0%	Policy Staff,Council
508	1.9.3.4.5.2	Evaluate fiscal year budget and planning documents	50 days	Fri 11/22/24	Wed 1/29/25	507	0%	Council,Policy Staff
509	1.9.3.4.5.3	Complete draft of comments for Council consideration and submit	10 days	Thu 1/30/25	Wed 2/12/25	508	0%	Council,Policy Staff
510	1.9.3.5	GNSO Standing Selection Committee	1301 days	Wed 7/1/20	Wed 6/18/25		12%	
511	1.9.3.5.1	SSC fill positions as assigned	1300 days	Wed 7/1/20	Wed 6/18/25		12%	SSC,Policy Staff
512	1.9.3.6	Strategic Planning Session	1142 days	Thu 10/1/20	Fri 2/7/25		8%	
513	1.9.3.6.1	2020-2021	52 days	Thu 10/1/20	Fri 12/11/20		100%	

ID	WBS	Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names	
S14	19.3.6.1.1	Establish and manage travel arrangements	1 day	Thu 10/1/20	Thu 10/1/20		100%	Council Leads, Policy Staff	
S15	19.3.6.1.2	Develop plan, topics, and materials for deliberation	30 days	Thu 10/1/20	Wed 11/11/20		100%	Council Leads, Policy Staff	
S16	19.3.6.1.3	Conduct planning session	13 days	Mon 11/2/20	Mon 11/23/20	S15	100%	Council Leads, Policy Staff	
S17	19.3.6.1.4	Develop post planning session report	15 days	Mon 11/23/20	Fri 12/11/20	S16	100%	Council Leads, Policy Staff	
S18	19.3.6.2	2021-2022	92 days	Fri 10/1/21	Fri 2/4/22		0%	Council Leads, Policy Staff	
S19	19.3.6.2.1	Establish and manage travel arrangements	75 days	Fri 10/1/21	Wed 1/12/22		0%	Council Leads, Policy Staff	
S20	19.3.6.2.2	Develop plan, topics, and materials for deliberation	65 days	Fri 10/1/21	Wed 12/29/21		0%	Council Leads, Policy Staff	
S21	19.3.6.2.3	Conduct planning session	5 days	Mon 10/1/22	Fri 1/14/22	S20	0%	Council Leads, Policy Staff	
S22	19.3.6.2.4	Develop post planning session report	15 days	Mon 1/17/22	Fri 2/4/22	S21	0%	Council Leads, Policy Staff	
S23	19.3.6.3	2022-2023	90 days	Sat 10/1/22	Fri 2/3/23		0%	Council Leads, Policy Staff	
S24	19.3.6.3.1	Establish and manage travel arrangements	75 days	Sat 10/1/22	Thu 1/12/23		0%	Council Leads, Policy Staff	
S25	19.3.6.3.2	Develop plan, topics, and materials for deliberation	65 days	Sat 10/1/22	Thu 12/29/22		0%	Council Leads, Policy Staff	
S26	19.3.6.3.3	Conduct planning session	5 days	Mon 1/9/23	Fri 1/13/23	S25	0%	Council Leads, Policy Staff	
S27	19.3.6.3.4	Develop post planning session report	15 days	Mon 1/16/23	Fri 2/3/23	S26	0%	Council Leads, Policy Staff	
S28	19.3.6.4	2023-2024	95 days	Sun 10/1/23	Fri 2/9/24		0%	Council Leads, Policy Staff	
S29	19.3.6.4.1	Establish and manage travel arrangements	75 days	Sun 10/1/23	Thu 1/11/24		0%	Council Leads, Policy Staff	
S30	19.3.6.4.2	Develop plan, topics, and materials for deliberation	65 days	Sun 10/1/23	Thu 12/28/23		0%	Council Leads, Policy Staff	
S31	19.3.6.4.3	Conduct planning session	5 days	Mon 1/15/24	Fri 1/19/24	S30	0%	Council Leads, Policy Staff	
S32	19.3.6.4.4	Develop post planning session report	15 days	Mon 1/22/24	Fri 2/9/24	S31	0%	Council Leads, Policy Staff	
S33	19.3.6.5	2024-2025	95 days	Tue 10/1/24	Fri 2/7/25		0%	Council Leads, Policy Staff	
S34	19.3.6.5.1	Establish and manage travel arrangements	75 days	Tue 10/1/24	Fri 1/10/25		0%	Council Leads, Policy Staff	
S35	19.3.6.5.2	Develop plan, topics, and materials for deliberation	65 days	Tue 10/1/24	Fri 12/27/24		0%	Council Leads, Policy Staff	
S36	19.3.6.5.3	Conduct planning session	5 days	Mon 1/13/25	Fri 1/17/25	S35	0%	Council Leads, Policy Staff	
S37	19.3.6.5.4	Develop post planning session report	15 days	Mon 1/20/25	Fri 2/7/25	S36	0%	Council Leads, Policy Staff	
S38	19.3.7	ICANN Meeting Planning, Meeting, Respond to GAC Advice	1570 days	Wed 7/1/20	Tue 6/30/26		6%	Council Leads, Policy Staff	
S39	19.3.7.1	ICANN69	97 days	Wed 7/1/20	Thu 11/12/20		100%	Council Leads, Policy Staff	
S40	19.3.7.1.1	Meeting Planning	75 days	Wed 7/1/20	Tue 10/13/20		100%	Council Leads, Policy Staff	
S41	19.3.7.1.2	ICANN Meeting	5 days	Sat 10/17/20	Thu 10/22/20	S40	100%	Council Leads, Policy Staff	
S42	19.3.7.1.3	Respond to GAC Advice	15 days	Fri 10/23/20	Thu 11/12/20	S41	100%	Council Leads, Policy Staff	
S43	19.3.7.2	ICANN70	99 days	Tue 12/1/20	Thu 4/15/21		0%	Council Leads, Policy Staff	
S44	19.3.7.2.1	Meeting Planning	75 days	Tue 12/1/20	Mon 3/15/21		0%	Council Leads, Policy Staff	
S45	19.3.7.2.2	ICANN Meeting	5 days	Sat 3/20/21	Thu 3/25/21	S44	0%	Council Leads, Policy Staff	
S46	19.3.7.2.3	Respond to GAC Advice	15 days	Fri 3/26/21	Thu 4/15/21	S45	0%	Council Leads, Policy Staff	
S47	19.3.7.3	ICANN71	70 days	Thu 4/1/21	Wed 7/7/21		0%	Council Leads, Policy Staff	
S48	19.3.7.3.1	Meeting Planning	50 days	Thu 4/1/21	Wed 6/9/21		0%	Council Leads, Policy Staff	
S49	19.3.7.3.2	ICANN Meeting	5 days	Thu 6/10/21	Wed 6/16/21	S48	0%	Council Leads, Policy Staff	
S50	19.3.7.3.3	Respond to GAC Advice	15 days	Thu 6/17/21	Wed 7/7/21	S49	0%	Council Leads, Policy Staff	
S51	19.3.7.4	ICANN72	102 days	Thu 7/1/21	Thu 11/18/21		0%	Council Leads, Policy Staff	
S52	19.3.7.4.1	Meeting Planning	75 days	Thu 7/1/21	Wed 10/13/21		0%	Council Leads, Policy Staff	
S53	19.3.7.4.2	ICANN Meeting	5 days	Sat 10/23/21	Thu 10/28/21	S52	0%	Council Leads, Policy Staff	
S54	19.3.7.4.3	Respond to GAC Advice	15 days	Fri 10/29/21	Thu 11/18/21	S53	0%	Council Leads, Policy Staff	
S55	19.3.7.5	ICANN73	95 days	Wed 12/1/21	Tue 4/12/22		0%	Council Leads, Policy Staff	
S56	19.3.7.5.1	Meeting Planning	75 days	Wed 12/1/21	Tue 3/15/22		0%	Council Leads, Policy Staff	
S57	19.3.7.5.2	ICANN Meeting	5 days	Wed 3/16/22	Tue 3/22/22	S56	0%	Council Leads, Policy Staff	
S58	19.3.7.5.3	Respond to GAC Advice	15 days	Wed 3/23/22	Tue 4/12/22	S57	0%	Council Leads, Policy Staff	
S59	19.3.7.6	ICANN74	70 days	Fri 4/1/22	Thu 7/7/22		0%	Council Leads, Policy Staff	
S60	19.3.7.6.1	Meeting Planning	50 days	Fri 4/1/22	Thu 6/9/22		0%	Council Leads, Policy Staff	
S61	19.3.7.6.2	ICANN Meeting	5 days	Fri 6/10/22	Thu 6/16/22	S60	0%	Council Leads, Policy Staff	
S62	19.3.7.6.3	Respond to GAC Advice	15 days	Fri 6/17/22	Thu 7/7/22	S61	0%	Council Leads, Policy Staff	
S63	19.3.7.7	ICANN75	95 days	Wed 6/1/22	Tue 10/11/22		0%	Council Leads, Policy Staff	
S64	19.3.7.7.1	Meeting Planning	75 days	Wed 6/1/22	Tue 9/13/22		0%	Council Leads, Policy Staff	
S65	19.3.7.7.2	ICANN Meeting	5 days	Wed 9/14/22	Tue 9/20/22	S64	0%	Council Leads, Policy Staff	
S66	19.3.7.7.3	Respond to GAC Advice	15 days	Wed 9/21/22	Tue 10/11/22	S65	0%	Council Leads, Policy Staff	
S67	19.3.7.8	ICANN76	95 days	Thu 12/1/22	Tue 4/11/23		0%	Council Leads, Policy Staff	
S68	19.3.7.8.1	Meeting Planning	75 days	Thu 12/1/22	Wed 3/15/23		0%	Council Leads, Policy Staff	
S69	19.3.7.8.2	ICANN Meeting	5 days	Thu 3/16/23	Wed 3/22/23	S68	0%	Council Leads, Policy Staff	
S70	19.3.7.8.3	Respond to GAC Advice	15 days	Thu 3/23/23	Tue 4/11/23	S69	0%	Council Leads, Policy Staff	
S71	19.3.7.9	ICANN77	70 days	Sat 4/1/23	Wed 7/5/23		0%	Council Leads, Policy Staff	
S72	19.3.7.9.1	Meeting Planning	50 days	Sat 4/1/23	Thu 6/8/23		0%	Council Leads, Policy Staff	
S73	19.3.7.9.2	ICANN Meeting	5 days	Fri 6/9/23	Thu 6/15/23	S72	0%	Council Leads, Policy Staff	
S74	19.3.7.9.3	Respond to GAC Advice	15 days	Fri 6/16/23	Wed 7/5/23	S73	0%	Council Leads, Policy Staff	
S75	19.3.7.10	ICANN78	95 days	Sat 7/1/23	Thu 11/9/23		0%	Council Leads, Policy Staff	
S76	19.3.7.10.1	Meeting Planning	75 days	Sat 7/1/23	Thu 10/12/23		0%	Council Leads, Policy Staff	
S77	19.3.7.10.2	ICANN Meeting	5 days	Fri 10/13/23	Thu 10/19/23	S76	0%	Council Leads, Policy Staff	
S78	19.3.7.10.3	Respond to GAC Advice	15 days	Fri 10/20/23	Thu 11/9/23	S77	0%	Council Leads, Policy Staff	
S79	19.3.7.11	ICANN79	95 days	Fri 12/1/23	Thu 4/11/24		0%	Council Leads, Policy Staff	
S80	19.3.7.11.1	Meeting Planning	75 days	Fri 12/1/23	Thu 3/14/24		0%	Council Leads, Policy Staff	
S81	19.3.7.11.2	ICANN Meeting	5 days	Fri 3/15/24	Thu 3/21/24	S80	0%	Council Leads, Policy Staff	
S82	19.3.7.11.3	Respond to GAC Advice	15 days	Fri 3/22/24	Thu 4/11/24	S81	0%	Council Leads, Policy Staff	
S83	19.3.7.12	ICANN80	70 days	Mon 4/1/24	Fri 7/5/24		0%	Council Leads, Policy Staff	
S84	19.3.7.12.1	Meeting Planning	50 days	Mon 4/1/24	Fri 6/7/24		0%	Council Leads, Policy Staff	
S85	19.3.7.12.2	ICANN Meeting	5 days	Mon 6/10/24	Fri 6/14/24	S84	0%	Council Leads, Policy Staff	
S86	19.3.7.12.3	Respond to GAC Advice	15 days	Mon 6/17/24	Fri 7/5/24	S85	0%	Council Leads, Policy Staff	
S87	19.3.7.13	ICANN81	95 days	Mon 7/1/24	Fri 11/8/24		0%	Council Leads, Policy Staff	
S88	19.3.7.13.1	Meeting Planning	75 days	Mon 7/1/24	Fri 10/11/24		0%	Council Leads, Policy Staff	
S89	19.3.7.13.2	ICANN Meeting	5 days	Mon 10/14/24	Fri 10/18/24	S88	0%	Council Leads, Policy Staff	
S90	19.3.7.13.3	Respond to GAC Advice	15 days	Mon 10/21/24	Fri 11/8/24	S89	0%	Council Leads, Policy Staff	
S91	19.3.7.14	ICANN82	95 days	Sun 12/1/24	Thu 4/10/25		0%	Council Leads, Policy Staff	
S92	19.3.7.14.1	Meeting Planning	75 days	Sun 12/1/24	Thu 3/13/25		0%	Council Leads, Policy Staff	
S93	19.3.7.14.2	ICANN Meeting	5 days	Fri 3/14/25	Thu 3/20/25	S92	0%	Council Leads, Policy Staff	
S94	19.3.7.14.3	Respond to GAC Advice	15 days	Fri 3/21/25	Thu 4/10/25	S93	0%	Council Leads, Policy Staff	
S95	19.3.7.15	ICANN83	70 days	Tue 4/1/25	Mon 7/7/25		0%	Council Leads, Policy Staff	
S96	19.3.7.15.1	Meeting Planning	50 days	Tue 4/1/25	Mon 6/9/25		0%	Council Leads, Policy Staff	
S97	19.3.7.15.2	ICANN Meeting	5 days	Tue 6/10/25	Mon 6/16/25	S96	0%	Council Leads, Policy Staff	
S98	19.3.7.15.3	Respond to GAC Advice	15 days	Tue 6/17/25	Mon 7/7/25	S97	0%	Council Leads, Policy Staff	
S99	19.3.7.16	ICANN84	95 days	Tue 7/1/25	Mon 11/10/25		0%	Council Leads, Policy Staff	
S100	19.3.7.16.1	Meeting Planning	75 days	Tue 7/1/25	Mon 10/13/25		0%	Council Leads, Policy Staff	
S101	19.3.7.16.2	ICANN Meeting	5 days	Tue 10/14/25	Mon 10/20/25	S100	0%	Council Leads, Policy Staff	
S102	19.3.7.16.3	Respond to GAC Advice	15 days	Tue 10/21/25	Mon 11/10/25	S101	0%	Council Leads, Policy Staff	
S103	19.3.7.17	ICANN85	95 days	Mon 12/1/25	Fri 4/10/26		0%	Council Leads, Policy Staff	
S104	19.3.7.17.1	Meeting Planning	75 days	Mon 12/1/25	Fri 3/13/26		0%	Council Leads, Policy Staff	
S105	19.3.7.17.2	ICANN Meeting	5 days	Mon 3/16/26	Fri 3/20/26	S104	0%	Council Leads, Policy Staff	
S106	19.3.7.17.3	Respond to GAC Advice	15 days	Mon 3/23/26	Fri 4/10/26	S105	0%	Council Leads, Policy Staff	
S107	19.3.7.18	ICANN86	65 days	Wed 4/1/26	Tue 6/30/26		0%	Council Leads, Policy Staff	
S108	19.3.7.18.1	Meeting Planning	50 days	Wed 4/1/26	Tue 6/9/26		0%	Council Leads, Policy Staff	
S109	19.3.7.18.2	ICANN Meeting	5 days	Wed 6/10/26	Tue 6/16/26	S108	0%	Council Leads, Policy Staff	
S110	19.3.7.18.3	Respond to GAC Advice	10 days	Wed 6/17/26	Tue 6/30/26	S109	0%	Council Leads, Policy Staff	

