

# Project Tracking & Rollup DASHBOARD


**Project Name** PDP: Transfer Policy Review **Program** Transfers **Project Sponsor** GNSO Council

**Project Information**

**58%**  
% Complete

**02/18/21**  
Actual Start

**06/19/25**  
Planned Finish

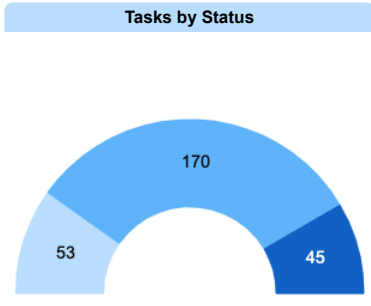

**Project Contacts**


**Roger Carney**  
Chair

**n/a**  
Vice\_Chair

**Oswaldo Novoa**  
Liaison

**Caitlin Tubergen**  
Staff\_Lead

**Berry Cobb**  
Project\_Manager



**Project Status & Health**

Project\_Status: Revised Schedule  
Project\_Health: On-Target

**Summary Gantt & Key Milestones**

Health	Primary Task	Current Start	Current Finish	% Complete	Status	Timeline (2021-2025)																							
						2021 Q1	2021 Q2	2021 Q3	2021 Q4	2022 Q1	2022 Q2	2022 Q3	2022 Q4	2023 Q1	2023 Q2	2023 Q3	2023 Q4	2024 Q1	2024 Q2	2024 Q3	2024 Q4	2025 Q1	2025 Q2	2025 Q3	2025 Q4				
	<b>PDP: Transfer Policy Review</b>	02/18/21	06/19/25	58%	In Progress	[Gantt Bar]																							
	<b>PROJECT CONTROL</b>	02/18/21	06/19/25	68%	In Progress	[Gantt Bar]																							
	<b>GROUP DELIBERATIONS</b>	05/13/21	11/14/24	72%	In Progress	[Gantt Bar]																							
	Group 1A Policy Topics	06/03/21	05/11/22	100%	Complete	[Gantt Bar]																							
	Group 1B Policy Topics	09/28/23	06/05/24	26%	In Progress	[Gantt Bar]																							
	Group 2 Policy Topics	02/02/23	09/27/23	93%	In Progress	[Gantt Bar]																							
	<b>INITIAL REPORT</b>	06/24/21	11/06/24	63%	In Progress	[Gantt Bar]																							
	Publish Initial Report - Group 1A	06/15/22	06/15/22	100%	Complete	[Gantt Bar]																							
	Publish Initial Report - Groups (1A, 1B & 2)	08/21/24	08/21/24	Not Started	Not Started	[Gantt Bar]																							
	<b>FINAL REPORT</b>	08/04/22	02/05/25	22%	In Progress	[Gantt Bar]																							
	Review of public comments - Group 1A	08/04/22	09/14/22	100%	Complete	[Gantt Bar]																							
	Review of public comments - Groups (1A, 1B & 2)	11/07/24	12/18/24	Not Started	Not Started	[Gantt Bar]																							
	Submission of Groups (1A, 1B & 2) Final Report to the GNSO Council	02/05/25	02/05/25	Not Started	Not Started	[Gantt Bar]																							

**Project Description**

On 18 February 2021, The GNSO Council passed a resolution to initiate a two-phased PDP to review the Transfer Policy. The PDP working group is tasked with determining if changes to the policy are needed to improve the ease, security, and efficacy of inter-registrar and inter-registrant transfers.

[Mailing List](#)  
[Meeting Schedule](#)  
[Wiki](#)  
[Charter](#)

**Completed in Prior Period**

- Completed substantive deliberations on the Transfer Emergency Action Contact (TEAC), reversal of a transfer, the Transfer Dispute Resolution Policy (TDRP), and Wave 1 - Rec #27 items related to TEAC and TDRP.
- Completed and distributed [Project Package](#).

**Open Issues & Risks**



- None at this time.



**Current Activities & Tasks**

- Continue deliberations on ICANN-Approved Transfers.

**Planned Activities & Tasks**

- Conduct a “where we’re at” materials & WG session regarding all topics from Groups 1A, 1B, and Group 2.
- Return to Group 1A deliberations on Change of Registrant.

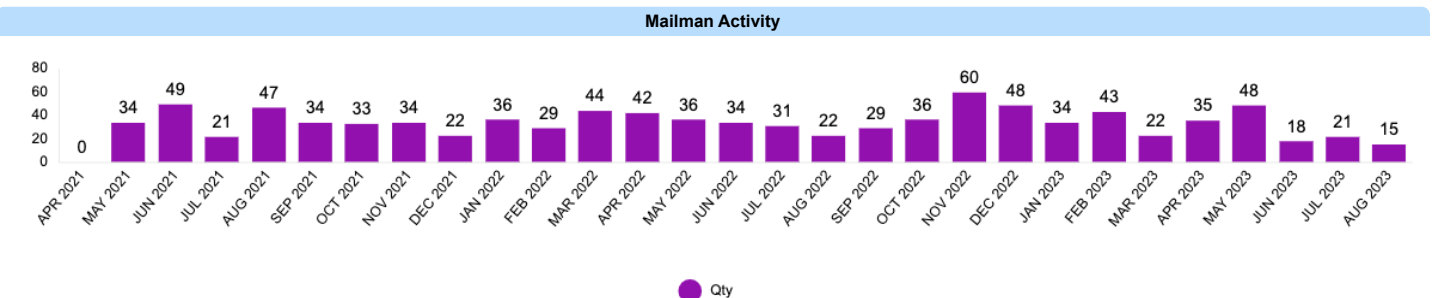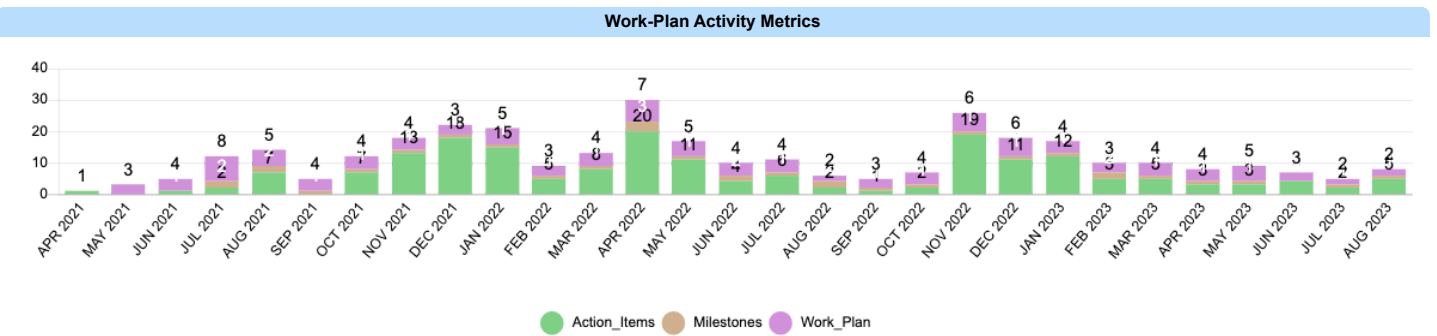

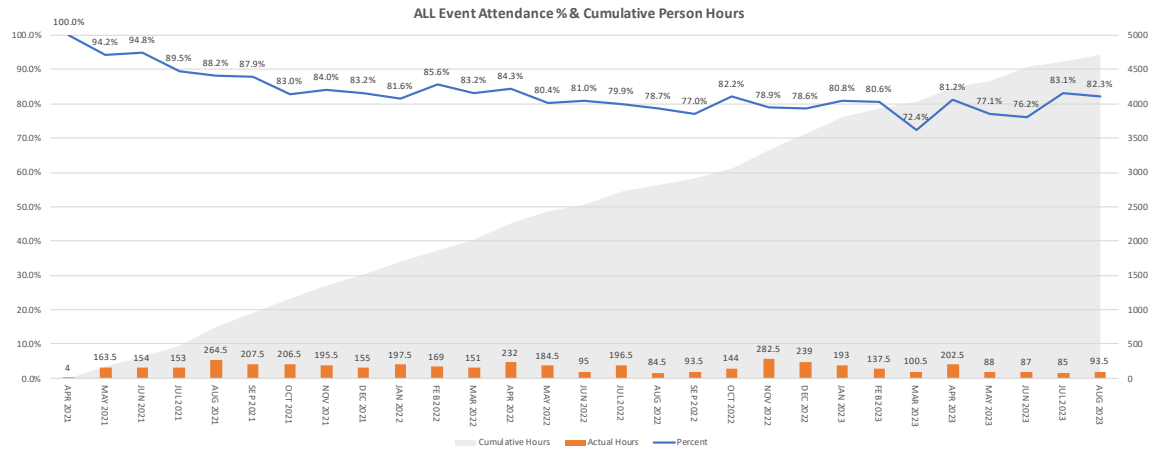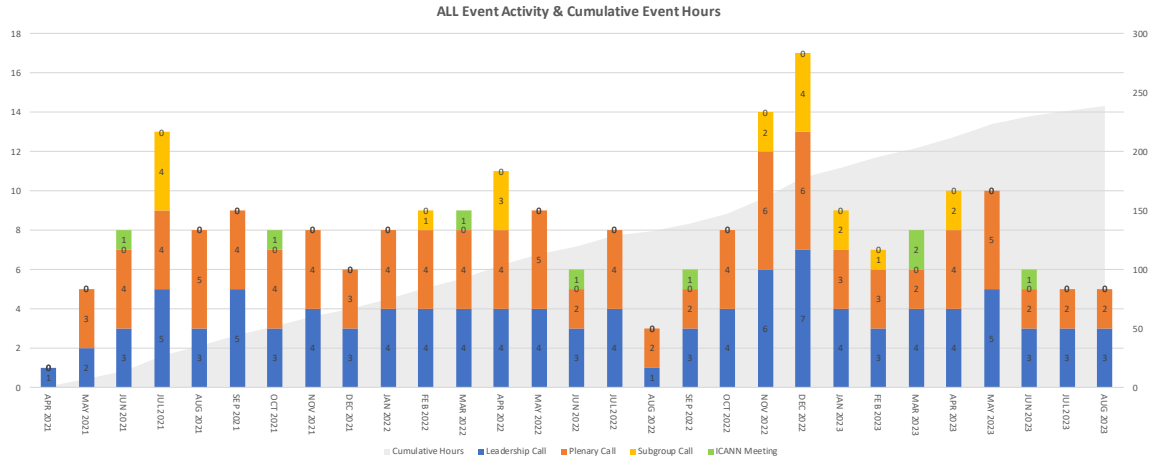

### Plenary Roster and Attendance Only

Member	Row Labels	Sum of Invited Qty	Sum of Attended Qty	Percent	Role	SOI	Start Date	Depart Date
<b>Member</b>		<b>2071</b>	<b>1530</b>	<b>73.9%</b>				
<b>At-Large Advisory Committee (ALAC)</b>		<b>188</b>	<b>119</b>	<b>63.3%</b>				
Nanghaka Daniel Khauka		94	41	43.6%		<a href="https://community.icann.org/x/xieAw">https://community.icann.org/x/xieAw</a>	5/4/2021	
Steinar Grøttersd		94	78	83.0%		<a href="https://community.icann.org/x/LoK1CO">https://community.icann.org/x/LoK1CO</a>	5/5/2021	
<b>Commercial Business Users Constituency (BC)</b>		<b>94</b>	<b>82</b>	<b>87.2%</b>				
Zak Muscovitch		94	82	87.2%		<a href="https://community.icann.org/x/UEmAAw">https://community.icann.org/x/UEmAAw</a>	4/23/2021	
<b>GNSO Council</b>		<b>194</b>	<b>159</b>	<b>82.0%</b>				
Gregory DiBlase		69	41	59.4%	Liaison	<a href="https://community.icann.org/x/CEpAw">https://community.icann.org/x/CEpAw</a>	6/4/2021	12/21/2022
Roger Carney		101	101	100.0%	Chair	<a href="https://community.icann.org/x/COMdAw">https://community.icann.org/x/COMdAw</a>	4/23/2021	
Oswaldo Novoa		24	17	70.8%	Liaison	<a href="https://community.icann.org/x/HpbPAw">https://community.icann.org/x/HpbPAw</a>	12/21/2022	
<b>Independent</b>		<b>94</b>	<b>13</b>	<b>13.8%</b>				
Stephen Crocker		94	13	13.8%	Subject Matter Expert	<a href="https://community.icann.org/x/cBK8B">https://community.icann.org/x/cBK8B</a>	4/26/2021	
<b>Intellectual Property Constituency (IPC)</b>		<b>188</b>	<b>47</b>	<b>25.0%</b>				
Mike Rodenbaugh		94	39	41.5%		<a href="https://community.icann.org/x/Ah9-Aw">https://community.icann.org/x/Ah9-Aw</a>	4/21/2021	
Salvador Camacho Hernandez		94	8	8.5%		<a href="https://community.icann.org/x/L1-AAw">https://community.icann.org/x/L1-AAw</a>	4/26/2021	
<b>Internet Service Providers and Connectivity Providers Constituency</b>		<b>94</b>	<b>74</b>	<b>78.7%</b>				
John Woodworth		94	74	78.7%		<a href="https://community.icann.org/x/GwK1CO">https://community.icann.org/x/GwK1CO</a>	4/14/2021	
<b>Non-Commercial Stakeholder Group (NCSG)</b>		<b>59</b>	<b>29</b>	<b>49.2%</b>				
Juan Manuel Rojas		23	20	87.0%		<a href="https://community.icann.org/x/E8PbAQ">https://community.icann.org/x/E8PbAQ</a>	6/22/2022	
Raoul Plommer		34	7	20.6%		<a href="https://community.icann.org/x/RQabAw">https://community.icann.org/x/RQabAw</a>	7/12/2022	6/27/2023
Kenneth Herman		2	2	100.0%		<a href="https://community.icann.org/x/AIbDg">https://community.icann.org/x/AIbDg</a>	7/25/2023	
<b>Registrar Stakeholder Group (RrSG)</b>		<b>1008</b>	<b>884</b>	<b>87.7%</b>				
Catherine Merdinger		94	71	75.5%		<a href="https://community.icann.org/x/SAW1CO">https://community.icann.org/x/SAW1CO</a>	4/27/2021	
Eric Rokobauer		93	86	92.5%		<a href="https://community.icann.org/x/dCK4Aw">https://community.icann.org/x/dCK4Aw</a>	4/26/2021	
Jody Kolker		87	86	98.9%		<a href="https://community.icann.org/x/eAKAAw">https://community.icann.org/x/eAKAAw</a>	5/7/2021	
Jothan Frakes		87	86	98.9%		<a href="https://community.icann.org/x/Gb-hAg">https://community.icann.org/x/Gb-hAg</a>	4/23/2021	
Keiron Tobin		70	59	84.3%		<a href="https://community.icann.org/x/dAppCO">https://community.icann.org/x/dAppCO</a>	6/7/2021	2/10/2023
Owen Smigelski		94	81	86.2%		<a href="https://community.icann.org/x/BalWBg">https://community.icann.org/x/BalWBg</a>	4/27/2021	
Prudence Malinki		94	79	84.0%		<a href="https://community.icann.org/x/NoC1CO">https://community.icann.org/x/NoC1CO</a>	4/27/2021	
Richard Merdinger		4	4	100.0%		<a href="https://community.icann.org/x/RASnAw">https://community.icann.org/x/RASnAw</a>	5/5/2021	6/7/2021
Sarah Wylde		94	81	86.2%		<a href="https://community.icann.org/x/PwS6Ag">https://community.icann.org/x/PwS6Ag</a>	4/23/2021	
Theo Geurts		94	81	86.2%		<a href="https://community.icann.org/x/jRqWAg">https://community.icann.org/x/jRqWAg</a>	4/23/2021	
Thomas Keller		16	9	56.3%		<a href="https://community.icann.org/x/bEh-Aw">https://community.icann.org/x/bEh-Aw</a>	4/26/2021	9/27/2021
Volker Greimann		87	71	81.6%		<a href="https://community.icann.org/x/IsBwAg">https://community.icann.org/x/IsBwAg</a>	4/24/2021	
Nan Chu		94	90	95.7%		<a href="https://community.icann.org/x/DYUzAw">https://community.icann.org/x/DYUzAw</a>	5/6/2021	
<b>Registry Stakeholder Group (RySG)</b>		<b>152</b>	<b>123</b>	<b>80.9%</b>				
James Galvin		94	73	77.7%		<a href="https://community.icann.org/x/IsE1Aw">https://community.icann.org/x/IsE1Aw</a>	4/27/2021	
Richard Wilhelm		58	50	86.2%		<a href="https://community.icann.org/x/BbK1Cw">https://community.icann.org/x/BbK1Cw</a>	11/23/2022	
<b>Alternate</b>		<b>578</b>	<b>474</b>	<b>82.0%</b>				
<b>At-Large Advisory Committee (ALAC)</b>		<b>76</b>	<b>68</b>	<b>89.5%</b>				
Lutz Donnerhacke		40	36	90.0%		<a href="https://community.icann.org/x/BAHOQO">https://community.icann.org/x/BAHOQO</a>	5/8/2021	
Raymond Selorm Mamattah		36	32	88.9%		<a href="https://community.icann.org/x/FptEB">https://community.icann.org/x/FptEB</a>	5/4/2021	
<b>Commercial Business Users Constituency (BC)</b>		<b>81</b>	<b>80</b>	<b>98.8%</b>				
Ariola Akinyemi		81	80	98.8%		<a href="https://community.icann.org/x/yAF-Cg">https://community.icann.org/x/yAF-Cg</a>	8/12/2021	
<b>Non-Commercial Stakeholder Group (NCSG)</b>		<b>147</b>	<b>61</b>	<b>41.5%</b>				
Farzaneh Badiei		57	16	28.1%		<a href="https://community.icann.org/x/UhenAw">https://community.icann.org/x/UhenAw</a>	6/1/21	7/24/2023
Wisdom Dankor		90	45	50.0%		<a href="https://community.icann.org/x/112AAw">https://community.icann.org/x/112AAw</a>	6/1/2021	
<b>Registrar Stakeholder Group (RrSG)</b>		<b>257</b>	<b>248</b>	<b>96.5%</b>				
Andrew Reberry		5	4	80.0%			4/23/2021	
Arnaud Wittersheim		66	65	98.5%		<a href="https://community.icann.org/x/CEBQnAw">https://community.icann.org/x/CEBQnAw</a>	5/5/2021	
Essie Musallov		81	81	100.0%		<a href="https://community.icann.org/x/aQW1CO">https://community.icann.org/x/aQW1CO</a>	4/23/2021	
Jacques Blanc		7	4	57.1%		<a href="https://community.icann.org/x/6oK1CO">https://community.icann.org/x/6oK1CO</a>	4/29/2021	
Min Feng		5	2	40.0%		<a href="https://community.icann.org/x/VIK1CO">https://community.icann.org/x/VIK1CO</a>	4/26/2021	
Pam Little		2	1	50.0%		<a href="https://community.icann.org/x/IsBwAg">https://community.icann.org/x/IsBwAg</a>	4/26/2021	5/30/2023
Richard Brown		83	83	100.0%		<a href="https://community.icann.org/x/VAW1CO">https://community.icann.org/x/VAW1CO</a>	4/26/2021	
Christopher Patterson		7	7	100.0%		<a href="https://community.icann.org/x/w4pXDG">https://community.icann.org/x/w4pXDG</a>	5/14/2021	
<b>Registry Stakeholder Group (RySG)</b>		<b>15</b>	<b>15</b>	<b>100.0%</b>				
Benny Simuelsen		1	1	100.0%			4/23/2021	
<b>Registry Stakeholder Group (RySG)</b>		<b>15</b>	<b>15</b>	<b>100.0%</b>				
Carolyn Mitchell		15	15	100.0%		<a href="https://community.icann.org/x/abm4Aw">https://community.icann.org/x/abm4Aw</a>	3/7/2023	
<b>Not-for-Profit Operational Concerns (NPOC)</b>		<b>2</b>	<b>2</b>	<b>100.0%</b>				
Bolutife Adisa		2	2	100.0%		<a href="https://community.icann.org/x/kIKCDg">https://community.icann.org/x/kIKCDg</a>	7/25/2023	
<b>Grand Total</b>		<b>2649</b>	<b>2004</b>	<b>75.7%</b>				

### Staff Support Roster

Row Labels					
<b>Internet Corporation for Assigned Names &amp; Numbers (ICANN)</b>					
Berry Cobb					2/18/2021
Caitlin Tubergen					2/18/2021
Devan Reed					11/16/2021
Emily Barabas					2/18/2021
Holida Yanik					7/17/2023
Isabelle Colas					4/30/2021
Julie Hedlund					6/10/2021
Terri Agnew					2/18/2021
Julia Bisland					2/18/2021
Christian Wheeler					7/27/2023

Health	WBS	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	Q1												Q2												Q3												Q4											
									Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun						
		<b>PDP: Transfer Policy Review</b>	<b>11314</b>	<b>02/18/21</b>	<b>06/19/25</b>		<b>58%</b>	<b>In Progress</b>																																																
		<b>PROJECT CONTROL</b>																																																						
1.1		Project start confirmed	0	02/18/21	02/18/21		100%	Complete																																																
1.2		Adopt/Confirm charter	254	02/18/21	03/24/21	3	100%	Complete																																																
1.3		Confirmation of Team	504	02/18/21	04/28/21	3	100%	Complete																																																
1.4		Appointment of Team Chair	504	02/18/21	04/28/21	3	100%	Complete																																																
1.5		Appointment of Liaison to GNSO Council	504	02/18/21	04/28/21	3	100%	Complete																																																
1.6		Chair / Staff preparations	104	04/29/21	05/12/21	6	100%	Complete																																																
1.7		<b>Project Management</b>	<b>10814</b>	<b>04/29/21</b>	<b>06/19/25</b>		<b>62%</b>	<b>In Progress</b>																																																
1.7.1		Develop and confirm Project Plan	304	04/29/21	06/09/21	6	100%	Complete																																																
1.7.2		Obtain project plan approval from GNSO Council	304	06/10/21	07/21/21	10	100%	Complete																																																
1.7.3		<b>Develop monthly Project Packages and deliver to Group &amp; Council</b>	<b>9004</b>	<b>07/22/21</b>	<b>01/01/25</b>	<b>11</b>	<b>60%</b>	<b>In Progress</b>																																																
1.7.4		<b>Leadership Sub team</b>	<b>9704</b>	<b>04/29/21</b>	<b>01/15/25</b>		<b>62%</b>	<b>In Progress</b>																																																
1.7.4.1		On-going preparation and planning of group activities	9704	04/29/21	01/15/25	6	62%	In Progress																																																
1.7.5		Close project and transition project to implementation	14	06/19/25	06/19/25	14, 267		Not Started																																																
		<b>GROUP DELIBERATIONS</b>	<b>9164</b>	<b>05/13/21</b>	<b>11/14/24</b>		<b>72%</b>	<b>In Progress</b>																																																
2.1		First meeting of Team	14	05/13/21	05/13/21	8	100%	Complete																																																
2.2		Understand Charter, organize materials and develop initial approach	104	05/13/21	05/26/21	8	100%	Complete																																																
2.3		Overview & initial discussion of all Policy Topics	154	05/13/21	06/02/21	8	100%	Complete																																																
2.4		Develop definitions and terminology	304	05/13/21	06/23/21	8	100%	Complete																																																
2.5		Input from other SO/ACs & GNSO SG/CS	914	05/27/21	09/30/21		100%	Complete																																																
2.6		Group 1A Policy Topics	2454	06/03/21	05/11/22		100%	Complete																																																
2.6.1		Topic 1 Deliberations - Gaining FOA	404	12/02/21	01/26/22		100%	Complete																																																
2.6.2		Topic 2 Deliberations - Losing FOA	404	10/07/21	12/01/21		100%	Complete																																																
2.6.3		Topic 3 Deliberations - Additional Security Measures	404	08/12/21	10/06/21		100%	Complete																																																
2.6.4		Topic 4 Deliberations - Auth-Info Code Management	1804	06/03/21	02/09/22		100%	Complete																																																
2.6.5		Topic 5 Deliberations - Bulk Use of Auth-Info Codes	404	02/10/22	04/06/22		100%	Complete																																																
2.6.6		Topic 6 Deliberations - Wave 1, Recommendation 27	254	04/07/22	05/11/22		100%	Complete																																																
2.6.7		Topic 7 Deliberations - Denying Transfers	354	02/10/22	03/30/22		100%	Complete																																																
2.7		Group 1B Policy Topics - Preliminary Discussions	1854	08/16/22	02/01/23	24855	100%	Complete																																																
2.8		Group 1B Policy Topics	1804	09/28/23	06/05/24		26%	In Progress																																																
2.8.1		Topic 7 Deliberations - Change of Registrant / Overall Policy	404	09/28/23	11/22/23		50%	In Progress																																																
2.8.2		Topic 8 Deliberations - Change of Registrant / 60-Day Lock	404	11/23/23	01/17/24		13%	In Progress																																																
2.8.3		Topic 9 Deliberations - Change of Registrant / Privacy/Proxy Customers	354	01/18/24	03/05/24		14%	In Progress																																																
2.8.4		Topic 10 Deliberations - Change of Registrant / Designated Agent	254	03/07/24	04/10/24		20%	In Progress																																																
2.8.5		Topic 11 Deliberations - Change of Registrant / Additional Questions	204	04/11/24	05/08/24		29%	In Progress																																																
2.8.6		Topic 12 Deliberations - Change of Registrant / Wave 1 - Recommendation 27	204	05/08/24	06/05/24		29%	In Progress																																																
2.9		Group 2 Policy Topics	1704	02/02/23	09/27/23		93%	In Progress																																																
2.9.1		Input from other SO/ACs & GNSO SG/CS - Group 2 Topics	814	03/02/23	05/23/23		100%	Complete																																																
2.9.2		Topic 13 Deliberations - Transfer Emergency Action Contact (Inter-Registrar Transfers)	554	03/02/23	04/19/23		100%	Complete																																																
2.9.3		Topic 14 Deliberations - Transfer Dispute Resolution Policy (Inter-Registrar Transfers)	554	04/20/23	07/05/23		100%	Complete																																																
2.9.4		Topic 15 Deliberations - ICANN approved Transfers	404	07/06/23	08/30/23		59%	In Progress																																																
2.9.5		Topic 16 Deliberations - Wave 1, Recommendation 27 Report (RTPP + CoR)	204	08/17/23	08/27/23		100%	Complete																																																
2.10		Key Group Events	794	10/25/21	11/14/24		59%	In Progress																																																
		<b>INITIAL REPORT</b>	<b>8604</b>	<b>08/24/21</b>	<b>11/08/24</b>		<b>65%</b>	<b>In Progress</b>																																																
3.1		Group 1A Initial Report	2904	08/24/21	08/03/22		100%	Complete																																																
3.1.1		Populate stable drafts as required	2304	08/24/21	05/11/22	20	100%	Complete																																																
3.1.2		Discuss/approve findings and interim recommendations	104	05/12/22	05/25/22	27, 40, 51, 60, 72, 83	100%	Complete																																																
3.1.3		Consolidate interim recommendations and findings	104	05/26/22	06/08/22	243	100%	Complete																																																
3.1.4		Build Draft Report for public comment	104	05/26/22	06/08/22	243	100%	Complete																																																
3.1.5		Approve Draft Report for public comment	54	06/08/22	06/15/22	245	100%	Complete																																																
3.1.6		Publish Initial Report - Group 1A	0	06/15/22	06/15/22	246	100%	Complete																																																
3.1.7		Communicate Initial Report	54	06/16/22	06/22/22	246	100%	Complete																																																
3.1.8		Public comment forum on the Initial Report (45 days) +14 Days	354	06/16/22	08/03/22	246	100%	Complete																																																
3.2		Groups (1A, 1B & 2) Initial Report	6254	06/16/22	11/06/24		46%	In Progress																																																
3.2.1		Populate stable drafts as required	5204	06/16/22	06/12/24	247	58%	In Progress																																																
3.2.2		Discuss/approve findings and interim recommendations	204	06/13/24	07/10/24	104, 172, 251		Not Started																																																
3.2.3		Consolidate interim recommendations and findings	204	07/11/24	08/07/24	252		Not Started																																																
3.2.4		Build Draft Report for public comment	204	07/11/24	08/07/24	252		Not Started																																																
3.2.5		Approve Draft Report for public comment	104	08/08/24	08/21/24	254		Not Started																																																
3.2.6		Publish Initial Report - Groups (1A, 1B & 2)	0	08/21/24	08/21/24	255		Not Started																																																
3.2.7		Communicate Initial Report	54	08/22/24	08/28/24	255		Not Started																																																
3.2.8		Public comment forum on the Groups (1A, 1B & 2) Initial Report (60 days)	554	08/22/24	11/06/24	255		Not Started																																																
		<b>FINAL REPORT</b>	<b>6554</b>	<b>08/04/22</b>	<b>02/05/25</b>		<b>22%</b>	<b>In Progress</b>																																																
4.1		Review of public comments - Group 1A	304	08/04/22	09/14/22	249	100%	Complete																																																
4.2		Review of public comments - Groups (1A, 1B & 2)	304	11/07/24	12/18/24	258		Not Started																																																
4.3		Continue deliberations of policy topics towards a Final Report	504	11/07/24	01/15/25	249, 258		Not Started																																																
4.4		Build Final Report & Final Deliberations	54	01/16/25	01/22/25	262		Not Started																																																
4.5		Determine consensus levels on interim recommendations	104	01/23/25	02/05/25	263		Not Started																																																
4.6		Adopt final recommendations and report	104	01/23/25	02/05/25	263		Not Started																																																
4.7		Submission of Groups (1A, 1B & 2) Final Report to the GNSO Council	0	02/05/25	02/05/25	265		Not Started																																																
		<b>POST GROUP TASKS</b>	<b>954</b>	<b>02/06/25</b>	<b>06/18/25</b>			<b>Not Started</b>																																																
5.1		Approval of Final Report and Recommendations by the GNSO Council	454	02/06/25	04/09/25	266		Not Started																																																
5.2		Report to the Board	154	04/10/25	04/30/25	268		Not Started																																																
5.3		Publish Recommendations for Public Comment	354	05/01/25	06/18/25	269		Not Started																																																
5.4		Inform GAC if Recommendations affect public policy	54	05/01/25	05/07/25	269		Not Started																																																
		<b>PDP CHECKLIST</b>	<b>2934</b>	<b>06/20/20</b>	<b>08/04/21</b>		<b>0%</b>																																																	

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting ICANN77 TEAC/TDRP	↓	TPR WG	06/12/23	06/12/23	Complete	
	AI	Charter question f5: WG to consider the feasibility of the recommendation of email to "start the clock" for the 24-hour response timeframe.	—	TPR WG	06/27/23	06/27/23	Complete	
	AI	Charter question g3: WG should consider the two types of disputes – inside and outside the policy – and provide additional rationale/comments.	—	TPR WG	06/27/23	06/27/23	Complete	
	WP	Meeting #95 Review draft responses to Charter Questions g3 - g5; ICANN Approved Transfers	↓	TPR WG	06/27/23	06/27/23	Complete	
	AI	Re: Recap Outcomes from ICANN77 Meeting on TEAC and TDRP -- charter questions f5, and g3, g4, and g5 -- See: <a href="https://docs.google.com/document/d/1zBYlaFTF5bRrUdhnGifP5CGHvuOoHqKPOhGnU46uGM/edit">https://docs.google.com/document/d/1zBYlaFTF5bRrUdhnGifP5CGHvuOoHqKPOhGnU46uGM/edit</a> [docs.google.com] and <a href="https://docs.google.com/document/d/1I2DNZLXCKfmoSyffCIUL7lot3V3Zk96X5Q3eaTrEvp4/edit">https://docs.google.com/document/d/1I2DNZLXCKfmoSyffCIUL7lot3V3Zk96X5Q3eaTrEvp4/edit</a> [docs.google.com]; WG members to review the text in the two documents and provide comments in advance of the next meeting on Tuesday, 11 July.	—	TPR WG	07/11/23	07/11/23	Complete	
	AI	Re: Bulk Transfers – WG to review charter questions in advance of the discussion at the next meeting: i1) In light of these challenges described in section 3.1.7.2 of the Final Issue Report, should the required fee in Section I.B.2 of the Transfer Policy be revisited or removed in certain circumstances i2) Should the scope of voluntary bulk transfers, including partial bulk transfers, be expanded and/or made uniform across all registry operators? If so, what types of rules and considerations should govern voluntary bulk transfers and partial bulk transfers	—	TPR WG	07/11/23	07/11/23	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	07/10/23	07/10/23	Complete	
	WP	Meeting #96 ICANN Approved Transfers - Charter Question i1	↓	TPR WG	07/11/23	07/11/23	Complete	
	WP	Meeting #97 ICANN Approved Transfers	↓	TPR WG	07/25/23	07/25/23	Complete	
	AI	Charter Question i1 ICANN-Approved Transfer (Bulk Transfers) -- Staff will create a working document in Google for WG members to provide comments/suggestions.	—	Policy Support Staff	08/01/23	08/01/23	Complete	
	AI	1.B proposed updates: Staff will create a working document in Google for WG members to provide comments/suggestions.	—	Policy Support Staff	08/01/23	08/01/23	Complete	
	WP	Meeting #98 ICANN Approved Transfers	↓	TPR WG	08/01/23	08/01/23	Complete	
	AI	Charter question i1 staff to create a working document with the preliminary agreements for WG members to review and suggest revisions.	—	Policy Support Staff	08/07/23	08/01/23	Complete	
	WP	Meeting #99 ICANN Approved Transfers	↓	TPR WG	08/08/23	08/08/23	Complete	
	AI	Any WG members who have comments or concerns regarding charter question i1 preliminary agreements please note them in the ICANN-Approved Transfers Working Document [docs.google.com] in advance of the next meeting.	—	TPR WG	08/14/23	08/14/23	Complete	
	AI	Continue today's discussion on the mailing list: Should there be locks, notices, and/or opt-out options for registrants?	—	TPR WG	08/14/23	08/14/23	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	08/14/23	08/14/23	Complete	
	WP	Meeting #100 ICANN Approved Transfers	↓	TPR WG	08/15/23		In Progress	
	WP	Meeting #101 ICANN Approved Transfers	↓	TPR WG	08/22/23		Not Started	
	WP	Meeting #102 ICANN Approved Transfers	↓	TPR WG	08/29/23		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	09/11/23		Not Started	
	WP	Meeting #103 "Where we're at" review across Groups 1A, 1B & 2	↓	TPR WG	09/12/23		Not Started	
	WP	Meeting #104 Change of Registrant	↓	TPR WG	09/19/23		Not Started	
	WP	Meeting #105 Change of Registrant	↓	TPR WG	09/26/23		Not Started	
	WP	Meeting #106 Change of Registrant	↓	TPR WG	10/03/23		Not Started	
	WP	Meeting #107 Change of Registrant	↓	TPR WG	10/10/23		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	10/15/23		Not Started	
	WP	ICANN78 Meeting TBD	↓	TPR WG	10/21/23		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	11/06/23		Not Started	
	MS	Submit Consolidated Initial Report to GNSO Council & Public Comment	!	TPR WG	08/21/24		Not Started	
