

# Project Tracking & Rollup DASHBOARD

**Project Name** PDP: Transfer Policy Review **Program** Transfers **Project Sponsor** GNSO Council

**Project Information**


**61%**  
% Complete

**02/18/21**  
Actual Start

**06/19/25**  
Planned Finish

**Project Status & Health**

Project\_Status: Revised Schedule (Red), Project\_Health: On-Target (Green)

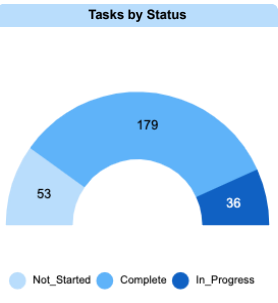

**Project Contacts**


**Roger Carney**  
Chair

**n/a**  
Vice\_Chair

**Oswaldo Novoa**  
Liaison

**Caitlin Tubergen**  
Staff\_Lead

**Berry Cobb**  
Project\_Manager

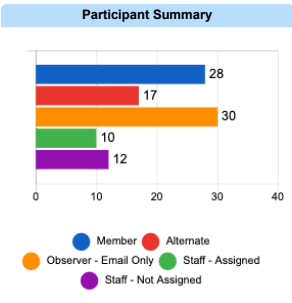

**Summary Gantt & Key Milestones**

Health	Primary Task	Current Start	Current Finish	% Complete	Status	2021	2022	2023	2024	2025					
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	
	<b>PDP: Transfer Policy Review</b>	02/18/21	06/19/25	61%	In Progress	[Gantt bars for PDP: Transfer Policy Review]									
	<b>PROJECT CONTROL</b>	02/18/21	06/19/25	72%	In Progress	[Gantt bars for PROJECT CONTROL]									
	<b>GROUP DELIBERATIONS</b>	05/13/21	11/14/24	73%	In Progress	[Gantt bars for GROUP DELIBERATIONS]									
	Group 1A Policy Topics	06/03/21	05/11/22	100%	Complete	[Gantt bars for Group 1A Policy Topics]									
	Group 1B Policy Topics	09/28/23	06/05/24	26%	In Progress	[Gantt bars for Group 1B Policy Topics]									
	Group 2 Policy Topics	02/02/23	09/27/23	100%	Complete	[Gantt bars for Group 2 Policy Topics]									
	<b>INITIAL REPORT</b>	06/24/21	11/06/24	69%	In Progress	[Gantt bars for INITIAL REPORT]									
	Publish Initial Report - Group 1A	06/15/22	06/15/22	100%	Complete	[Gantt bars for Publish Initial Report - Group 1A]									
	Publish Initial Report - Groups (1A, 1B & 2)	08/21/24	08/21/24	Not Started	Not Started	[Gantt bars for Publish Initial Report - Groups (1A, 1B & 2)]									
	<b>FINAL REPORT</b>	08/04/22	02/05/25	22%	In Progress	[Gantt bars for FINAL REPORT]									
	Review of public comments - Group 1A	08/04/22	09/14/22	100%	Complete	[Gantt bars for Review of public comments - Group 1A]									
	Review of public comments - Groups (1A, 1B & 2)	11/07/24	12/18/24	Not Started	Not Started	[Gantt bars for Review of public comments - Groups (1A, 1B & 2)]									
	Submission of Groups (1A, 1B & 2) Final Report to the GNSO Council	02/05/25	02/05/25	Not Started	Not Started	[Gantt bars for Submission of Groups (1A, 1B & 2) Final Report to the GNSO Council]									

**Project Description**

On 18 February 2021, The GNSO Council passed a resolution to initiate a two-phased PDP to review the Transfer Policy. The PDP working group is tasked with determining if changes to the policy are needed to improve the ease, security, and efficacy of inter-registrar and inter-registrant transfers.

[Mailing List](#)  
[Meeting Schedule](#)  
[Wiki](#)  
[Charter](#)

**Completed in Prior Period**

- Completed deliberations on ICANN-Approved Transfers.
- Completed and distributed [Project Package](#).

**Open Issues & Risks**



Deliberations on ICANN-Approved Transfers are behind schedule, and now impacting the critical path to pivot over to Change of Registrant charter topics. The WG will consider a quicker pace through ICANN79 to make up time.



**Current Activities & Tasks**

- Working session at ICANN78 in Hamburg focused on the last items for TDRP.
- Conduct a "where we're at" materials and WG session regarding all topics from Groups 1A, 1B, & Group 2.

**Planned Activities & Tasks**

- Conduct a "where we're at" materials & WG session regarding all topics from Groups 1A, 1B, and Group 2.

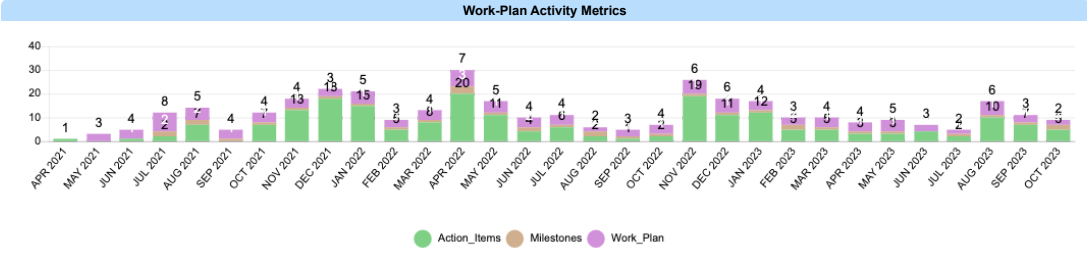

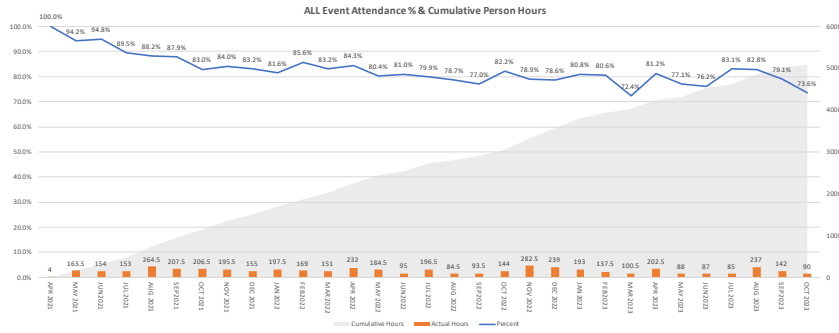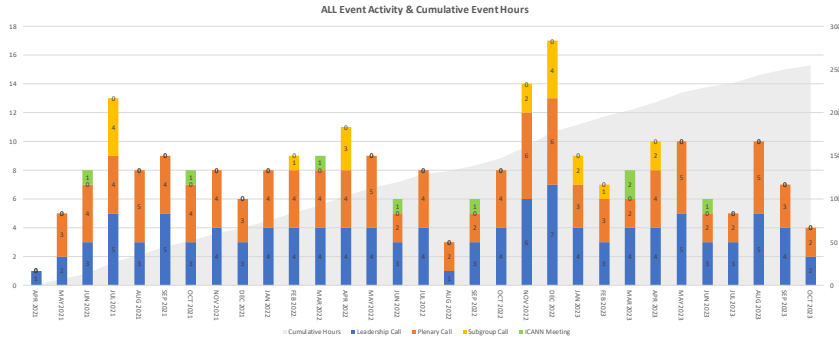

### Plenary Roster and Attendance Only

Row Labels	Sum of limited Qty	Sum of Attended Qty	Percent	Role	SOI	Start Date	Depart Date
<b>Member</b>	<b>2255</b>	<b>1650</b>	<b>73.2%</b>				
At-Large Advisory Committee (ALAC)	204	124	60.8%				
Nangima Daniel Khauka	102	81	40.2%		<a href="https://community.icann.org/v/1h0d8w">https://community.icann.org/v/1h0d8w</a>	5/4/2021	
Stenar Grotterud	102	83	81.4%		<a href="https://community.icann.org/v/1sk1CQ">https://community.icann.org/v/1sk1CQ</a>	5/5/2021	
Commercial Business Users Constituency (BC)	102	89	87.3%				
Zak Muscovitch	102	89	87.3%		<a href="https://community.icann.org/v/1f6m8Aw">https://community.icann.org/v/1f6m8Aw</a>	4/23/2021	
<b>GNSS Council</b>	<b>210</b>	<b>174</b>	<b>82.9%</b>				
Gregory Dilliaux	69	41	59.4%	Liaison	<a href="https://community.icann.org/v/1u7EnAw">https://community.icann.org/v/1u7EnAw</a>	6/4/2021	12/21/2022
Roger Carney	109	109	100.0%	Chair	<a href="https://community.icann.org/v/1C0M87w">https://community.icann.org/v/1C0M87w</a>	4/23/2021	
Osvaldo Novoa	31	24	75.0%	Liaison	<a href="https://community.icann.org/v/1y6p8AD">https://community.icann.org/v/1y6p8AD</a>	12/11/2023	
<b>Independent</b>	<b>102</b>	<b>13</b>	<b>12.7%</b>				
Stephen Crocker	102	13	12.7%	Subject Matter Expert	<a href="https://community.icann.org/v/1c8k8B">https://community.icann.org/v/1c8k8B</a>	4/26/2021	
Intellectual Property Constituency (IPC)	204	49	24.0%				
Mike Roddenough	102	43	42.2%		<a href="https://community.icann.org/v/1A9-4g">https://community.icann.org/v/1A9-4g</a>	4/21/2021	
Salvador Camacho Hernandez	102	8	7.8%		<a href="https://community.icann.org/v/11-1Ag">https://community.icann.org/v/11-1Ag</a>	4/26/2021	
Internet Service Providers and Connectivity Providers Constituency	102	80	78.4%				
John Woodworth	102	80	78.4%		<a href="https://community.icann.org/v/1GwK2O">https://community.icann.org/v/1GwK2O</a>	4/14/2021	
<b>Non-Commercial Stakeholder Group (NCSG)</b>	<b>75</b>	<b>42</b>	<b>56.0%</b>				
Juan Manuel Rojas	31	25	80.6%		<a href="https://community.icann.org/v/1E8P8Ac">https://community.icann.org/v/1E8P8Ac</a>	6/22/2022	
Raoul Plommer	24	7	29.2%		<a href="https://community.icann.org/v/1c388w">https://community.icann.org/v/1c388w</a>	7/12/2022	6/27/2023
Kenneth Herman	10	10	100.0%		<a href="https://community.icann.org/v/1f6p8w">https://community.icann.org/v/1f6p8w</a>	7/25/2023	
<b>Registrar Stakeholder Group (RSG)</b>	<b>1088</b>	<b>944</b>	<b>86.8%</b>				
Callienne Merzinger	102	76	74.5%		<a href="https://community.icann.org/v/158k8C">https://community.icann.org/v/158k8C</a>	4/27/2021	
Eric Robozauer	101	94	93.1%		<a href="https://community.icann.org/v/1G5-4Aw">https://community.icann.org/v/1G5-4Aw</a>	4/26/2021	
Jody Kolker	95	91	95.8%		<a href="https://community.icann.org/v/1e61Aw">https://community.icann.org/v/1e61Aw</a>	5/7/2021	
Jothan Frakes	95	92	96.8%		<a href="https://community.icann.org/v/1G6-38g">https://community.icann.org/v/1G6-38g</a>	4/23/2021	
Kenan Toban	70	59	84.3%		<a href="https://community.icann.org/v/1678CQ">https://community.icann.org/v/1678CQ</a>	4/7/2021	3/10/2023
Owen Smigelski	102	88	86.3%		<a href="https://community.icann.org/v/18a1W8">https://community.icann.org/v/18a1W8</a>	4/27/2021	
Prudence Malinski	102	85	83.3%		<a href="https://community.icann.org/v/18c-1CQ">https://community.icann.org/v/18c-1CQ</a>	4/27/2021	
Richard Merzinger	4	4	100.0%		<a href="https://community.icann.org/v/1c388w">https://community.icann.org/v/1c388w</a>	5/5/2021	6/7/2021
Sarah Wylid	102	86	84.3%		<a href="https://community.icann.org/v/176w8g">https://community.icann.org/v/176w8g</a>	4/23/2021	
Theo Geurts	102	89	87.3%		<a href="https://community.icann.org/v/176p8g">https://community.icann.org/v/176p8g</a>	4/23/2021	
Thomas Keller	16	8	50.0%		<a href="https://community.icann.org/v/18b-1Aw">https://community.icann.org/v/18b-1Aw</a>	4/26/2021	9/27/2021
Volker Gerstman	95	74	77.9%		<a href="https://community.icann.org/v/1c388w">https://community.icann.org/v/1c388w</a>	4/24/2021	
Nan Chu	102	97	95.1%		<a href="https://community.icann.org/v/1D01Aw">https://community.icann.org/v/1D01Aw</a>	5/6/2021	
<b>Registry Stakeholder Group (RSG)</b>	<b>168</b>	<b>135</b>	<b>80.4%</b>				
James Gilbert	102	79	77.5%		<a href="https://community.icann.org/v/18q1-1Aw">https://community.icann.org/v/18q1-1Aw</a>	4/27/2021	
Richard Wilhelm	66	56	84.8%		<a href="https://community.icann.org/v/18b1Cw">https://community.icann.org/v/18b1Cw</a>	11/23/2022	
<b>Alternate</b>	<b>64</b>	<b>53</b>	<b>83.5%</b>				
At-Large Advisory Committee (ALAC)	83	72	88.0%				
Lutz Donnerhacke	43	39	90.7%		<a href="https://community.icann.org/v/18a1W8CQ">https://community.icann.org/v/18a1W8CQ</a>	5/8/2021	
Raymond Salfom Mamatah	40	34	85.0%		<a href="https://community.icann.org/v/18a1E8">https://community.icann.org/v/18a1E8</a>	5/4/2021	
Commercial Business Users Constituency (BC)	89	88	98.9%				
Ariana Aljomei	89	88	98.9%		<a href="https://community.icann.org/v/18a1Eg">https://community.icann.org/v/18a1Eg</a>	8/12/2021	
<b>Non-Commercial Stakeholder Group (NCSG)</b>	<b>149</b>	<b>63</b>	<b>42.3%</b>				
Farzaneh Badiei	57	16	28.1%		<a href="https://community.icann.org/v/18a1E8w">https://community.icann.org/v/18a1E8w</a>	6/1/21	7/24/2023
Wisdom Donkai	92	47	51.1%		<a href="https://community.icann.org/v/18a1E8w">https://community.icann.org/v/18a1E8w</a>	6/1/2021	
<b>Registrar Stakeholder Group (RSG)</b>	<b>297</b>	<b>288</b>	<b>97.0%</b>				
Andrew Reberny	5	4	80.0%		<a href="https://community.icann.org/v/18a1E8w">https://community.icann.org/v/18a1E8w</a>	4/23/2021	
Arnold Wittenheim	73	72	98.6%		<a href="https://community.icann.org/v/18a1E8w">https://community.icann.org/v/18a1E8w</a>	5/5/2021	
Estie Musalov	83	83	100.0%		<a href="https://community.icann.org/v/18a1E8w">https://community.icann.org/v/18a1E8w</a>	4/23/2021	
Jacques Blanc	7	4	57.1%		<a href="https://community.icann.org/v/18a1E8w">https://community.icann.org/v/18a1E8w</a>	4/29/2021	
Min Feng	5	2	40.0%		<a href="https://community.icann.org/v/18a1E8w">https://community.icann.org/v/18a1E8w</a>	4/26/2021	
Pam Little	2	1	50.0%		<a href="https://community.icann.org/v/18a1E8w">https://community.icann.org/v/18a1E8w</a>	4/26/2021	5/30/2023
Richard Brown	91	91	100.0%		<a href="https://community.icann.org/v/18a1E8w">https://community.icann.org/v/18a1E8w</a>	4/26/2021	
Christopher Patterson	15	15	100.0%		<a href="https://community.icann.org/v/18a1E8w">https://community.icann.org/v/18a1E8w</a>	5/14/2021	
Benny Samalson	9	9	100.0%		<a href="https://community.icann.org/v/18a1E8w">https://community.icann.org/v/18a1E8w</a>	4/23/2021	
Heidi Revets	7	7	100.0%		<a href="https://community.icann.org/v/18a1E8w">https://community.icann.org/v/18a1E8w</a>	7/24/2023	
<b>Registry Stakeholder Group (RSG)</b>	<b>22</b>	<b>22</b>	<b>100.0%</b>				
Carolyn Mitchell	22	22	100.0%		<a href="https://community.icann.org/v/18a1E8w">https://community.icann.org/v/18a1E8w</a>	3/7/2023	
<b>Not-for-Profit Operational Concerns (NPOC)</b>	<b>4</b>	<b>4</b>	<b>100.0%</b>				
Bolufife Adisa	4	4	100.0%		<a href="https://community.icann.org/v/18a1E8w">https://community.icann.org/v/18a1E8w</a>	7/25/2023	
<b>Grand Total</b>	<b>2899</b>	<b>2188</b>	<b>75.5%</b>				

### Staff Support Roster

Row Labels	Start Date	Depart Date
<b>Internet Corporation for Assigned Names &amp; Numbers (ICANN)</b>		
Berry Cobb	2/18/2021	
Caitlin Tubergen	2/18/2021	
Devan Reed	11/16/2021	
Emily Barban	2/18/2021	7/17/2023
Hollis Park	4/30/2021	
Isabelle Colas	6/10/2021	
Julie Hedlund	2/18/2021	
Terri Agnew	2/18/2021	
Julia Bistand	2/18/2021	
Christian Wheeler	7/27/2023	

Health	WBS	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	Q1												Q2												Q3												Q4											
									Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
		<b>PDP: Transfer Policy Review</b>	<b>11316</b>	<b>02/18/21</b>	<b>06/19/25</b>		<b>61%</b>	<b>In Progress</b>																																																
		<b>PROJECT CONTROL</b>																																																						
1		Project start confirmed	0	02/18/21	02/18/21		100%	Complete																																																
1.1		Adopt/Confirm charter	254	02/18/21	03/24/21	3	100%	Complete																																																
1.2		Confirmation of Team	504	02/18/21	04/28/21	3	100%	Complete																																																
1.3		Appointment of Team Chair	504	02/18/21	04/28/21	3	100%	Complete																																																
1.4		Appointment of Liaison to GNSO Council	504	02/18/21	04/28/21	3	100%	Complete																																																
1.5		Chair / Staff preparations	104	04/29/21	05/12/21	6	100%	Complete																																																
1.6		<b>Project Management</b>	<b>10814</b>	<b>04/29/21</b>	<b>06/19/25</b>		<b>67%</b>	<b>In Progress</b>																																																
1.7		Develop and confirm Project Plan	304	04/29/21	06/09/21	6	100%	Complete																																																
1.7.1		Obtain project plan approval from GNSO Council	304	06/10/21	07/21/21	10	100%	Complete																																																
1.7.2		<b>Develop monthly Project Packages and deliver to Group &amp; Council</b>	<b>9004</b>	<b>07/22/21</b>	<b>01/01/25</b>	<b>11</b>	<b>65%</b>	<b>In Progress</b>																																																
1.7.3		<b>Leadership Sub team</b>	<b>9704</b>	<b>04/29/21</b>	<b>01/15/25</b>		<b>67%</b>	<b>In Progress</b>																																																
1.7.4		On-going preparation and planning of group activities	9704	04/29/21	01/15/25	6	67%	In Progress																																																
1.7.4.1		Close project and transition project to implementation	14	06/19/25	06/19/25	14, 267		Not Started																																																
1.7.5																																																								
2		<b>GROUP DELIBERATIONS</b>	<b>9164</b>	<b>06/13/21</b>	<b>11/14/24</b>		<b>73%</b>	<b>In Progress</b>																																																
2.1		First meeting of Team	14	05/13/21	05/13/21	8	100%	Complete																																																
2.2		Understand Charter, organize materials and develop initial approach	104	05/13/21	05/26/21	8	100%	Complete																																																
2.3		Overview & initial discussion of all Policy Topics	154	05/13/21	06/02/21	8	100%	Complete																																																
2.4		Develop definitions and terminology	304	05/13/21	06/23/21	8	100%	Complete																																																
2.5		Input from other SO/ACs & GNSO SG/CS	914	05/27/21	09/30/21		100%	Complete																																																
2.6		Group 1A Policy Topics	2454	06/03/21	05/11/22		100%	Complete																																																
2.6.1		Topic 1 Deliberations - Gaining FOA	404	12/02/21	01/26/22		100%	Complete																																																
2.6.2		Topic 2 Deliberations - Losing FOA	404	10/07/21	12/01/21		100%	Complete																																																
2.6.3		Topic 3 Deliberations - Additional Security Measures	404	08/12/21	10/06/21		100%	Complete																																																
2.6.4		Topic 4 Deliberations - Auth-Info Code Management	1804	06/03/21	02/09/22		100%	Complete																																																
2.6.5		Topic 5 Deliberations - Bulk Use of Auth-Info Codes	404	02/10/22	04/06/22		100%	Complete																																																
2.6.6		Topic 6 Deliberations - Wave 1, Recommendation 27	254	04/07/22	05/11/22		100%	Complete																																																
2.6.7		Topic 7 Deliberations - Denying Transfers	354	02/10/22	03/30/22		100%	Complete																																																
2.7		Group 1B Policy Topics - Preliminary Discussions	1854	08/16/22	02/01/23	24855	100%	Complete																																																
2.8		Group 1B Policy Topics	1804	09/28/23	06/05/24		26%	In Progress																																																
2.8.1		Topic 7 Deliberations - Change of Registrant / Overall Policy	404	09/28/23	11/22/23		50%	In Progress																																																
2.8.2		Topic 8 Deliberations - Change of Registrant / 60-Day Lock	404	11/23/23	01/17/24		13%	In Progress																																																
2.8.3		Topic 9 Deliberations - Change of Registrant / Privacy/Proxy Customers	354	01/18/24	03/05/24		14%	In Progress																																																
2.8.4		Topic 10 Deliberations - Change of Registrant / Designated Agent	254	03/07/24	04/10/24		20%	In Progress																																																
2.8.5		Topic 11 Deliberations - Change of Registrant / Additional Questions	204	04/11/24	05/08/24		29%	In Progress																																																
2.8.6		Topic 12 Deliberations - Change of Registrant / Wave 1 - Recommendation 27	204	05/08/24	06/05/24		29%	In Progress																																																
2.9		Group 2 Policy Topics	1704	02/03/23	09/27/23		100%	Complete																																																
2.9.1		Input from other SO/ACs & GNSO SG/CS - Group 2 Topics	914	02/03/23	05/25/23		100%	Complete																																																
2.9.2		Topic 13 Deliberations - Transfer Emergency Action Contact (Inter-Registrar Transfers)	554	02/03/23	04/19/23		100%	Complete																																																
2.9.3		Topic 14 Deliberations - Transfer Dispute Resolution Policy (Inter-Registrar Transfers)	554	04/20/23	07/05/23		100%	Complete																																																
2.9.4		Topic 15 Deliberations - ICANN approved Transfers	404	07/08/23	08/30/23		100%	Complete																																																
2.9.5		Topic 16 Deliberations - Wave 1, Recommendation 27 Report (RTP + CoR)	204	09/11/23	09/27/23		100%	Complete																																																
2.10		Key Group Events	794	10/25/21	11/14/24		59%	In Progress																																																
3		<b>INITIAL REPORT</b>	<b>8604</b>	<b>08/24/21</b>	<b>11/08/24</b>		<b>69%</b>	<b>In Progress</b>																																																
3.1		Group 1A Initial Report	2904	08/24/21	08/03/22		100%	Complete																																																
3.1.1		Populate stable drafts as required	2304	08/24/21	05/11/22	20	100%	Complete																																																
3.1.2		Discuss/approve findings and interim recommendations	104	05/12/22	05/25/22	27, 40, 51, 60, 72, 83	100%	Complete																																																
3.1.3		Consolidate interim recommendations and findings	104	05/26/22	06/08/22	243	100%	Complete																																																
3.1.4		Build Draft Report for public comment	104	05/26/22	06/08/22	243	100%	Complete																																																
3.1.5		Approve Draft Report for public comment	54	06/09/22	06/15/22	245	100%	Complete																																																
3.1.6		Publish Initial Report - Group 1A	0	06/15/22	06/15/22	246	100%	Complete																																																
3.1.7		Communicate Initial Report	54	06/16/22	06/22/22	246	100%	Complete																																																
3.1.8		Public comment forum on the Initial Report (45 days) +14 Days	354	06/16/22	08/03/22	246	100%	Complete																																																
3.2		Groups (1A, 1B & 2) Initial Report	6254	06/16/22	11/06/24		54%	In Progress																																																
3.2.1		Populate stable drafts as required	5204	06/16/22	06/12/24	247	67%	In Progress																																																
3.2.2		Discuss/approve findings and interim recommendations	204	06/13/24	07/10/24	104, 172, 251		Not Started																																																
3.2.3		Consolidate interim recommendations and findings	204	07/11/24	08/07/24	252		Not Started																																																
3.2.4		Build Draft Report for public comment	204	07/11/24	08/07/24	252		Not Started																																																
3.2.5		Approve Draft Report for public comment	104	08/08/24	08/21/24	254		Not Started																																																
3.2.6		Publish Initial Report - Groups (1A, 1B & 2)	0	08/21/24	08/21/24	255		Not Started																																																
3.2.7		Communicate Initial Report	54	08/22/24	08/28/24	255		Not Started																																																
3.2.8		Public comment forum on the Groups (1A, 1B & 2) Initial Report (60 days)	554	08/22/24	11/06/24	255		Not Started																																																
4		<b>FINAL REPORT</b>	<b>6554</b>	<b>08/04/22</b>	<b>02/05/25</b>		<b>22%</b>	<b>In Progress</b>																																																
4.1		Review of public comments - Group 1A	304	08/04/22	09/14/22	249	100%	Complete																																																
4.2		Review of public comments - Groups (1A, 1B & 2)	304	11/07/24	12/18/24	258		Not Started																																																
4.3		Continue deliberations of policy topics towards a Final Report	504	11/07/24	01/15/25	249, 258		Not Started																																																
4.4		Build Final Report & Final Deliberations	54	01/16/25	01/22/25	262		Not Started																																																
4.5		Determine consensus levels on interim recommendations	104	01/23/25	02/05/25	263		Not Started																																																
4.6		Adopt final recommendations and report	104	01/23/25	02/05/25	263		Not Started																																																
4.7		Submission of Groups (1A, 1B & 2) Final Report to the GNSO Council	0	02/05/25	02/05/25	265		Not Started																																																
5		<b>POST GROUP TASKS</b>	<b>954</b>	<b>02/06/25</b>	<b>06/18/25</b>			<b>Not Started</b>																																																
5.1		Approval of Final Report and Recommendations by the GNSO Council	454	02/06/25	04/09/25	266		Not Started																																																
5.2		Report to the Board	154	04/10/25	04/30/25	268		Not Started																																																
5.3		Publish Recommendations for Public Comment	354	05/01/25	06/18/25	269		Not Started																																																
5.4		Inform GAC if Recommendations affect public policy	54	05/01/25	05/07/25	269		Not Started																																																
		<b>PDP CHECKLIST</b>	<b>2934</b>	<b>06/20/20</b>	<b>08/04/21</b>		<b>0%</b>																																																	

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #102 ICANN Approved Transfers	↓	TPR WG	08/29/23	08/29/23	Complete	
	AI	Staff to update the TPR Working Document [docs.google.com] based on today's discussion, including the 5 questions posed during the call (Re: Concepts 3 & 4).	—	Policy Support Staff	09/11/23	09/11/23	Complete	
	AI	Re: Charter Question i2) – WG members to provide their comments/suggestions in the Working Document [docs.google.com] regarding whether the scope of voluntary bulk transfers, including partial bulk transfers, should be expanded and/or made uniform across: 1. all registry operators (via an update to the Transfer Policy), or 2. all registry operators who offer the BTAPPA (via recommended updates to the BTAPPA)	—	TPR WG	09/11/23	09/11/23	Complete	
	AI	WG to specifically respond to the 6 questions from the 29 August call regarding bulk transfers.	—	TPR WG	09/11/23	09/11/23	Complete	
	WP	Meeting #XXX No meeting this week	↓	TPR WG	09/05/23	08/14/23	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	09/11/23	09/11/23	Complete	
	WP	Meeting #103 ICANN Approved Transfers	↓	TPR WG	09/12/23	09/12/23	Complete	
	AI	Staff to draft options for preliminary recommendation language for the Working Group to review and discuss on the next call.	—	Policy Support Staff	09/13/23	09/13/23	Complete	
	WP	Meeting #104 ICANN Approved Transfers	↓	TPR WG	09/19/23	09/19/23	Complete	
	AI	WG members to review the preliminary recommendations in the document at <a href="https://docs.google.com/document/d/1gX1N8d3qoktbnRmfGE4-8Un9dPavIKQ3IZYaoe9b0E/edit?usp=sharing">https://docs.google.com/document/d/1gX1N8d3qoktbnRmfGE4-8Un9dPavIKQ3IZYaoe9b0E/edit?usp=sharing</a> [docs.google.com] beginning on page 4 and provide comments.	—	TPR WG	09/25/23	09/25/23	Complete	
	AI	WG members and RySG in particular to indicate which option(s) they favor in the document at <a href="https://docs.google.com/document/d/1gX1N8d3qoktbnRmfGE4-8Un9dPavIKQ3IZYaoe9b0E/edit?usp=sharing">https://docs.google.com/document/d/1gX1N8d3qoktbnRmfGE4-8Un9dPavIKQ3IZYaoe9b0E/edit?usp=sharing</a> [docs.google.com] on page 11.	—	TPR WG	09/25/23	09/25/23	Complete	
	WP	Meeting #105 ICANN Approved Transfers	↓	TPR WG	09/26/23	09/26/23	Complete	
	AI	Staff to provide the data on the number of registries that offer BTAPPA services.	—	Policy Support Staff	09/28/23	09/28/23	Complete	
	AI	WG members to provide their feedback/preferences on the 4 options: <a href="https://docs.google.com/document/d/1b0KlvhRyyO5QSEI4DB4vP78muKvqHneaXQZTcvliBPQ/edit?usp=sharing">https://docs.google.com/document/d/1b0KlvhRyyO5QSEI4DB4vP78muKvqHneaXQZTcvliBPQ/edit?usp=sharing</a> [docs.google.com]	—	TPR WG	10/02/23	10/02/23	Complete	
	WP	Meeting #106 ICANN Approved Transfers	↓	TPR WG	10/03/23	10/03/23	Complete	
	AI	Staff to update the draft recommendations based on today's discussion	—	Policy Support Staff	10/06/23	10/06/23	Complete	
	AI	WG members to review the updates and provide feedback by COB Monday, 09 Oct	—	TPR WG	10/09/23	10/09/23	Complete	
	WP	Meeting #107 ICANN Approved Transfers / TDRP-Rec27	↓	TPR WG	10/10/23	10/10/23	Complete	
	AI	Staff to update the draft recommendations based on today's discussion	—	Policy Support Staff	10/12/23	10/12/23	Complete	
	AI	WG members to review the updated recommendations and provide any feedback by COB Tuesday, 17 Oct	—	TPR WG	10/17/23	10/17/23	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	10/15/23	10/15/23	Complete	
	WP	ICANN78 Meeting Remaining items on TDRP	↓	TPR WG	10/21/23		In Progress	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	11/06/23	10/15/23	Complete	No package created given short timing between Oct/Nov Council meetings.
	WP	Meeting #108 "Where we're at" review across Groups 1A, 1B & 2	↓	TPR WG	11/07/23		Not Started	
	WP	Meeting #109 Begin deliberations on Change of Registrant	↓	TPR WG	11/14/23		Not Started	
	WP	Meeting #110 Continue deliberations on Change of Registrant	↓	TPR WG	11/28/23		Not Started	
	WP	Meeting #111 Continue deliberations on Change of Registrant	↓	TPR WG	12/05/23		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	12/11/23		Not Started	
	WP	Meeting #112 Continue deliberations on Change of Registrant	↓	TPR WG	12/12/23		Not Started	
	WP	Meeting #113 Continue deliberations on Change of Registrant	↓	TPR WG	12/19/23		Not Started	
	WP	Meeting #114 Continue deliberations on Change of Registrant	↓	TPR WG	01/09/24		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	01/15/24		Not Started	
	MS	Submit Consolidated Initial Report to GNSO Council & Public Comment	!	TPR WG	08/21/24		Not Started	
