

# Project Tracking & Rollup DASHBOARD

**Project Name** PDP: Transfer Policy Review - Phase 1 **Program** Transfers **Project Sponsor** GNSO Council


**Project Information**

**33%**  
% Complete

**02/18/21**  
Actual Start

**12/28/23**  
Planned Finish

**Tasks by Status**

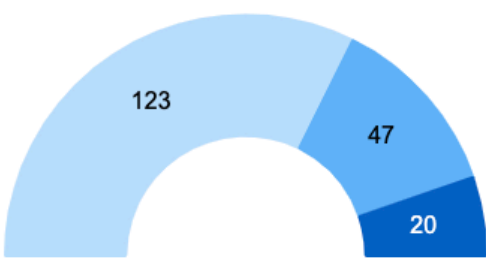

● Not\_Started ● Complete ● In\_Progress

**Project Contacts**

**Roger Carney**  
Chair


**n/a**  
Vice\_Chair

**Greg DiBiase**  
Liaison

**Emily Barabas**  
Staff\_Lead

**Berry Cobb**  
Project\_Manager

**Participant Summary**



● Member ● Alternate ● Observer\_Email\_Only  
● Staff\_Assigned ● Staff\_Not\_Assigned

**Project Status & Health**

**Project Status:** On-Schedule

**Project Health:** On-Target

**Summary Gantt & Key Milestones**

Health	Primary Task	Current Start	Current Finish	% Complete	Status	2021 2022 2023											
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
	<b>PDP: Transfer Policy Review - Phase 1</b>	<b>02/18/21</b>	<b>12/28/23</b>	<b>33%</b>	<b>In Progress</b>	PDP: Transfer Policy Review - Phase 1											
	<b>PROJECT CONTROL</b>	<b>02/18/21</b>	<b>12/28/23</b>	<b>42%</b>	<b>In Progress</b>	PROJECT CONTROL											
	<b>GROUP DELIBERATIONS</b>	<b>05/13/21</b>	<b>02/22/23</b>	<b>59%</b>	<b>In Progress</b>	GROUP DELIBERATIONS											
	Phase 1A Policy Topics	06/02/21	05/11/22	78%	In Progress	Phase 1A Policy Topics											
	Phase 1B Policy Topics	06/15/22	02/22/23			Phase 1B Policy Topics											
	<b>INITIAL REPORT</b>	<b>06/24/21</b>	<b>05/17/23</b>	<b>21%</b>	<b>In Progress</b>	INITIAL REPORT											
	Publish Initial Report	06/15/22	06/15/22			◆ Publish Initial Report											
	Publish Initial Report	03/29/23	03/29/23			◆ Publish Initial Report											
	<b>FINAL REPORT</b>	<b>08/04/22</b>	<b>08/16/23</b>		<b>Not Started</b>	FINAL REPORT											
	Review of public comments - Phase 1A	08/04/22	09/14/22			□ Review of public comments - Phase 1A											
	Review of public comments - Phase 1B	05/18/23	06/28/23			□ Review of public comments - Phase 1B											
	Submission of Final Report to the GNSO Council	08/16/23	08/16/23			◆ Submission of Final Report to the GNSO Council											

## 4 - Working Group

**Title:** PDP: Transfer Policy Review - Phase 1 (TPR\_P1)

**Description & Scope:** On 18 February 2021, The GNSO Council passed a resolution to initiate a two-phased PDP to review the Transfer Policy. The PDP working group is tasked with determining if changes to the policy are needed to improve the ease, security, and efficacy of inter-registrar and inter-registrant transfers.

**Composition:**

<b>Chair(s):</b>	Roger Carney
<b>Council Liaison:</b>	Greg Dibiase
<b>Staff:</b>	E. Barabas, J. Hedlund, C. Tubergen
<b># Participants:</b>	39 Participants ( <a href="#">link</a> )
<b># Observers:</b>	30
<b>Tools:</b>	<a href="#">Mailing List</a> / <a href="#">Meeting Schedule</a> / <a href="#">Wiki</a>
<b>Charter:</b>	<a href="#">Charter</a>

**Project Management:**

Token Holder	Planned Start Date	Actual Start Date	# of Days	Planned End Date	Actual End Date
WG	18 Feb 2021	18 Feb 2021	301	28 Dec 2023	TBD

Program	Progress	Status	Health
Transfers	33%	<span style="color: green; font-size: 2em;">●</span>	<span style="color: green; font-size: 2em;">■</span>

**STATUS:** ■ Planned ● On-schedule ● Revised schedule ▲ Behind schedule ◆ Target will be missed ■ On-hold

**HEALTH:** ■ On-Target ■ At-Risk ■ In-Trouble

**Milestones/Work plan ([link](#)):**

Milestone/Task	Date	
<a href="#">Final Issue Report</a> to Council	Jan-21	✓
Project Start	Feb-21	✓
<a href="#">Charter</a> Approved	Mar-21	✓
Chair appointment	Apr-21	✓
1st Plenary meeting	May-21	✓
Project Plan and Work plan Adoption	Jul-21	✓
SO/AC & SG/C Input to PDP	Aug-21	✓
Phase 1A Issue Deliberations	Aug-22	■
Populate stable draft papers w/ potential recs.	May-22	■
Discuss/approve findings and interim recs.	May-22	
Consolidate interim recommendations and findings	Jun-22	
Issue Phase 1A Initial Report for public comment	Jun-22	
Review public comment input	Sep-22	
Phase 1B Issue Deliberations	Mar-23	
Populate stable draft papers w/ potential recs.	Feb-23	
Discuss/approve findings and interim recs.	Mar-23	
Consolidate interim recommendations and findings	Mar-23	
Issue Phase 1B Initial Report for public comment	Mar-23	
Review public comment input & prepare final report	Mar-23	
Finalize Report	Jul-23	
Determine consensus levels on recommendations	Jun-23	
Adopt final recommendations and report (Phase 1A+1B)	Jul-23	
Send final report to GNSO Council	Aug-23	
GNSO Council adoption of consensus recs.	Oct-23	
Issue public comment for Board consideration	Oct-23	
ICANN Board adoption of consensus recs.	Jan-24	
Prior period % Complete	30%	■

**Status/Health Rationale:**

- The project schedule is confirmed by the GNSO Council and Status is “On-schedule” and the Health is “On-Target”.

**Current Activities:**

- Continue deliberations on Auth-Info Code Management; review of candidate recommendations on the Transfer Authorization Code.
- Continue deliberations on Losing & Gaining FOA; review candidate recommendations.
- Continue deliberations on Additional Security Measures.
- Council review of PCR to migrate the Phase 2 topic of “NACK of Transfers” to Phase 1A.

**Planned Activities:**

- Transfer policy package: review of TAC, Losing FOA, Gaining FOA, and Additional Security Measures candidate recommendations.

**Open Issues, Risks & Mitigation Plan:**

- None at this time.

**Completed in prior period(s):**

- Completed and distributed Project Package for November.
-

# Project Tracking & Rollup DASHBOARD



## Project Roster

Participant	Participant Type	Role	Participation Start Date	Participation End Date	Legacy SOI Link
Group Selected / Nominated By: Group Name <b>At-Large Advisory Committee (ALAC)</b>					
Nanghaka Daniel Khauka	Member		05/04/21		<a href="https://community.icann.org">https://community.icann.org</a>
Steinar Grøtterød	Member		05/05/21		<a href="https://community.icann.org">https://community.icann.org</a>
Raymond Mamattah	Alternate		05/04/21		<a href="https://community.icann.org">https://community.icann.org</a>
Lutz Donnerhacke	Alternate		05/08/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>Commercial Business Users Constituency (BC)</b>					
Zak Muscovitch	Member		04/23/21		<a href="https://community.icann.org">https://community.icann.org</a>
Arinola Akinyemi	Alternate		08/12/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>GNSO Council</b>					
Gregory DiBiase	Member	Liaison	06/04/21		<a href="https://community.icann.org">https://community.icann.org</a>
Roger Carney	Member	Chair	04/23/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>Independent</b>					
Steve Crocker	Member	Subject Matter Expert	04/26/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>Intellectual Property Constituency (IPC)</b>					
Mike Rodenbaugh	Member		04/21/21		<a href="https://community.icann.org">https://community.icann.org</a>
Salvador Camacho Hernandez	Member		04/26/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>Internet Corporation for Assigned Names &amp; Numbers (ICANN)</b>					
Isabelle Colas	Staff - Assigned	Liaison	06/10/21		
Devan Reed	Staff - Assigned		11/16/21		
Berry Cobb	Staff - Assigned		02/18/21		
Emily Barabas	Staff - Assigned		02/18/21		
Michelle DeSmyter	Staff - Assigned		02/18/21		
Terri Agnew	Staff - Assigned		02/18/21		
Caitlin Tubergen	Staff - Assigned		02/18/21		
Julie Bisland	Staff - Assigned		02/18/21		
Julie Hedlund	Staff - Assigned		02/18/21		
Nathalie Peregrine	Staff - Assigned		02/18/21		
Holida Yanik	Staff - Assigned		04/30/21		
Group Selected / Nominated By: Group Name <b>Internet Service Providers and Connectivity Providers Constituency (ISPCP)</b>					
John Woodworth	Member		04/14/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>Non-Commercial Stakeholder Group (NCSG)</b>					
Wisdom Donkor	Member		06/01/21		<a href="https://community.icann.org">https://community.icann.org</a>
Farzaneh Badiei	Member		06/01/21		<a href="https://community.icann.org">https://community.icann.org</a>
Akinremi Peter Taiwo	Alternate		06/02/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>Registrar Stakeholder Group (RrSG)</b>					
Keiron Tobin	Member		06/07/21		<a href="https://community.icann.org">https://community.icann.org</a>
Thomas Keller	Member		04/26/21	09/27/21	<a href="https://community.icann.org">https://community.icann.org</a>
Eric Rokobauer	Member		04/26/21		<a href="https://community.icann.org">https://community.icann.org</a>
Theo Geurts	Member		04/23/21		<a href="https://community.icann.org">https://community.icann.org</a>
Kristian Ørmen	Member		04/23/21		<a href="https://community.icann.org">https://community.icann.org</a>
Crystal Ondo	Member		04/23/21		<a href="https://community.icann.org">https://community.icann.org</a>
Sarah Wyld	Member		04/23/21		<a href="https://community.icann.org">https://community.icann.org</a>
Prudence Malinki	Member		04/27/21		<a href="https://community.icann.org">https://community.icann.org</a>
Catherine Merdinger	Member		04/27/21		<a href="https://community.icann.org">https://community.icann.org</a>
Owen Smigelski	Member		04/27/21		<a href="https://community.icann.org">https://community.icann.org</a>
Richard Merdinger	Member		05/05/21	06/07/21	<a href="https://community.icann.org">https://community.icann.org</a>
Antonia Nan Chu	Member		05/06/21		<a href="https://community.icann.org">https://community.icann.org</a>
Volker Greimann	Alternate		04/24/21		<a href="https://community.icann.org">https://community.icann.org</a>
Jothan Frakes	Alternate		04/23/21		<a href="https://community.icann.org">https://community.icann.org</a>
Essie Musailov	Alternate		04/23/21		<a href="https://community.icann.org">https://community.icann.org</a>
Pam Little	Alternate		04/26/21		<a href="https://community.icann.org">https://community.icann.org</a>
Richard Brown	Alternate		04/26/21		<a href="https://community.icann.org">https://community.icann.org</a>
Min Feng	Alternate		04/26/21		<a href="https://community.icann.org">https://community.icann.org</a>
Jacques Blanc	Alternate		04/29/21		<a href="https://community.icann.org">https://community.icann.org</a>
Arnaud Wittersheim	Alternate		05/05/21		<a href="https://community.icann.org">https://community.icann.org</a>
Jody Kolker	Alternate		05/07/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name					


**Registry Stakeholder Group (RySG)**

James Galvin	Member		04/27/21		<a href="https://community.icann.org">https://community.icann.org</a>
Barbara Knight	Member		05/04/21		<a href="https://community.icann.org">https://community.icann.org</a>
Beth Bacon	Alternate		05/04/21		<a href="https://community.icann.org">https://community.icann.org</a>


# Project Tracking & Rollup

## DASHBOARD


Work-Plan Activity Metrics

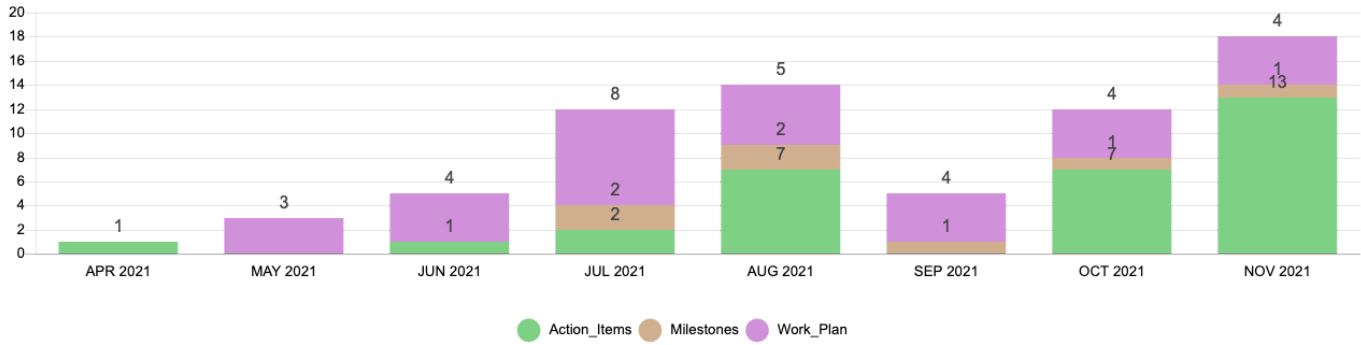

Mailman Activity

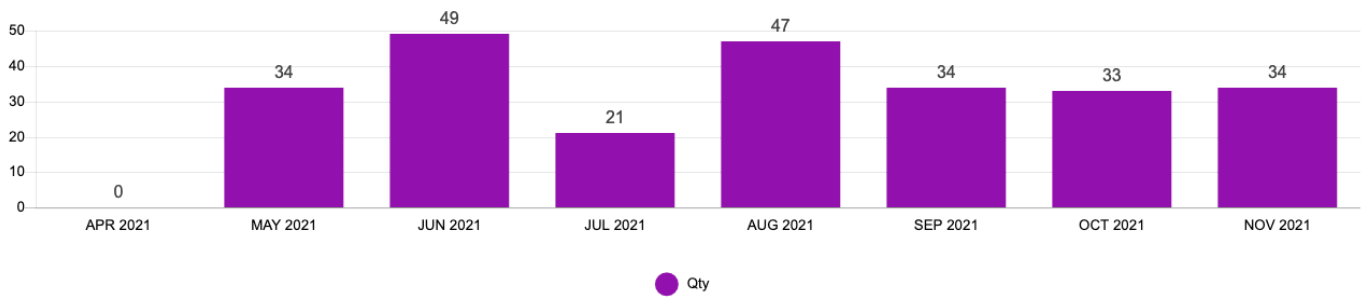

Meeting Activity

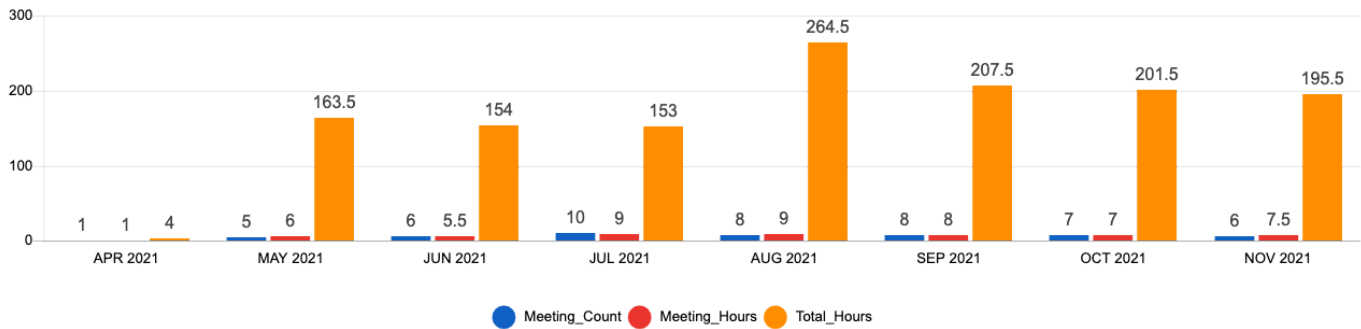

# Project Tracking & Rollup

## DASHBOARD



### Plenary Attendance

Group Represented	Invited Qty	Attended Qty	Attendance
<b>Total</b>	Sum <b>778</b>	Sum <b>660</b>	Avg <b>84.8%</b>
Primary <b>At-Large Advisory Committee (ALAC)</b>	Sum <b>79</b>	Sum <b>71</b>	Avg <b>89.9%</b>
Attendee Name <b>Lutz Donnerhacke</b>	Sum <b>13</b>	Sum <b>12</b>	Avg <b>92.3%</b>
Attendee Name <b>Nanghaka Daniel Khauka</b>	Sum <b>25</b>	Sum <b>22</b>	Avg <b>88.0%</b>
Attendee Name <b>Raymond Mamattah</b>	Sum <b>16</b>	Sum <b>15</b>	Avg <b>93.8%</b>
Attendee Name <b>Steinar Grøtterød</b>	Sum <b>25</b>	Sum <b>22</b>	Avg <b>88.0%</b>
Primary <b>Commercial Business Users Constituency (BC)</b>	Sum <b>37</b>	Sum <b>35</b>	Avg <b>94.6%</b>
Attendee Name <b>Arinola Akinyemi</b>	Sum <b>12</b>	Sum <b>12</b>	Avg <b>100.0%</b>
Attendee Name <b>Zak Muscovitch</b>	Sum <b>25</b>	Sum <b>23</b>	Avg <b>92.0%</b>
Primary <b>GNSO Council</b>	Sum <b>46</b>	Sum <b>40</b>	Avg <b>87.0%</b>
Attendee Name <b>Gregory DiBiase</b>	Sum <b>21</b>	Sum <b>15</b>	Avg <b>71.4%</b>
Attendee Name <b>Roger Carney</b>	Sum <b>25</b>	Sum <b>25</b>	Avg <b>100.0%</b>
Primary <b>Independent</b>	Sum <b>25</b>	Sum <b>11</b>	Avg <b>44.0%</b>
Attendee Name <b>Steve Crocker</b>	Sum <b>25</b>	Sum <b>11</b>	Avg <b>44.0%</b>
Primary <b>Intellectual Property Constituency (IPC)</b>	Sum <b>50</b>	Sum <b>19</b>	Avg <b>38.0%</b>
Attendee Name <b>Mike Rodenbaugh</b>	Sum <b>25</b>	Sum <b>11</b>	Avg <b>44.0%</b>
Attendee Name <b>Salvador Camacho Hernandez</b>	Sum <b>25</b>	Sum <b>8</b>	Avg <b>32.0%</b>
Primary <b>Internet Service Providers and Connectivity Providers Constituency (ISPCP)</b>	Sum <b>25</b>	Sum <b>22</b>	Avg <b>88.0%</b>
Attendee Name <b>John Woodworth</b>	Sum <b>25</b>	Sum <b>22</b>	Avg <b>88.0%</b>
Primary <b>Non-Commercial Stakeholder Group (NCSG)</b>	Sum <b>48</b>	Sum <b>32</b>	Avg <b>66.7%</b>
Attendee Name <b>Akinremi Peter Taiwo</b>	Sum <b>4</b>	Sum <b>3</b>	Avg <b>75.0%</b>
Attendee Name <b>Farzaneh Badiei</b>	Sum <b>22</b>	Sum <b>11</b>	Avg <b>50.0%</b>
Attendee Name <b>Wisdom Donkor</b>	Sum <b>22</b>	Sum <b>18</b>	Avg <b>81.8%</b>
Primary <b>Registrar Stakeholder Group (RrSG)</b>	Sum <b>399</b>	Sum <b>367</b>	Avg <b>92.0%</b>
Attendee Name <b>Antonia Nan Chu</b>	Sum <b>25</b>	Sum <b>25</b>	Avg <b>100.0%</b>
Attendee Name <b>Arnaud Wittersheim</b>	Sum <b>16</b>	Sum <b>16</b>	Avg <b>100.0%</b>
Attendee Name <b>Catherine Merdinger</b>	Sum <b>25</b>	Sum <b>21</b>	Avg <b>84.0%</b>
Attendee Name <b>Crystal Ondo</b>	Sum <b>25</b>	Sum <b>18</b>	Avg <b>72.0%</b>
Attendee Name <b>Eric Rokobauer</b>	Sum <b>24</b>	Sum <b>24</b>	Avg <b>100.0%</b>
Attendee Name <b>Essie Musailov</b>	Sum <b>24</b>	Sum <b>24</b>	Avg <b>100.0%</b>
Attendee Name <b>Jacques Blanc</b>	Sum <b>5</b>	Sum <b>4</b>	Avg <b>80.0%</b>
Attendee Name <b>Jody Kolker</b>	Sum <b>23</b>	Sum <b>23</b>	Avg <b>100.0%</b>
Attendee Name <b>Jothan Frakes</b>	Sum <b>24</b>	Sum <b>24</b>	Avg <b>100.0%</b>

Attendee Name <b>Keiron Tobin</b>	Sum <b>21</b>	Sum <b>18</b>	Avg <b>85.7%</b>
Attendee Name <b>Kristian Ørmen</b>	Sum <b>25</b>	Sum <b>23</b>	Avg <b>92.0%</b>
Attendee Name <b>Min Feng</b>	Sum <b>3</b>	Sum <b>2</b>	Avg <b>66.7%</b>
Attendee Name <b>Owen Smigelski</b>	Sum <b>25</b>	Sum <b>23</b>	Avg <b>92.0%</b>
Attendee Name <b>Pam Little</b>	Sum <b>1</b>	Sum <b>1</b>	Avg <b>100.0%</b>
Attendee Name <b>Prudence Malinki</b>	Sum <b>25</b>	Sum <b>25</b>	Avg <b>100.0%</b>
Attendee Name <b>Richard Brown</b>	Sum <b>18</b>	Sum <b>18</b>	Avg <b>100.0%</b>
Attendee Name <b>Richard Merdinger</b>	Sum <b>4</b>	Sum <b>4</b>	Avg <b>100.0%</b>
Attendee Name <b>Sarah Wyld</b>	Sum <b>25</b>	Sum <b>22</b>	Avg <b>88.0%</b>
Attendee Name <b>Theo Geurts</b>	Sum <b>25</b>	Sum <b>23</b>	Avg <b>92.0%</b>
Attendee Name <b>Thomas Keller</b>	Sum <b>16</b>	Sum <b>9</b>	Avg <b>56.3%</b>
Attendee Name <b>Volker Greimann</b>	Sum <b>20</b>	Sum <b>20</b>	Avg <b>100.0%</b>
Primary <b>Registry Stakeholder Group (RySG)</b>	Sum <b>69</b>	Sum <b>63</b>	Avg <b>91.3%</b>
Attendee Name <b>Barbara Knight</b>	Sum <b>25</b>	Sum <b>23</b>	Avg <b>92.0%</b>
Attendee Name <b>Beth Bacon</b>	Sum <b>19</b>	Sum <b>19</b>	Avg <b>100.0%</b>
Attendee Name <b>James Galvin</b>	Sum <b>25</b>	Sum <b>21</b>	Avg <b>84.0%</b>

[Open source report to view more](#)

#### Plenary - Alternates Replacing Members Log



<https://community.icann.org/x/V4aUCQ>

Health	WBS	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	Baseline Start	Baseline Finish	Q1			Q2			Q3			Q4			Q1			Q2			Q3								
											Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
		<b>PDP: Transfer Policy Review - Phase 1</b>	<b>746d</b>	<b>02/18/21</b>	<b>12/28/23</b>		<b>33%</b>	<b>In Progress</b>	<b>02/18/21</b>	<b>12/28/23</b>																											
		<b>PROJECT CONTROL</b>	<b>746d</b>	<b>02/18/21</b>	<b>12/28/23</b>		<b>42%</b>	<b>In Progress</b>	<b>02/18/21</b>	<b>12/28/23</b>																											
1.1		Project start confirmed	0	02/18/21	02/18/21		100%	Complete	02/18/21	02/18/21																											
1.2		Adopt/Confirm charter	25d	02/18/21	03/24/21	3	100%	Complete	02/18/21	03/24/21																											
1.3		Confirmation of Team	50d	02/18/21	04/28/21	3	100%	Complete	02/18/21	04/28/21																											
1.4		Appointment of Team Chair	50d	02/18/21	04/28/21	3	100%	Complete	02/18/21	04/28/21																											
1.5		Appointment of Liaison to GNSO Council	50d	02/18/21	04/28/21	3	100%	Complete	02/18/21	04/28/21																											
1.6		Chair / Staff preparations	10d	04/29/21	05/12/21	6	100%	Complete	04/29/21	05/12/21																											
1.7		<b>Project Management</b>	<b>696d</b>	<b>04/29/21</b>	<b>12/28/23</b>		<b>26%</b>	<b>In Progress</b>	<b>04/29/21</b>	<b>12/28/23</b>																											
1.7.1		Develop and confirm Project Plan	30d	04/29/21	06/09/21	6	100%	Complete	04/29/21	06/09/21																											
1.7.2		Obtain project plan approval from GNSO Council	30d	06/10/21	07/21/21	10	100%	Complete	06/10/21	07/21/21																											
1.7.3		Develop monthly Project Packages and deliver to Group & Council	540d	07/22/21	08/16/23	11	18%	In Progress	07/22/21	08/16/23																											
1.7.4		<b>Leadership Sub team</b>	<b>600d</b>	<b>04/29/21</b>	<b>08/16/23</b>		<b>26%</b>	<b>In Progress</b>	<b>04/29/21</b>	<b>08/16/23</b>																											
1.7.4.1		On-going preparation and planning of group activities	600d	04/29/21	08/16/23	6	26%	In Progress	04/29/21	08/16/23																											
1.7.5		Close project and transition project to implementation	1d	12/28/23	12/28/23	14, 222			12/28/23	12/28/23																											
2		<b>GROUP DELIBERATIONS</b>	<b>465d</b>	<b>05/13/21</b>	<b>02/22/23</b>		<b>59%</b>	<b>In Progress</b>	<b>05/13/21</b>	<b>02/22/23</b>																											
2.1		First meeting of Team	1d	05/13/21	05/13/21	8	100%	Complete	05/13/21	05/13/21																											
2.2		Understand Charter, organize materials and develop initial approach	10d	05/13/21	05/26/21	8	100%	Complete	05/13/21	05/26/21																											
2.3		Overview & initial discussion of all Policy Topics	15d	05/13/21	06/02/21	8	100%	Complete	05/13/21	06/02/21																											
2.4		Develop definitions and terminology	30d	05/13/21	06/23/21	8	100%	Complete	05/13/21	06/23/21																											
2.5		Input from other SOIACs & GNSO SG/ICs	91d	05/27/21	09/30/21		100%	Complete	05/27/21	09/30/21																											
2.6		<b>Phase 1A Policy Topics</b>	<b>245d</b>	<b>06/02/21</b>	<b>05/11/22</b>		<b>78%</b>	<b>In Progress</b>	<b>06/02/21</b>	<b>05/11/22</b>																											
2.6.1		Topic 1 Deliberations - Gaining FOA	40d	12/02/21	01/26/22		90%	In Progress	12/02/21	01/26/22																											
2.6.2		Topic 2 Deliberations - Losing FOA	40d	10/07/21	12/01/21		93%	In Progress	10/07/21	12/01/21																											
2.6.3		Topic 3 Deliberations - Additional Security Measures	40d	08/12/21	10/06/21		86%	In Progress	08/12/21	10/06/21																											
2.6.4		Topic 4 Deliberations - Auth-Info Code Management	180d	06/03/21	02/09/22		98%	In Progress	06/03/21	02/09/22																											
2.6.5		Topic 5 Deliberations - Bulk Use of Auth-Info Codes	40d	10/12/22	04/06/22				10/12/22	04/06/22																											
2.6.6		Topic 6 Deliberations - Wave 1, Recommendation 27	25d	04/07/22	05/11/22				04/07/22	05/11/22																											
2.6.7		Unplanned Issues & Tasks	0	06/02/21	06/02/21				06/02/21	06/02/21																											
2.7		<b>Phase 1B Policy Topics</b>	<b>180d</b>	<b>06/15/22</b>	<b>02/22/23</b>				<b>06/15/22</b>	<b>02/22/23</b>																											
2.7.1		Topic 7 Deliberations - Change of Registrant / Overall Policy	40d	06/16/22	08/10/22				06/16/22	08/10/22																											
2.7.2		Topic 8 Deliberations - Change of Registrant / 60-Day Lock	40d	08/11/22	10/05/22				08/11/22	10/05/22																											
2.7.3		Topic 9 Deliberations - Change of Registrant / Privacy/Proxy Customers	35d	10/06/22	11/23/22				10/06/22	11/23/22																											
2.7.4		Topic 10 Deliberations - Change of Registrant / Designated Agent	25d	11/24/22	12/28/22				11/24/22	12/28/22																											
2.7.5		Topic 11 Deliberations - Change of Registrant / Additional Questions	20d	12/29/22	01/25/23				12/29/22	01/25/23																											
2.7.6		Topic 12 Deliberations - Change of Registrant / Wave 1 - Recommendation 27	20d	01/26/23	02/22/23				01/26/23	02/22/23																											
2.7.7		Unplanned Issues & Tasks	0	06/15/22	06/15/22				06/15/22	06/15/22																											
3		<b>INITIAL REPORT</b>	<b>495d</b>	<b>06/24/21</b>	<b>05/17/23</b>		<b>21%</b>	<b>In Progress</b>	<b>06/24/21</b>	<b>05/17/23</b>																											
3.1		<b>Phase 1A Initial Report</b>	<b>290d</b>	<b>06/24/21</b>	<b>08/03/22</b>		<b>38%</b>	<b>In Progress</b>	<b>06/24/21</b>	<b>08/03/22</b>																											
3.1.1		Populate stable drafts as required	230d	06/24/21	05/11/22	20	50%	In Progress	06/24/21	05/11/22																											
3.1.2		Discuss/approve findings and interim recommendations	10d	05/12/22	05/25/22	27, 40, 51, 60, 72, 83			05/12/22	05/25/22																											
3.1.3		Consolidate interim recommendations and findings	10d	05/26/22	06/08/22	198			05/26/22	06/08/22																											
3.1.4		Build Draft Report for public comment	10d	05/26/22	06/08/22	198			05/26/22	06/08/22																											
3.1.5		Approve Draft Report for public comment	5d	06/09/22	06/15/22	200			06/09/22	06/15/22																											
3.1.6		Publish Initial Report	0	06/15/22	06/15/22	201			06/15/22	06/15/22																											
3.1.7		Communicate Initial Report	5d	06/16/22	06/22/22	201			06/16/22	06/22/22																											
3.1.8		Public comment forum on the Initial Report (45 days)	35d	06/16/22	08/03/22	201			06/16/22	08/03/22																											
3.2		<b>Phase 1B Initial Report</b>	<b>240d</b>	<b>06/16/22</b>	<b>05/17/23</b>				<b>06/16/22</b>	<b>05/17/23</b>																											
3.2.1		Populate stable drafts as required	60d	06/16/22	09/07/22	202			06/16/22	09/07/22																											
3.2.2		Discuss/approve findings and interim recommendations	10d	02/23/23	03/08/23	111, 122, 135, 146, 1			02/23/23	03/08/23																											
3.2.3		Consolidate interim recommendations and findings	10d	03/09/23	03/22/23	207			03/09/23	03/22/23																											
3.2.4		Build Draft Report for public comment	10d	03/09/23	03/22/23	207			03/09/23	03/22/23																											
3.2.5		Approve Draft Report for public comment	5d	03/23/23	03/29/23	209			03/23/23	03/29/23																											
3.2.6		Publish Initial Report	0	03/29/23	03/29/23	210			03/29/23	03/29/23																											
3.2.7		Communicate Initial Report	5d	03/30/23	04/05/23	210			03/30/23	04/05/23																											
3.2.8		Public comment forum on the Initial Report (45 days)	35d	03/30/23	05/17/23	210			03/30/23	05/17/23																											
4		<b>FINAL REPORT</b>	<b>270d</b>	<b>08/04/22</b>	<b>08/16/23</b>			<b>Not Started</b>	<b>08/04/22</b>	<b>08/16/23</b>																											
4.1		Review of public comments - Phase 1A	30d	08/04/22	09/14/22	204			08/04/22	09/14/22																											
4.2		Review of public comments - Phase 1B	30d	05/18/23	06/28/23	213			05/18/23	06/28/23																											
4.3		Continue deliberations of policy topics towards a Final Report	50d	05/18/23	07/26/23	204, 213			05/18/23	07/26/23																											
4.4		Build Final Report & Final Deliberations	5d	07/27/23	08/02/23	217			07/27/23	08/02/23																											
4.5		Determine consensus levels on interim recommendations	10d	08/03/23	08/16/23	218			08/03/23	08/16/23																											
4.6		Adopt final recommendations and report	10d	08/03/23	08/16/23	218			08/03/23	08/16/23																											
4.7		Submission of Final Report to the GNSO Council	0	08/16/23	08/16/23	220			08/16/23	08/16/23																											
5		<b>POST GROUP TASKS</b>	<b>95d</b>	<b>08/17/23</b>	<b>12/27/23</b>			<b>Not Started</b>	<b>08/17/23</b>	<b>12/27/23</b>																											
		<b>PDP CHECKLIST</b>	<b>824d</b>	<b>06/20/20</b>	<b>08/16/23</b>		<b>0%</b>																														



Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	11/05/21	11/04/21	Complete	
	AI	WG members to contribute to a list of additional security measures and provide other comments/suggestions in the Google doc for Additional Security Measures Working Document <a href="https://docs.google.com/document/d/1q7xaJuxi50Q6TDD26H92P6wOfz8luap1wdW0tIgv7o/edit">https://docs.google.com/document/d/1q7xaJuxi50Q6TDD26H92P6wOfz8luap1wdW0tIgv7o/edit</a>	—	TPR WG	11/08/21	11/08/21	Complete	
	WP	Meeting #23 Continue Additional Security Measures + Review of Compliance data	↓	TPR WG	11/09/21	11/09/21	Complete	
	AI	Staff to enquire for clarification. See below: NOTE THIS: <a href="https://www.icann.org/resources/pages/text-2012-02-25-en">https://www.icann.org/resources/pages/text-2012-02-25-en</a> , On that page: Please note that you may not transfer your domain name to a new registrar within the first 60 days after initial registration, or the first 60 days after a transfer. NOTE THIS: <a href="https://www.icann.org/resources/pages/policy-transfers-2014-07-02-en">https://www.icann.org/resources/pages/policy-transfers-2014-07-02-en</a> , On that page, it becomes optional for the sponsoring registrar to NACK the transfer for being within the 60-day window. No longer enforced by registry by policy.	—	Policy Support Staff	11/15/21	11/15/21	Complete	
	WP	Meeting #24 Losing FOA Review of candidate recommendations	↓	TPR WG	11/16/21	11/16/21	Complete	
	AI	Candidate Recommendation #12: Staff will add a reference/footnote.	—	Policy Support Staff	11/22/21	11/22/21	Complete	
	AI	Candidate Recommendation #13: Staff to review the discussions to clarify the rationale for this recommendation to have two communications.	—	Policy Support Staff	11/22/21	11/22/21	Complete	
	AI	Candidate Recommendation #13: WG members to suggest wording for the method of sending and period of time (text in brackets).	—	TPR WG	11/22/21	11/22/21	Complete	
	AI	Candidate Recommendation #14: WG members to suggest wording re: the method of sending and period of time (text in brackets).	—	TPR WG	11/22/21	11/22/21	Complete	
	AI	Candidate Recommendation #15: WG members to suggest wording re: the method of sending and period of time (text in brackets).	—	TPR WG	11/22/21	11/22/21	Complete	
	AI	Candidate Recommendation #15: Staff to update the context to add text on when this makes sense to be used.	—	Policy Support Staff	11/22/21	11/22/21	Complete	
	AI	Candidate Recommendation #16: WG members to suggest wording re: the method of sending and period of time (text in brackets).	—	TPR WG	11/22/21	11/22/21	Complete	
	WP	Meeting #25 Losing FOA	↓	TPR WG	11/23/21	11/23/21	Complete	
	AI	Losing FOA, Candidate Recommendation #13: Staff to suggest working to replace "using email", and concerning the timing/order and language of the notification and TAC presentation/provision. Need to make sure the RNH is notified no matter how the TAC is presented.	—	Policy Support Staff	11/29/21	11/29/21	Complete	
	AI	Losing FOA, Candidate Recommendation #14: Ask if there are volunteers for a small team that delves into whether it's possible to provide the Gaining Registrar name, or if the IANA ID is okay – looking at making IANA ID mandatory and the name of the Gaining Registrar optional. Also update the wording so that multiple notifications can go out regardless of different Gaining Registrars.	—	TPR WG	11/29/21	11/29/21	Complete	
	AI	Losing FOA, Candidate Recommendation #15: Make the same changes to the language to be consistent with previous related candidate recommendations.	—	Policy Support Staff	11/29/21	11/29/21	Complete	
	AI	Losing FOA, Candidate Recommendation #16: Eliminate this candidate recommendation.	—	Policy Support Staff	11/29/21	11/29/21	Complete	
	WP	Meeting #26 Losing FOA; Gaining FOA	↓	TPR WG	11/30/21	11/30/21	Complete	
	AI	Losing FOA, Candidate Recommendation #12: Staff to amend footnote 1 as follows: "The Working Group recommends notes that, in place of the Losing FOA, notifications are sent to the RNH [in relation to an inter-registrar transfer] when key changes take place with their account in relation to a transfer, as detailed in recommendations 13-15."	—	Policy Support Staff	12/02/21		In Progress	
	AI	Losing FOA, Candidate Recommendation #13 & 14: Staff to determine whether footnotes 2 and 3 need to be duplicates or if they can be combined.	—	Policy Support Staff	12/02/21		In Progress	
	AI	Losing FOA, Candidate Recommendation #14: Replace with new text suggested with clarification.	—	Policy Support Staff	12/02/21		In Progress	
	AI	Losing FOA, Candidate Recommendation #14: Jim Galvin to take the question to the Registries Stakeholder Group as to the feasibility of providing the IANA ID and/or name of the Gaining Registrar. Leave in the requirement in the candidate recommendation until we get a response.	—	James Galvin	12/14/21		In Progress	
	AI	Rationale for Elimination of the Gaining FOA: WG members should review the rationale for eliminating the Gaining FOA in preparation for next week's meeting. <a href="https://docs.google.com/document/d/1QOCzblh7w4hdjipAsg6_lybdr0nlsFDcWjdZ5e21Qo/edit">https://docs.google.com/document/d/1QOCzblh7w4hdjipAsg6_lybdr0nlsFDcWjdZ5e21Qo/edit</a>	—	TPR WG	12/06/21		In Progress	
	WP	Meeting #27 Gaining FOA; Revisit TAC	↓	TPR WG	12/07/21		Not Started	
	WP	Meeting #28 Second reading of FOA/TAC; 60 day lock	↓	TPR WG	12/14/21		Not Started	
	WP	Meeting #29 60 day lock; NACK	↓	TPR WG	12/21/21		Not Started	
	WP	Meeting #30 NACK	↓	TPR WG	01/04/22		Not Started	
	WP	Meeting #31 Review recommendations package - Phase 1A	↓	TPR WG	01/11/22		Not Started	
	WP	Meeting #32 Start bulk discussion	↓	TPR WG	01/18/22		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	12/06/21		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	01/07/22		Not Started	
	MS	Submit Phase 1A Initial Report for Public Comment	!	TPR WG	06/15/22		Not Started	
