

Project Tracking & Rollup DASHBOARD


Project Name EPDP: Internationalized Domain Names **Program** gTLD **Project Sponsor** GNSO Council

Project Information


05/20/21
Current Start

08/18/23
Current Finish

25%
% Complete

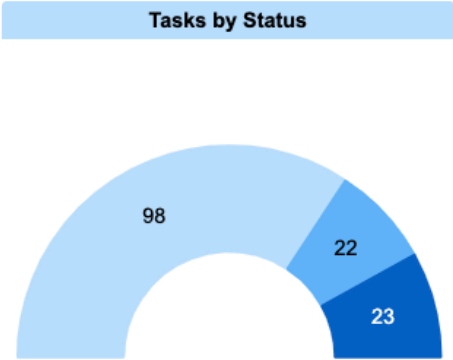

- Project Contacts**
- Donna Austin** - Chair
 - Justine Chew** - Vice_Chair
 - Farell Folly** - Liaison
 - Ariel Liang** - Staff_Lead
 - Steve Chan** - Project_Manager



Project Status & Health

Project Status: On-Schedule

Project Health: On-Target

Legend for Project Status & Health:

- Not_Started
- Complete
- In_Progress

Legend for Participant Summary:

- Member
- Participant_Count
- Observer_Email_Only
- Staff_Assigned
- Staff_Not_Assigned

Summary Gantt & Key Milestones

Health	Primary Task	Current Start	Current Finish	% Complete	Status	Timeline (2021-2023)											
						2021 Q1	2021 Q2	2021 Q3	2021 Q4	2022 Q1	2022 Q2	2022 Q3	2022 Q4	2023 Q1	2023 Q2	2023 Q3	
	EPDP: Internationalized Domain Names	05/20/21	08/18/23	25%	In Progress	[Gantt bar for EPDP: Internationalized Domain Names]											
	PROJECT CONTROL	05/20/21	07/10/23	41%	In Progress	[Gantt bar for PROJECT CONTROL]											
	GROUP DELIBERATIONS	08/11/21	03/16/23	24%	In Progress	[Gantt bar for GROUP DELIBERATIONS]											
●	Topic A Deliberations: Consistent definition and technical utilization of RZ-LGR	08/25/21	11/02/21	38%	In Progress	[Gantt bar for Topic A Deliberations]											
●	Topic B Deliberations: "Same entity" at the top-level	11/03/21	12/28/21			[Gantt bar for Topic B Deliberations]											
	Topic C Deliberations: "Same entity" at the second-level	12/29/21	02/22/22			[Gantt bar for Topic C Deliberations]											
	Topic D Deliberations: Adjustments in registry agreement, registry service, registry transition process, and other processes/procedures related to the domain name lifecycle	02/23/22	05/24/22			[Gantt bar for Topic D Deliberations]											
	Topic E Deliberations: Adjustments to objection process, string similarity review, string contention resolution, reserved strings, and other policies and procedures	05/25/22	08/02/22			[Gantt bar for Topic E Deliberations]											
	Topic F Deliberations: Adjustments in registration dispute resolution procedures and trademark protection mechanisms	08/03/22	09/27/22			[Gantt bar for Topic F Deliberations]											
	Topic G Deliberations: Process to update the IDN Implementation Guidelines	09/28/22	11/04/22			[Gantt bar for Topic G Deliberations]											
	INITIAL REPORT	09/20/21	02/03/23	12%	In Progress	[Gantt bar for INITIAL REPORT]											
	Publish Initial Report	12/16/22	12/16/22			[Milestone for Publish Initial Report]											
	FINAL REPORT	02/06/23	04/07/23		Not Started	[Gantt bar for FINAL REPORT]											
	Review of public comments	02/06/23	03/17/23			[Gantt bar for Review of public comments]											
	Submission of Final Report to the GNSO Council	04/07/23	04/07/23			[Milestone for Submission of Final Report to the GNSO Council]											

4 - Working Group

Title: EPDP - Internationalized Domain Names (EPDP_IDN)

Description & Scope: On 20 May 2021, the GNSO Council passed a resolution to initiate the Expedited Policy Development Process (EPDP) on Internationalized Domain Names and adopt its charter. The EPDP Team is tasked with providing the GNSO Council with policy recommendations on: 1) the definition of gTLDs and the management of variant labels; and 2) how the IDN Implementation Guidelines, which Contracted Parties are required to comply with, should be updated in the future.

Composition:

Chair:	Donna Austin
Vice Chair:	Justine Chew
Council Liaison:	Farell Folly
Staff:	A. Liang, S. Chan, E. Barabas.
# Participants:	68 Participants (link)
# Observers:	7
Tools:	Mailing List / Meeting Schedule / Wiki
Charter:	Charter

Project Management:

Token Holder	Planned Start Date	Actual Start Date	# of Days	Planned End Date	Actual End Date
WG	20 May 2021	20 May 2021	210	09 Jun 2023	TBD

Program	Progress	Status	Health
gTLD	25%	●	■

STATUS: ■ Planned ● On-schedule ● Revised schedule ▲ Behind schedule ◆ Target will be missed ■ On-hold

HEALTH: ■ On-Target ■ At-Risk ■ In-Trouble

Milestones/Work plan (link):

Milestone/Task	Date	
Project Start	May-21	✓
Scoping Team Report	Jan-20	✓
Charter Approved	May-21	✓
EPDP Initiation Request Approved	May-21	✓
1st Plenary meeting	Aug-21	✓
SO/AC & SG/C Input to PDP	Nov-21	✓
Project Plan and Work plan Adoption	Oct-21	✓
Issue Deliberations	Mar-23	
Populate draft report w/ findings & potential recs.	Oct-22	
Assemble initial conclusions	Oct-22	
Discuss/approve findings and interim recs.	Nov-22	
Consolidate interim recommendations and findings	Nov-22	
Issue report for public comment	Dec-22	
Review public comment input & prepare final report	Mar-23	
Finalize Report	Apr-23	
Determine consensus levels on recommendations	Apr-23	
Adopt final recommendations and report	Apr-23	
Send final report to GNSO Council	Apr-23	
GNSO Council adoption of consensus recs.	May-23	
Issue public comment for Board consideration	Jun-23	
ICANN Board adoption of consensus recs.	Oct-23	
Prior period % Complete	23%	

Status/Health Rationale:

- This project was initiated on 20 May 2021 and continues with a Status of “On-Schedule” and Health of “On-Target”.

Current Activities:

- Continue substantive deliberations on Topic A.

Planned Activities:

- Initiate Topics B & C deliberations.

Open Issues, Risks & Mitigation Plan:

- As Council is aware there were recent changes to the EPDP Leadership Team and as a result some time has been lost to accommodate for the transition process. The initial survey to gauge the amount of effort required for each topic may have been underestimated given what could be considered as slow progress on Topic A. The EPDP leadership team is aware that the EPDP is currently behind the published schedule and is investigating options that may recover some of the lost time, including extending the weekly call time to 90 minutes.
- At the time the Charter was developed, it was assumed that the SubPro recommendations, particularly those relating to IDNs under Topic 25, would have been approved by the ICANN Board. The IDN EPDP is conducting its work with the expectation that the SubPro recommendations will be approved by the Board at some future date. However, it has been necessary for the EPDP Team to make assumptions about the implementation of those recommendations in order to address the Charter questions. While these assumptions are believed to be sound, the Council should be aware of the possible ripple effect or potential risk to the EPDP Team work in the event that the Board does not adopt the related SubPro recommendations.

Completed in prior period(s):

- ccNSO, SSAC, and RySG provided early input.
- The ICANN Board appointed Edmon Chung and Akinori Maemura as liaisons to the EPDP Team.
- Completed and distributed [Project Package](#) for November.

Project Tracking & Rollup DASHBOARD




Project Roster

Participant	Participant Type	Role	Participation Start Date	Participation End Date	Legacy SOI Link
Group Selected / Nominated By: Group Name At-Large Advisory Committee (ALAC)					
Justine Chew	Participant	Vice-chair	05/25/21		https://community.icann.c
TV Gopal	Participant		05/25/21		https://community.icann.c
Hadia Elminiawi	Participant		07/14/21		https://community.icann.c
Satish Babu	Member		05/25/21		https://community.icann.c
Lianna Galstyan	Member		05/25/21		https://community.icann.c
Abdulkarim Oloyede	Member		05/25/21		https://community.icann.c
Group Selected / Nominated By: Group Name Commercial Business Users Constituency (BC)					
Mark William Datysgeld	Member		05/25/21		https://community.icann.c
Group Selected / Nominated By: Group Name Expedited Policy Development Process - IDNs					
Donna Austin	Member	Chair	08/10/21		https://community.icann.c
Group Selected / Nominated By: Group Name GNSO Council					
Ekue Farell Folly	Member	Liaison	07/27/21		https://community.icann.c
Group Selected / Nominated By: Group Name Governmental Advisory Committee (GAC)					
Hamza Onoruoiza Salami	Participant		05/25/21		https://community.icann.c
T. Santhosh	Member		05/25/21		https://community.icann.c
Nigel Hickson	Member		07/12/21		https://community.icann.c
Group Selected / Nominated By: Group Name ICANN Board					
Edmon Chung	Member	Liaison	07/27/21		https://community.icann.c
Akinori Maemura	Member	Liaison	11/18/21		https://community.icann.c
Group Selected / Nominated By: Group Name Independent					
Abdalmonem Galila	Participant		05/25/21		https://community.icann.c
Gao Lei	Participant		05/25/21		https://community.icann.c
Nabil Benamar	Participant		05/25/21		https://community.icann.c
Lisa Liang	Participant		05/25/21		https://community.icann.c
Anil Jain	Participant		07/30/21		https://community.icann.c
Quoc Pham	Participant		08/13/21		https://community.icann.c
Group Selected / Nominated By: Group Name Intellectual Property Constituency (IPC)					
Brian King	Member		05/25/21	11/08/21	https://community.icann.c
Jeffrey Neuman	Member		05/25/21		https://community.icann.c
Group Selected / Nominated By: Group Name Internet Corporation for Assigned Names & Numbers (ICANN)					
Michael Karakash	Staff - Assigned	Liaison	05/25/21		
Steve Chan	Staff - Assigned		05/25/21		
Emily Barabas	Staff - Assigned		05/25/21		
Terri Agnew	Staff - Assigned		05/25/21		
Sarmad Hussain	Staff - Assigned	Liaison	05/25/21		
Nathalie Peregrine	Staff - Assigned		05/25/21		
Pitinan Kooarmompatana	Staff - Assigned		05/25/21		
Ariel Liang	Staff - Assigned		05/25/21		
Julie Bisland	Staff - Assigned		05/25/21		
Michelle DeSmyter	Staff - Assigned		08/18/21		
Devan Reed	Staff - Assigned		12/02/21		
Group Selected / Nominated By: Group Name Internet Service Providers and Connectivity Providers Constituency (ISPCP)					
Christian Dawson	Participant		07/12/21		https://community.icann.c
Group Selected / Nominated By: Group Name Non-Commercial Stakeholder Group (NCSG)					
Tomslin Samme-Nlar	Member		05/25/21		https://community.icann.c
Akinremi Peter Taiwo	Member		07/15/21		https://community.icann.c
Group Selected / Nominated By: Group Name Registrar Stakeholder Group (RrSG)					
Michael Bauland	Member		05/25/21		https://community.icann.c
Duwei Chen	Member		09/26/21		https://community.icann.c
Group Selected / Nominated By: Group Name Registry Stakeholder Group (RySG)					
Jennifer Chung	Participant		05/25/21		https://community.icann.c
Jerrv Sen	Participant		05/25/21		https://community.icann.c


Wei (Wesley) Wang	Participant	07/13/21	https://community.icann.org
Maxim Alzoba	Member	05/25/21	https://community.icann.org
Joseph Chiu-Kit Yee	Member	07/06/21	https://community.icann.org
Dennis Tan Tanaka	Member	05/25/21	https://community.icann.org
Group Selected / Nominated By: Group Name Blank			

Project Tracking & Rollup DASHBOARD


Work-Plan Activity Metrics

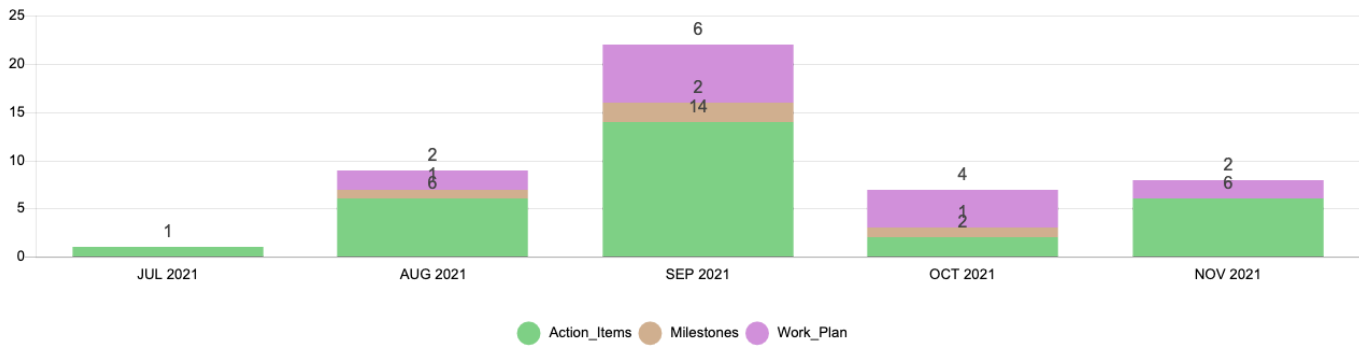

Mailman Activity

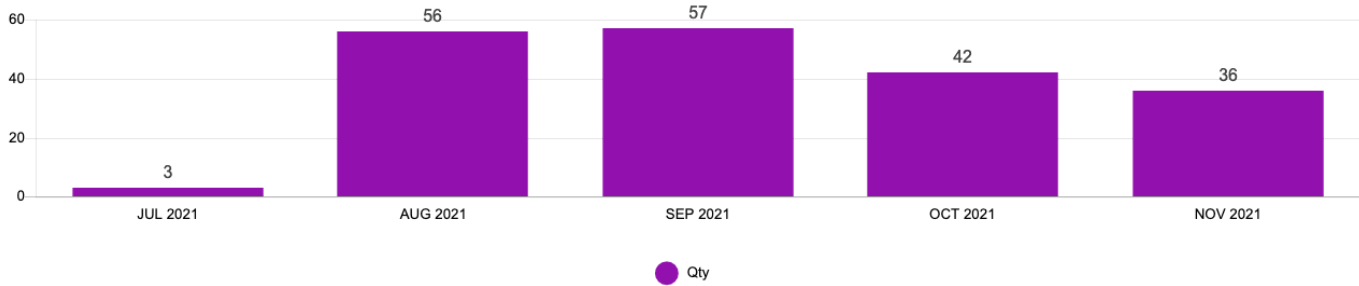

Meeting Activity

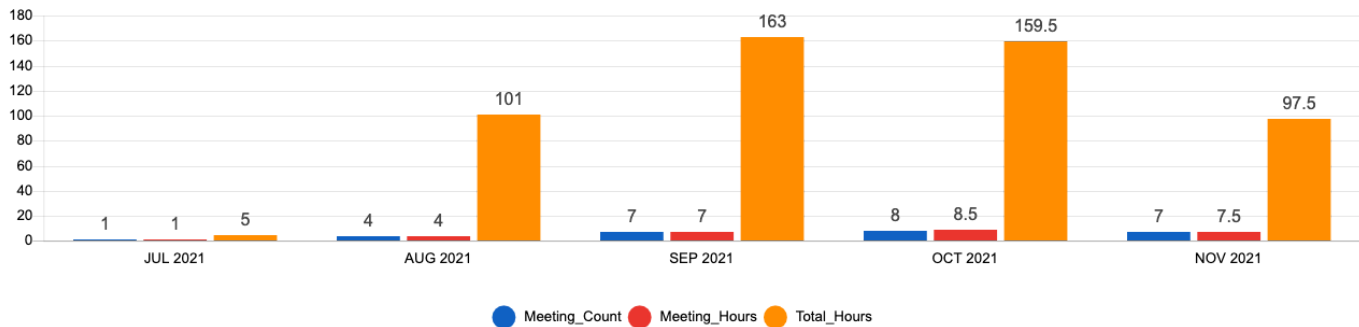

Plenary Attendance

Group Represented	Invited Qty	Attended Qty	Attendance
Total	Sum 437	Sum 313	Avg 71.6%
Primary At-Large Advisory Committee (ALAC)	Sum 84	Sum 71	Avg 84.5%
Attendee Name Abdulkarim Oloyede	Sum 14	Sum 13	Avg 92.9%
Attendee Name Hadia Elminiawi	Sum 14	Sum 13	Avg 92.9%
Attendee Name Justine Chew	Sum 14	Sum 14	Avg 100.0%
Attendee Name Lianna Galstyan	Sum 14	Sum 12	Avg 85.7%
Attendee Name Satish Babu	Sum 14	Sum 13	Avg 92.9%
Attendee Name TV Gopal	Sum 14	Sum 6	Avg 42.9%
Primary Commercial Business Users Constituency (BC)	Sum 14	Sum 2	Avg 14.3%
Attendee Name Mark William Datysgeld	Sum 14	Sum 2	Avg 14.3%

Primary	Expedited Policy Development Process - IDNs	Sum	14	Sum	13	Avg	92.9%
Attendee Name	Donna Austin	Sum	14	Sum	13	Avg	92.9%
Primary	GNSO Council	Sum	14	Sum	11	Avg	78.6%
Attendee Name	Ekue Farell Folly	Sum	14	Sum	11	Avg	78.6%
Primary	Governmental Advisory Committee (GAC)	Sum	42	Sum	33	Avg	78.6%
Attendee Name	Hamza Onoruoiza Salami	Sum	14	Sum	11	Avg	78.6%
Attendee Name	Nigel Hickson	Sum	14	Sum	12	Avg	85.7%
Attendee Name	T. Santhosh	Sum	14	Sum	10	Avg	71.4%
Primary	ICANN Board	Sum	14	Sum	13	Avg	92.9%
Attendee Name	Edmon Chung	Sum	14	Sum	13	Avg	92.9%
Primary	Independent	Sum	81	Sum	39	Avg	48.1%
Attendee Name	Abdalmonem Galila	Sum	14	Sum	2	Avg	14.3%
Attendee Name	ANIL JAIN	Sum	14	Sum	13	Avg	92.9%
Attendee Name	Gao Lei	Sum	13	Sum	1	Avg	7.7%
Attendee Name	Kenny Huang	Sum	1	Sum	1	Avg	100.0%
Attendee Name	Lisa Liang	Sum	14	Sum	13	Avg	92.9%
Attendee Name	Nabil Benamar	Sum	13	Sum	0	Avg	0.0%
Attendee Name	Quoc Pham	Sum	12	Sum	9	Avg	75.0%
Primary	Intellectual Property Constituency (IPC)	Sum	27	Sum	21	Avg	77.8%
Attendee Name	Brian King	Sum	13	Sum	10	Avg	76.9%
Attendee Name	Jeffrey Neuman	Sum	14	Sum	11	Avg	78.6%
Primary	Internet Service Providers and Connectivity Providers Constituency (ISPCP)	Sum	14	Sum	9	Avg	64.3%
Attendee Name	Christian Dawson	Sum	14	Sum	9	Avg	64.3%
Primary	Non-Commercial Stakeholder Group (NCSG)	Sum	28	Sum	14	Avg	50.0%
Attendee Name	Akinremi Peter Taiwo	Sum	14	Sum	6	Avg	42.9%
Attendee Name	Tomslin Samme-Nlar	Sum	14	Sum	8	Avg	57.1%
Primary	Registrar Stakeholder Group (RrSG)	Sum	21	Sum	18	Avg	85.7%
Attendee Name	Duowei Chen	Sum	7	Sum	5	Avg	71.4%
Attendee Name	Michael Bauland	Sum	14	Sum	13	Avg	92.9%
Primary	Registry Stakeholder Group (RySG)	Sum	84	Sum	69	Avg	82.1%
Attendee Name	Dennis Tan Tanaka	Sum	14	Sum	13	Avg	92.9%
Attendee Name	Jennifer Chung	Sum	14	Sum	13	Avg	92.9%
Attendee Name	Jerry Sen	Sum	14	Sum	14	Avg	100.0%
Attendee Name	Joseph Chiu-Kit Yee	Sum	14	Sum	13	Avg	92.9%
Attendee Name	Maxim Alzoba	Sum	14	Sum	13	Avg	92.9%
Attendee Name	Wei (Wesley) Wang	Sum	14	Sum	3	Avg	21.4%

Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	Q1					Q2					Q3					Q4														
							Q1					Q2					Q3					Q4														
							Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
1 EPDP: Internationalized Domain Names	587d	05/20/21	08/18/23		25%	In Progress	[Gantt bar spanning from May 2021 to August 2023]																													
2 PROJECT CONTROL	558d	05/20/21	07/10/23		41%	In Progress	[Gantt bar spanning from May 2021 to July 2023]																													
3 Project start confirmed	0	05/20/21	05/20/21		100%	Complete	[Gantt bar at May 2021]																													
4 Adopt/Confirm charter	0	05/20/21	05/20/21	3	100%	Complete	[Gantt bar at May 2021]																													
5 Confirmation of Team	60d	05/20/21	08/11/21	3	100%	Complete	[Gantt bar from May to August 2021]																													
6 Appointment of Team Chair	46d	05/20/21	07/22/21	3	100%	Complete	[Gantt bar from May to July 2021]																													
7 Appointment of Liaison to GNSO Council	46d	05/20/21	07/22/21	3	100%	Complete	[Gantt bar from May to July 2021]																													
8 Chair / Staff preparations	13d	07/23/21	08/10/21	6	100%	Complete	[Gantt bar from July to August 2021]																													
9 Project Management	512d	07/23/21	07/10/23		22%	In Progress	[Gantt bar spanning from July 2021 to July 2023]																													
10 Develop and confirm Project Plan	50d	07/23/21	09/30/21	6	100%	Complete	[Gantt bar from July to September 2021]																													
11 Obtain project plan approval from GNSO Council	20d	10/01/21	10/28/21	10	100%	Complete	[Gantt bar from October 2021]																													
12 Develop monthly Project Packages and deliver to Group & Council	370d	10/29/21	03/30/23	11	7%	In Progress	[Gantt bar spanning from October 2021 to March 2023]																													
13 Leadership Sub team	440d	07/23/21	03/30/23		22%	In Progress	[Gantt bar spanning from July 2021 to March 2023]																													
14 On-going preparation and planning of group activities	440d	07/23/21	03/30/23	6	22%	In Progress	[Gantt bar spanning from July 2021 to March 2023]																													
15 Close project and transition project to implementation	1d	07/10/23	07/10/23	14, 165	0%		[Gantt bar at July 2023]																													
16 GROUP DELIBERATIONS	417d	08/11/21	03/16/23		24%	In Progress	[Gantt bar spanning from August 2021 to March 2023]																													
17 First meeting of Team	1d	08/11/21	08/11/21	8	100%	Complete	[Gantt bar at August 2021]																													
18 Understand Charter, organize materials and develop initial approach	10d	08/11/21	08/24/21	8	100%	Complete	[Gantt bar from August to September 2021]																													
19 Overview & initial discussion of all Policy Topics	10d	08/11/21	08/24/21	8	100%	Complete	[Gantt bar from August to September 2021]																													
20 Develop definitions and terminology	28d	08/11/21	09/17/21	8	100%	Complete	[Gantt bar from August to October 2021]																													
21 Input from other SO/ACs & GNSO SG/Cs	58d	09/09/21	11/29/21		100%	Complete	[Gantt bar from September to November 2021]																													
26 Topic A Deliberations: Consistent definition and technical utilization of RZ-LGR	50d	08/25/21	11/02/21		38%	In Progress	[Gantt bar from August to November 2021]																													
44 Topic B Deliberations: "Same entity" at the top-level	40d	11/03/21	12/28/21				[Gantt bar from November 2021]																													
57 Topic C Deliberations: "Same entity" at the second-level	40d	12/29/21	02/22/22				[Gantt bar from December 2021]																													
71 Topic D Deliberations: Adjustments in registry agreement, registry service, registry transition process, and other processes/procedures related to the domain name lifecycle	65d	02/23/22	05/24/22				[Gantt bar from February to May 2022]																													
87 Topic E Deliberations: Adjustments to objection process, string similarity review, string contention resolution, reserved strings, and other policies and procedures	50d	05/25/22	08/02/22				[Gantt bar from May to August 2022]																													
102 Topic F Deliberations: Adjustments in registration dispute resolution procedures and trademark protection mechanisms	40d	08/03/22	09/27/22				[Gantt bar from August to September 2022]																													
112 Topic G Deliberations: Process to update the IDN Implementation Guidelines	28d	09/28/22	11/04/22				[Gantt bar from September 2022]																													
121 Unplanned Issues & Tasks	0	08/24/21	08/24/21				[Gantt bar at August 2021]																													
138 Key Group Events	364d	10/25/21	03/16/23		17%	In Progress	[Gantt bar spanning from October 2021 to March 2023]																													
145 INITIAL REPORT	360d	09/20/21	02/03/23		12%	In Progress	[Gantt bar spanning from September 2021 to February 2023]																													
146 Populate stable drafts as required	300d	09/20/21	11/11/22	20	15%	In Progress	[Gantt bar spanning from September 2021 to November 2022]																													
147 Discuss/approve findings and interim recommendations	10d	11/14/22	11/25/22	146			[Gantt bar from November 2022]																													
148 Consolidate interim recommendations and findings	10d	11/28/22	12/09/22	147			[Gantt bar from November to December 2022]																													
149 Build Draft Report for public comment	10d	11/28/22	12/09/22	147			[Gantt bar from November to December 2022]																													
150 Approve Draft Report for public comment	5d	12/12/22	12/16/22	149			[Gantt bar from December 2022]																													
151 Publish Initial Report	0	12/16/22	12/16/22	150			[Gantt bar at December 2022]																													
152 Communicate Initial Report	5d	12/19/22	12/23/22	150			[Gantt bar from December 2022]																													
153 Public comment forum on the Initial Report (40 days)	35d	12/19/22	02/03/23	150			[Gantt bar from December 2022 to February 2023]																													
154 FINAL REPORT	45d	02/06/23	04/07/23			Not Started	[Gantt bar from February to April 2023]																													
155 Review of public comments	30d	02/06/23	03/17/23	153			[Gantt bar from February to March 2023]																													
156 Continue deliberations of policy topics towards a Final Report	30d	02/06/23	03/17/23	153			[Gantt bar from February to March 2023]																													
157 Build Final Report & Final Deliberations	5d	03/20/23	03/24/23	156			[Gantt bar from March 2023]																													
158 Determine consensus levels on interim recommendations	10d	03/27/23	04/07/23	157			[Gantt bar from March to April 2023]																													
159 Adopt final recommendations and report	10d	03/27/23	04/07/23	157			[Gantt bar from March to April 2023]																													
160 Submission of Final Report to the GNSO Council	0	04/07/23	04/07/23	159			[Gantt bar at April 2023]																													
161 POST GROUP TASKS	95d	04/10/23	08/18/23			Not Started	[Gantt bar spanning from April 2023 to August 2023]																													
162 Approval of Final Report and Recommendations by the GNSO Council	45d	04/10/23	06/09/23	160			[Gantt bar from April to June 2023]																													
163 Report to the Board	15d	06/12/23	06/30/23	162			[Gantt bar from June 2023]																													
164 Publish Recommendations for Public Comment	35d	07/03/23	08/18/23	163			[Gantt bar from July to August 2023]																													
165 Inform GAC if Recommendations affect public policy	5d	07/03/23	07/07/23	163			[Gantt bar from July 2023]																													
166																																				
167 PDP CHECKLIST	99d	01/01/21	05/20/21				[Gantt bar from January 2021 to May 2021]																													

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	AI	Action Item #1: Leadership Team to follow up with WG regarding transition to 90-minute meetings in November.	—	EPDP_IDN Leadership	11/11/21	11/11/21	Complete	
	AI	Action Item #1: The liaisons (Alireza/Anil and Dennis) will discuss where additional coordination may be needed beyond VM management, if applicable.	—	EPDP_IDN Leadership	11/18/21	11/18/21	Complete	
	AI	Action Item #2: Review the process flow and provide questions and comments before the next meeting, which should support discussions on the potential challenge mechanisms.	—	EPDP_IDN	10/26/21	11/04/21	Complete	
	WP	Meeting #12 Topic A/Question 3A: discuss the procedural application of RZ-LGR, challenge process diagram, and high-level questions	↓	EPDP_IDN	11/04/21	11/04/21	Complete	
	AI	Staff will formulate EPDP Team's draft agreement for a3.	—	Ariel Liang	11/18/21	11/18/21	Complete	
	WP	Meeting #13 Topic A/Question A3: confirm EPDP Team agreement and discuss relevant SubPro recommendations and implementation guidance Discuss data collection result related to Topic A/Questions A1-A2	↓	EPDP_IDN	11/18/21	11/18/21	Complete	
	AI	Staff will formulate a draft outcome for a3, taking into consideration EPDP Team discussion.	—	Ariel Liang	11/29/21	11/29/21	Complete	
	WP	Meeting #14 Report on SO/AC Early Input; Topic A/Question A4 Analysis; Topic A/Question A5 Introduction	—	EPDP_IDN	12/02/21	12/02/21	Complete	
	AI	Action Item #1: WG to review draft response to charter questions and provide input by Monday 13 December 2021	—	EPDP_IDN	12/13/21		In Progress	
	AI	Action Item #2: Staff to draft placeholder response to charter question a4 based on the analysis conducted. WG will return to close the question once it has deliberated on charter question b4	—	Ariel Liang	12/09/21		In Progress	
	AI	Action Item #3: Leadership team to see if there are additional background materials that can be leveraged to inform discussion on charter question A5	—	EPDP_IDN Leadership	12/16/21			
	WP	Meeting #15 TBD	—	EPDP_IDN	12/09/21			
	WP	Meeting #16 TBD	—	EPDP_IDN	12/16/21			
	WP	Meeting #18 TBD	—	EPDP_IDN	12/23/21			
	MS	Submit project package to GNSO Council	!	Ariel Liang Ekue Farell Folly	12/03/21			
	MS	Submit project package to GNSO Council	!	Ariel Liang	01/07/22			
