

Project Tracking & Rollup DASHBOARD

Project Name EPDP: Internationalized Domain Names **Program** IDNs **Project Sponsor** GNSO Council

Project Information **Tasks by Status** **Project Contacts** **Participant Summary**

05/20/21


Current Start

08/18/23

Current Finish

54%

% Complete



Project Contacts

Donna Austin

Chair

Justine Chew

Vice_Chair

Farell Folly

Liaison


AL Ariel Liang

Staff_Lead

SC Steve Chan

Project_Manager

Participant Summary



Member Participant_Count
Observer_Email_Only Staff_Assigned
Staff_Not_Assigned

Project Status & Health

Project_Status **Behind Schedule** Project_Health **On-Target**

Not_Started Complete In_Progress

Summary Gantt & Key Milestones

Health	Primary Task	Current Start	Current Finish	% Complete	Status	Summary Gantt & Key Milestones											
						2021 Q1	2021 Q2	2021 Q3	2021 Q4	2022 Q1	2022 Q2	2022 Q3	2022 Q4	2023 Q1	2023 Q2	2023 Q3	2023 Q4
	EPDP: Internationalized Domain Names	05/20/21	08/18/23	54%	In Progress	EPDP: Internationalized Domain Names											
	PROJECT CONTROL	05/20/21	07/10/23	72%	In Progress	PROJECT CONTROL											
	GROUP DELIBERATIONS	08/11/21	03/16/23	64%	In Progress	GROUP DELIBERATIONS											
●	Group 1: Definition of All gTLDs Using RZ-LGR	08/25/21	02/17/22	94%	In Progress	Group 1: Definition of All gTLDs Using RZ-LGR											
●	Group 2: Same Entity at Top-Level	02/04/22	03/31/22	86%	In Progress	Group 2: Same Entity at Top-Level											
●	Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	03/18/22	06/02/22	57%	In Progress	Group 3: Objection Processes, String Similarity Review, String Contention Resolution, ...											
●	Group 4: Same Entity at Second-Level	05/20/22	08/04/22	15%	In Progress	Group 4: Same Entity at Second-Level											
●	Group 5: Domain Name Lifecycle	07/22/22	09/16/22			Group 5: Domain Name Lifecycle											
●	Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	09/05/22	10/24/22			Group 6: Registration Dispute Resolution Procedures and Trademark Protection											
●	Group 7: IDN Implementation Guidelines	10/11/22	11/11/22			Group 7: IDN Implementation Guidelines											
	INITIAL REPORT	09/20/21	02/03/23	36%	In Progress	INITIAL REPORT											
	Publish Initial Report	12/16/22	12/16/22			Publish Initial Report											
	Public comment forum on the Initial Report (40 days)	12/19/22	02/03/23			Public comment forum on the Initial Report (40 days)											
	FINAL REPORT	02/06/23	04/07/23		Not Started	FINAL REPORT											
	Review of public comments	02/06/23	03/17/23			Review of public comments											
	Submission of Final Report to the GNSO Council	04/07/23	04/07/23			Submission of Final Report to the GNSO Council											

4 - Working Group

Title:	EPDP - Internationalized Domain Names (EPDP_IDN)
Description & Scope:	On 20 May 2021, the GNSO Council passed a resolution to initiate the Expedited Policy Development Process (EPDP) on Internationalized Domain Names and adopt its charter. The EPDP Team is tasked with providing the GNSO Council with policy recommendations on: 1) the definition of gTLDs and the management of variant labels; and 2) how the IDN Implementation Guidelines, which Contracted Parties are required to comply with, should be updated in the future.

Composition:

Chair:	Donna Austin
Vice Chair:	Justine Chew
Council Liaison:	Farell Folly
Policy Staff:	A. Liang, S. Chan, E. Barabas
GDS Staff:	S. Hussain, M. Karakash
# Participants:	36 Participants (link)
# Observers:	11
Tools:	Mailing List / Meeting Schedule / Wiki
Charter:	Charter

Project Management:

Token Holder	Planned Start Date	Actual Start Date	# of Days	Planned End Date	Actual End Date
WG	20 May 2021	20 May 2021	489	09 Jun 2023	TBD

Program	Progress	Status	Health
IDNs	54%		

STATUS: ■ Planned ● On-schedule ● Revised schedule ▲ Behind schedule ◆ Target will be missed ■ On-hold

HEALTH: ■ On-Target ■ At-Risk ■ In-Trouble

Milestones/Work plan (link):

Milestone/Task	Date	
Project Start	May-21	✓
Scoping Team Report	Jan-20	✓
Charter Approved	May-21	✓
EPDP Initiation Request Approved	May-21	✓
1st Plenary meeting	Aug-21	✓
SO/AC & SG/C Input to PDP	Nov-21	✓
Project Plan and Work plan Adoption	Oct-21	✓
Issue Deliberations	Mar-23	■
Populate draft report w/ findings & potential recs.	Oct-22	■
Assemble initial conclusions	Oct-22	■
Discuss/approve findings and interim recs.	Nov-22	■
Consolidate interim recommendations and findings	Nov-22	■
Issue report for public comment	Dec-22	■
Review public comment input & prepare final report	Mar-23	■
Finalize Report	Apr-23	■
Determine consensus levels on recommendations	Apr-23	■
Adopt final recommendations and report	Apr-23	■
Send final report to GNSO Council	Apr-23	■
GNSO Council adoption of consensus recs.	May-23	■
Issue public comment for Board consideration	Jun-23	■
ICANN Board adoption of consensus recs.	Oct-23	■
Prior period % Complete	52%	■

Status/Health Rationale:

- This project Status was downgraded to “Behind Schedule” on 31 Aug 2022 and Health of “On-Target”.

Current Activities:

- Discussing String Similarity Small Group’s draft recommendations with regard to the String Similarity Review, as well as the Objection process, taking into account the impact of variant implementation.
- Conducting second reading of draft outcome language for Group 2 charter questions related to the “same entity” principle at the top-level and Group 3 charter questions related to the New gTLD Program as impacted by variant labels.
- Developing a working glossary list to define key terms frequently used during deliberation and recommendation drafting.
- Conducting strawman analysis to understand whether aspects of the New gTLD Program not already explicitly captured in the Charter, will be impacted due to the implementation of variants.

Planned Activities:

- Deliberate the parked items among Group 1-3 charter questions.
- Ask Chinese, Japanese, and Korean Generation Panels to conduct potential work related to Charter Question E7 on single-character TLDs.
- Review Arabic and Chinese TLD registry survey results in conjunction with the strawman analysis to discuss the process and mechanism by which existing registries can request to activate variant labels.
- Conduct risk analysis exercises to deliberate on String Similarity Small Group’s recommendations.
- Submit project change request to the GNSO Council, requesting to first publish Part 1 of the Initial Report by focusing on top-level variant management related recommendations, and defer deliberation on second-level variant management issues after obtaining necessary data.
- Conduct data collection to assist EPDP Team’s deliberation on second-level variant management related issues.

Open Issues, Risks & Mitigation Plan:


- Deliberations of certain Charter questions depend on the critical input from external parties and additional data collection efforts.
- The EPDP Team plans to first publish Part 1 of the Initial Report by focusing on top-level variant management related recommendations while collecting necessary data to assist its deliberation on the remaining charter questions related to second-level variant management issues. The EPDP Team plans to submit a project change request to the Council, seeking approval for the updated project plan.
- At the time the Charter was developed, it was assumed that the SubPro recommendations, particularly those relating to IDNs under Topic 25, would have been approved by the ICANN Board. The IDN EPDP is conducting its work with the expectation that the SubPro recommendations will be approved by the Board at some future date. However, it has been necessary for the EPDP Team to make assumptions about the implementation of those recommendations in order to address the Charter questions. While these assumptions are believed to be sound, the Council should be aware of the possible ripple effect or potential risk to the EPDP Teamwork in the event that the Board does not adopt the related SubPro recommendations.

Completed in prior period(s):


- Completed the first reading of draft outcome language for Group 3 charter questions.
- Completed and distributed [Project Package](#) for August.

Project Tracking & Rollup DASHBOARD


Work-Plan Activity Metrics

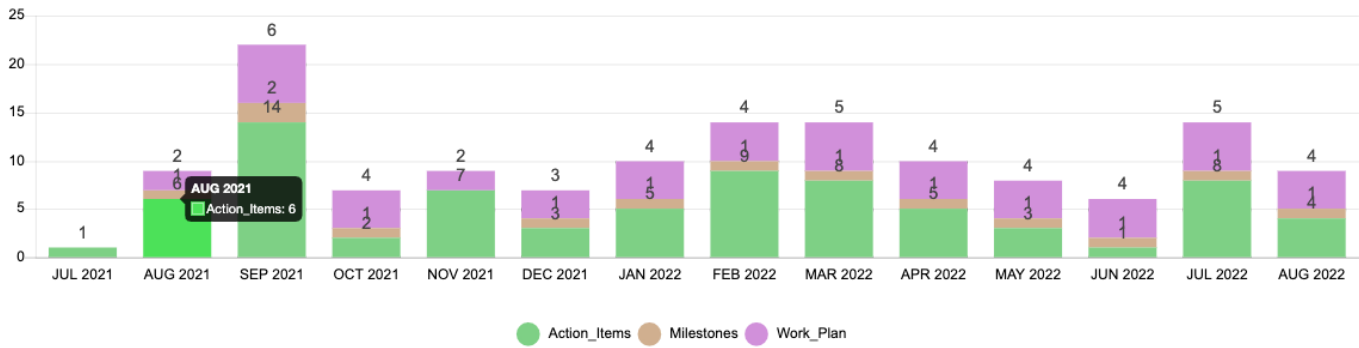

Mailman Activity

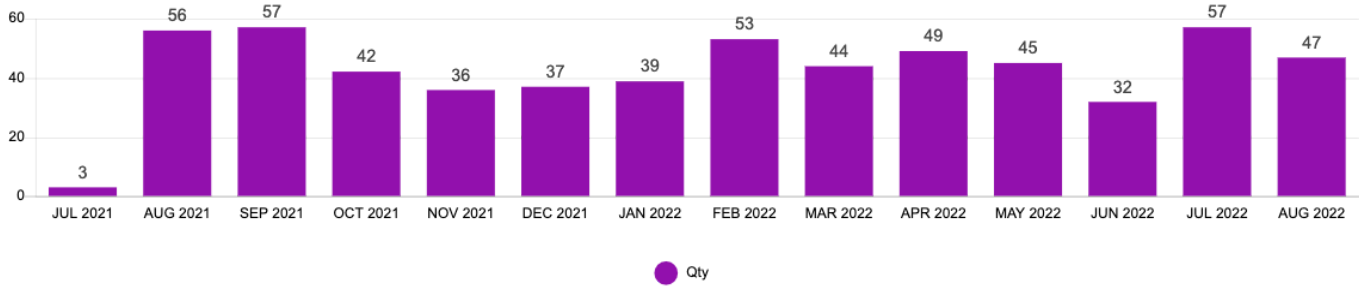

Meeting Activity

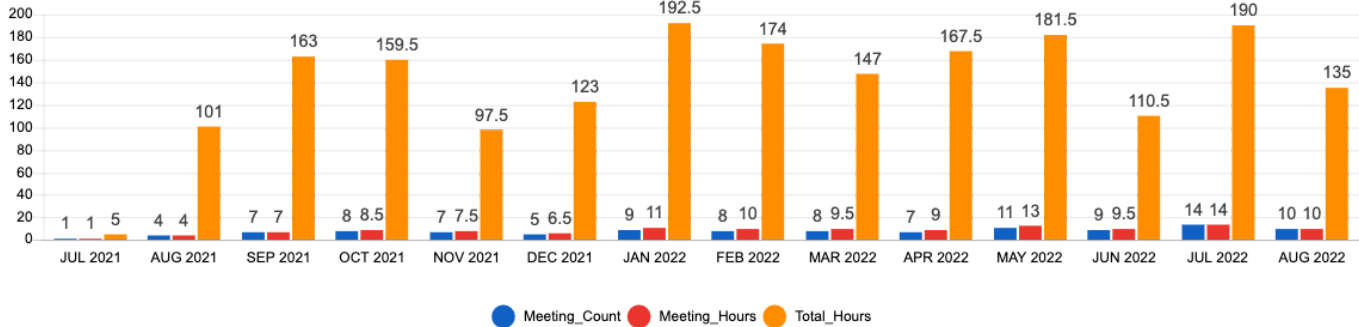

Plenary Attendance

Group Represented	Invited Qty	Attended Qty	Attendance
Total	Sum 1454	Sum 905	Avg 62.2%
Primary At-Large Advisory Committee (ALAC)	Sum 257	Sum 211	Avg 82.1%
Attendee Name Abdulkarim Oloyede	Sum 46	Sum 40	Avg 87.0%
Attendee Name Hadia Elminiawi	Sum 47	Sum 46	Avg 97.9%
Attendee Name Justine Chew	Sum 47	Sum 47	Avg 100.0%
Attendee Name Lianna Galstyan	Sum 46	Sum 28	Avg 60.9%
Attendee Name Satish Babu	Sum 47	Sum 44	Avg 93.6%
Attendee Name TV Gopal	Sum 24	Sum 6	Avg 25.0%
Primary Commercial Business Users Constituency (BC)	Sum 34	Sum 2	Avg 5.9%
Attendee Name Mark William Datysgeld	Sum 34	Sum 2	Avg 5.9%

Primary	Sum	Sum	Avg
Expedited Policy Development Process - IDNs	47	44	93.6%
Attendee Name	Sum	Sum	Avg
Donna Austin	47	44	93.6%
Primary	Sum	Sum	Avg
GNSO Council	47	36	76.6%
Attendee Name	Sum	Sum	Avg
Ekue Farell Folly	47	36	76.6%
Primary	Sum	Sum	Avg
Governmental Advisory Committee (GAC)	137	82	59.9%
Attendee Name	Sum	Sum	Avg
Hamza Onoruoiza Salami	45	33	73.3%
Attendee Name	Sum	Sum	Avg
Nigel Hickson	46	29	63.0%
Attendee Name	Sum	Sum	Avg
T. Santhosh	46	20	43.5%
Primary	Sum	Sum	Avg
ICANN Board	78	71	91.0%
Attendee Name	Sum	Sum	Avg
Akinori Maemura	32	27	84.4%
Attendee Name	Sum	Sum	Avg
Edmon Chung	46	44	95.7%
Primary	Sum	Sum	Avg
Independent	292	104	35.6%
Attendee Name	Sum	Sum	Avg
Abdalmonem Galila	45	2	4.4%
Attendee Name	Sum	Sum	Avg
ANIL JAIN	46	39	84.8%
Attendee Name	Sum	Sum	Avg
Gao Lei	44	1	2.3%
Attendee Name	Sum	Sum	Avg
Imran Hossen	14	5	35.7%
Attendee Name	Sum	Sum	Avg
Kenny Huang	1	1	100.0%
Attendee Name	Sum	Sum	Avg
Lisa Liang	46	44	95.7%
Attendee Name	Sum	Sum	Avg
Nabil Benamar	44	0	0.0%
Attendee Name	Sum	Sum	Avg
Quoc Pham	43	12	27.9%
Attendee Name	Sum	Sum	Avg
Wael Nasr	9	0	0.0%
Primary	Sum	Sum	Avg
Intellectual Property Constituency (IPC)	59	40	67.8%
Attendee Name	Sum	Sum	Avg
Brian King	13	10	76.9%
Attendee Name	Sum	Sum	Avg
Jeffrey Neuman	46	30	65.2%
Primary	Sum	Sum	Avg
Internet Service Providers and Connectivity Providers Constituency (ISPCP)	45	15	33.3%
Attendee Name	Sum	Sum	Avg
Christian Dawson	45	15	33.3%
Primary	Sum	Sum	Avg
Non-Commercial Stakeholder Group (NCSG)	92	19	20.7%
Attendee Name	Sum	Sum	Avg
Akinremi Peter Taiwo	46	8	17.4%
Attendee Name	Sum	Sum	Avg
Emmanuel Vitus Agbenonwossi	7	2	28.6%
Attendee Name	Sum	Sum	Avg
Tomslin Samme-Nlar	39	9	23.1%
Primary	Sum	Sum	Avg
Registrar Stakeholder Group (RrSG)	87	76	87.4%
Attendee Name	Sum	Sum	Avg
Duowei Chen	16	11	68.8%
Attendee Name	Sum	Sum	Avg
Michael Bauland	47	41	87.2%
Attendee Name	Sum	Sum	Avg
Zhang Zuan	24	24	100.0%
Primary	Sum	Sum	Avg
Registry Stakeholder Group (RySG)	274	200	73.0%
Attendee Name	Sum	Sum	Avg
Dennis Tan Tanaka	46	42	91.3%
Attendee Name	Sum	Sum	Avg
Jennifer Chung	45	34	75.6%

Attendee Name Jerry Sen	Sum 46	Sum 46	Avg 100.0%
Attendee Name Joseph Chiu-Kit Yee	Sum 46	Sum 39	Avg 84.8%
Attendee Name Maxim Alzoba	Sum 46	Sum 36	Avg 78.3%
Attendee Name Wei (Wesley) Wang	Sum 45	Sum 3	Avg 6.7%
Primary Security and Stability Advisory Committee (SSAC)	Sum 5	Sum 5	Avg 100.0%
Attendee Name Jiankang Yao	Sum 1	Sum 1	Avg 100.0%
Attendee Name John R. Levine	Sum 1	Sum 1	Avg 100.0%
Attendee Name Lyman Chapin	Sum 1	Sum 1	Avg 100.0%
Attendee Name Patrik Fältström	Sum 1	Sum 1	Avg 100.0%
Attendee Name Ram Mohan	Sum 1	Sum 1	Avg 100.0%

Project Tracking & Rollup DASHBOARD



Project Roster

Participant	Participant Type	Role	Participation Start Date	Participation End Date	Legacy SOI Link
Group Selected / Nominated By: Group Name At-Large Advisory Committee (ALAC)					
Justine Chew	Participant	Vice-chair	05/25/21		https://community.icann.org
TV Gopal	Participant		05/25/21	03/21/22	https://community.icann.org
Hadia Elminiawi	Participant		07/14/21		https://community.icann.org
Satish Babu	Member		05/25/21		https://community.icann.org
Lianna Galstyan	Member		05/25/21		https://community.icann.org
Abdulkarim Oloyede	Member		05/25/21		https://community.icann.org
Group Selected / Nominated By: Group Name Commercial Business Users Constituency (BC)					
Mark William Datysgeld	Member		05/25/21	05/12/22	https://community.icann.org
Group Selected / Nominated By: Group Name Expedited Policy Development Process - IDNs					
Donna Austin	Member	Chair	08/10/21		https://community.icann.org
Group Selected / Nominated By: Group Name GNSO Council					
Ekue Farell Folly	Member	Liaison	07/27/21		https://community.icann.org
Group Selected / Nominated By: Group Name Governmental Advisory Committee (GAC)					
Hamza Onoruoiza Salami	Participant		05/25/21		https://community.icann.org
T. Santhosh	Member		05/25/21		https://community.icann.org
Nigel Hickson	Member		07/12/21		https://community.icann.org
Group Selected / Nominated By: Group Name ICANN Board					
Edmon Chung	Member	Liaison	07/27/21		https://community.icann.org
Akinori Maemura	Member	Liaison	11/18/21		https://community.icann.org
Group Selected / Nominated By: Group Name Independent					
Abdalmonem Galila	Participant		05/25/21		https://community.icann.org
Gao Lei	Participant		05/25/21		https://community.icann.org
Nabil Benamar	Participant		05/25/21		https://community.icann.org
Lisa Liang	Participant		05/25/21		https://community.icann.org
Anil Jain	Participant		07/30/21		https://community.icann.org
Quoc Pham	Participant		08/13/21		https://community.icann.org
Imran Hossen	Participant		11/04/21		https://community.icann.org
Wael Nasr	Participant		06/09/22		https://community.icann.org
Kenny Huang	Guest		10/26/21	10/26/21	
Group Selected / Nominated By: Group Name Intellectual Property Constituency (IPC)					
Brian King	Member		05/25/21	11/08/21	https://community.icann.org
Jeffrey Neuman	Member		05/25/21		https://community.icann.org
Group Selected / Nominated By: Group Name Internet Corporation for Assigned Names & Numbers (ICANN)					
Michael Karakash	Staff - Assigned	Liaison	05/25/21		
Steve Chan	Staff - Assigned		05/25/21		
Emily Barabas	Staff - Assigned		05/25/21		
Terri Agnew	Staff - Assigned		05/25/21		
Sarmad Hussain	Staff - Assigned	Liaison	05/25/21		
Nathalie Peregrine	Staff - Assigned		05/25/21		
Pitinan Kooarmompatana	Staff - Assigned		05/25/21		
Ariel Liang	Staff - Assigned		05/25/21		
Julie Bisland	Staff - Assigned		05/25/21		
Michelle DeSmyter	Staff - Assigned		08/18/21		
Devan Reed	Staff - Assigned		12/02/21		
Group Selected / Nominated By: Group Name Internet Service Providers and Connectivity Providers Constituency (ISPCP)					
Christian Dawson	Participant		07/12/21		https://community.icann.org
Group Selected / Nominated By: Group Name Non-Commercial Stakeholder Group (NCSG)					
Emmanuel Vitus Agbenonwossi	Member		07/13/22		https://community.icann.org
Akinremi Peter Taiwo	Member		07/15/21		https://community.icann.org
Group Selected / Nominated By: Group Name Registrar Stakeholder Group (RrSG)					
Michael Bauland	Member		05/25/21		https://community.icann.org
Duowei Chen	Member		09/26/21	02/13/22	https://community.icann.org
Zhang Zhan	Member		02/14/22		https://community.icann.org

Group Name	MEMBER	DATE	LINK
Group Selected / Nominated By: Group Name			
Registry Stakeholder Group (RySG)			
Jennifer Chung	Participant	05/25/21	https://community.icann.org
Jerry Sen	Participant	05/25/21	https://community.icann.org
Wei (Wesley) Wang	Participant	07/13/21	https://community.icann.org
Maxim Alzoba	Member	05/25/21	https://community.icann.org
Joseph Chiu-Kit Yee	Member	07/06/21	https://community.icann.org
Dennis Tan Tanaka	Member	05/25/21	https://community.icann.org
Group Selected / Nominated By: Group Name			
Security and Stability Advisory Committee (SSAC)			
Lyman Chapin	Guest	01/13/22	
Jiankang Yao	Guest	01/13/22	
John R. Levine	Guest	01/13/22	
Ram Mohan	Guest	01/13/22	
Patrik Fältström	Guest	01/13/22	

Health	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	Baseline Start	Baseline Finish	Q1		Q2		Q3		Q4		Q1		Q2		Q3		Q4		Q1		Q2		Q3									
										Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
1	EPDP: Internationalized Domain Names	587d	05/20/21	08/18/23		54%	In Progress	05/20/21	08/18/23																														
2	PROJECT CONTROL	558d	05/20/21	07/10/23		72%	In Progress	05/20/21	07/10/23																														
3	Project start confirmed	0	05/20/21	05/20/21		100%	Complete	05/20/21	05/20/21																														
4	Adopt/Confirm charter	0	05/20/21	05/20/21	3	100%	Complete	05/20/21	05/20/21																														
5	Confirmation of Team	60d	05/20/21	08/11/21	3	100%	Complete	05/20/21	08/11/21																														
6	Appointment of Team Chair	46d	05/20/21	07/22/21	3	100%	Complete	05/20/21	07/22/21																														
7	Appointment of Liaison to GNSO Council	46d	05/20/21	07/22/21	3	100%	Complete	05/20/21	07/22/21																														
8	Chair / Staff preparations	13d	07/23/21	08/10/21	6	100%	Complete	07/23/21	08/10/21																														
9	Project Management	512d	07/23/21	07/10/23		63%	In Progress	07/23/21	07/10/23																														
10	Develop and confirm Project Plan	50d	07/23/21	09/30/21	6	100%	Complete	07/23/21	09/30/21																														
11	Obtain project plan approval from GNSO Council	20d	10/01/21	10/28/21	10	100%	Complete	10/01/21	10/28/21																														
12	Develop monthly Project Packages and deliver to Group & Council	370d	10/29/21	03/30/23	11	52%	In Progress	10/29/21	03/30/23																														
13	Leadership Sub team	440d	07/23/21	03/30/23		67%	In Progress	07/23/21	03/30/23																														
14	On-going preparation and planning of group activities	440d	07/23/21	03/30/23	6	67%	In Progress	07/23/21	03/30/23																														
15	Close project and transition project to implementation	1d	07/10/23	07/10/23	14, 164	0%		07/10/23	07/10/23																														
16	GROUP DELIBERATIONS	417d	08/11/21	03/16/23		64%	In Progress	08/11/21	03/16/23																														
17	First meeting of Team	1d	08/11/21	08/11/21	8	100%	Complete	08/11/21	08/11/21																														
18	Understand Charter, organize materials and develop initial approach	10d	08/11/21	08/24/21	8	100%	Complete	08/11/21	08/24/21																														
19	Overview & initial discussion of all Policy Topics	10d	08/11/21	08/24/21	8	100%	Complete	08/11/21	08/24/21																														
20	Develop definitions and terminology	28d	08/11/21	09/17/21	8	100%	Complete	08/11/21	09/17/21																														
21	Input from other SO/ACs & GNSO SG/Cs	58d	09/09/21	11/29/21		100%	Complete	09/09/21	12/01/21																														
26	Group 1: Definition of All gTLDs Using RZ-LGR	127d	08/25/21	02/17/22		94%	In Progress	08/25/21	11/02/21																														
44	Group 2: Same Entity at Top-Level	40d	02/04/22	03/31/22		86%	In Progress	11/03/21	12/28/21																														
58	Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	55d	03/18/22	06/02/22		57%	In Progress	12/29/21	02/22/22																														
74	Group 4: Same Entity at Second-Level	55d	05/20/22	08/04/22		15%	In Progress	02/23/22	05/24/22																														
88	Group 5: Domain Name Lifecycle	41d	07/22/22	09/16/22				05/25/22	08/02/22																														
101	Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	36d	09/05/22	10/24/22				08/03/22	09/27/22																														
111	Group 7: IDN Implementation Guidelines	24d	10/11/22	11/11/22				09/28/22	11/04/22																														
120	Unplanned Issues & Tasks	0	08/24/21	08/24/21				08/24/21	08/24/21																														
137	Key Group Events	364d	10/25/21	03/16/23		67%	In Progress	10/25/21	03/16/23																														
138	ICANN Meetings/WG Team F2F Meeting	364d	10/25/21	03/16/23		67%	In Progress	10/25/21	03/16/23																														
139	ICANN72	4d	10/25/21	10/28/21		100%	Complete	10/25/21	10/28/21																														
140	ICANN73	5d	03/05/22	03/10/22		100%	Complete	03/05/22	03/10/22																														
141	ICANN74	4d	06/13/22	06/16/22		100%	Complete	06/13/22	06/16/22																														
142	ICANN75	5d	09/17/22	09/22/22		50%	In Progress	09/17/22	09/22/22																														
143	ICANN76	5d	03/11/23	03/16/23				03/11/23	03/16/23																														
144	INITIAL REPORT	360d	09/20/21	02/03/23		36%	In Progress	09/20/21	02/03/23																														
145	Populate stable drafts as required	300d	09/20/21	11/11/22	20	45%	In Progress	09/20/21	11/11/22																														
146	Discuss/approve findings and interim recommendations	10d	11/14/22	11/25/22	145			11/14/22	11/25/22																														
147	Consolidate interim recommendations and findings	10d	11/28/22	12/09/22	146			11/28/22	12/09/22																														
148	Build Draft Report for public comment	10d	11/28/22	12/09/22	146			11/28/22	12/09/22																														
149	Approve Draft Report for public comment	5d	12/12/22	12/16/22	148			12/12/22	12/16/22																														
150	Publish Initial Report	0	12/16/22	12/16/22	149			12/16/22	12/16/22																														
151	Communicate Initial Report	5d	12/19/22	12/23/22	149			12/19/22	12/23/22																														
152	Public comment forum on the Initial Report (40 days)	35d	12/19/22	02/03/23	149			12/19/22	02/03/23																														
153	FINAL REPORT	45d	02/06/23	04/07/23			Not Started	02/06/23	04/07/23																														
160	POST GROUP TASKS	95d	04/10/23	08/18/23			Not Started	04/10/23	08/18/23																														
165																																							
166	PDP CHECKLIST	99d	01/01/21	05/20/21																																			

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #45 Additional discussion on Recommendation 2.3 under Charter Question B2, and Recommendations 2.5 and 2.6 under Charter Question D1b	↓	EPDP_IDN	07/28/22	07/28/22	Complete	
	WP	Meeting #46 Glossary	↓	EPDP_IDN	08/04/22	08/04/22	Complete	
	AI	Leadership team will send proposed revisions to Recommendation 2.3 under Charter Question B2, and Recommendations 2.5 and 2.6 under Charter Question D1b (part 2) to the mailing list to give those not on the call an opportunity to review the revised text.	—	EPDP_IDN Leadership	08/12/22	08/12/22	Complete	
	AI	Staff to consider if rationale for recommendation 2.5 can be further clarified, perhaps by adding "Where the primary label is sought with one or more variant labels at the same time."	—	EPDP_IDN Leadership	08/04/22	08/04/22	Complete	
	AI	EPDP Team members to review slides 15-18 of today's deck. The Team will return to the topic of strings ineligible for delegation on the next call.	—	EPDP_IDN	08/04/22	08/18/22	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	08/05/22	08/15/22	Complete	
	WP	Meeting #47 String Similarity small group outputs on String Similarity Review	↓	EPDP_IDN	08/11/22	08/11/22	Complete	
	AI	Action Item 1: EPDP Team members to provide input on whether it is acceptable to move the 25 August EPDP Team meeting 24 hours later to 26 August at 13:30 UTC to avoid a scheduling conflict with the August GNSO Council meeting.	↓	EPDP_IDN	08/16/22	08/16/22	Complete	
	WP	Meeting #48 Small Group outputs - objections	↓	EPDP_IDN	08/18/22	08/18/22	Complete	
	WP	Meeting #49 Continue discussions on string similarity review	↓	EPDP_IDN	08/26/22	08/26/22	Complete	
●	WP	Meeting #50 Charter Question E5 (Part 2)	↓	EPDP_IDN	09/01/22		In Progress	
	AI	Leadership team to propose recommendation language to bring back to the EPDP Team for Charter Question E5 (Part 2).		EPDP_IDN Leadership	09/22/22		In Progress	
	AI	Action Item 2: ALAC representatives to propose a path forward on Rationale for Recommendation 2.6.		EPDP_IDN	09/08/22		In Progress	
	WP	Meeting #51 TBD	↓	EPDP_IDN	09/08/22		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	09/09/22		Not Started	
	WP	Meeting #52 ---Cancelled---	↓	EPDP_IDN	09/15/22		Not Started	
	WP	ICANN75 - Session 1 TBD	↓	EPDP_IDN	09/17/22		Not Started	
	WP	ICANN75 - Session 2 TBD	↓	EPDP_IDN	09/17/22		Not Started	
	WP	Meeting #53 TBD	↓	EPDP_IDN	10/06/22		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	10/07/22		Not Started	
	WP	Meeting #54 TBD	↓	EPDP_IDN	10/13/22		Not Started	
	WP	Meeting #55 TBD	↓	EPDP_IDN	10/20/22		Not Started	
	WP	Meeting #56 TBD	↓	EPDP_IDN	10/27/22		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	11/04/22		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	12/09/22		Not Started	
	MS	Submit Initial Report for Public Comment	!	EPDP_IDN	12/19/22		Not Started	
