

Project Tracking & Rollup DASHBOARD




Project Name EPDP: Internationalized Domain Names **Program** IDNs **Project Sponsor** GNSO Council

Project Information

05/20/21
Current Start

03/20/26
Current Finish

28%
% Complete

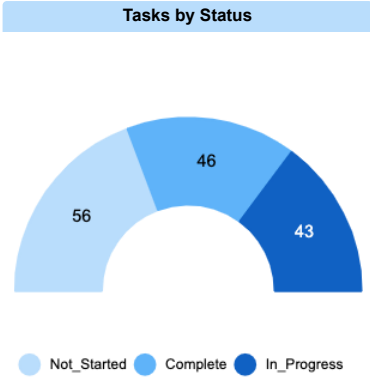

Project Contacts


Donna Austin
Chair

Justine Chew
Vice_Chair

Farell Folly
Liaison

AL Ariel Liang
Staff_Lead

SC Steve Chan
Project_Manager



Project Status & Health

Project_Status: Revised Schedule
Project_Health: On-Target

Summary Gantt & Key Milestones

Health	Primary Task	Current Start	Current Finish	% Complete	Status	2021	2022	2023	2024	2025													
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1					
	EPDP: Internationalized Domain Names	05/20/21	03/20/26	28%	In Progress	[Gantt bar]																	
	PROJECT CONTROL	05/20/21	02/09/26	40%	In Progress	[Gantt bar]																	
	GROUP DELIBERATIONS	08/11/21	10/30/25	33%	In Progress	[Gantt bar]																	
●	Group 1: Definition of All gTLDs Using RZ-LGR	08/25/21	02/17/22	99%	In Progress	[Gantt bar]																	
●	Group 2: Same Entity at Top-Level	02/04/22	03/31/22	88%	In Progress	[Gantt bar]																	
	Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	03/18/22	01/06/23	56%	In Progress	[Gantt bar]																	
	Data Collection to Facilitate Phase 2 Deliberations	11/07/22	07/07/23	0%	In Progress	[Gantt bar]																	
	Group 4: Same Entity at Second-Level	11/06/23	03/29/24	11%	In Progress	[Gantt bar]																	
	Group 5: Domain Name Lifecycle	04/01/24	08/23/24			[Gantt bar]																	
	Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	08/26/24	10/25/24			[Gantt bar]																	
	Group 7: IDN Implementation Guidelines	10/28/24	01/03/25			[Gantt bar]																	
	INITIAL REPORT	09/20/21	06/13/25	28%	In Progress	[Gantt bar]																	
	Publish Phase 1 Initial Report	04/21/23	04/21/23			[Gantt bar]																	
	Public comment forum on Phase 1 Initial Report (40 days)	04/24/23	06/09/23			[Gantt bar]																	
	Publish Phase 2 Initial Report	04/25/25	04/25/25			[Gantt bar]																	
	Public comment forum on Phase 2 Initial Report (40 days)	04/28/25	06/13/25			[Gantt bar]																	
	FINAL REPORT	06/12/23	11/07/25		Not Started	[Gantt bar]																	
	Review of public comments	06/12/23	07/21/23			[Gantt bar]																	
	Submission of Phase 1 Final Report to the GNSO Council	11/03/23	11/03/23			[Gantt bar]																	
	Review of public comments	06/16/25	07/25/25			[Gantt bar]																	
	Submission of Phase 2 Final Report to the GNSO Council	11/07/25	11/07/25			[Gantt bar]																	

4 - Working Group

Title: EPDP - Internationalized Domain Names (EPDP_IDN)



Description & Scope: On 20 May 2021, the GNSO Council passed a resolution to initiate the Expedited Policy Development Process (EPDP) on Internationalized Domain Names and adopt its charter. The EPDP Team is tasked with providing the GNSO Council with policy recommendations on: 1) the definition of gTLDs and the management of variant labels; and 2) how the IDN Implementation Guidelines, which Contracted Parties are required to comply with, should be updated in the future.

Composition:

Chair:	Donna Austin
Vice Chair:	Justine Chew
Council Liaison:	Farell Folly
Policy Staff:	A. Liang, S. Chan, E. Barabas
GDS Staff:	S. Hussain, M. Karakash
# Participants:	36 Participants (link)
# Observers:	13
Tools:	Mailing List / Meeting Schedule / Wiki
Charter:	Charter

Project Management:

Token Holder	Planned Start Date	Actual Start Date	# of Days	Planned End Date	Actual End Date
WG	20 May 2021	20 May 2021	574	07 Nov 2025	TBD

Program	Progress	Status	Health
IDNs	28%	 1	

STATUS: ■ Planned ● On-schedule ● Revised schedule ▲ Behind schedule ◆ Target will be missed ■ On-hold

HEALTH: ■ On-Target ■ At-Risk ■ In-Trouble

Milestones/Work plan (link):

Milestone/Task	Date	
Project Start	May-21	✓
Scoping Team Report	Jan-20	✓
Charter Approved	May-21	✓
EPDP Initiation Request Approved	May-21	✓
1st Plenary meeting	Aug-21	✓
SO/AC & SG/C Input to PDP	Nov-21	✓
Project Plan and Work plan Adoption	Oct-21	✓
Phase 1 - Issue Deliberations	Dec-22	
Populate draft report w/ findings & potential recs.	Mar-23	
Assemble initial conclusions	Mar-23	
Discuss/approve findings and interim recs.	Mar-23	
Consolidate interim recommendations and findings	Apr-23	
Issue Phase 1 report for public comment	Apr-23	
Review public comment input & prepare final report	Jul-23	
Finalize Report	Oct-23	
Determine consensus levels on recommendations	Oct-23	
Adopt final recommendations and report	Oct-23	
Send Phase 1 final report to GNSO Council	Nov-23	
GNSO Council adoption of Phase 1 consensus recs.	Jan-24	
Issue public comment for Board consideration	Feb-24	
ICANN Board adoption of Phase 1 consensus recs.	May-24	
Phase 2 - Issue Deliberations	Jan-25	
Populate draft report w/ findings & potential recs.	Mar-25	
Assemble initial conclusions	Mar-25	
Discuss/approve findings and interim recs.	Mar-25	
Consolidate interim recommendations and findings	Apr-25	
Issue Phase 2 report for public comment	Apr-25	
Review public comment input & prepare final report	Jul-25	
Finalize Report	Oct-25	
Determine consensus levels on recommendations	Nov-25	
Adopt final recommendations and report	Nov-25	
Send Phase 2 final report to GNSO Council	Nov-25	
GNSO Council adoption of Phase 2 consensus recs.	Jan-26	
Issue public comment for Board consideration	Feb-26	
ICANN Board adoption of Phase 2 consensus recs.	May-26	
Prior period % Complete	26%	

Status/Health Rationale:

- The project Status was upgraded to “Revised Schedule” on 17 Nov 2022 and Health of “On-Target”.

Current Activities:

- Consider ICANN org input on draft Phase 1 recommendations.
- Wrapping up Phase 1 deliberations of charter questions related to top-level variant management.

Planned Activities:

- Prepare public comment for the Phase 1 Initial Report, focusing on top-level variant management related recommendations.
- Conduct data collection among contracted parties to assist EPDP Team’s deliberation on second-level variant management related issues in Phase 2.

Open Issues & Risks:


- Deliberations of certain Charter questions depend on the critical input from external parties and additional data collection efforts.

Completed in prior period(s):


- The GNSO Council adopted a motion for a project change request adjusting the project scope and schedule at its meeting on 17 Nov 2022.
- Completed and distributed [Project Package](#) for November.

Project Tracking & Rollup DASHBOARD


Work-Plan Activity Metrics

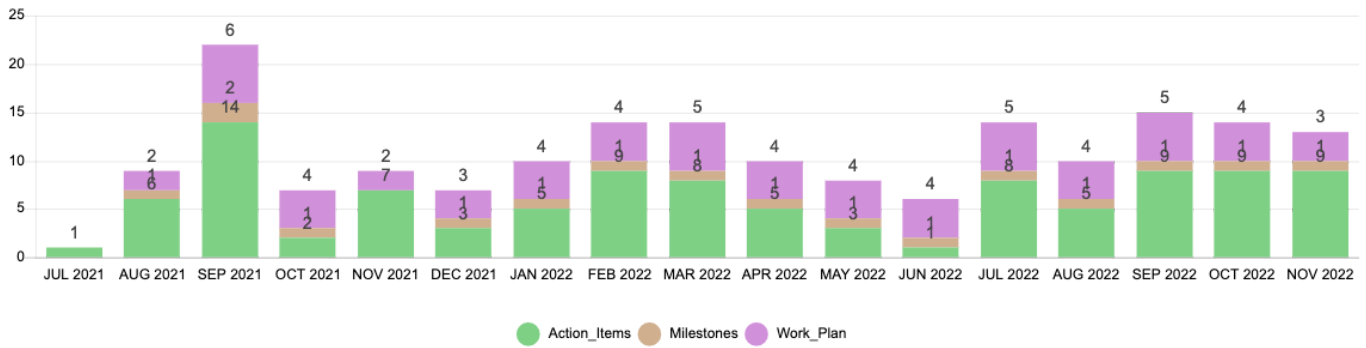

Mailman Activity

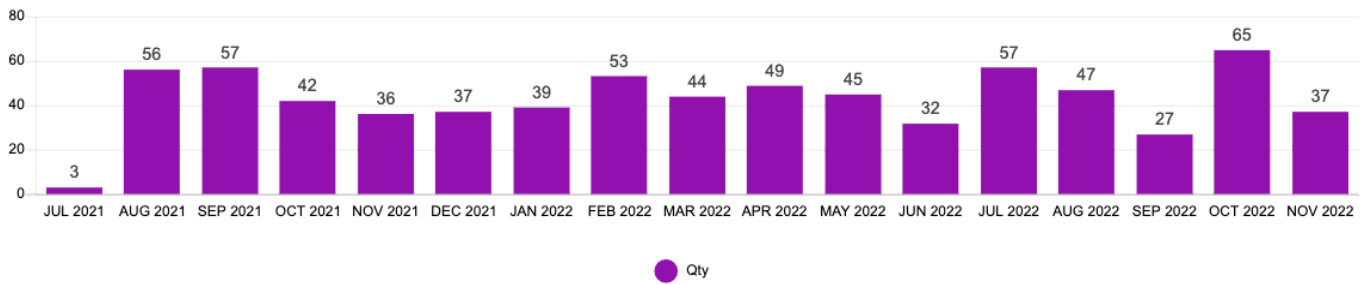

Meeting Activity

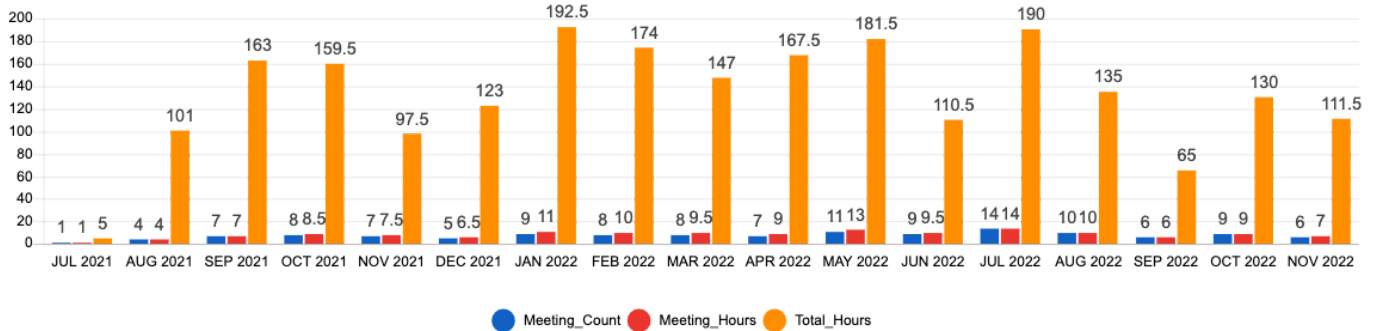

Plenary Attendance

Group Represented	Invited Qty	Attended Qty	Attendance
Total		Sum 1737	Sum 1055 Avg 60.7%
Primary At-Large Advisory Committee (ALAC)		Sum 302	Sum 239 Avg 79.1%
Attendee Name Abdulkarim Oloyede		Sum 55	Sum 45 Avg 81.8%
Attendee Name Hadia Elminiawi		Sum 56	Sum 54 Avg 96.4%
Attendee Name Justine Chew		Sum 56	Sum 55 Avg 98.2%
Attendee Name Lianna Galstyan		Sum 55	Sum 29 Avg 52.7%
Attendee Name Satish Babu		Sum 56	Sum 50 Avg 89.3%
Attendee Name TV Gopal		Sum 24	Sum 6 Avg 25.0%
Primary Commercial Business Users Constituency (BC)		Sum 34	Sum 2 Avg 5.9%
Attendee Name Mark William Datysgeld		Sum 34	Sum 2 Avg 5.9%

Primary	Sum	Sum	Avg
Expedited Policy Development Process - IDNs	56	53	94.6%
Attendee Name	Sum	Sum	Avg
Donna Austin	56	53	94.6%
Primary	Sum	Sum	Avg
GNSO Council	56	42	75.0%
Attendee Name	Sum	Sum	Avg
Ekue Farell Folly	56	42	75.0%
Primary	Sum	Sum	Avg
Governmental Advisory Committee (GAC)	164	92	56.1%
Attendee Name	Sum	Sum	Avg
Hamza Onoruoiza Salami	54	40	74.1%
Attendee Name	Sum	Sum	Avg
Nigel Hickson	55	32	58.2%
Attendee Name	Sum	Sum	Avg
T. Santhosh	55	20	36.4%
Primary	Sum	Sum	Avg
ICANN Board	91	79	86.8%
Attendee Name	Sum	Sum	Avg
Akinori Maemura	36	29	80.6%
Attendee Name	Sum	Sum	Avg
Edmon Chung	55	50	90.9%
Primary	Sum	Sum	Avg
Independent	364	122	33.5%
Attendee Name	Sum	Sum	Avg
Abdalmonem Galila	54	4	7.4%
Attendee Name	Sum	Sum	Avg
ANIL JAIN	55	44	80.0%
Attendee Name	Sum	Sum	Avg
Gao Lei	53	1	1.9%
Attendee Name	Sum	Sum	Avg
Imran Hossen	23	7	30.4%
Attendee Name	Sum	Sum	Avg
Kenny Huang	1	1	100.0%
Attendee Name	Sum	Sum	Avg
Lisa Liang	55	53	96.4%
Attendee Name	Sum	Sum	Avg
Nabil Benamar	53	0	0.0%
Attendee Name	Sum	Sum	Avg
Quoc Pham	52	12	23.1%
Attendee Name	Sum	Sum	Avg
Wael Nasr	18	0	0.0%
Primary	Sum	Sum	Avg
Intellectual Property Constituency (IPC)	68	45	66.2%
Attendee Name	Sum	Sum	Avg
Brian King	13	10	76.9%
Attendee Name	Sum	Sum	Avg
Jeffrey Neuman	55	35	63.6%
Primary	Sum	Sum	Avg
Internet Service Providers and Connectivity Providers Constituency (ISPCP)	54	18	33.3%
Attendee Name	Sum	Sum	Avg
Christian Dawson	54	18	33.3%
Primary	Sum	Sum	Avg
Non-Commercial Stakeholder Group (NCSG)	110	24	21.8%
Attendee Name	Sum	Sum	Avg
Akinremi Peter Taiwo	55	8	14.5%
Attendee Name	Sum	Sum	Avg
Emmanuel Vitus Agbenonwossi	16	7	43.8%
Attendee Name	Sum	Sum	Avg
Tomslin Samme-Nlar	39	9	23.1%
Primary	Sum	Sum	Avg
Registrar Stakeholder Group (RrSG)	105	93	88.6%
Attendee Name	Sum	Sum	Avg
Duowei Chen	16	11	68.8%
Attendee Name	Sum	Sum	Avg
Michael Bauland	56	50	89.3%
Attendee Name	Sum	Sum	Avg
Zhang Zuan	33	32	97.0%
Primary	Sum	Sum	Avg
Registry Stakeholder Group (RySG)	328	241	73.5%
Attendee Name	Sum	Sum	Avg
Dennis Tan Tanaka	55	51	92.7%
Attendee Name	Sum	Sum	Avg
Jennifer Chung	54	41	75.9%

Attendee Name Jerry Sen	Sum 55	Sum 54	Avg 98.2%
Attendee Name Joseph Chiu-Kit Yee	Sum 55	Sum 48	Avg 87.3%
Attendee Name Maxim Alzoba	Sum 55	Sum 44	Avg 80.0%
Attendee Name Wei (Wesley) Wang	Sum 54	Sum 3	Avg 5.6%
Primary Security and Stability Advisory Committee (SSAC)	Sum 5	Sum 5	Avg 100.0%
Attendee Name Jiankang Yao	Sum 1	Sum 1	Avg 100.0%
Attendee Name John R. Levine	Sum 1	Sum 1	Avg 100.0%
Attendee Name Lyman Chapin	Sum 1	Sum 1	Avg 100.0%
Attendee Name Patrik Fältström	Sum 1	Sum 1	Avg 100.0%
Attendee Name Ram Mohan	Sum 1	Sum 1	Avg 100.0%

Project Tracking & Rollup DASHBOARD



Project Roster

Participant	Participant Type	Role	Participation Start Date	Participation End Date	Legacy SOI Link
Group Selected / Nominated By: Group Name At-Large Advisory Committee (ALAC)					
Justine Chew	Participant	Vice-chair	05/25/21		https://community.icann.org
TV Gopal	Participant		05/25/21	03/21/22	https://community.icann.org
Hadia Elminiawi	Participant		07/14/21		https://community.icann.org
Satish Babu	Member		05/25/21		https://community.icann.org
Lianna Galstyan	Member		05/25/21		https://community.icann.org
Abdulkarim Oloyede	Member		05/25/21		https://community.icann.org
Group Selected / Nominated By: Group Name Commercial Business Users Constituency (BC)					
Mark William Datysgeld	Member		05/25/21	05/12/22	https://community.icann.org
Group Selected / Nominated By: Group Name Expedited Policy Development Process - IDNs					
Donna Austin	Member	Chair	08/10/21		https://community.icann.org
Group Selected / Nominated By: Group Name GNSO Council					
Ekue Farell Folly	Member	Liaison	07/27/21		https://community.icann.org
Group Selected / Nominated By: Group Name Governmental Advisory Committee (GAC)					
Hamza Onoruoiza Salami	Participant		05/25/21		https://community.icann.org
T. Santhosh	Member		05/25/21		https://community.icann.org
Nigel Hickson	Member		07/12/21		https://community.icann.org
Group Selected / Nominated By: Group Name ICANN Board					
Edmon Chung	Member	Liaison	07/27/21		https://community.icann.org
Akinori Maemura	Member	Liaison	11/18/21	09/22/22	https://community.icann.org
Group Selected / Nominated By: Group Name Independent					
Abdalmonem Galila	Participant		05/25/21		https://community.icann.org
Gao Lei	Participant		05/25/21		https://community.icann.org
Nabil Benamar	Participant		05/25/21		https://community.icann.org
Lisa Liang	Participant		05/25/21		https://community.icann.org
Anil Jain	Participant		07/30/21		https://community.icann.org
Quoc Pham	Participant		08/13/21		https://community.icann.org
Imran Hossen	Participant		11/04/21		https://community.icann.org
Wael Nasr	Participant		06/09/22		https://community.icann.org
Kenny Huang	Guest		10/26/21	10/26/21	
Group Selected / Nominated By: Group Name Intellectual Property Constituency (IPC)					
Brian King	Member		05/25/21	11/08/21	https://community.icann.org
Jeffrey Neuman	Member		05/25/21		https://community.icann.org
Group Selected / Nominated By: Group Name Internet Corporation for Assigned Names & Numbers (ICANN)					
Michael Karakash	Staff - Assigned	Liaison	05/25/21		
Steve Chan	Staff - Assigned		05/25/21		
Emily Barabas	Staff - Assigned		05/25/21		
Terri Agnew	Staff - Assigned		05/25/21		
Sarmad Hussain	Staff - Assigned	Liaison	05/25/21		
Nathalie Peregrine	Staff - Assigned		05/25/21		
Pitinan Kooarmompatana	Staff - Assigned		05/25/21		
Ariel Liang	Staff - Assigned		05/25/21		
Julie Bisland	Staff - Assigned		05/25/21		
Michelle DeSmyter	Staff - Assigned		08/18/21		
Devan Reed	Staff - Assigned		12/02/21		
Group Selected / Nominated By: Group Name Internet Service Providers and Connectivity Providers Constituency (ISPCP)					
Christian Dawson	Participant		07/12/21		https://community.icann.org
Group Selected / Nominated By: Group Name Non-Commercial Stakeholder Group (NCSG)					
Emmanuel Vitus Agbenonwossi	Member		07/13/22		https://community.icann.org
Akinremi Peter Taiwo	Member		07/15/21		https://community.icann.org
Group Selected / Nominated By: Group Name Registrar Stakeholder Group (RrSG)					
Michael Bauland	Member		05/25/21		https://community.icann.org
Duowei Chen	Member		09/26/21	02/13/22	https://community.icann.org
Zhang Zhan	Member		02/14/22		https://community.icann.org

Group Selected / Nominated By: Group Name	MEMBER	MEMBER	MEMBER	MEMBER	MEMBER
Registry Stakeholder Group (RySG)					
Jennifer Chung	Participant		05/25/21		https://community.icann.org
Jerry Sen	Participant		05/25/21		https://community.icann.org
Wei (Wesley) Wang	Participant		07/13/21		https://community.icann.org
Maxim Alzoba	Member		05/25/21		https://community.icann.org
Joseph Chiu-Kit Yee	Member		07/06/21		https://community.icann.org
Dennis Tan Tanaka	Member		05/25/21		https://community.icann.org
Security and Stability Advisory Committee (SSAC)					
Lyman Chapin	Guest		01/13/22	11/15/22	
Jiankang Yao	Guest		01/13/22	11/15/22	
John R. Levine	Guest		01/13/22		
Ram Mohan	Guest		01/13/22		
Patrik Fältström	Guest		01/13/22		

Health	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	Baseline Start	Baseline Finish	2021				2022				2023				2024				2025				2026			
										Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
1	EPDP: Internationalized Domain Names	1262d	05/20/21	03/20/26		28%	In Progress	05/20/21	03/20/26																								
2	PROJECT CONTROL	1233d	05/20/21	02/09/26		40%	In Progress	05/20/21	02/09/26																								
3	Project start confirmed	0	05/20/21	05/20/21		100%	Complete	05/20/21	05/20/21																								
4	Adopt/Confirm charter	0	05/20/21	05/20/21	3	100%	Complete	05/20/21	05/20/21																								
5	Confirmation of Team	60d	05/20/21	08/11/21	3	100%	Complete	05/20/21	08/11/21																								
6	Appointment of Team Chair	46d	05/20/21	07/22/21	3	100%	Complete	05/20/21	07/22/21																								
7	Appointment of Liaison to GNSO Council	46d	05/20/21	07/22/21	3	100%	Complete	05/20/21	07/22/21																								
8	Chair / Staff preparations	13d	07/23/21	08/10/21	6	100%	Complete	07/23/21	08/10/21																								
9	Project Management	1187d	07/23/21	02/09/26		32%	In Progress	07/23/21	02/09/26																								
10	Develop and confirm Project Plan	50d	07/23/21	09/30/21	6	100%	Complete	07/23/21	09/30/21																								
11	Obtain project plan approval from GNSO Council	20d	10/01/21	10/28/21	10	100%	Complete	10/01/21	10/28/21																								
12	Develop monthly Project Packages and deliver to Group & Council	1050d	10/29/21	11/06/25	11	28%	In Progress	10/29/21	11/06/25																								
13	Leadership Sub team	1130d	07/23/21	11/20/25		32%	In Progress	07/23/21	11/20/25																								
14	On-going preparation and planning of group activities	1130d	07/23/21	11/20/25	6	32%	In Progress	07/23/21	11/20/25																								
15	Close project and transition project to implementation	1d	02/09/26	02/09/26	14, 179	0%		02/09/26	02/09/26																								
16	GROUP DELIBERATIONS	1102d	08/11/21	10/30/25		33%	In Progress	08/11/21	10/30/25																								
17	First meeting of Team	1d	08/11/21	08/11/21	8	100%	Complete	08/11/21	08/11/21																								
18	Understand Charter, organize materials and develop initial approach	10d	08/11/21	08/24/21	8	100%	Complete	08/11/21	08/24/21																								
19	Overview & initial discussion of all Policy Topics	10d	08/11/21	08/24/21	8	100%	Complete	08/11/21	08/24/21																								
20	Develop definitions and terminology	28d	08/11/21	09/17/21	8	100%	Complete	08/11/21	09/17/21																								
21	Input from other SO/ACs & GNSO SG/Cs	58d	09/09/21	11/29/21		100%	Complete	09/09/21	11/29/21																								
26	Phase 1 Deliberations	403d	08/25/21	03/10/23		66%	In Progress	08/25/21	03/10/23																								
27	Group 1: Definition of All gTLDs Using RZ-LGR	127d	08/25/21	02/17/22		99%	In Progress	08/25/21	02/17/22																								
44	Group 2: Same Entity at Top-Level	40d	02/04/22	03/31/22		88%	In Progress	02/04/22	03/31/22																								
58	Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	211d	03/18/22	01/06/23		56%	In Progress	03/18/22	01/06/23																								
75	Review ICANN Org Input for Phase 1 Draft Recommendations	55d	12/26/22	03/10/23	72	10%	In Progress	12/26/22	03/10/23																								
76	Data Collection to Facilitate Phase 2 Deliberations	175d	11/07/22	07/07/23		0%	In Progress	11/07/22	07/07/23																								
77	Phase 2 Deliberations	355d	11/06/23	03/14/25		3%	In Progress	11/06/23	03/14/25																								
78	Group 4: Same Entity at Second-Level	105d	11/06/23	03/29/24		11%	In Progress	11/06/23	03/29/24																								
92	Group 5: Domain Name Lifecycle	105d	04/01/24	08/23/24				04/01/24	08/23/24																								
106	Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	45d	08/26/24	10/25/24				08/26/24	10/25/24																								
116	Group 7: IDN Implementation Guidelines	50d	10/28/24	01/03/25				10/28/24	01/03/25																								
125	Review ICANN Org Input for Phase 2 Draft Recommendations	50d	01/06/25	03/14/25	124			01/06/25	03/14/25																								
126	Key Group Events	1049d	10/25/21	10/30/25		30%	In Progress	10/25/21	10/30/25																								
141	INITIAL REPORT	975d	09/20/21	06/13/25		28%	In Progress	09/20/21	06/13/25																								
142	Phase 1 Initial Report	450d	09/20/21	06/09/23		54%	In Progress	09/20/21	06/09/23																								
143	Populate stable drafts as required	385d	09/20/21	03/10/23	20	65%	In Progress	09/20/21	03/10/23																								
144	Discuss/approve findings and interim recommendations	15d	03/13/23	03/31/23	143			03/13/23	03/31/23																								
145	Consolidate interim recommendations and findings	10d	04/03/23	04/14/23	144			04/03/23	04/14/23																								
146	Build Draft Report for public comment	10d	04/03/23	04/14/23	144			04/03/23	04/14/23																								
147	Approve Draft Report for public comment	5d	04/17/23	04/21/23	146			04/17/23	04/21/23																								
148	Publish Phase 1 Initial Report	0	04/21/23	04/21/23	147			04/21/23	04/21/23																								
149	Communicate Phase 1 Initial Report	5d	04/24/23	04/28/23	147			04/24/23	04/28/23																								
150	Public comment forum on Phase 1 Initial Report (40 days)	35d	04/24/23	06/09/23	147			04/24/23	06/09/23																								
151	Phase 2 Initial Report	415d	11/13/23	06/13/25				11/13/23	06/13/25																								
160	FINAL REPORT	630d	06/12/23	11/07/25			Not Started	06/12/23	11/07/25																								
161	Phase 1 Final Report	105d	06/12/23	11/03/23				06/12/23	11/03/23																								
162	Review of public comments	30d	06/12/23	07/21/23	150			06/12/23	07/21/23																								
163	Continue deliberations of policy topics towards the Phase 1 Final Report	60d	07/24/23	10/13/23	162			07/24/23	10/13/23																								
164	Build Phase 1 Final Report & Final Deliberations	5d	10/16/23	10/20/23	163			10/16/23	10/20/23																								
165	Determine consensus levels on interim recommendations	10d	10/23/23	11/03/23	164			10/23/23	11/03/23																								
166	Adopt final recommendations and report	10d	10/23/23	11/03/23	164			10/23/23	11/03/23																								
167	Submission of Phase 1 Final Report to the GNSO Council	0	11/03/23	11/03/23	166			11/03/23	11/03/23																								
168	Phase 2 Final Report	105d	06/16/25	11/07/25				06/16/25	11/07/25																								
175	POST GROUP TASKS	95d	11/10/25	03/20/26			Not Started	11/10/25	03/20/26																								
180																																	
181	PDP CHECKLIST	99d	01/01/21	05/20/21																													

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #55 D1b & B4	↓	EPDP_IDN	10/20/22	10/20/22	Complete	
	AI	Leadership Team to develop draft recommendation in response to Charter Question D1b based on EPDP Team discussion.	—	EPDP_IDN Leadership	11/03/22	11/04/22	Complete	
	AI	Leadership Team to draft recommendation on discussion question 1 for Charter Question B4.	—	EPDP_IDN Leadership	11/03/22	11/04/22	Complete	
	AI	In relation to discussion of Charter Question B4, staff to investigate the consequence on the process an applicant delegating a variant ahead of a primary.	—	Policy Support Staff	11/10/22	11/04/22	Complete	
	WP	Meeting #56 B4, E2, E6	↓	EPDP_IDN	10/27/22	10/27/22	Complete	
	AI	Staff to follow up about which EPDP Team meetings may need to be cancelled in November and December.	—	Policy Support Staff	11/03/22	10/28/22	Complete	
	AI	EPDP members to provide input via mailing list on Charter Question E2 regarding the Legal Rights Objection. Staff to summarize key points for this discussion and Leadership to suggest a path forward.	—	EPDP_IDN Leadership EPDP_IDN Policy Support Staff	11/10/22	11/10/22	Complete	
	AI	Leadership team to consider additional framing for the question at hand regarding Charter Question E2 for Community Objections and bring this back to the EPDP Team.	—	EPDP_IDN Leadership	11/10/22	11/10/22	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	11/08/22	11/08/22	Complete	
	AI	Staff to find out if there are documents that the ccPDP can share ahead of the 29 November joint call.	—	Ariel Liang	11/17/22	11/17/22	Complete	
	AI	Leadership team to develop some examples of the consequences of the different options for Community and Legal Rights Objections processes.	—	EPDP_IDN Leadership	11/24/22	11/24/22	Complete	
	AI	Leadership team to propose a path forward on E6 based on the conclusions of the meeting #57 discussion.	—	EPDP_IDN Leadership	11/24/22	11/24/22	Complete	
	WP	Meeting #57 E2 & E6	↓	EPDP_IDN	11/10/22	11/10/22	Complete	
	WP	Meeting #58 B4	↓	EPDP_IDN	11/17/22	11/17/22	Complete	
●	AI	EPDP Team members to review input from ICANN org and send any clarification questions to the mailing list.	—	EPDP_IDN	12/01/22		In Progress	
●	AI	Leadership Team to draft text in response to Charter Question B4 based on today's discussion.	—	EPDP_IDN Leadership	12/01/22		In Progress	
	WP	Meeting #59 Joint meeting w/ ccPDP4	↓	EPDP_IDN	11/29/22	11/29/22	Complete	
●	WP	Meeting #60 E2	↓	EPDP_IDN	12/01/22		In Progress	
	AI	Clarify in B4, Response to Discussion Question 2 that an RO can request an extension on the 12-month delegation timeline for variants, consistent with the opportunity to do so for other strings.	—	Policy Support Staff	12/22/22		In Progress	
	AI	Staff to investigate examples of rationales provided by ROs for requesting an extension on the 12-month delegation timeframe. Staff to investigate if there was a limit of the number of strings for which an RO could request an extension.	—	Policy Support Staff	12/22/22		In Progress	
	WP	Meeting #61 TBD	↓	EPDP_IDN	12/08/22		In Progress	
	MS	Submit project package to GNSO Council	!	Ariel Liang	12/09/22		In Progress	
	WP	Meeting #62 TBD	↓	EPDP_IDN	12/15/22		Not Started	
	WP	Meeting #63 TBD	↓	EPDP_IDN	12/22/22		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	01/06/23		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	02/10/23		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	03/10/23		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	04/07/23		Not Started	
	MS	Submit Initial Report for Public Comment	!	EPDP_IDN	04/21/23		Not Started	
