

# Project Tracking & Rollup DASHBOARD



**Project Name** EPDP: Internationalized Domain Names - Phase 2 **Program** IDNs **Project Sponsor** GNSO Council

**Project Information**

**41%**  
% Complete

**05/20/21**  
Current Start

**03/20/26**  
Current Finish

**Tasks by Status**

● Not Started ● Complete ● In Progress

**Project Contacts**

**Donna Austin**  
Chair

**Justine Chew**  
Vice\_Chair

**Farell Folly**  
Liaison

**Ariel Liang**  
Staff\_Lead

**Steve Chan**  
Project\_Manager

**Participant Summary**

● Member ● Participant ● Observer - Email Only  
● Staff - Assigned ● Staff - Not Assigned

**Project Status & Health**

Project_Status	Project_Health
Revised Schedule	On-Target

**Summary Gantt & Key Milestones**

Health	Primary Task	Current Start	Current Finish	% Complete	Status	2021	2022	2023	2024	2025					
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	
	<b>EPDP: Internationalized Domain Names - Phase 2</b>	<b>05/20/21</b>	<b>03/20/26</b>	<b>41%</b>	<b>In Progress</b>	[Gantt Bar]									
	<b>PROJECT CONTROL</b>	<b>05/20/21</b>	<b>02/09/26</b>	<b>51%</b>	<b>In Progress</b>	[Gantt Bar]									
	<b>GROUP DELIBERATIONS</b>	<b>08/11/21</b>	<b>10/30/25</b>	<b>51%</b>	<b>In Progress</b>	[Gantt Bar]									
	Group 1: Definition of All gTLDs Using RZ-LGR	08/25/21	02/17/22	100%	Complete	[Gantt Bar]									
	Group 2: Same Entity at Top-Level	02/04/22	03/31/22	100%	Complete	[Gantt Bar]									
	Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	03/18/22	01/06/23	100%	Complete	[Gantt Bar]									
	Data Collection to Facilitate Phase 2 Deliberations	11/07/22	07/07/23	75%	In Progress	[Gantt Bar]									
	Group 4: Same Entity at Second-Level	11/06/23	03/29/24	15%	In Progress	[Gantt Bar]									
	Group 5: Domain Name Lifecycle	04/01/24	08/23/24			[Gantt Bar]									
	Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	08/26/24	10/25/24			[Gantt Bar]									
	Group 7: IDN Implementation Guidelines	10/28/24	01/03/25			[Gantt Bar]									
	<b>INITIAL REPORT</b>	<b>09/20/21</b>	<b>06/13/25</b>	<b>49%</b>	<b>In Progress</b>	[Gantt Bar]									
	Publish Phase 1 Initial Report	04/21/23	04/21/23	100%	Complete	[Gantt Bar]									
	Public comment forum on Phase 1 Initial Report (40 days)	04/24/23	06/09/23	30%	In Progress	[Gantt Bar]									
	Publish Phase 2 Initial Report	04/25/25	04/25/25			[Gantt Bar]									
	Public comment forum on Phase 2 Initial Report (40 days)	04/28/25	06/13/25			[Gantt Bar]									
	<b>FINAL REPORT</b>	<b>06/12/23</b>	<b>11/07/25</b>		<b>Not Started</b>	[Gantt Bar]									
	Review of public comments	06/12/23	07/21/23			[Gantt Bar]									
	Submission of Phase 1 Final Report to the GNSO Council	11/03/23	11/03/23			[Gantt Bar]									
	Review of public comments	06/16/25	07/25/25			[Gantt Bar]									
	Submission of Phase 2 Final Report to the GNSO Council	11/07/25	11/07/25			[Gantt Bar]									

**Project Description**

On 20 May 2021, the GNSO Council passed a resolution to initiate the Expedited Policy Development Process (EPDP) on Internationalized Domain Names and adopt its charter. The EPDP Team is tasked with providing the GNSO Council with policy recommendations on: 1) the definition of gTLDs and the management of variant labels; and 2) how the IDN Implementation Guidelines, which Contracted Parties are required to comply with, should be updated in the future.

[Mailing List](#)  
[Meeting Schedule](#)  
[Wiki](#)  
[Charter](#)

**Completed in Prior Period**

- Published Phase 1 Initial Report for Public Comment on 24 April 2023.
- Completed review of Phase 2 charter questions, identified the ones that may impact the next Applicant Guidebook, updated timeline estimation, and confirmed approach for Phase 2 work.
- Conducted a community webinar to encourage public comment for Phase 1 Initial Report and present the highlights on preliminary recommendations.
- Completed and distributed [Project Package](#).

**Current Activities & Tasks**

- Conduct the Public Comment process for Phase 1 Initial Report (24 April - 5 June 2023).
- Analyze Phase 2 charter questions and identify the ones that will impact the next Applicant Guidebook.
- Consider potential updates to project plan and timeline, as well as appropriate mechanisms, to deliver relevant Phase 2 recommendations to the GNSO Council in an expeditious manner.
- Conduct data collection among contracted parties to assist EPDP Team's deliberation on second-level variant management related issues in Phase 2.

**Planned Activities & Tasks**



- Review public comments received on Phase 1 Initial Report.

**Work-Plan Activity Metrics**

Month	Action_Items	Milestones	Work_Plan
JUL 2021	1	0	0
AUG 2021	8	0	2
SEP 2021	14	0	6
OCT 2021	5	0	4
NOV 2021	7	0	2
DEC 2021	3	0	3
JAN 2022	5	0	4
FEB 2022	9	0	4
MAR 2022	8	0	5
APR 2022	5	0	4
MAY 2022	3	0	4
JUN 2022	1	0	4
JUL 2022	8	0	5
AUG 2022	5	0	4
SEP 2022	9	0	5
OCT 2022	9	0	4
NOV 2022	7	0	3
DEC 2022	7	0	4
JAN 2023	2	0	6
FEB 2023	12	0	4
MAR 2023	20	0	6
APR 2023	26	0	3

**Mailman Activity**

Month	Activity Count
JUL 2021	3
AUG 2021	56
SEP 2021	57
OCT 2021	42
NOV 2021	36
DEC 2021	37
JAN 2022	39
FEB 2022	53
MAR 2022	44
APR 2022	49
MAY 2022	45
JUN 2022	32
JUL 2022	57
AUG 2022	47
SEP 2022	27
OCT 2022	65
NOV 2022	37
DEC 2022	38
JAN 2023	39
FEB 2023	31
MAR 2023	55
APR 2023	63
MAY 2023	20

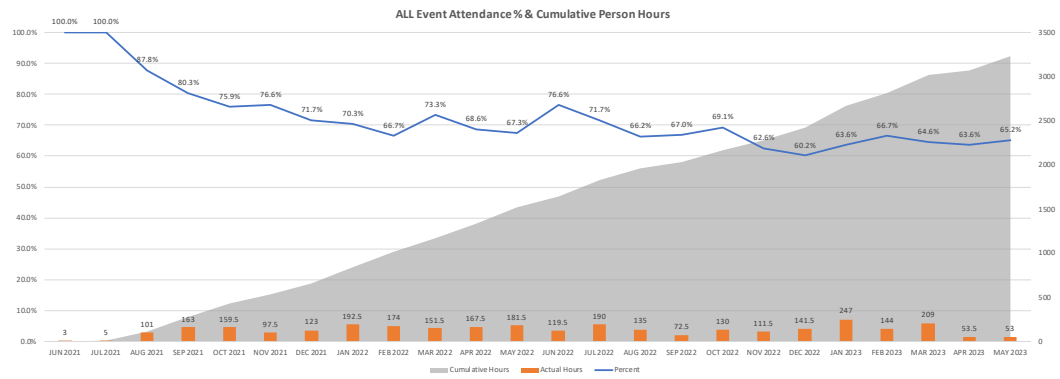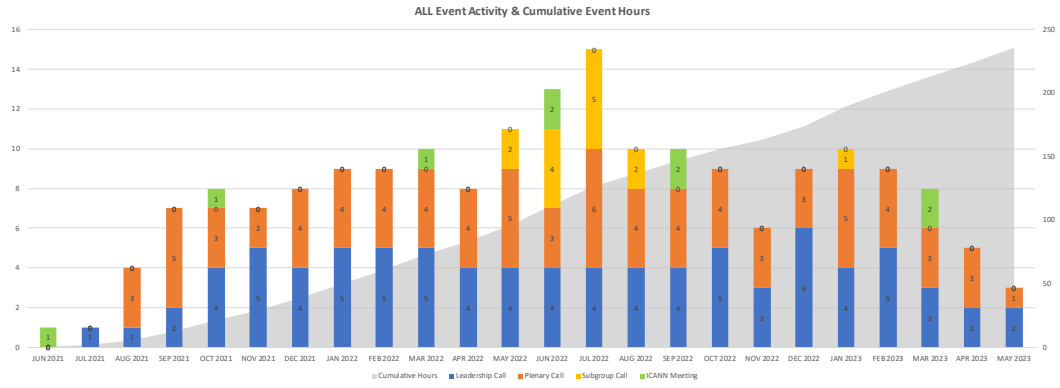

### Plenary Roster and Attendance Only

Participant	Row Labels	Sum of Invited Qty	Sum of Attended Qty	Percent	Role	SOI	Start Date	Depart Date
<b>At Large Advisory Committee (ALAC)</b>		<b>995</b>	<b>442</b>	<b>44.4%</b>				
Justine Chew		76	75	98.7%	Vice-chair	<a href="https://community.icann.org/t/7eTefAg">https://community.icann.org/t/7eTefAg</a>	5/25/2021	
TV Gopal		24	6	25.0%		<a href="https://community.icann.org/t/8Yf8CQ">https://community.icann.org/t/8Yf8CQ</a>	5/25/2021	3/21/2022
<b>Independent</b>		<b>523</b>	<b>149</b>	<b>28.5%</b>				
Abdalmoneem Gallia		74	5	6.8%		<a href="https://community.icann.org/t/24DjGQ">https://community.icann.org/t/24DjGQ</a>	5/25/2021	
Gea Li		73	1	1.4%		<a href="https://community.icann.org/t/4C0TjGQ">https://community.icann.org/t/4C0TjGQ</a>	5/25/2021	
Nabil Benamar		73	0	0.0%		<a href="https://community.icann.org/t/3wTjGQ">https://community.icann.org/t/3wTjGQ</a>	5/25/2021	
Lisa Liang		75	70	93.3%		<a href="https://community.icann.org/t/2wTjGQ">https://community.icann.org/t/2wTjGQ</a>	5/25/2021	
Anil Jain		75	54	72.0%		<a href="https://community.icann.org/t/1P8CQ">https://community.icann.org/t/1P8CQ</a>	7/30/2021	
Quoc Pham		72	12	16.7%		<a href="https://community.icann.org/t/4QDjGQ">https://community.icann.org/t/4QDjGQ</a>	8/13/2021	
Imran Hossein		43	7	16.3%		<a href="https://community.icann.org/t/1PMGcw">https://community.icann.org/t/1PMGcw</a>	11/4/2021	
Wael Nasr		38	0	0.0%		<a href="https://community.icann.org/t/BAEVD">https://community.icann.org/t/BAEVD</a>	6/9/2022	
<b>Internet Service Providers and Connectivity Providers Constituency (ISPCP)</b>		<b>74</b>	<b>28</b>	<b>37.8%</b>				
Christian Dawson		74	28	37.8%		<a href="https://community.icann.org/t/NivRAg">https://community.icann.org/t/NivRAg</a>	7/12/2021	
<b>Registry Stakeholder Group (RySG)</b>		<b>223</b>	<b>130</b>	<b>58.3%</b>				
Jennifer Chung		74	54	73.0%		<a href="https://community.icann.org/t/6AOuAg">https://community.icann.org/t/6AOuAg</a>	5/25/2021	
Jerry Sen		75	73	97.3%		<a href="https://community.icann.org/t/AM8CQ">https://community.icann.org/t/AM8CQ</a>	5/25/2021	
Wei (Wesley) Wang		74	3	4.1%		<a href="https://community.icann.org/t/0YPA8CQ">https://community.icann.org/t/0YPA8CQ</a>	7/13/2021	
<b>Governmental Advisory Committee (GAC)</b>		<b>75</b>	<b>54</b>	<b>72.0%</b>				
Namaa Ghonoulza Salami		74	54	73.0%		<a href="https://community.icann.org/t/4P8CQ">https://community.icann.org/t/4P8CQ</a>	5/25/2021	
Shiva Upadhyay		1	0	0.0%		<a href="https://community.icann.org/t/0pX0G">https://community.icann.org/t/0pX0G</a>	4/27/2023	
<b>Member</b>		<b>1257</b>	<b>890</b>	<b>70.8%</b>				
<b>At-Large Advisory Committee (ALAC)</b>		<b>227</b>	<b>198</b>	<b>87.2%</b>				
Sattish Babu		76	68	89.5%		<a href="https://community.icann.org/t/RLd8Aw">https://community.icann.org/t/RLd8Aw</a>	5/25/2021	
Abdulkarim Oloyede		75	59	78.7%		<a href="https://community.icann.org/t/5vD2B">https://community.icann.org/t/5vD2B</a>	5/25/2021	
Nadia Elminawi		76	71	93.4%		<a href="https://community.icann.org/t/wKrD8Aw">https://community.icann.org/t/wKrD8Aw</a>	7/14/2021	
<b>Commercial Business Users Constituency (BC)</b>		<b>34</b>	<b>2</b>	<b>5.9%</b>				
Mark William Datysgeld		34	2	5.9%		<a href="https://community.icann.org/t/Fwb0C">https://community.icann.org/t/Fwb0C</a>	5/25/2021	5/12/2022
<b>GNSS Council</b>		<b>159</b>	<b>133</b>	<b>83.6%</b>				
Dennis Austin		83	78	94.0%	Chair	<a href="https://community.icann.org/t/2B8EAg">https://community.icann.org/t/2B8EAg</a>	8/10/2021	
Farell Folly		76	55	72.4%	Liaison	<a href="https://community.icann.org/t/1S1tAg">https://community.icann.org/t/1S1tAg</a>	7/27/2021	
<b>Intellectual Property Constituency (IPC)</b>		<b>88</b>	<b>46</b>	<b>52.3%</b>				
Brian King		13	10	76.9%		<a href="https://community.icann.org/t/054f8G">https://community.icann.org/t/054f8G</a>	5/25/2021	11/8/2021
Jeffrey Neuman		75	36	48.0%		<a href="https://community.icann.org/t/0iBwAg">https://community.icann.org/t/0iBwAg</a>	5/25/2021	
<b>Non-Commercial Stakeholder Group (NCSG)</b>		<b>111</b>	<b>27</b>	<b>24.3%</b>				
Emmanuel Vitus Agbenonvosii		36	18	50.0%		<a href="https://community.icann.org/t/H4zG">https://community.icann.org/t/H4zG</a>	7/13/2022	
Taiwo Akinremi		75	9	12.0%		<a href="https://community.icann.org/t/5qul8A">https://community.icann.org/t/5qul8A</a>	7/15/2021	
<b>Registry Stakeholder Group (RySG)</b>		<b>145</b>	<b>131</b>	<b>90.3%</b>				
Michael Bawland		76	68	89.5%		<a href="https://community.icann.org/t/1Pw0CQ">https://community.icann.org/t/1Pw0CQ</a>	5/25/2021	
Ducwet Chen		16	11	68.8%		<a href="https://community.icann.org/t/0QHCF">https://community.icann.org/t/0QHCF</a>	9/26/2021	2/13/2022
Zhang Zuan		53	52	98.1%		<a href="https://community.icann.org/t/7gg6A">https://community.icann.org/t/7gg6A</a>	2/14/2022	
<b>Registry Stakeholder Group (RySG)</b>		<b>224</b>	<b>189</b>	<b>84.4%</b>				
Maxim Alizba		75	59	78.7%		<a href="https://community.icann.org/t/8Tv8Ag">https://community.icann.org/t/8Tv8Ag</a>	5/25/2021	
Dennis Tan Tanaka		75	71	94.7%		<a href="https://community.icann.org/t/44ZAg">https://community.icann.org/t/44ZAg</a>	5/25/2021	
Joseph Chiu-Kit Yee		74	59	79.7%		<a href="https://community.icann.org/t/5Y8CQ">https://community.icann.org/t/5Y8CQ</a>	7/6/2021	5/2/2023
<b>Governmental Advisory Committee (GAC)</b>		<b>150</b>	<b>63</b>	<b>42.0%</b>				
T. Santhosh		75	21	28.0%		<a href="https://community.icann.org/t/2Z8Aw">https://community.icann.org/t/2Z8Aw</a>	5/25/2021	
Nigel Hickson		75	42	56.0%		<a href="https://community.icann.org/t/94P8CQ">https://community.icann.org/t/94P8CQ</a>	7/12/2021	
<b>ICANN Board</b>		<b>119</b>	<b>103</b>	<b>84.9%</b>				
Edmon Chung		76	66	86.8%	Liaison	<a href="https://community.icann.org/t/SWAAw">https://community.icann.org/t/SWAAw</a>	7/27/2021	
Akinori Maemura		36	29	80.6%	Liaison	<a href="https://community.icann.org/t/4H0CQ">https://community.icann.org/t/4H0CQ</a>	11/18/2021	9/22/2022
Alan Barrett		7	6	85.7%	Liaison	<a href="https://community.icann.org/t/2QPSDQ">https://community.icann.org/t/2QPSDQ</a>	3/16/2023	
<b>Grand Total</b>		<b>2252</b>	<b>1332</b>	<b>59.1%</b>				

### Staff Support Roster

Row Labels	
<b>Internet Corporation for Assigned Names &amp; Numbers (ICANN)</b>	
Devan Reed	
Emily Barabas	
Julie Bizland	
Michelle DeSmyster	
Nathalie Peregrine	
Terri Agnew	
Steve Chan	
Anel Liang	
Michael Karakash	
Sarmad Hussain	
Pitinan Koamornpatana	

Health	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	2021				2022				2023				2024				2025				2026							
								Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4				
1	<b>EPDP: Internationalized Domain Names</b>	1262d	05/20/21	03/20/26		41%	In Progress																												
2	<b>PROJECT CONTROL</b>	1233d	05/20/21	02/09/26		51%	In Progress																												
3	Project start confirmed	0	05/20/21	05/20/21		100%	Complete																												
4	Adopt/Confirm charter	0	05/20/21	05/20/21	3	100%	Complete																												
5	Confirmation of Team	60d	05/20/21	08/11/21	3	100%	Complete																												
6	Appointment of Team Chair	46d	05/20/21	07/22/21	3	100%	Complete																												
7	Appointment of Liaison to GNSO Council	46d	05/20/21	07/22/21	3	100%	Complete																												
8	Chair / Staff preparations	13d	07/23/21	08/10/21	6	100%	Complete																												
9	<b>Project Management</b>	1187d	07/23/21	02/09/26		44%	In Progress																												
10	Develop and confirm Project Plan	50d	07/23/21	09/30/21	6	100%	Complete																												
11	Obtain project plan approval from GNSO Council	20d	10/01/21	10/28/21	10	100%	Complete																												
12	Develop monthly Project Packages and deliver to Group & Council	1050d	10/29/21	11/06/25	11	40%	In Progress																												
13	<b>Leadership Sub team</b>	1130d	07/23/21	11/20/25		44%	In Progress																												
14	On-going preparation and planning of group activities	1130d	07/23/21	11/20/25	6	44%	In Progress																												
15	Close project and transition project to implementation	1d	02/09/26	02/09/26	14, 179	0%																													
16	<b>GROUP DELIBERATIONS</b>	1102d	08/11/21	10/30/25		51%	In Progress																												
17	First meeting of Team	1d	08/11/21	08/11/21	8	100%	Complete																												
18	Understand Charter, organize materials and develop initial approach	10d	08/11/21	08/24/21	8	100%	Complete																												
19	Overview & initial discussion of all Policy Topics	10d	08/11/21	08/24/21	8	100%	Complete																												
20	Develop definitions and terminology	28d	08/11/21	09/17/21	8	100%	Complete																												
21	<b>Input from other SO/ACs &amp; GNSO SG/Cs</b>	58d	09/09/21	11/29/21		100%	Complete																												
22	Develop template for input	15d	09/09/21	09/29/21		100%	Complete																												
23	Announce input opportunity	30d	09/30/21	11/10/21	22	100%	Complete																												
24	Collect and collate input in to Review Tool	8d	11/11/21	11/22/21	23	100%	Complete																												
25	Group to review input and determine relevance to policy deliberations on issues within scope	5d	11/23/21	11/29/21	24	100%	Complete																												
26	<b>Phase 1 Deliberations</b>	403d	08/25/21	03/10/23		100%	Complete																												
76	Data Collection to Facilitate Phase 2 Deliberations	175d	11/07/22	07/07/23		75%	In Progress																												
77	<b>Phase 2 Deliberations</b>	355d	11/06/23	03/14/25		4%	In Progress																												
126	<b>Key Group Events</b>	1049d	10/25/21	10/30/25		39%	In Progress																												
141	<b>INITIAL REPORT</b>	975d	09/20/21	06/13/25		49%	In Progress																												
142	<b>Phase 1 Initial Report</b>	450d	09/20/21	06/09/23		95%	In Progress																												
143	Populate stable drafts as required	385d	09/20/21	03/10/23	20	100%	Complete																												
144	Discuss/approve findings and interim recommendations	15d	03/13/23	03/31/23	143	100%	Complete																												
145	Consolidate interim recommendations and findings	10d	04/03/23	04/14/23	144	100%	Complete																												
146	Build Draft Report for public comment	10d	04/03/23	04/14/23	144	100%	Complete																												
147	Approve Draft Report for public comment	5d	04/17/23	04/21/23	146	100%	Complete																												
148	Publish Phase 1 Initial Report	0	04/21/23	04/21/23	147	100%	Complete																												
149	Communicate Phase 1 Initial Report	5d	04/24/23	04/28/23	147	100%	Complete																												
150	Public comment forum on Phase 1 Initial Report (40 days)	35d	04/24/23	06/09/23	147	30%	In Progress																												
151	<b>Phase 2 Initial Report</b>	415d	11/13/23	06/13/25																															
152	Populate stable drafts as required	350d	11/13/23	03/14/25	80																														
153	Discuss/approve findings and interim recommendations	15d	03/17/25	04/04/25	152																														
154	Consolidate interim recommendations and findings	10d	04/07/25	04/18/25	153																														
155	Build Draft Report for public comment	10d	04/07/25	04/18/25	153																														
156	Approve Draft Report for public comment	5d	04/21/25	04/25/25	155																														
157	Publish Phase 2 Initial Report	0	04/25/25	04/25/25	156																														
158	Communicate Phase 2 Initial Report	5d	04/28/25	05/02/25	156																														
159	Public comment forum on Phase 2 Initial Report (40 days)	35d	04/28/25	06/13/25	156																														
160	<b>FINAL REPORT</b>	630d	06/12/23	11/07/25			Not Started																												
161	<b>Phase 1 Final Report</b>	105d	06/12/23	11/03/23																															
162	Review of public comments	30d	06/12/23	07/21/23	150																														
163	Continue deliberations of policy topics towards the Phase 1 Final Report	60d	07/24/23	10/13/23	162																														
164	Build Phase 1 Final Report & Final Deliberations	5d	10/16/23	10/20/23	163																														
165	Determine consensus levels on interim recommendations	10d	10/23/23	11/03/23	164																														
166	Adopt final recommendations and report	10d	10/23/23	11/03/23	164																														
167	Submission of Phase 1 Final Report to the GNSO Council	0	11/03/23	11/03/23	166																														



Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #75 Third reading of draft text, review of standard sections of the draft Initial Report	↓	EPDP_IDN	03/30/23	03/30/23	Complete	
	AI	In public comment input form, change open-ended question "Are there any recommendations the EPDP Team has not considered?" to "Are there any issues pertaining to top-level variant gTLDs the EPDP Team has not considered?"	—	Policy Support Staff	04/07/23	04/03/23	Complete	
	AI	In header for Section 9 – Change "Variant Label State" to "Variant Label States"	—	Policy Support Staff	04/07/23	04/03/23	Complete	
	AI	Add additional question for each recommendation asking for any input on the rationale.	—	Policy Support Staff	04/07/23	04/03/23	Complete	
	AI	Revise Recommendation 1.5 to read: "In order to encourage a positive and predictable registrant experience, a framework for developing guidelines for the management of gTLDs and their variant labels at the top level by registries and registrars must be created during implementation." In addition, change "best practice guidelines" to "guidelines" in Implementation Guidance 1.6.	—	Policy Support Staff	04/07/23	04/03/23	Complete	
	AI	Move suggested IG under Recommendation 2.2 to rationale for Recommendation 2.2.	—	Policy Support Staff	04/07/23	04/03/23	Complete	
	AI	Update Recommendation 2.24 with: "A future gTLD applicant applying for an IDN gTLD and up to [x] variant labels will incur the same base application fee as any other gTLD applicant who does not apply for variant labels in that round."	—	Policy Support Staff	04/07/23	04/03/23	Complete	
	AI	Update Recommendation 2.25 to read: "An applicant or an existing registry operator from the 2012 round that exceeds [x] variant labels in their application may incur additional fees that ICANN org considers to be proportionate with any additional costs associated with evaluating the application and consistent with the cost recovery principle." Add language also including the concept "or if the variant label(s) are applied for in more than one application round."	—	Policy Support Staff	04/07/23	04/03/23	Complete	
	AI	Update Recommendation 2.29 to read: "As a one time exception for the immediate next new gTLD application round, the base application fee for allocatable variant labels by existing IDN gTLD registry operators from the 2012 round will be waived."	—	Policy Support Staff	04/07/23	04/03/23	Complete	
	AI	EPDP Team members to suggest additional text to explain glossary item "same entity."	—	EPDP_IDN	04/07/23	04/03/23	Complete	
	AI	Add an item to the glossary for label states.	—	Policy Support Staff	04/07/23	04/03/23	Complete	
	AI	Update definition of "string" to read: "A combination of characters / letters that form the top-level domain name."	—	Policy Support Staff	04/07/23	04/03/23	Complete	
	AI	Update definition of "string" to read: "A combination of characters / letters that form the top-level domain name."	—	Policy Support Staff	04/07/23	04/03/23	Complete	
	WP	Meeting #76 Review Initial Report to prepare for public comment	↓	EPDP_IDN	04/03/23	04/03/23	Complete	
	WP	Meeting #77 --Cancelled--	↓	EPDP_IDN	04/06/23	04/03/23	Complete	
	AI	Draft rec as "discounted fee" and specifically call out for comment the options considered. Rationale will also be updated to be consistent with this outcome.	—	Policy Support Staff	04/07/23	04/03/23	Complete	
	AI	Use "Explanation" or "Meaning" instead of "Definition" for the column header.	—	Policy Support Staff	04/07/23	04/03/23	Complete	
	AI	Pull in definition into Rec 1.12	—	Policy Support Staff	04/07/23	04/03/23	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	04/07/23	04/06/23	Complete	
	WP	Meeting #78 --Cancelled--	↓	EPDP_IDN	04/13/23	04/03/23	Complete	
	WP	Meeting #79 Review Phase 2 Charter Questions	↓	EPDP_IDN	04/20/23	04/20/23	Complete	
	MS	Submit Initial Report for Public Comment	!	EPDP_IDN	04/21/23	04/24/23	Complete	
	AI	Update the time allocated for specific charter questions as follows: D4 - allocate 4 meetings (previously 3); D5 - allocate 2 meetings (previously 1); D6a - allocate 2 meetings (previously 1).	—	Policy Support Staff	04/27/23	04/27/23	Complete	
	WP	Meeting #80 Review Phase 2 Charter Questions & IDN Tables	↓	EPDP_IDN	04/27/23	04/27/23	Complete	
	AI	EPDP Team members are requested to let the leadership team know if they will be attending ICANN77 sessions.	—	EPDP_IDN	05/04/23	05/04/23	Complete	
	WP	Meeting #81 IDN Table Harmonization	↓	EPDP_IDN	05/11/23	05/11/23	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	05/15/23	05/15/23	Complete	
	WP	Meeting - IDNs Community Webinar IDN Table Harmonization	↓	EPDP_IDN	05/17/23		In Progress	
	WP	Meeting #82 TBD	↓	EPDP_IDN	05/18/23		Not Started	
	WP	Meeting #83 TBD	↓	EPDP_IDN	05/25/23		Not Started	
	WP	Meeting #84 TBD	↓	EPDP_IDN	05/25/23		Not Started	
	WP	Meetings ICANN77 (Session 1) TBD	↓	EPDP_IDN	06/12/23		Not Started	
	WP	Meetings ICANN77 (Session 2) TBD	↓	EPDP_IDN	06/13/23		Not Started	
	WP	Meetings ICANN77 (Session 3) TBD	↓	EPDP_IDN	06/14/23		Not Started	
	WP	Meetings ICANN77 (Session 4) TBD	↓	EPDP_IDN	06/15/23		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	07/10/23		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	08/14/23		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	09/11/23		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	10/15/23		Not Started	
	MS	Submission of Phase 1 Final Report to the GNSO Council	!	EPDP_IDN	11/03/23		Not Started	
