

Project Tracking & Rollup DASHBOARD



Project Name: **EPDP: Internationalized Domain Names** Program: **IDNs** Project Sponsor: **GNSO Council**

Project Information

67%
% Complete

05/20/21
Actual Start

02/24/25
Planned Finish

Tasks by Status

● Not_Started ● Complete ● In_Progress

Project Contacts

Donna Austin
Chair

Justine Chew
Vice_Chair

Farell Folly
Liaison

AL Ariel Liang
Staff_Lead

SC Steve Chan
Project_Manager

Participant Summary

● Member ● Participant ● Observer - Email Only
● Staff - Assigned ● Staff - Not Assigned

Project Status & Health

Project_Status	Project_Health
Revised Schedule	On-Target

Summary Gantt & Key Milestones						2021												2022												2023												2024												2025											
Health	Primary Task	Current Start	Current Finish	% Complete	Status	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1																																			
	EPDP: Internationalized Domain Names	05/20/21	02/24/25	67%	In Progress	[Gantt bar for EPDP: Internationalized Domain Names]																																																											
	PROJECT CONTROL	05/20/21	01/14/25	68%	In Progress	[Gantt bar for PROJECT CONTROL]																																																											
	GROUP DELIBERATIONS	08/11/21	06/13/24	77%	In Progress	[Gantt bar for GROUP DELIBERATIONS]																																																											
	Group 1: Definition of All gTLDs Using RZ-LGR	08/25/21	02/17/22	100%	Complete	[Gantt bar for Group 1: Definition of All gTLDs Using RZ-LGR]																																																											
	Group 2: Same Entity at Top-Level	02/04/22	03/31/22	100%	Complete	[Gantt bar for Group 2: Same Entity at Top-Level]																																																											
	Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	03/18/22	01/06/23	100%	Complete	[Gantt bar for Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants]																																																											
	Data Collection to Facilitate Phase 2 Deliberations	11/07/22	07/07/23	100%	Complete	[Gantt bar for Data Collection to Facilitate Phase 2 Deliberations]																																																											
	Group 4: Same Entity at Second-Level	11/13/23	12/22/23	75%	In Progress	[Gantt bar for Group 4: Same Entity at Second-Level]																																																											
	Group 5: Domain Name Lifecycle	11/13/23	01/19/24	44%	In Progress	[Gantt bar for Group 5: Domain Name Lifecycle]																																																											
	Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	11/13/23	01/26/24	11%	In Progress	[Gantt bar for Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms]																																																											
	Group 7: IDN Implementation Guidelines	01/15/24	03/01/24	18%	In Progress	[Gantt bar for Group 7: IDN Implementation Guidelines]																																																											
	INITIAL REPORT	09/20/21	06/03/24	84%	In Progress	[Gantt bar for INITIAL REPORT]																																																											
	Publish Phase 1 Initial Report	04/21/23	04/21/23	100%	Complete	[Gantt bar for Publish Phase 1 Initial Report]																																																											
	Public comment forum on Phase 1 Initial Report (56 calendar days)	04/24/23	06/19/23	100%	Complete	[Gantt bar for Public comment forum on Phase 1 Initial Report (56 calendar days)]																																																											
	Publish Phase 2 Initial Report	04/22/24	04/22/24			[Gantt bar for Publish Phase 2 Initial Report]																																																											
	Public comment forum on Phase 2 Initial Report (40 calendar days)	04/23/24	06/03/24			[Gantt bar for Public comment forum on Phase 2 Initial Report (40 calendar days)]																																																											
	FINAL REPORT	06/20/23	10/14/24	30%	In Progress	[Gantt bar for FINAL REPORT]																																																											
	Review of public comments	06/20/23	09/11/23	100%	Complete	[Gantt bar for Review of public comments]																																																											
	Submission of Phase 1 Final Report to the GNSO Council	11/10/23	11/10/23			[Gantt bar for Submission of Phase 1 Final Report to the GNSO Council]																																																											
	Review of public comments	06/04/24	08/26/24			[Gantt bar for Review of public comments]																																																											
	Submission of Phase 2 Final Report to the GNSO Council	10/14/24	10/14/24			[Gantt bar for Submission of Phase 2 Final Report to the GNSO Council]																																																											
	POST GROUP TASKS	10/15/24	02/24/25		Not Started	[Gantt bar for POST GROUP TASKS]																																																											
	Approval of Final Report and Recommendations by the GNSO Council	10/15/24	12/16/24			[Gantt bar for Approval of Final Report and Recommendations by the GNSO Council]																																																											
	Publish Recommendations for Public Comment for Board consideration	01/07/25	02/24/25			[Gantt bar for Publish Recommendations for Public Comment for Board consideration]																																																											

Project Description

On 20 May 2021, the GNSO Council passed a resolution to initiate the Expedited Policy Development Process (EPDP) on Internationalized Domain Names and adopt its charter. The EPDP Team is tasked with providing the GNSO Council with policy recommendations on: 1) the definition of gTLDs and the management of variant labels; and 2) how the IDN Implementation Guidelines, which Contracted Parties are required to comply with, should be updated in the future.

[Mailing List](#)

[Meeting Schedule](#)

[Wiki](#)

[Charter](#)

Completed in Prior Period

- Completed the initial review of Public Comment received for Phase 1 Initial Report.
- Provide GNSO Council a revised schedule for completing two phases of work, with the projected end date on October 2024.
- Completed and distributed [Project Package](#).

Current Activities & Tasks

- Continue deliberations of policy topics toward Phase 1 Final Report.
- Conduct Phase 2 charter question deliberations.
- Conduct first reading and second reading for draft Phase 2 recommendations that the EPDP Team completed preliminary deliberation.


Open Issues & Risks

- Deliberations of certain charter questions dependent upon input from external parties.
- Deliberations of certain Public Comment input for Phase 1 Initial Report, which specifically relate to the input from PointQuebec and CORE Association, dependent upon guidance from the GNSO Council.
- The EPDP Team will require additional resources and support as well as explore other mechanisms in order to complete Phase 2 work in an expeditious manner.

Planned Activities & Tasks



- Plan for the dedicated face-to-face workshop in December 2023.

Work-Plan Activity Metrics

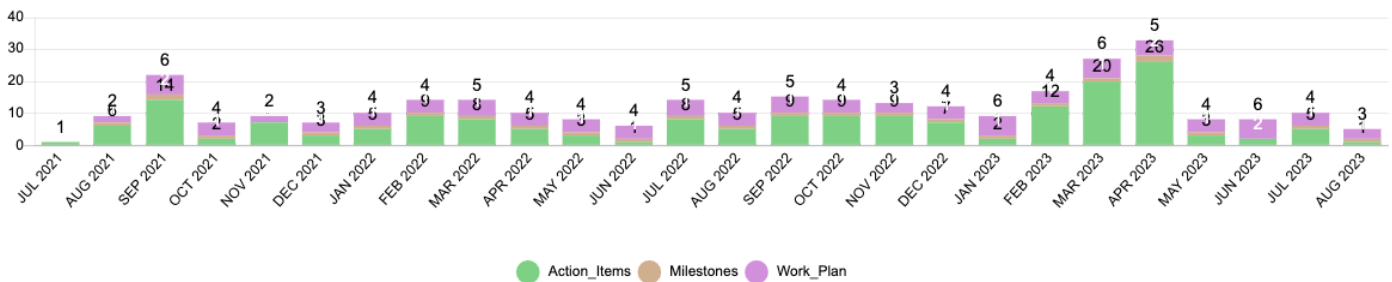

Mailman Activity



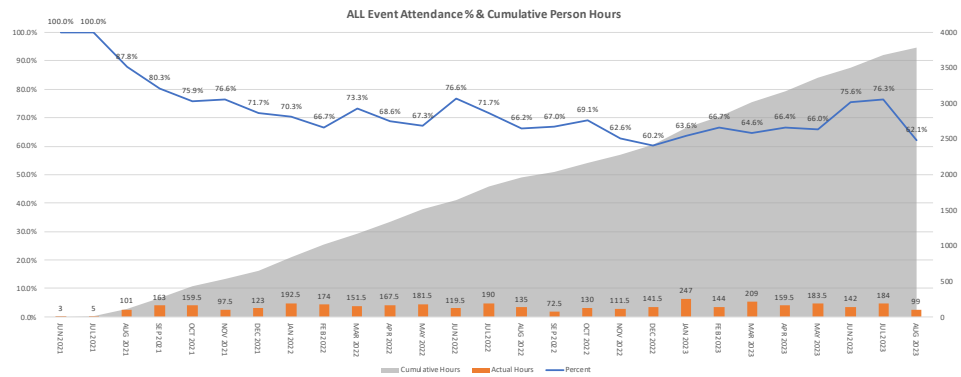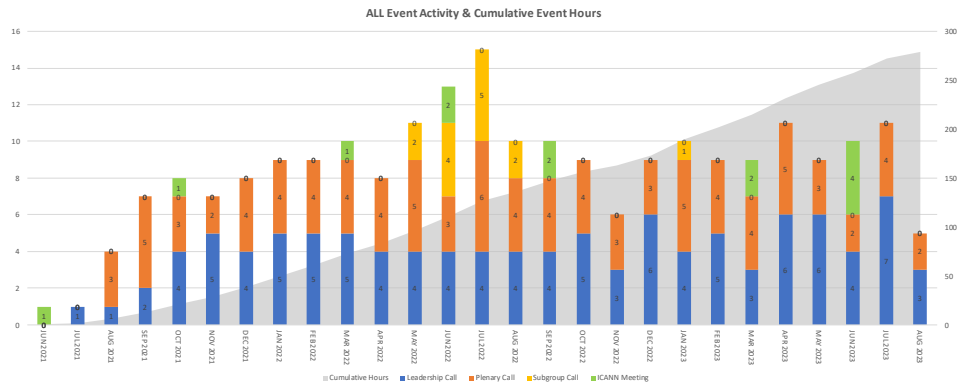

Plenary Roster and Attendance Only

Participant	Row Labels	Sum of Invited Qty	Sum of Attended Qty	Percent	Role	SOI	Start Date	Depart Date
At Large Advisory Committee (ALAC)		958	405	42.3%				
Justine Chew		89	88	98.9%	Vice-chair	https://community.icann.org/v/TefAg	5/25/2021	
TV Gopal		24	6	25.0%		https://community.icann.org/v/BVt8CQ	5/25/2021	3/21/2022
Independent		595	168	28.2%				
Abdilmomem Gallia		83	5	6.0%		https://community.icann.org/v/2D1pCQ	5/25/2021	
Nabil Benamar		82	0	0.0%		https://community.icann.org/v/3w1pCQ	5/25/2021	
Anil Jain		84	59	70.2%		https://community.icann.org/v/1P8CQ	7/30/2021	
Quoc Pham		81	12	14.8%		https://community.icann.org/v/C02bAw	8/13/2021	
Imran Hosen		52	12	23.1%		https://community.icann.org/v/191MGcW	11/4/2021	
Wael Naeir		47	0	0.0%		https://community.icann.org/v/3B4UD	6/9/2022	
Lei Gao		82	1	1.2%		https://community.icann.org/v/4C1pCQ	5/25/2021	
Shuo Liang		84	79	94.0%		https://community.icann.org/v/2w1pCQ	5/25/2021	
Registry Stakeholder Group (RySG)		167	84	50.3%				
Jerry Sen		84	81	96.4%		https://community.icann.org/v/1W8CC	5/25/2021	
Wei (Wesley) Wang		83	3	3.6%		https://community.icann.org/v/0V98CQ	7/13/2021	
Governmental Advisory Committee (GAC)		83	59	71.1%				
Hamza Onorizuola Salami		81	57	70.4%		https://community.icann.org/v/4P8CQ	5/25/2021	7/20/2023
Amina Ramallan		2	2	100.0%		https://community.icann.org/v/81pCQ	7/20/2023	
Member		1583	1090	68.9%				
At Large Advisory Committee (ALAC)		254	223	87.8%				
Satish Babu		85	76	89.4%		https://community.icann.org/v/BL4bAw	5/25/2021	
Abdulkarim Oloyede		84	68	81.0%		https://community.icann.org/v/AVQ2Bg	5/25/2021	
Hadia Elminzawi		85	79	92.9%		https://community.icann.org/v/3w1pCQ	7/14/2021	
Commercial Business Users Constituency (BC)		34	2	5.9%				
Mark William Datsygold		34	2	5.9%		https://community.icann.org/v/PwbOC	5/25/2021	5/12/2022
GNSO Council		181	148	81.8%				
Donna Austin		96	91	94.8%	Chair	https://community.icann.org/v/08EAg	8/10/2021	
Farell Folly		85	57	67.1%	Liaison	https://community.icann.org/v/151tAw	7/27/2021	
Intellectual Property Constituency (IPC)		97	46	47.4%				
Brian King		13	10	76.9%		https://community.icann.org/v/CSAF8Q	5/25/2021	11/8/2021
Jeffrey Neuman		84	36	42.9%		https://community.icann.org/v/0iBwAg	5/25/2021	
Internet Service Providers and Connectivity Providers Constituency (ISPCP)		89	35	39.3%				
Christian Dawson		83	30	36.1%		https://community.icann.org/v/NiVtAg	7/12/2021	
Miriam Walia		6	5	83.3%		https://community.icann.org/v/3obXQg	5/31/2023	
Non-Commercial Stakeholder Group (NCSG)		131	37	28.2%				
Emmanuel Vitus Agbenonwosi		45	23	51.1%		https://community.icann.org/v/H4z8C	7/13/2022	
Taiwo Akinremi		84	14	16.7%		https://community.icann.org/v/3w1pCQ	7/15/2021	
Grace Githiga		2	0	0.0%		https://community.icann.org/v/14t5Dg	7/26/2023	
Registry Stakeholder Group (RySG)		163	146	89.6%				
Michael Bauland		85	74	87.1%		https://community.icann.org/v/9wvOCQ	5/25/2021	
Duowei Chen		16	11	68.8%		https://community.icann.org/v/1GQHcG	9/26/2021	2/13/2022
Zhang Zuan		62	61	98.4%		https://community.icann.org/v/7g6bAg	2/14/2022	
Registry Stakeholder Group (RySG)		325	265	81.5%				
Martin Alzate		84	66	78.5%		https://community.icann.org/v/8Vt8Ag	5/25/2021	
Geniss Tan Tanaka		84	78	92.9%		https://community.icann.org/v/14LF6g	5/25/2021	
Jennifer Chung		83	62	74.7%		https://community.icann.org/v/6A0uAg	5/25/2021	
Joseph Chiu-kit Yee		74	59	79.7%		https://community.icann.org/v/5Y8CQ	7/6/2021	5/2/2023
Governmental Advisory Committee (GAC)		168	68	40.5%				
T. Santhosh		84	21	25.0%		https://community.icann.org/v/7Z8Aw	5/25/2021	
Nigel Hickson		84	47	56.0%		https://community.icann.org/v/94P8CQ	7/12/2021	
ICANN Board		141	120	85.1%				
Edmon Chung		88	76	86.4%	Liaison	https://community.icann.org/v/5sWAAw	7/27/2021	
Akinori Matsumura		36	29	80.6%	Liaison	https://community.icann.org/v/14HOCR	11/18/2021	9/22/2022
Alan Barrett		17	15	88.2%	Liaison	https://community.icann.org/v/1OP3Dg	3/16/2023	
Grand Total		2541	1495	58.8%				

Staff Support Roster

Row Labels	Start Date	Depart Date
Internet Corporation for Assigned Names & Numbers (ICANN)		
Devan Reed	12/2/2021	
Emily Barabas	5/25/2021	7/18/2023
Terri Agnew	5/25/2021	
Steve Chan	5/25/2021	
Ariel Liang	5/25/2021	
Michael Karakash	5/25/2021	
Sarmad Hussain	5/25/2021	
Pitinan Kooarmornpatana	5/25/2021	
Julia Bisland	5/25/2021	

Health	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	2021				2022				2023				2024				2025			
								Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
1	EPDP: Internationalized Domain Names	983d	05/20/21	02/24/25		67%	In Progress																				
2	PROJECT CONTROL	954d	05/20/21	01/14/25		68%	In Progress																				
3	Project start confirmed	0	05/20/21	05/20/21		100%	Complete																				
4	Adopt/Confirm charter	0	05/20/21	05/20/21	3	100%	Complete																				
5	Confirmation of Team	60d	05/20/21	08/11/21	3	100%	Complete																				
6	Appointment of Team Chair	46d	05/20/21	07/22/21	3	100%	Complete																				
7	Appointment of Liaison to GNSO Council	46d	05/20/21	07/22/21	3	100%	Complete																				
8	Chair / Staff preparations	13d	07/23/21	08/10/21	6	100%	Complete																				
9	Project Management	908d	07/23/21	01/14/25		62%	In Progress																				
10	Develop and confirm Project Plan	50d	07/23/21	09/30/21	6	100%	Complete																				
11	Obtain project plan approval from GNSO Council	20d	10/01/21	10/28/21	10	100%	Complete																				
12	Develop monthly Project Packages and deliver to Group & Council	789d	10/29/21	11/06/24	11	59%	In Progress																				
13	Leadership Sub team	869d	07/23/21	11/20/24		61%	In Progress																				
14	On-going preparation and planning of group activities	869d	07/23/21	11/20/24	6	61%	In Progress																				
15	Close project and transition project to implementation	1d	01/14/25	01/14/25	14, 177	0%																					
16	GROUP DELIBERATIONS	742d	08/11/21	06/13/24		77%	In Progress																				
17	First meeting of Team	1d	08/11/21	08/11/21	8	100%	Complete																				
18	Understand Charter, organize materials and develop initial approach	10d	08/11/21	08/24/21	8	100%	Complete																				
19	Overview & initial discussion of all Policy Topics	10d	08/11/21	08/24/21	8	100%	Complete																				
20	Develop definitions and terminology	28d	08/11/21	09/17/21	8	100%	Complete																				
21	+ Input from other SO/ACs & GNSO SG/Cs	58d	09/09/21	11/29/21		100%	Complete																				
26	Phase 1 Deliberations	403d	08/25/21	03/10/23		100%	Complete																				
27	+ Group 1: Definition of All gTLDs Using RZ-LGR	127d	08/25/21	02/17/22		100%	Complete																				
44	+ Group 2: Same Entity at Top-Level	40d	02/04/22	03/31/22		100%	Complete																				
58	+ Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	211d	03/18/22	01/06/23		100%	Complete																				
75	Review ICANN Org Input for Phase 1 Draft Recommendations	55d	12/26/22	03/10/23	72	100%	Complete																				
76	Data Collection to Facilitate Phase 2 Deliberations	175d	11/07/22	07/07/23		100%	Complete																				
77	Phase 2 Deliberations	235d	05/01/23	03/22/24		42%	In Progress																				
78	Preliminary deliberations for Phase 2 Charter Questions (C1, C2, C4, C4a, C5, C6, D4, D6, D7)	36d	05/01/23	06/19/23	147	100%	Complete																				
79	+ Group 4: Same Entity at Second-Level	30d	11/13/23	12/22/23		75%	In Progress																				
93	+ Group 5: Domain Name Lifecycle	50d	11/13/23	01/19/24		44%	In Progress																				
108	+ Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	55d	11/13/23	01/26/24		11%	In Progress																				
118	+ Group 7: IDN Implementation Guidelines	35d	01/15/24	03/01/24		18%	In Progress																				
127	Review ICANN Org Input for Phase 2 Draft Recommendations	15d	03/04/24	03/22/24	126																						
128	+ Key Group Events	689d	10/25/21	06/13/24		66%	In Progress																				
139	INITIAL REPORT	706d	09/20/21	06/03/24		84%	In Progress																				
140	+ Phase 1 Initial Report	456d	09/20/21	06/19/23		100%	Complete																				
149	Phase 2 Initial Report	141d	11/20/23	06/03/24		32%	In Progress																				
150	Populate stable drafts as required	95d	11/20/23	03/29/24	81	50%	In Progress																				
151	Discuss/approve findings and interim recommendations	1d	04/01/24	04/01/24	150																						
152	Consolidate interim recommendations and findings	1d	04/02/24	04/02/24	151																						
153	Build Draft Report for public comment	10d	04/02/24	04/15/24	151																						
154	Approve Draft Report for public comment	5d	04/16/24	04/22/24	153																						
155	Publish Phase 2 Initial Report	0	04/22/24	04/22/24	154																						
156	Communicate Phase 2 Initial Report	5d	04/23/24	04/29/24	154																						
157	Public comment forum on Phase 2 Initial Report (40 calendar days)	30d	04/23/24	06/03/24	154																						
158	FINAL REPORT	345d	06/20/23	10/14/24		30%	In Progress																				
159	Phase 1 Final Report	104d	06/20/23	11/10/23		58%	In Progress																				
160	Review of public comments	60d	06/20/23	09/11/23	148	100%	Complete																				
161	Continue deliberations of policy topics towards the Phase 1 Final Report	80d	06/20/23	10/09/23	148	50%	In Progress																				
162	Build Phase 1 Final Report & Final Deliberations	10d	10/10/23	10/23/23	161	25%	In Progress																				
163	Determine consensus levels on interim recommendations	14d	10/24/23	11/10/23	162																						

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meetings ICANN77 (Session 1) D4	↓	EPDP_IDN	06/12/23	06/12/23	Complete	
	AI	Check in with members regarding availability for F2F to help understand the ideal dates.	—	Policy Support Staff	06/12/23	07/07/23	Complete	
	WP	Meetings ICANN77 (Session 2) D4, D6, D7	↓	EPDP_IDN	06/13/23	06/13/23	Complete	
	WP	Meetings ICANN77 (Session 3) D4, D6, D7	↓	EPDP_IDN	06/14/23	06/14/23	Complete	
	WP	Meetings ICANN77 (Session 4) D4, D6, D7	↓	EPDP_IDN	06/15/23	06/15/23	Complete	
	WP	Meeting #85 Preview Preliminary Agreements; C4a	↓	EPDP_IDN	06/29/23	06/29/23	Complete	
	AI	Develop visual aid to assist in understanding impact of changes to the source domain.	—	Policy Support Staff	06/29/23	07/13/23	Complete	
	WP	Meeting #86 Review Preliminary Agreements (C4, C5, C6, C1, C2, D4, D6, D7)	↓	EPDP_IDN	07/06/23	07/06/23	Complete	
	AI	Leadership will inform Council of the comments and seek their guidance on whether or not the issue should be considered and if so, how.	—	EPDP_IDN Leadership	07/14/23	07/14/23	Complete	
	AI	Revise language in a manner consistent with the comments and discussion. Staff to make suggested edits to Rec 1.1.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	Leverage RySG comment to modify Rec 2.1 and remove the asterisk language (globally).	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	Add a note in the introductory section to recommend that readers to review the glossary prior to reading recommendations.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	Come back to Rec 3.4 during a future meeting and look at the second part of the ICANN Org comment in particular.	—	EPDP_IDN	10/09/23		In Progress	
	AI	EPDP Team to review the comments received prior to the next meeting, to help facilitate further review in the coming weeks	—	EPDP_IDN	08/04/23	08/04/23	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	07/10/23	07/10/23	Complete	
	WP	Meeting #87 Continue with Public Comment Review (Start at Rec 3.8)	↓	EPDP_IDN	07/13/23	07/13/23	Complete	
	AI	Reformulate IG 3.8. Consider removing "standards" to reflect "criteria and tests" or "widely accepted practices". Add public comment/consultation component. Change "may" to "should".	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	In respect of Rec 3.16, define "established institution", potentially in the glossary.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	Update references to Reserved Names for Recs 3.18 and 3.19.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	WP	Meeting #88 Conservatism Principle Discussion; Continue with Public Comment Review (Start at IG 3.23)	↓	EPDP_IDN	07/20/23	07/20/23	Complete	
	AI	Leadership Team to propose a suggested update / enhancement to IG 3.6, IG 3.8, and IG 3.9 in order to align with the conservatism principle.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	Leadership team to propose suggested edits to clarify Rec 3.24 and Rec 4.1 by taking into account public comment received.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	WP	Meeting #89 ---Cancelled---	↓	EPDP_IDN	07/27/23	07/27/23	Complete	
	WP	Meeting #90 Continue with Public Comment Review (Start at Rec 4.2)	↓	EPDP_IDN	08/03/23	08/03/23	Complete	
	AI	Leadership to consider amendment to the rationale of Rec 4.2 by taking into account the new input from ICANN org.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	Leadership to consider amendment to Rec 4.4 by taking into account the new input from ICANN org.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	Leadership to consider amendment to Rec 5.3 by taking into account ICANN org input.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	Leadership to consider amendment to Rec 6.2 and discuss the semantic differences between "Process" and "Evaluate".	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	Leadership to check with GDS and the RySG regarding the proposed additional text to Recommendation 7.1	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	Leadership to consider amendment to Rec 7.3 and soften the language. The Team will solicit RySG feedback on Rec 7.3 and the complexity of RAs	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	Leadership to propose an overarching statement on registration data protection in order to address the CCWP-HR's input for 7.7, 7.8, 7.9, 7.12, and 7.13.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	Leadership to consider amendment to Rec 7.10 by taking into account ICANN org's input.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	EPDP Team to further discuss ICANN org's input for IG 7.14.	—	EPDP_IDN	10/09/23		In Progress	
	AI	Leadership to consider amendment to Rec 8.2 by taking into account ICANN org comment.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	Leadership to consider replacing "can" with a more appropriate word in Rec 8.5.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	Leadership to consider amendment to Rec 8.7 by taking into account ICANN org input.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	WP	Meeting #91 Continue with Public Comment Review (Start at Rec 8.8); Discuss Global Change Around Terminology	↓	EPDP_IDN	08/10/23	08/10/23	Complete	
	AI	Leadership will review the options to address ICANN Org comments on Implementation Guidance 8.9.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	For Recommendation 8.11, The team will work on drafting implementation guidance on the request to remove a variant from the root zone which would require a request or a transition plan submitted to ICANN org for consideration to finalize the request.	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	The comment on Rec 8.12 will be accepted without objection. EPDP Support Staff will revise the Recommendation to say "In the event a TLD is removed from the root zone the rest of the variant label set (if any) must be removed from the root zone."	—	EPDP_IDN Leadership	10/09/23		In Progress	
	AI	The comment for I.G. 9.4 will be accepted, pending the changes to the language below: a. Starting text (9.4.3) "from "rejected" to "withheld-same-entity": This transition happens when the rejected state of a label comes off; such a variant label can be treated as any other withheld-same-entity label." b. New text (9.4.3) "from "rejected" to "withheld-same-entity": This transition happens when the "the condition which led to the rejection of the label no longer applies; such a variant label can be treated as any other withheld-same-entity label."	—	EPDP_IDN Leadership	10/09/23		In Progress	

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	AI	Leadership will develop revised text for the Global Change based on the following principles: a. Delete "IDN" b. Delete "2012 Round" c. Use "existing" when referring to all of the gTLDs that have been delegated in the root zone d. Remove the statement led by the asterisk and emphasize the indeed messaging in rationale	—	EPDP_IDN Leadership	10/09/23		In Progress	
	MS	Submit project package to GNSO Council	!	Ariel Liang	08/14/23	08/14/23	Complete	
	WP	Meeting #92 TBD	↓	EPDP_IDN	08/17/23		In Progress	
	WP	Meeting #93 ---Cancelled---	↓	EPDP_IDN	08/24/23	08/14/23	Complete	
	WP	Meeting #94 TBD	↓	EPDP_IDN	08/31/23		Not Started	
	WP	Meeting #95 TBD	↓	EPDP_IDN	09/07/23		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	09/11/23		Not Started	
	WP	Meeting #96 TBD	↓	EPDP_IDN	09/14/23		Not Started	
	WP	Meeting #97 TBD	↓	EPDP_IDN	09/21/23		Not Started	
	WP	Meeting #98 TBD	↓	EPDP_IDN	09/28/23		Not Started	
	WP	Meeting #99 TBD	↓	EPDP_IDN	10/05/23		Not Started	
	WP	Meeting #100 TBD	↓	EPDP_IDN	10/12/23		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	10/15/23		Not Started	
	MS	Submission of Phase 1 Final Report to the GNSO Council	!	EPDP_IDN	11/03/23		Not Started	
