

Project Tracking & Rollup DASHBOARD

Project Name EPDP: Internationalized Domain Names **Program** IDNs **Project Sponsor** GNSO Council

Project Information

69%
% Complete

05/20/21
Actual Start

02/21/25
Planned Finish

Tasks by Status

● Not_Started ● Complete ● In_Progress

Project Contacts

Donna Austin
Chair

Justine Chew
Vice_Chair

Farell Folly
Liaison

AL Ariel Liang
Staff_Lead

SC Steve Chan
Project_Manager

Participant Summary

● Member ● Participant ● Observer - Email Only
● Staff - Assigned ● Staff - Not Assigned

Project Status & Health

Project_Status	Project_Health
Revised Schedule	On-Target

Summary Gantt & Key Milestones						2021												2022				2023				2024				2025					
Health	Primary Task	Current Start	Current Finish	% Complete	Status	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1					
	EPDP: Internationalized Domain Names	05/20/21	02/21/25	69%	In Progress	[Gantt bar for EPDP: Internationalized Domain Names]																													
	PROJECT CONTROL	05/20/21	01/13/25	70%	In Progress	[Gantt bar for PROJECT CONTROL]																													
	GROUP DELIBERATIONS	08/11/21	06/13/24	77%	In Progress	[Gantt bar for GROUP DELIBERATIONS]																													
	Group 1: Definition of All gTLDs Using RZ-LGR	08/25/21	02/17/22	100%	Complete	[Gantt bar for Group 1: Definition of All gTLDs Using RZ-LGR]																													
	Group 2: Same Entity at Top-Level	02/04/22	03/31/22	100%	Complete	[Gantt bar for Group 2: Same Entity at Top-Level]																													
	Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	03/18/22	01/06/23	100%	Complete	[Gantt bar for Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants]																													
	Data Collection to Facilitate Phase 2 Deliberations	11/07/22	07/07/23	100%	Complete	[Gantt bar for Data Collection to Facilitate Phase 2 Deliberations]																													
	Group 4: Same Entity at Second-Level	11/10/23	12/21/23	79%	In Progress	[Gantt bar for Group 4: Same Entity at Second-Level]																													
	Group 5: Domain Name Lifecycle	11/10/23	01/18/24	45%	In Progress	[Gantt bar for Group 5: Domain Name Lifecycle]																													
	Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	11/10/23	01/25/24	11%	In Progress	[Gantt bar for Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms]																													
	Group 7: IDN Implementation Guidelines	01/12/24	02/29/24	18%	In Progress	[Gantt bar for Group 7: IDN Implementation Guidelines]																													
	INITIAL REPORT	09/20/21	05/31/24	84%	In Progress	[Gantt bar for INITIAL REPORT]																													
	Publish Phase 1 Initial Report	04/21/23	04/21/23	100%	Complete	[Gantt bar for Publish Phase 1 Initial Report]																													
	Public comment forum on Phase 1 Initial Report (56 calendar days)	04/24/23	06/19/23	100%	Complete	[Gantt bar for Public comment forum on Phase 1 Initial Report (56 calendar days)]																													
	Publish Phase 2 Initial Report	04/19/24	04/19/24			[Gantt bar for Publish Phase 2 Initial Report]																													
	Public comment forum on Phase 2 Initial Report (40 calendar days)	04/22/24	05/31/24			[Gantt bar for Public comment forum on Phase 2 Initial Report (40 calendar days)]																													
	FINAL REPORT	06/20/23	10/11/24	40%	In Progress	[Gantt bar for FINAL REPORT]																													
	Review of public comments - Phase 1	06/20/23	09/11/23	100%	Complete	[Gantt bar for Review of public comments - Phase 1]																													
	Submission of Phase 1 Final Report to the GNSO Council	11/09/23	11/09/23			[Gantt bar for Submission of Phase 1 Final Report to the GNSO Council]																													
	Review of public comments - Phase 2	06/03/24	08/23/24			[Gantt bar for Review of public comments - Phase 2]																													
	Submission of Phase 2 Final Report to the GNSO Council	10/11/24	10/11/24			[Gantt bar for Submission of Phase 2 Final Report to the GNSO Council]																													
	POST GROUP TASKS	10/14/24	02/21/25	Not Started		[Gantt bar for POST GROUP TASKS]																													
	Approval of Final Report and Recommendations by the GNSO Council	10/14/24	12/13/24			[Gantt bar for Approval of Final Report and Recommendations by the GNSO Council]																													
	Publish Recommendations for Public Comment for Board consideration	01/06/25	02/21/25			[Gantt bar for Publish Recommendations for Public Comment for Board consideration]																													

Project Description

On 20 May 2021, the GNSO Council passed a resolution to initiate the Expedited Policy Development Process (EPDP) on Internationalized Domain Names and adopt its charter. The EPDP Team is tasked with providing the GNSO Council with policy recommendations on: 1) the definition of gTLDs and the management of variant labels; and 2) how the IDN Implementation Guidelines, which Contracted Parties are required to comply with, should be updated in the future.

[Mailing List](#)

[Meeting Schedule](#)

[Wiki](#)

[Charter](#)

Completed in Prior Period

- Completed the first reading for draft Phase 2 recommendations that the EPDP Team completed preliminary deliberation.
- Completed and distributed [Project Package](#).

Current Activities & Tasks

- Continue deliberations of policy topics toward Phase 1 Final Report.
- Conduct Phase 2 charter question deliberations.


Open Issues & Risks

- Deliberations of certain charter questions dependent upon input from external parties.
- Deliberations of certain Public Comment input for Phase 1 Initial Report, which specifically relate to the input from PointQuebec and CORE Association, dependent upon guidance from the GNSO Council.
- The EPDP Team will require additional resources and support as well as explore other mechanisms in order to complete Phase 2 work in an expeditious manner.


Planned Activities & Tasks

- Conduct consensus designation on Phase 1 final recommendations.
- Plan for the dedicated face-to-face workshop in December 2023.


Work-Plan Activity Metrics

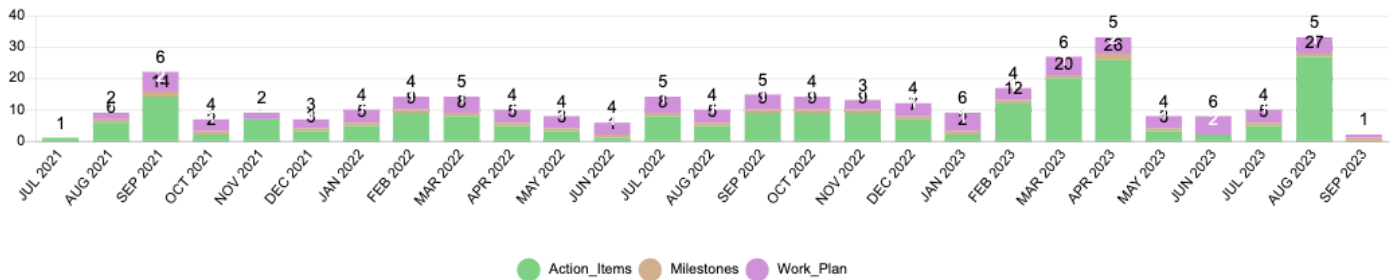


Mailman Activity

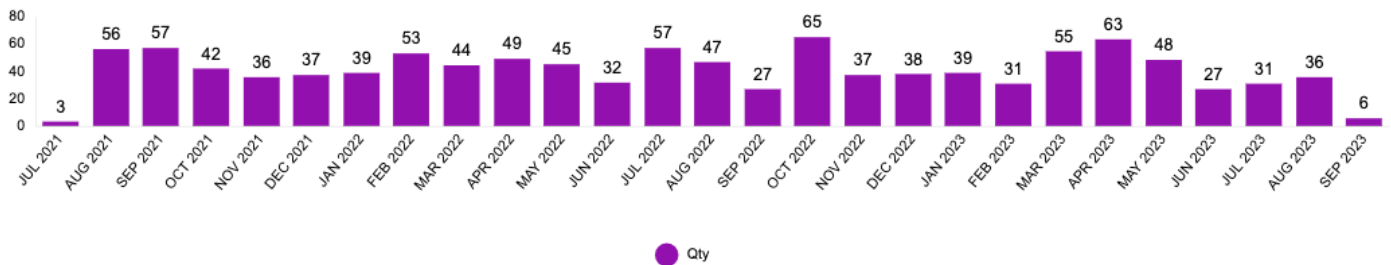

ALL Event Activity & Cumulative Event Hours

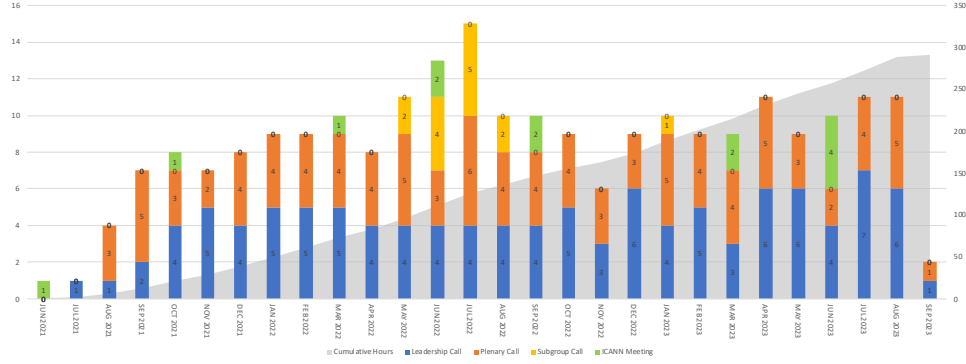

ALL Event Attendance % & Cumulative Person Hours

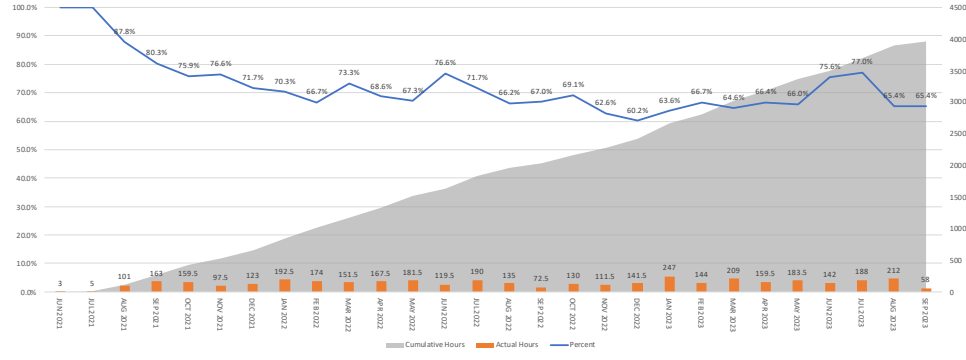

Plenary Roster and Attendance Only

Participant	Row Labels	Sum of Invited Qty	Sum of Attended Qty	Percent	Role	SOI	Start Date	Depart Date
At Large Advisory Committee (ALAC)								
Justine Chew		92	91	98.9%	Vice-chair	https://community.icann.org/x/tYefag	5/25/2021	
TV Gopal		24	6	25.0%		https://community.icann.org/x/8Yf9CQ	5/25/2021	3/21/2022
Independent								
Abdalmonek Gallia		86	5	5.8%		https://community.icann.org/x/2Z0TgCQ	5/25/2021	
Nabil Benamar		85	6	7.1%		https://community.icann.org/x/2w7f6CQ	5/25/2021	
Anil Jain		87	62	71.3%		https://community.icann.org/x/1P8CQ	7/30/2021	
Quoc Pham		84	12	14.3%		https://community.icann.org/x/02bWg	8/13/2021	
Imran Hosen		55	13	23.6%		https://community.icann.org/x/1P9M6CQ	11/4/2021	
Wael Nasr		50	0	0.0%		https://community.icann.org/x/84d3g	6/9/2022	
Lei Gao		85	1	1.2%		https://community.icann.org/x/8CTPCQ	5/25/2021	
Shuo Liang		81	93.1%			https://community.icann.org/x/2w7f6CQ	5/25/2021	
Abdulnadir Roba		2	1	50.0%			8/22/2023	
Registry Stakeholder Group (RySG)								
Jerry Son		87	84	96.6%		https://community.icann.org/x/1A98CQ	5/25/2021	
Wei (Wesley) Wang		86	3	3.5%		https://community.icann.org/x/0Y98CQ	7/13/2021	
Governmental Advisory Committee (GAC)								
Hama Onoruozia Salami		81	57	70.4%		https://community.icann.org/x/4P8CQ	5/25/2021	7/20/2023
Amna Ramalan		2	2	100.0%		https://community.icann.org/x/RI0CQg	7/20/2022	
Member								
At Large Advisory Committee (ALAC)								
Satish Babu		88	79	89.8%		https://community.icann.org/x/8LrAw	5/25/2021	
Abdulkarim Oloyede		87	71	81.6%		https://community.icann.org/x/Y702Bg	5/25/2021	
Hadia Elmimawi		88	82	93.2%		https://community.icann.org/x/wkrBaw	7/14/2021	
Commercial Business Users Constituency (BC)								
Mark William Datsygeid		34	2	5.9%		https://community.icann.org/x/fwbQC	5/25/2021	5/12/2022
GNSO Council								
Donna Austin		99	94	94.9%	Chair	https://community.icann.org/x/gBEAg	8/10/2021	
Fareh Fotiy		88	60	68.2%	Liaison	https://community.icann.org/x/25tUAg	7/27/2021	
Intellectual Property Constituency (IPC)								
Brian King		13	10	76.9%		https://community.icann.org/x/0S4fBQ	5/25/2021	11/8/2021
Jeffrey Neuman		87	36	41.4%		https://community.icann.org/x/falWAg	5/25/2021	
Internet Service Providers and Connectivity Providers Constituency (ISPCP)								
Christian Dawson		86	31	36.0%		https://community.icann.org/x/8uVfAg	7/12/2021	
Nitin Walia		9	7	77.8%		https://community.icann.org/x/8ob8Ag	5/31/2023	
Non-Commercial Stakeholder Group (NCSG)								
Emmanuel Vitus Agbenonwosi		48	26	54.2%		https://community.icann.org/x/84zoc	7/13/2022	
Taiwo Akinremi		87	14	16.1%		https://community.icann.org/x/8quuBg	7/15/2021	
Grace Githago		5	0	0.0%		https://community.icann.org/x/84wBdg	7/26/2023	
Registrar Stakeholder Group (RySG)								
Michael Bauland		88	77	87.5%		https://community.icann.org/x/fwwQCQ	5/25/2021	
Duowei Chen		16	11	68.8%		https://community.icann.org/x/0QHcAg	9/26/2021	2/13/2022
Zhang Zuan		65	64	98.5%		https://community.icann.org/x/7gq6Ag	2/14/2022	
Registry Stakeholder Group (RySG)								
Maksim Alizbas		87	69	79.3%		https://community.icann.org/x/8TvfAg	5/25/2021	
Dennis Tan Tanaka		87	81	93.1%		https://community.icann.org/x/14LAg	5/25/2021	
Jennifer Chung		86	63	73.3%		https://community.icann.org/x/6AduAg	5/25/2021	
Joseph Chiu-Kit Yee		74	59	79.7%		https://community.icann.org/x/5VHRQC	7/6/2021	5/2/2023
Governmental Advisory Committee (GAC)								
T. Santhosh		174	71	40.8%				
Nigel Hickson		87	50	57.5%		https://community.icann.org/x/94P8CQ	7/12/2021	
ICANN Board								
Edmon Chung		91	77	84.6%	Liaison	https://community.icann.org/x/52WAAw	7/27/2021	
Alonori Akemura		36	29	80.6%	Liaison	https://community.icann.org/x/4dH0Cg	11/3/2021	9/22/2022
Alan Barrett		20	17	85.0%		https://community.icann.org/x/0P5DQ	3/16/2023	
Grand Total		2639	1548	58.7%				

Staff Support Roster

Row Labels	Start Date	Depart Date
Internet Corporation for Assigned Names & Numbers (ICANN)		
Dewan Reed		12/2/2021
Emily Barabas	5/25/2021	7/18/2023
Terri Agnew		5/25/2021
Steve Chan		5/25/2021
Anel Liang		5/25/2021
Michael Karakash		5/25/2021
Sarmad Hussain		5/25/2021
Pitinan Kooparmorpatana		5/25/2021
Julia Bisland		5/25/2021

Health	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	2021				2022				2023				2024				2025			
								Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
1	EPDP: Internationalized Domain Names	982d	05/20/21	02/21/25		69%	In Progress																				
2	PROJECT CONTROL	953d	05/20/21	01/13/25		70%	In Progress																				
3	Project start confirmed	0	05/20/21	05/20/21		100%	Complete																				
4	Adopt/Confirm charter	0	05/20/21	05/20/21	3	100%	Complete																				
5	Confirmation of Team	60d	05/20/21	08/11/21	3	100%	Complete																				
6	Appointment of Team Chair	46d	05/20/21	07/22/21	3	100%	Complete																				
7	Appointment of Liaison to GNSO Council	46d	05/20/21	07/22/21	3	100%	Complete																				
8	Chair / Staff preparations	13d	07/23/21	08/10/21	6	100%	Complete																				
9	Project Management	907d	07/23/21	01/13/25		65%	In Progress																				
10	Develop and confirm Project Plan	50d	07/23/21	09/30/21	6	100%	Complete																				
11	Obtain project plan approval from GNSO Council	20d	10/01/21	10/28/21	10	100%	Complete																				
12	Develop monthly Project Packages and deliver to Group & Council	789d	10/29/21	11/06/24	11	62%	In Progress																				
13	Leadership Sub team	869d	07/23/21	11/20/24		64%	In Progress																				
14	On-going preparation and planning of group activities	869d	07/23/21	11/20/24	6	64%	In Progress																				
15	Close project and transition project to implementation	1d	01/13/25	01/13/25	14, 177	0%																					
16	GROUP DELIBERATIONS	742d	08/11/21	06/13/24		77%	In Progress																				
17	First meeting of Team	1d	08/11/21	08/11/21	8	100%	Complete																				
18	Understand Charter, organize materials and develop initial approach	10d	08/11/21	08/24/21	8	100%	Complete																				
19	Overview & initial discussion of all Policy Topics	10d	08/11/21	08/24/21	8	100%	Complete																				
20	Develop definitions and terminology	28d	08/11/21	09/17/21	8	100%	Complete																				
21	+ Input from other SO/ACs & GNSO SG/Cs	58d	09/09/21	11/29/21		100%	Complete																				
26	- Phase 1 Deliberations	403d	08/25/21	03/10/23		100%	Complete																				
27	+ Group 1: Definition of All gTLDs Using RZ-LGR	127d	08/25/21	02/17/22		100%	Complete																				
44	+ Group 2: Same Entity at Top-Level	40d	02/04/22	03/31/22		100%	Complete																				
58	+ Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	211d	03/18/22	01/06/23		100%	Complete																				
75	Review ICANN Org Input for Phase 1 Draft Recommendations	55d	12/26/22	03/10/23	72	100%	Complete																				
76	Data Collection to Facilitate Phase 2 Deliberations	175d	11/07/22	07/07/23		100%	Complete																				
77	- Phase 2 Deliberations	234d	05/01/23	03/21/24		43%	In Progress																				
78	Preliminary deliberations for Phase 2 Charter Questions (C1, C2, C4, C4a, C5, C6, D4, D6, D7)	36d	05/01/23	06/19/23	147	100%	Complete																				
79	+ Group 4: Same Entity at Second-Level	30d	11/10/23	12/21/23		79%	In Progress																				
93	+ Group 5: Domain Name Lifecycle	50d	11/10/23	01/18/24		45%	In Progress																				
108	+ Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	55d	11/10/23	01/25/24		11%	In Progress																				
118	+ Group 7: IDN Implementation Guidelines	35d	01/12/24	02/29/24		18%	In Progress																				
127	Review ICANN Org Input for Phase 2 Draft Recommendations	15d	03/01/24	03/21/24	126																						
128	+ Key Group Events	689d	10/25/21	06/13/24		66%	In Progress																				
139	INITIAL REPORT	705d	09/20/21	05/31/24		84%	In Progress																				
140	+ Phase 1 Initial Report	456d	09/20/21	06/19/23		100%	Complete																				
149	- Phase 2 Initial Report	141d	11/17/23	05/31/24		32%	In Progress																				
150	Populate stable drafts as required	95d	11/17/23	03/28/24	81	50%	In Progress																				
151	Discuss/approve findings and interim recommendations	1d	03/29/24	03/29/24	150																						
152	Consolidate interim recommendations and findings	1d	04/01/24	04/01/24	151																						
153	Build Draft Report for public comment	10d	04/01/24	04/12/24	151																						
154	Approve Draft Report for public comment	5d	04/15/24	04/19/24	153																						
155	Publish Phase 2 Initial Report	0	04/19/24	04/19/24	154																						
156	Communicate Phase 2 Initial Report	5d	04/22/24	04/26/24	154																						
157	Public comment forum on Phase 2 Initial Report (40 calendar days)	30d	04/22/24	05/31/24	154																						
158	FINAL REPORT	344d	06/20/23	10/11/24		40%	In Progress																				
159	- Phase 1 Final Report	103d	06/20/23	11/09/23		76%	In Progress																				
160	Review of public comments	60d	06/20/23	09/11/23	148	100%	Complete																				
161	Continue deliberations of policy topics towards the Phase 1 Final Report	80d	06/20/23	10/09/23	148	80%	In Progress																				
162	Build Phase 1 Final Report & Final Deliberations	10d	10/10/23	10/23/23	161	90%	In Progress																				
163	Determine consensus levels on interim recommendations	13d	10/24/23	11/09/23	162																						

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #90 Continue with Public Comment Review (Start at Rec 4.2)	↓	EPDP_IDN	08/03/23	08/03/23	Complete	
	AI	Leadership to consider amendment to the rationale of Rec 4.2 by taking into account the new input from ICANN org.	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	AI	Leadership to consider amendment to Rec 4.4 by taking into account the new input from ICANN org.	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	AI	Leadership to consider amendment to Rec 5.3 by taking into account ICANN org input.	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	AI	Leadership to consider amendment to Rec 6.2 and discuss the semantic differences between "Process" and "Evaluate".	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	AI	Leadership to check with GDS and the RySG regarding the proposed additional text to Recommendation 7.1	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	AI	Leadership to consider amendment to Rec 7.3 and soften the language. The Team will solicit RySG feedback on Rec 7.3 and the complexity of RAs	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	AI	Leadership to propose an overarching statement on registration data protection in order to address the CCWP-HR's input for 7.7, 7.8, 7.9, 7.12, and 7.13.	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	AI	Leadership to consider amendment to Rec 7.10 by taking into account ICANN org's input.	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	AI	EPDP Team to further discuss ICANN org's input for IG 7.14.	—	EPDP_IDN	10/09/23	08/29/23	Complete	
	AI	Leadership to consider amendment to Rec 8.2 by taking into account ICANN org comment.	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	AI	Leadership to consider replacing "can" with a more appropriate word in Rec 8.5.	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	AI	Leadership to consider amendment to Rec 8.7 by taking into account ICANN org input.	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	WP	Meeting #91 Continue with Public Comment Review (Start at Rec 8.8); Discuss Global Change Around Terminology	↓	EPDP_IDN	08/10/23	08/10/23	Complete	
	AI	Leadership will review the options to address ICANN Org comments on Implementation Guidance 8.9.	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	AI	For Recommendation 8.11, The team will work on drafting implementation guidance on the request to remove a variant from the root zone which would require a request or a transition plan submitted to ICANN org for consideration to finalize the request.	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	AI	The comment on Rec 8.12 will be accepted without objection. EPDP Support Staff will revise the Recommendation to say "In the event a TLD is removed from the root zone the rest of the variant label set (if any) must be removed from the root zone."	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	AI	The comment for I.G. 9.4 will be accepted, pending the changes to the language below: a. Starting text (9.4.3) "from "rejected" to "withheld-same-entity": This transition happens when the rejected state of a label comes off; such a variant label can be treated as any other withheld-same-entity label." b. New text (9.4.3) "from "rejected" to "withheld-same-entity": This transition happens when the "the condition which led to the rejection of the label no longer applies; such a variant label can be treated as any other withheld-same-entity label."	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	AI	Leadership will develop revised text for the Global Change based on the following principles: a. Delete "IDN" b. Delete "2012 Round" c. Use "existing" when referring to all of the gTLDs that have been delegated in the root zone d. Remove the statement led by the asterisk and emphasize the indeed messaging in rationale	—	EPDP_IDN Leadership	10/09/23	08/29/23	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	08/14/23	08/14/23	Complete	
	WP	Meeting #92 Continued discussion of Source Domain Name	↓	EPDP_IDN	08/17/23	08/17/23	Complete	
	AI	Leadership to propose suggested revisions to the rationale of Phase 2 Recommendation 5 by incorporating the discussion around the deletion and change of the source domain name	—	EPDP_IDN Leadership	09/28/23		In Progress	
	AI	Leadership to propose an update to the source domain name definition based on discussions today	—	EPDP_IDN Leadership	09/28/23		In Progress	
	AI	Sarmad will get back to the group regarding his proposition regarding identifying one source domain under each gTLD	—	Sarmad Hussain	09/28/23		In Progress	
	WP	Meeting #93 ---Cancelled---	↓	EPDP_IDN	08/24/23	08/14/23	Complete	
	WP	Meeting #94 Review of Proposed Updates of Phase 1 Final Recommendations	↓	EPDP_IDN	08/31/23	08/31/23	Complete	
	AI	Leadership will look to set an agenda for the F2F Workshop in December as to allow representative groups time to discuss and strategize for the meeting	—	EPDP_IDN Leadership	11/17/23		In Progress	
	AI	Leadership will reconsider Recommendation 3.xx for further clarification	—	EPDP_IDN Leadership	09/21/23		In Progress	
	AI	Leadership will work to re-write Rec. 3.5.4. to better address the responsibilities of the registry operator in relation to the end-user.	—	EPDP_IDN Leadership	09/21/23		In Progress	
	AI	Leadership will discuss the wording of 3.5.1 and determine if the second part of the statement is redundant due to the definition of variant.	—	EPDP_IDN Leadership	09/21/23		In Progress	
	AI	The ALAC will review the updated language in Rec 3.5 and IG 3.6	—	Abdulkarim Oloyede Hadia Elminiawi Satish Babu	09/21/23		In Progress	
	AI	The team will deliberate on IG 3.9 and how to proceed with the specifics of the application process	—	EPDP_IDN	09/21/23		In Progress	
	WP	Meeting #95 Review of Proposed Updates of Phase 1 Final Recommendations	↓	EPDP_IDN	09/07/23	09/07/23	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	09/11/23	09/11/23	Complete	
	WP	Meeting #96 TBD	↓	EPDP_IDN	09/14/23		Not Started	
	WP	Meeting #97 TBD	↓	EPDP_IDN	09/21/23		Not Started	
	WP	Meeting #98 TBD	↓	EPDP_IDN	09/28/23		Not Started	
	WP	Meeting #99 TBD	↓	EPDP_IDN	10/05/23		Not Started	

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #100 TBD	↓	EPDP_IDN	10/12/23		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	10/15/23		Not Started	
	MS	Submission of Phase 1 Final Report to the GNSO Council	!	EPDP_IDN	11/03/23		Not Started	
