

# Project Tracking & Rollup DASHBOARD



**Project Name** EPDP: Internationalized Domain Names **Program** IDNs **Project Sponsor** GNSO Council

**Project Information**

**89%**  
% Complete

**05/20/21**  
Actual Start

**02/27/25**  
Planned Finish

**Tasks by Status**

● Not\_Started ● Complete ● In\_Progress

**Project Contacts**

**Donna Austin**  
Chair

**Farell Folly**  
Vice\_Chair

**Manju Chen**  
Liaison

**SL Saewon Lee**  
Staff\_Lead

**SC Steve Chan**  
Project\_Manager

**Participant Summary**

● Member ● Participant ● Observer - Email Only  
● Staff - Assigned ● Staff - Not Assigned

Summary Gantt & Key Milestones						2021 2022 2023 2024 2025																				
Health	Primary Task	Current Start	Current Finish	% Complete	Status	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1				
	<b>EPDP: Internationalized Domain Names</b>	<b>05/20/21</b>	<b>02/27/25</b>	<b>89%</b>	<b>In Progress</b>	[Gantt Bar]																				
	<b>PROJECT CONTROL</b>	<b>05/20/21</b>	<b>01/17/25</b>	<b>91%</b>	<b>In Progress</b>	[Gantt Bar]																				
	<b>GROUP DELIBERATIONS</b>	<b>08/11/21</b>	<b>06/13/24</b>	<b>100%</b>	<b>In Progress</b>	[Gantt Bar]																				
	Group 1: Definition of All gTLDs Using RZ-LGR	08/25/21	02/17/22	100%	Complete	[Gantt Bar]																				
	Group 2: Same Entity at Top-Level	02/04/22	03/31/22	100%	Complete	[Gantt Bar]																				
	Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	03/18/22	01/06/23	100%	Complete	[Gantt Bar]																				
	Data Collection to Facilitate Phase 2 Deliberations	11/07/22	07/07/23	100%	Complete	[Gantt Bar]																				
	Group 4: Same Entity at Second-Level	11/10/23	12/21/23	100%	Complete	[Gantt Bar]																				
	Group 5: Domain Name Lifecycle	11/10/23	01/18/24	100%	Complete	[Gantt Bar]																				
	Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	11/10/23	01/25/24	100%	Complete	[Gantt Bar]																				
	Group 7: IDN Implementation Guidelines	01/12/24	02/29/24	100%	Complete	[Gantt Bar]																				
	<b>INITIAL REPORT</b>	<b>09/20/21</b>	<b>05/21/24</b>	<b>100%</b>	<b>In Progress</b>	[Gantt Bar]																				
	Publish Phase 1 Initial Report	04/21/23	04/21/23	100%	Complete	[Gantt Bar]																				
	Public comment forum on Phase 1 Initial Report (56 calendar days)	04/24/23	06/19/23	100%	Complete	[Gantt Bar]																				
	Publish Phase 2 Initial Report	04/11/24	04/11/24	100%	Complete	[Gantt Bar]																				
	Public comment forum on Phase 2 Initial Report (40 calendar days)	04/11/24	05/21/24	100%	Complete	[Gantt Bar]																				
	<b>FINAL REPORT</b>	<b>06/20/23</b>	<b>10/11/24</b>	<b>67%</b>	<b>In Progress</b>	[Gantt Bar]																				
	Review of public comments - Phase 1	06/20/23	09/11/23	100%	Complete	[Gantt Bar]																				
	Submission of Phase 1 Final Report to the GNSO Council	11/09/23	11/09/23	100%	Complete	[Gantt Bar]																				
	Review of public comments - Phase 2	05/22/24	08/13/24	50%	In Progress	[Gantt Bar]																				
	Submission of Phase 2 Final Report to the GNSO Council	10/11/24	10/11/24			[Gantt Bar]																				
	<b>POST GROUP TASKS</b>	<b>10/14/24</b>	<b>02/27/25</b>	<b>Not Started</b>		[Gantt Bar]																				
	Approval of Final Report and Recommendations by the GNSO Council	10/14/24	12/19/24			[Gantt Bar]																				

**Project Description**

On 20 May 2021, the GNSO Council passed a resolution to initiate EPDP on Internationalized Domain Names and adopt its charter. The EPDP Team is tasked with providing the GNSO Council with policy recommendations on: 1) the definition of gTLDs and the management of variant labels; and 2) how the IDN Implementation Guidelines, which Contracted Parties are required to comply with, should be updated in the future.

[Mailing List](#) [Meeting Schedule](#)  
[Wiki](#) [Charter](#)

**Completed in Prior Period**

- The ICANN Board adopted the EPDP's Phase 1 recommendations.
- Phase 2 Initial Report Public Comment closed on 21 May 2024.
- Staff completed the Summary Report of public comments for the Phase 2 Initial Report (pub. 20 JUN 2024).
- Completed and distributed Project Package.

**Current Activities & Tasks**



- EPDP Team to review public comments received and amend recommendations as appropriate.




**Open Issues & Risks**

- None for this period.

**Planned Activities & Tasks**

- Complete Phase 2 Final Report, including consensus designation, and deliver to the GNSO Council.

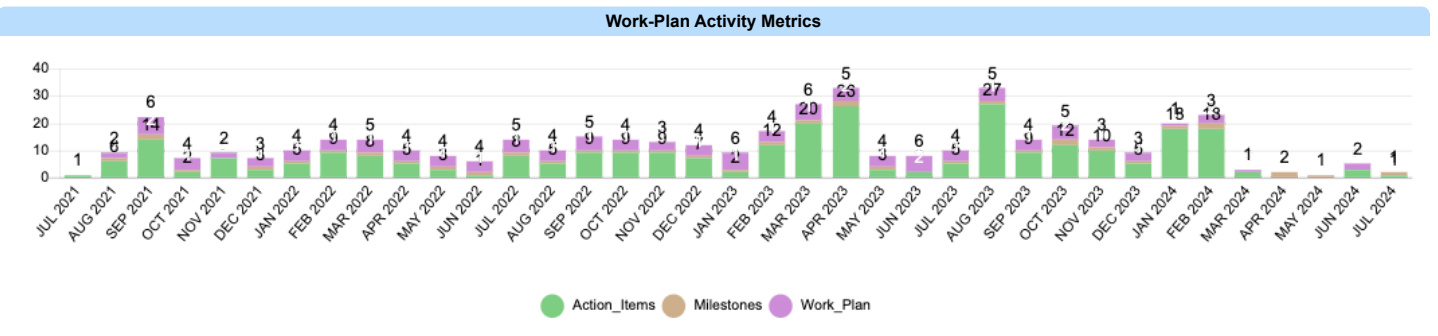

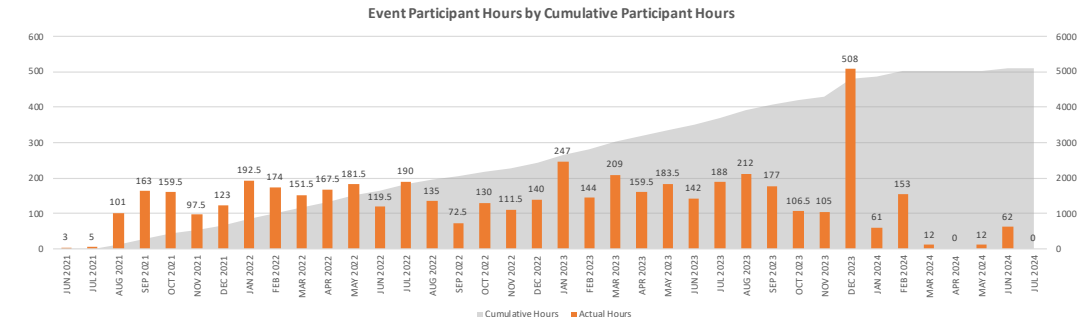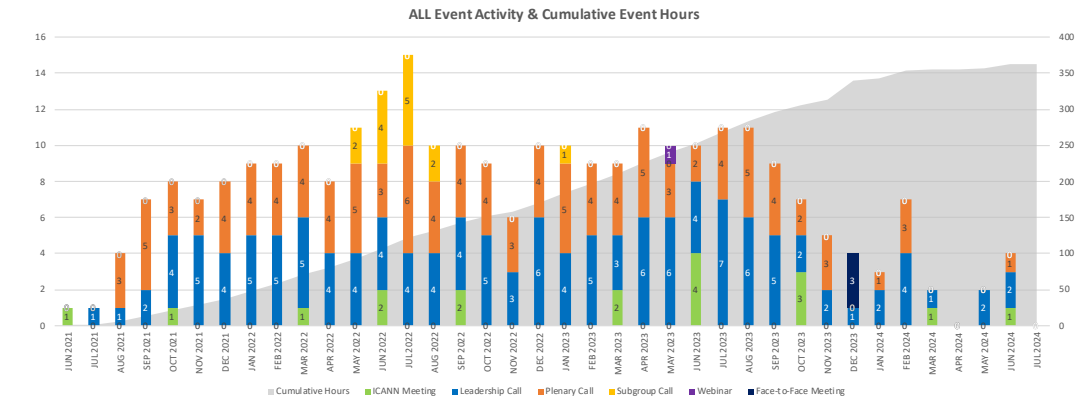

### Roster & Attendance - All Events

Row Labels	Invited	Attended	Percent	Role	SOI	Start Date	Depart Date
<b>Member</b>	<b>2618</b>	<b>1925</b>	<b>73.5%</b>				
<b>At-Large Advisory Committee (ALAC)</b>	<b>529</b>	<b>483</b>	<b>91.3%</b>				
Abdulkarim Oloyede	102	85	83.3%		<a href="https://community.icann.org/x/VY02Bq">https://community.icann.org/x/VY02Bq</a>	25.05.2021	
Nadia Elmriawi	102	95	93.1%		<a href="https://community.icann.org/x/vwQDaw">https://community.icann.org/x/vwQDaw</a>	14.07.2021	
Justine Chew	215	209	97.2%	Vice-chair	<a href="https://community.icann.org/x/bt7d4q">https://community.icann.org/x/bt7d4q</a>	25.05.2021	09.11.2023
Satish Babu	103	92	89.3%		<a href="https://community.icann.org/x/8Lst8q">https://community.icann.org/x/8Lst8q</a>	25.05.2021	
Wael Nasr	7	2	28.6%		<a href="https://community.icann.org/x/8AEVdQ">https://community.icann.org/x/8AEVdQ</a>	09.06.2022	
<b>Commercial Business Users Constituency (BC)</b>	<b>34</b>	<b>2</b>	<b>5.9%</b>				
Mark William Datsygold	34	2	5.9%		<a href="https://community.icann.org/x/FwbOC">https://community.icann.org/x/FwbOC</a>	25.05.2021	12.05.2022
<b>GNSO Council</b>	<b>361</b>	<b>276</b>	<b>76.5%</b>				
Donna Austin	245	229	93.5%	Chair	<a href="https://community.icann.org/x/t8BEAg">https://community.icann.org/x/t8BEAg</a>	10.08.2021	
Farell Folly	92	27	29.3%	Vice-chair	<a href="https://community.icann.org/x/15t1Aw">https://community.icann.org/x/15t1Aw</a>	27.07.2021	
Manju Chen	24	20	83.3%	Liaison	<a href="https://community.icann.org/x/4t1mCQ">https://community.icann.org/x/4t1mCQ</a>	11.07.2023	
<b>Governmental Advisory Committee (GAC)</b>	<b>200</b>	<b>81</b>	<b>40.5%</b>				
Nigel Hickson	103	60	58.3%		<a href="https://community.icann.org/x/94P8CQ">https://community.icann.org/x/94P8CQ</a>	12.07.2021	
SANTHOSH THAMPY	97	21	21.6%		<a href="https://community.icann.org/x/72-R8w">https://community.icann.org/x/72-R8w</a>	25.05.2021	
<b>ICANN Board</b>	<b>184</b>	<b>152</b>	<b>82.6%</b>				
Akinori MAEMURA	36	29	80.6%	Liaison	<a href="https://community.icann.org/x/4HOCe">https://community.icann.org/x/4HOCe</a>	18.11.2021	22.09.2022
Alan Barrett	32	28	87.5%	Liaison	<a href="https://community.icann.org/x/vOP5DQ">https://community.icann.org/x/vOP5DQ</a>	16.03.2023	
Edmon Chung	116	95	81.9%	Liaison	<a href="https://community.icann.org/x/SsWAaw">https://community.icann.org/x/SsWAaw</a>	27.07.2021	
<b>Intellectual Property Constituency (IPC)</b>	<b>111</b>	<b>46</b>	<b>41.4%</b>				
Brian King	13	10	76.9%		<a href="https://community.icann.org/x/OS4FBQ">https://community.icann.org/x/OS4FBQ</a>	25.05.2021	08.11.2021
Jeffrey Neuman	98	36	36.7%		<a href="https://community.icann.org/x/qjRwAg">https://community.icann.org/x/qjRwAg</a>	25.05.2021	
<b>Internet Corporation for Assigned Names &amp; Numbers (ICANN)</b>	<b>210</b>	<b>206</b>	<b>98.1%</b>				
Michael Karakash	101	99	98.0%	Liaison		25.05.2021	
Sarmad Hussain	109	107	98.2%	Liaison		25.05.2021	
<b>Internet Service Providers and Connectivity Providers Constituency (ISPCP)</b>	<b>119</b>	<b>54</b>	<b>45.4%</b>				
Christian Dawson	96	36	37.5%		<a href="https://community.icann.org/x/NivRAg">https://community.icann.org/x/NivRAg</a>	12.07.2021	
Nitin Wallia	23	18	78.3%		<a href="https://community.icann.org/x/b4bXDq">https://community.icann.org/x/b4bXDq</a>	31.05.2023	
<b>Non-Commercial Stakeholder Group (NCSG)</b>	<b>282</b>	<b>125</b>	<b>44.3%</b>				
Emmanuel Elogo Agbenonwosi	63	36	57.1%		<a href="https://community.icann.org/x/H4zC">https://community.icann.org/x/H4zC</a>	13.07.2022	
Farell Folly	103	71	68.9%	Vice-chair	<a href="https://community.icann.org/x/15t1Aw">https://community.icann.org/x/15t1Aw</a>	27.07.2021	
Grace Githaiga	17	1	5.9%		<a href="https://community.icann.org/x/b4bXDq">https://community.icann.org/x/b4bXDq</a>	26.07.2023	
Taiwo Akinremi	99	17	17.2%		<a href="https://community.icann.org/x/squlBg">https://community.icann.org/x/squlBg</a>	15.07.2021	
<b>Registrar Stakeholder Group (RrSG)</b>	<b>206</b>	<b>182</b>	<b>88.3%</b>				
Duowei Chen	16	11	68.8%		<a href="https://community.icann.org/x/rQOHCe">https://community.icann.org/x/rQOHCe</a>	26.09.2021	13.02.2022
Michael Bauland	114	98	86.0%		<a href="https://community.icann.org/x/vwQDaw">https://community.icann.org/x/vwQDaw</a>	25.05.2021	
Zhang Zuan	76	73	96.1%		<a href="https://community.icann.org/x/7gn6Ag">https://community.icann.org/x/7gn6Ag</a>	14.02.2022	
<b>Registry Stakeholder Group (RySG)</b>	<b>382</b>	<b>318</b>	<b>83.2%</b>				
Dennis Tanaka	99	92	92.9%		<a href="https://community.icann.org/x/14LFAg">https://community.icann.org/x/14LFAg</a>	25.05.2021	
Edmon Chung	8	8	100.0%	Liaison	<a href="https://community.icann.org/x/SsWAaw">https://community.icann.org/x/SsWAaw</a>	27.07.2021	
Jennifer Chung	100	76	76.0%		<a href="https://community.icann.org/x/6ADuAg">https://community.icann.org/x/6ADuAg</a>	25.05.2021	
Joseph Chiu-Kit Yee	74	59	79.7%		<a href="https://community.icann.org/x/5VH8CQ">https://community.icann.org/x/5VH8CQ</a>	06.07.2021	02.05.2023
MAXIM Alzoba	101	83	82.2%		<a href="https://community.icann.org/x/BTrRAg">https://community.icann.org/x/BTrRAg</a>	25.05.2021	
<b>Participant</b>	<b>1078</b>	<b>394</b>	<b>36.5%</b>				
<b>At-Large Advisory Committee (ALAC)</b>	<b>36</b>	<b>16</b>	<b>44.4%</b>				
Gopal Tadepalli	24	6	25.0%		<a href="https://community.icann.org/x/BYTB8Q">https://community.icann.org/x/BYTB8Q</a>	25.05.2021	21.03.2022
Nadia Elmriawi	12	10	83.3%		<a href="https://community.icann.org/x/vwQDaw">https://community.icann.org/x/vwQDaw</a>	14.07.2021	
<b>Governmental Advisory Committee (GAC)</b>	<b>101</b>	<b>68</b>	<b>67.3%</b>				
Amina Ramallan	19	10	52.6%		<a href="https://community.icann.org/x/RIOCdQ">https://community.icann.org/x/RIOCdQ</a>	20.07.2023	
Hamza Onoruoiza Salami	82	58	70.7%		<a href="https://community.icann.org/x/4P8CQ">https://community.icann.org/x/4P8CQ</a>	25.05.2021	20.07.2023
<b>Independent</b>	<b>734</b>	<b>204</b>	<b>27.8%</b>				
Abdulmonem Galila	97	5	5.2%		<a href="https://community.icann.org/x/2OTpCQ">https://community.icann.org/x/2OTpCQ</a>	25.05.2021	
Abdulnasser Roba	13	4	30.8%		<a href="https://community.icann.org/x/4d8Bsw">https://community.icann.org/x/4d8Bsw</a>	22.08.2023	
Anil Kumar Jain	100	69	69.0%		<a href="https://community.icann.org/x/1P98CQ">https://community.icann.org/x/1P98CQ</a>	30.07.2021	
Lei Gao	96	1	1.0%		<a href="https://community.icann.org/x/4DTpCQ">https://community.icann.org/x/4DTpCQ</a>	25.05.2021	
MD IMRAN HOSSEN	77	23	29.9%		<a href="https://community.icann.org/x/4DMCQw">https://community.icann.org/x/4DMCQw</a>	04.11.2021	
Nabil Benamar	96	0	0.0%		<a href="https://community.icann.org/x/3wTnCQ">https://community.icann.org/x/3wTnCQ</a>	25.05.2021	
Quoc Pham	95	12	12.6%		<a href="https://community.icann.org/x/O2bAw">https://community.icann.org/x/O2bAw</a>	13.08.2021	
Shuo Liang	99	90	90.9%		<a href="https://community.icann.org/x/2wTnCQ">https://community.icann.org/x/2wTnCQ</a>	25.05.2021	
Wael Nasr	61	0	0.0%		<a href="https://community.icann.org/x/8AEVdQ">https://community.icann.org/x/8AEVdQ</a>	09.06.2022	
<b>Registry Stakeholder Group (RySG)</b>	<b>207</b>	<b>106</b>	<b>51.2%</b>				
Jerry Sen	110	103	93.6%		<a href="https://community.icann.org/x/4X8CQ">https://community.icann.org/x/4X8CQ</a>	25.05.2021	
Wei (Wesley) Wang	97	3	3.1%		<a href="https://community.icann.org/x/0VP8CQ">https://community.icann.org/x/0VP8CQ</a>	13.07.2021	
<b>Grand Total</b>	<b>3696</b>	<b>2319</b>	<b>62.7%</b>				

### Staff Support Roster

Row Labels	Start Date	Depart Date
<b>Staff - Assigned</b>		
<b>Internet Corporation for Assigned Names &amp; Numbers (ICANN)</b>		
Ariel Liang	25.05.2021	
Daniel Gluck	13.07.2023	
Devan Reed	02.12.2021	
Emily Barabas	25.05.2021	18.07.2023
John Emery	14.05.2024	
Julia Bisland	25.05.2021	
Pitnan Kooarmornpatana	25.05.2021	
Saewon Lee	25.01.2024	
Steve Chan	25.05.2021	
Terri Agnew	25.05.2021	
<b>Grand Total</b>		

Health	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	2021				2022				2023				2024				2025			
								Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
1	<b>EPDP: Internationalized Domain Names</b>	<b>986d</b>	<b>05/20/21</b>	<b>02/27/25</b>		<b>89%</b>	<b>In Progress</b>																				
2	<b>PROJECT CONTROL</b>	<b>957d</b>	<b>05/20/21</b>	<b>01/17/25</b>		<b>91%</b>	<b>In Progress</b>																				
3	Project start confirmed	0	05/20/21	05/20/21		100%	Complete																				
4	Adopt/Confirm charter	0	05/20/21	05/20/21	3	100%	Complete																				
5	Confirmation of Team	60d	05/20/21	08/11/21	3	100%	Complete																				
6	Appointment of Team Chair	46d	05/20/21	07/22/21	3	100%	Complete																				
7	Appointment of Liaison to GNSO Council	46d	05/20/21	07/22/21	3	100%	Complete																				
8	Chair / Staff preparations	13d	07/23/21	08/10/21	6	100%	Complete																				
9	<b>Project Management</b>	<b>911d</b>	<b>07/23/21</b>	<b>01/17/25</b>		<b>89%</b>	<b>In Progress</b>																				
10	Develop and confirm Project Plan	50d	07/23/21	09/30/21	6	100%	Complete																				
11	Obtain project plan approval from GNSO Council	20d	10/01/21	10/28/21	10	100%	Complete																				
12	<b>Develop monthly Project Packages and deliver to Group &amp; Council</b>	<b>789d</b>	<b>10/29/21</b>	<b>11/06/24</b>	<b>11</b>	<b>89%</b>	<b>In Progress</b>																				
13	<b>Leadership Sub team</b>	<b>869d</b>	<b>07/23/21</b>	<b>11/20/24</b>		<b>89%</b>	<b>In Progress</b>																				
14	On-going preparation and planning of group activities	869d	07/23/21	11/20/24	6	89%	In Progress																				
15	Close project and transition project to implementation	1d	01/17/25	01/17/25	14, 178	0%																					
16	<b>GROUP DELIBERATIONS</b>	<b>742d</b>	<b>08/11/21</b>	<b>06/13/24</b>		<b>100%</b>	<b>In Progress</b>																				
17	First meeting of Team	1d	08/11/21	08/11/21	8	100%	Complete																				
18	Understand Charter, organize materials and develop initial approach	10d	08/11/21	08/24/21	8	100%	Complete																				
19	Overview & initial discussion of all Policy Topics	10d	08/11/21	08/24/21	8	100%	Complete																				
20	Develop definitions and terminology	28d	08/11/21	09/17/21	8	100%	Complete																				
21	+ Input from other SO/ACs & GNSO SG/Cs	58d	09/09/21	11/29/21		100%	Complete																				
26	<b>Phase 1 Deliberations</b>	<b>403d</b>	<b>08/25/21</b>	<b>03/10/23</b>		<b>100%</b>	<b>Complete</b>																				
27	+ Group 1: Definition of All gTLDs Using RZ-LGR	127d	08/25/21	02/17/22		100%	Complete																				
44	+ Group 2: Same Entity at Top-Level	40d	02/04/22	03/31/22		100%	Complete																				
58	+ Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	211d	03/18/22	01/06/23		100%	Complete																				
75	Review ICANN Org Input for Phase 1 Draft Recommendations	55d	12/26/22	03/10/23	72	100%	Complete																				
76	Data Collection to Facilitate Phase 2 Deliberations	175d	11/07/22	07/07/23		100%	Complete																				
77	<b>Phase 2 Deliberations</b>	<b>234d</b>	<b>05/01/23</b>	<b>03/21/24</b>		<b>100%</b>	<b>Complete</b>																				
78	Preliminary deliberations for Phase 2 Charter Questions (C1, C2, C4, C4a, C5, C6, D4, D6, D7)	36d	05/01/23	06/19/23	148	100%	Complete																				
79	+ Group 4: Same Entity at Second-Level	30d	11/10/23	12/21/23		100%	Complete																				
93	+ Group 5: Domain Name Lifecycle	50d	11/10/23	01/18/24		100%	Complete																				
108	+ Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	55d	11/10/23	01/25/24		100%	Complete																				
118	+ Group 7: IDN Implementation Guidelines	35d	01/12/24	02/29/24		100%	Complete																				
127	Review ICANN Org Input for Phase 2 Draft Recommendations	15d	03/01/24	03/21/24	126	100%	Complete																				
128	+ Key Group Events	689d	10/25/21	06/13/24		100%	In Progress																				
140	<b>INITIAL REPORT</b>	<b>697d</b>	<b>09/20/21</b>	<b>05/21/24</b>		<b>100%</b>	<b>In Progress</b>																				
141	<b>Phase 1 Initial Report</b>	<b>456d</b>	<b>09/20/21</b>	<b>06/19/23</b>		<b>100%</b>	<b>Complete</b>																				
142	Populate stable drafts as required	385d	09/20/21	03/10/23	20	100%	Complete																				
143	Discuss/approve findings and interim recommendations	15d	03/13/23	03/31/23	142	100%	Complete																				
144	Consolidate interim recommendations and findings	10d	04/03/23	04/14/23	143	100%	Complete																				
145	Build Draft Report for public comment	10d	04/03/23	04/14/23	143	100%	Complete																				
146	Approve Draft Report for public comment	5d	04/17/23	04/21/23	145	100%	Complete																				
147	Publish Phase 1 Initial Report	0	04/21/23	04/21/23	146	100%	Complete																				
148	Communicate Phase 1 Initial Report	5d	04/24/23	04/28/23	146	100%	Complete																				
149	Public comment forum on Phase 1 Initial Report (56 calendar days)	41d	04/24/23	06/19/23	146	100%	Complete																				
150	<b>Phase 2 Initial Report</b>	<b>133d</b>	<b>11/17/23</b>	<b>05/21/24</b>		<b>100%</b>	<b>Complete</b>																				
151	Populate stable drafts as required	95d	11/17/23	03/28/24	81	100%	Complete																				
152	Discuss/approve findings and interim recommendations	1d	03/29/24	03/29/24	151	100%	Complete																				
153	Consolidate interim recommendations and findings	1d	04/01/24	04/01/24	152	100%	Complete																				
154	Build Draft Report for public comment	5d	04/01/24	04/05/24	152	100%	Complete																				
155	Approve Draft Report for public comment	4d	04/08/24	04/11/24	154	100%	Complete																				
156	Publish Phase 2 Initial Report	0	04/11/24	04/11/24	155	100%	Complete																				



Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	ICANN79 - Session 1 Review of preliminary recommendations	↓	EPDP_IDN	03/02/24	03/02/24	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	04/08/24	04/08/24	Complete	
	MS	Submission of Phase 2 Initial Report for Public Comment	!	EPDP_IDN	04/22/24	04/11/24	Complete	
	MS	Phase 2 Initial Report for Public Comment closed	!	EPDP_IDN	05/21/24	05/21/24	Complete	
	AI	Staff to prepare for the ICANN80 session	—	Policy Support Staff	06/01/24	06/01/24	Complete	
	AI	Staff to prepare the PCRT for review of comments by the EPDP	—	Policy Support Staff	06/04/24	06/04/24	Complete	
	AI	Staff to prepare a public comment report	—	Policy Support Staff	06/04/24	06/04/24	Complete	
	WP	ICANN 80 - Meeting Begin Review of Public Comments	↓	EPDP_IDN	06/10/24	06/10/24	Complete	
	AI	Staff to prepare a review of public comment tool	—	Policy Support Staff	07/01/24	07/01/24	Complete	
	WP	Meeting #108 Review Initial Report Comments	↓	EPDP_IDN	06/27/24	06/27/24	Complete	
	AI	WG to review of public comment tool	—	EPDP_IDN	07/10/24		In Progress	
	MS	Submit project package to GNSO Council	!	Policy Support Staff	07/08/24	07/08/24	Complete	
	WP	Meeting #109 Review Initial Report Comments	↓	EPDP_IDN	07/11/24		In Progress	
	WP	Meeting #110 Review Initial Report Comments	↓	EPDP_IDN	07/18/24		Not Started	
	WP	Meeting #111 Review Initial Report Comments	↓	EPDP_IDN	07/25/24		Not Started	
	MS	Submit project package to GNSO Council	!	Policy Support Staff	07/29/24		Not Started	
	WP	Meeting #112 TBD	↓	EPDP_IDN	08/01/24		Not Started	
	WP	Meeting #113 TBD	↓	EPDP_IDN	08/08/24		Not Started	
	WP	Meeting #114 TBD	↓	EPDP_IDN	08/15/24		Not Started	
	WP	Meeting #115 TBD	↓	EPDP_IDN	08/22/24		Not Started	
	WP	Meeting #116 TBD	↓	EPDP_IDN	08/29/24		Not Started	
	WP	Meeting #117 TBD	↓	EPDP_IDN	09/05/24		Not Started	
	MS	Submit project package to GNSO Council	!	Policy Support Staff	09/09/24		Not Started	
	MS	Submission of Phase 2 Final Report to the GNSO Council	!	EPDP_IDN	10/11/24		Not Started	
