




Transition Implementation Status Reporting

26 July 2016

1. Overall Timeline
2. Status Update
3. Appendix: Projects Plans

Overall Timeline

Implementation Planning Timeline – Proposals Delivered in March 2016

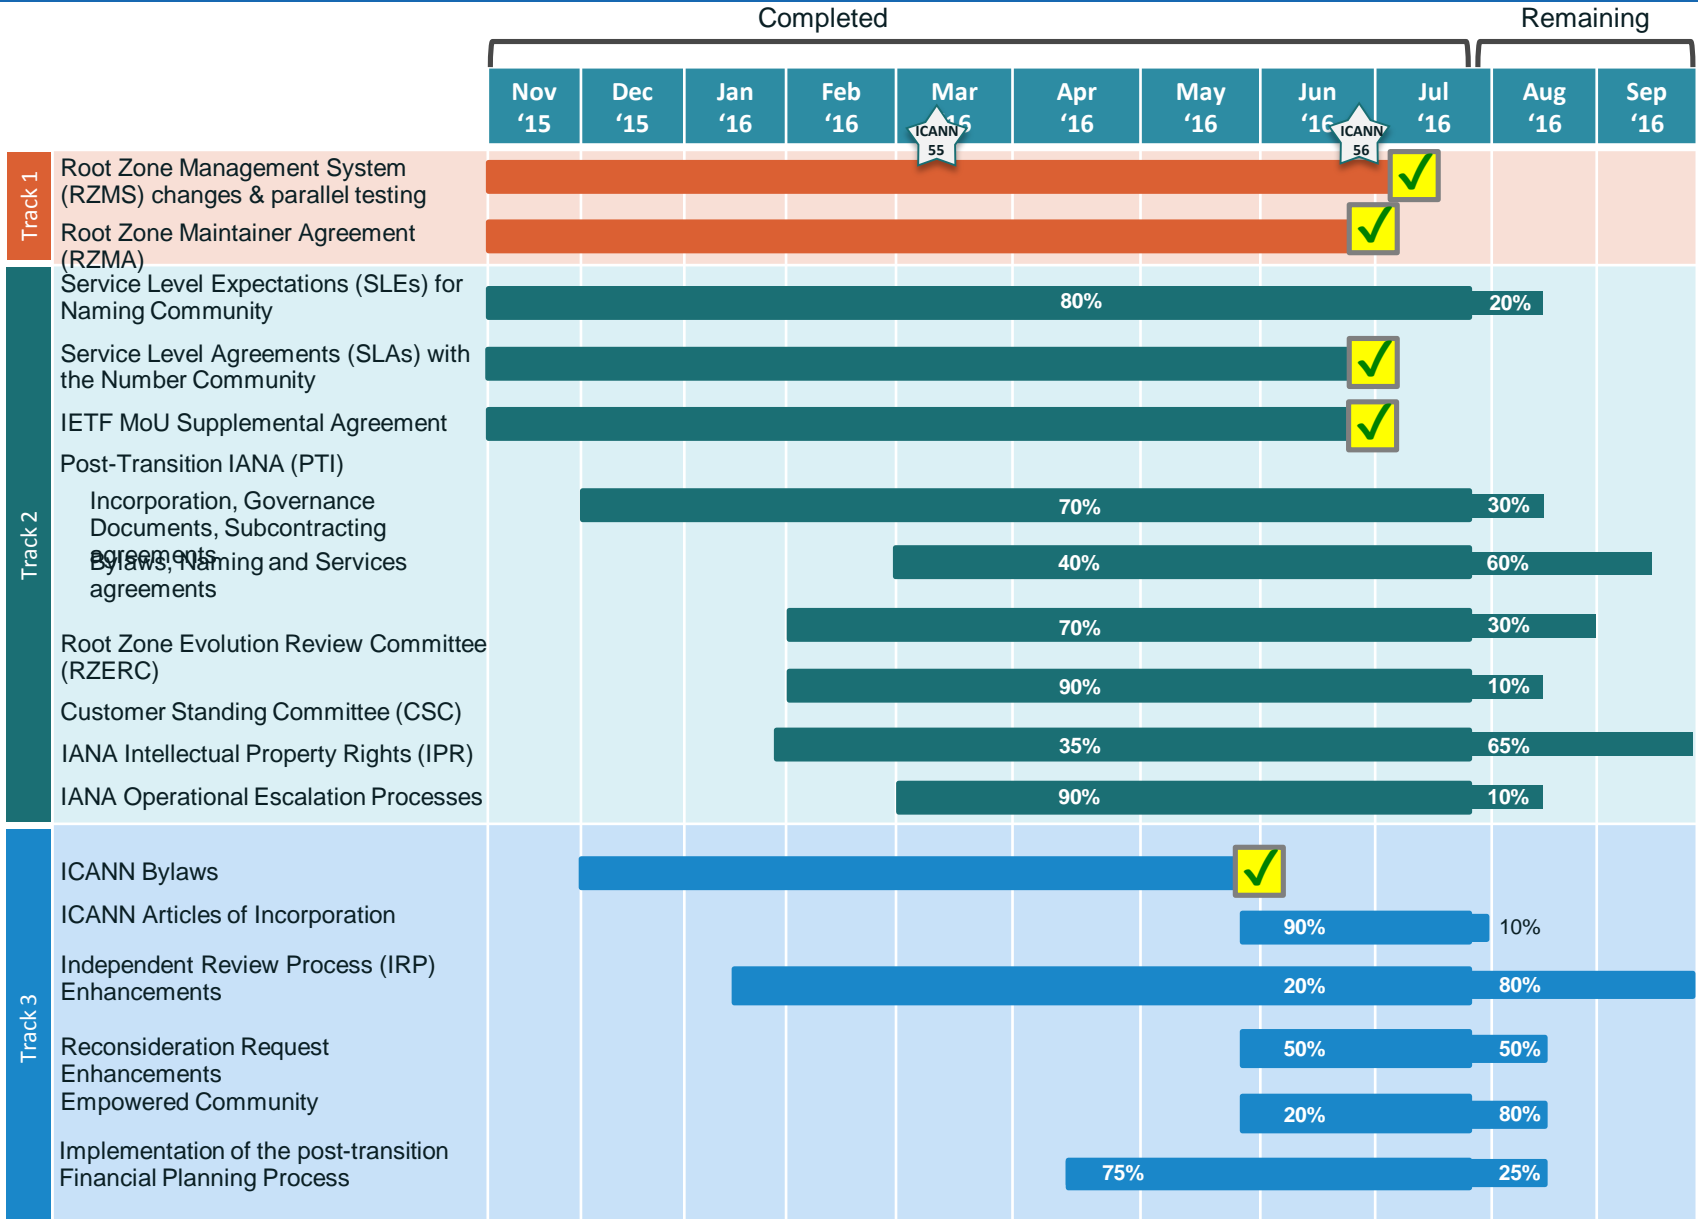

Overall % Complete

74%

Status Update


RZMS, RZMA & Names SLEs

Status As Of Date:

07/26/16

Project	Description	Plan Completion Date	Status	% Complete
RZMS changes to remove RZA role and support parallel testing	Remove NTIA's authorization process from RZMS (code changes for ICANN and Verisign, and parallel testing).	09/30/16 08/15/16 07/06/16		100%
Names SLEs (SLEs for Naming Community)	RZMS code changes to accommodate new SLEs, development of aggregation tool and dashboard reporting of SLAs, and setting of initial SLAs.	09/30/16 08/15/16		80%
RZMA (Agreement with Root Zone Maintainer)	Completion of draft RZMA.	01/31/16 / 02/29/16 04/15/16 / 04/30/16 05/15/16 / 05/31/16/ 06/30/16		100%

Key Dates:

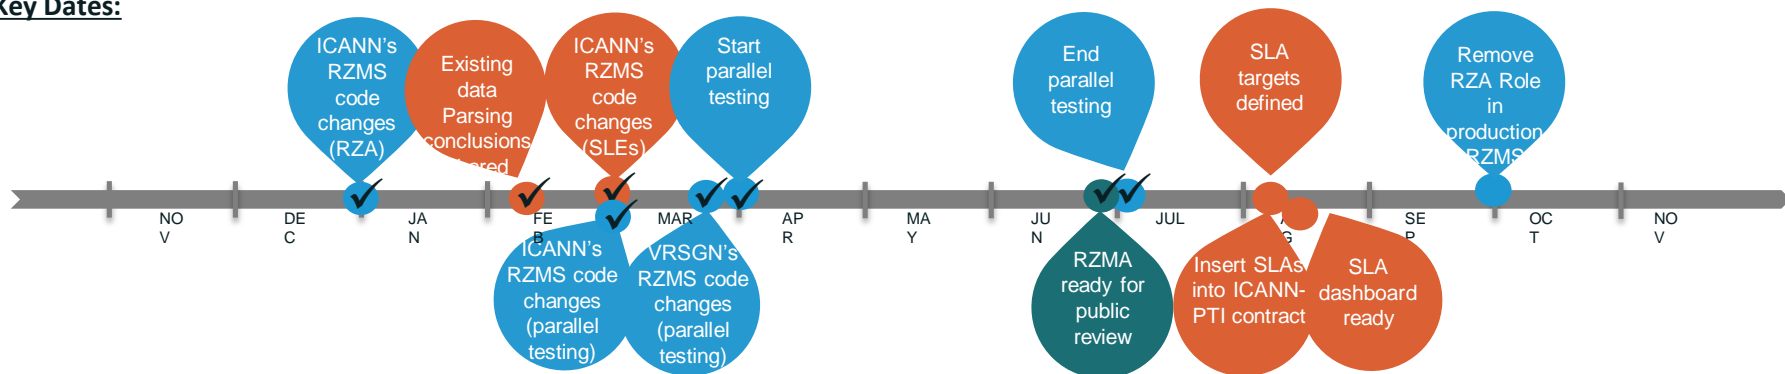

Project Updates:

- ✓ Shared proposed Name SLE performance targets with the CWG.
- ✓ Demo beta version of the reporting dashboard to CWG.

Upcoming Activities:

- Continue discussions with Names SLEs work group to finalize Name SLE performance targets.

Open Items:

- On-track
- Behind schedule, but recovery still possible
- Not started
- Target will be missed

DRAFT for Discussion

* All dates are estimates | 6

RIRs SLAs & IETF MoU Supplemental Agreement


Status As Of Date:

07/26/16

Project	Description	Plan Completion Date*	Status	% Complete
RIRs SLAs (Service Level Agreement with the Number Community)	Completion of draft agreement, including SLAs with RIRs, and operationalization of SLAs.	06/30/16		100%
IETF MoU Supplemental Agreement	Completion of draft ICANN-IETF MoU Supplemental Agreement.	06/30/16		100%

* Completion Date dependent on USG's approval of proposals

Key Dates:

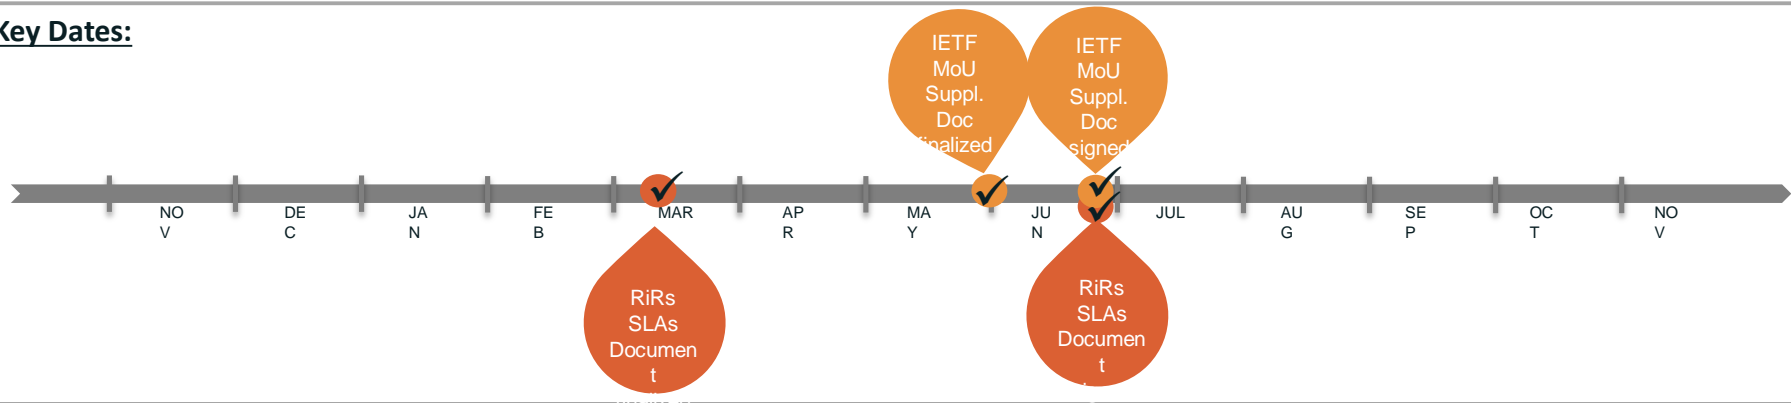

Project Updates:

- RIR SLA document signed.
- IETF MoU document signed.

Upcoming activities:

Open Items:



DRAFT for Discussion



On-track



Behind schedule, but recovery still possible



Not started




Target will be missed

* All dates are estimates | 7

Project	Description	Plan Completion Date	Status	% Complete
PTI Incorporation, Governance Documents, Subcontracting agreements	Formation of PTI entity: legal formation (incorporation of affiliate), governance documents). Numbers and Protocol Parameters subcontracting agreements drafting.	09/30/16 08/15/16		70%
PTI Naming and Services Agreements	PTI Naming and Services Agreements drafting, public comment period and board approval (Naming function contract, Inter-company agreement)	09/15/16		40%

Key Dates:

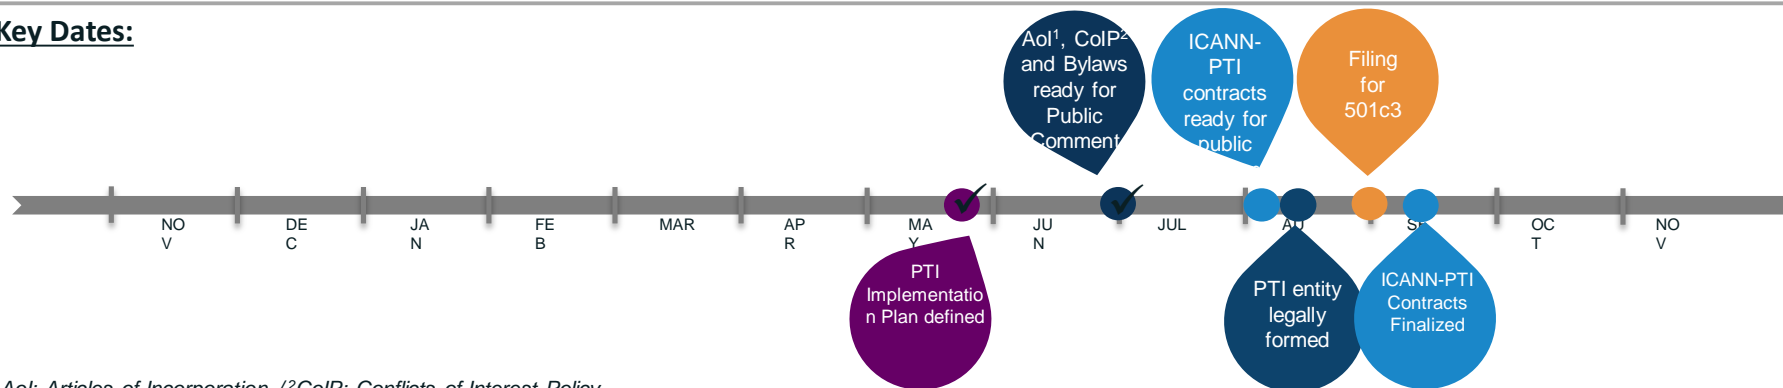

¹ Aol: Articles of Incorporation /²ColP: Conflicts of Interest Policy

Project Updates:

- ✓ Community reviewing Naming function agreement, Numbers and Protocol Parameters subcontracting agreement, and services agreement headers.
- ✓ CWG discussing PTI Bylaws, Articles of Incorporation and governance documents.

Upcoming activities:

- Staff analysis of revised Aol public comments.
- Continue review of agreements with the community.
- Share 1st draft of services agreement with the community.

Open Items:

Open Items:


IPR, RZERC, CSC & Escalation Processes

Status As Of Date:

07/26/16

Project	Description	Plan Completion Date	Status	% Complete
IANA IPR	Transfer of IANA IPR to a independent trust.	9/30/16		35%
RZERC <i>(Root Zone Evolution Review Committee)</i>	Formation of committee to advise ICANN Board on RZMS architectural and operational changes.	09/30/16 / 08/15/16 08/31/16		70%
CSC <i>(Customer Service Standing Committee)</i>	Formation of committee to monitor PTI performance.	09/30/16 08/15/16		90%
Escalation Processes	Updating of existing IANA operational complaint and escalation processes.	09/30/16 08/15/16		90%

Key Dates:

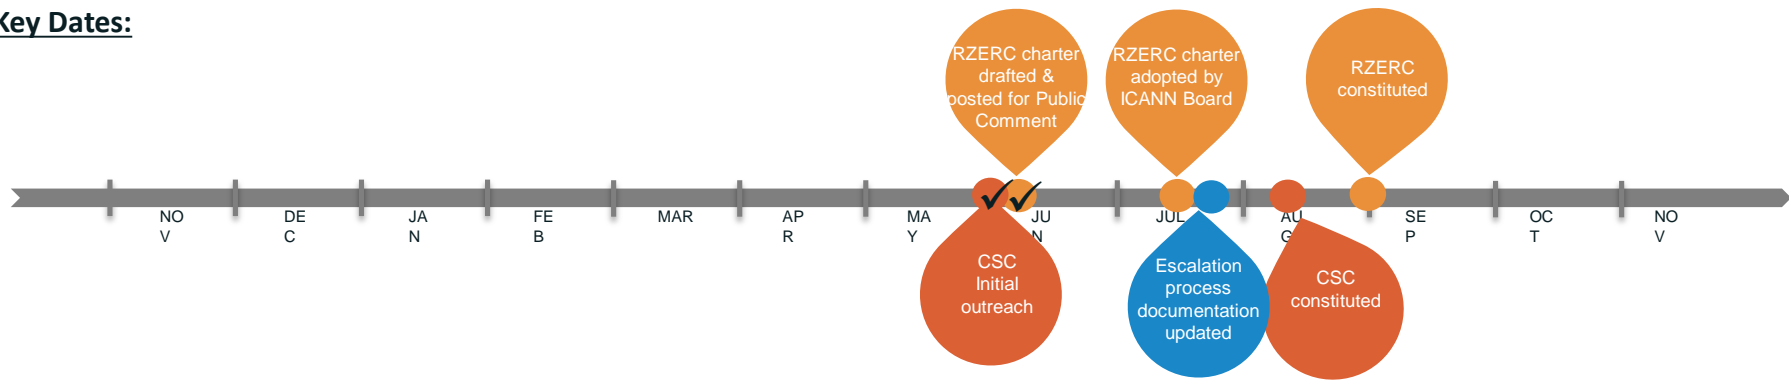

Project Updates:

- ✓ Finalizing analysis of public comments and revising RZERC charter based on comments.

Upcoming Activities:

- ICANN to send request for representatives to the RZERC to appointing organizations.
- ICANN Board approval of RZERC charter.
- Send CSC candidates to gNSO/ccNSO.
- Finalize escalation processes documentation.

Open Items:



DRAFT for Discussion

- On-track
- Behind schedule, but recovery still possible
- Not started
- Target will be missed

* All dates are estimates | 9


Enhancing ICANN's Accountability

Status As Of Date:

07/26/16

Project	Description	Plan Completion Date	Status	% Complete
ICANN's Bylaws	Updating of ICANN Bylaws.	06/09/16 05/27/16		100%
ICANN's Articles of Incorporation (Aol)	Updating of ICANN Articles of Incorporation	07/31/16		90%
IRP Enhancements	Implement enhancements to Independent Review Process.	09/30/16 - 08/15/16 09/30/16		20%
RR Enhancements	Implement enhancements to ICANN's reconsideration request process.	09/30/16 08/15/16		50%
Empowered Community Support Mechanisms	Implement processes and mechanisms in support of the empowered community.	09/30/16 08/15/16		20%
Financial Planning Process Updates	ICANN caretaker budget, PTI caretaker budget and PTI budget.	08/15/16		75%

Key Dates:

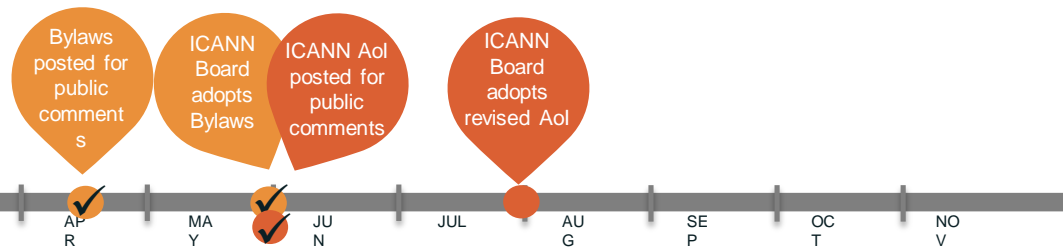

Project Updates:

- ✓ Finalizing analysis of public comments and revised Aol.
- ✓ Updating Request for Reconsideration process documentation.
- ✓ Consulted with the DT-O on a tentative financial planning process and timeline, including a community engagement plan.

Upcoming Activities:

- Post staff analysis and revised Aol.
- ICANN board adoption of revised Aol.
- Finalize Request for Reconsideration process documentation.
- Finalize financial planning process.

Open Items:



DRAFT for Discussion


- On-track
- Behind schedule, but recovery still possible
- Not started
- Target will be missed

* All dates are estimates | 10



Appendix High-Level Project Plans

RZMS & SLEs for Naming Community

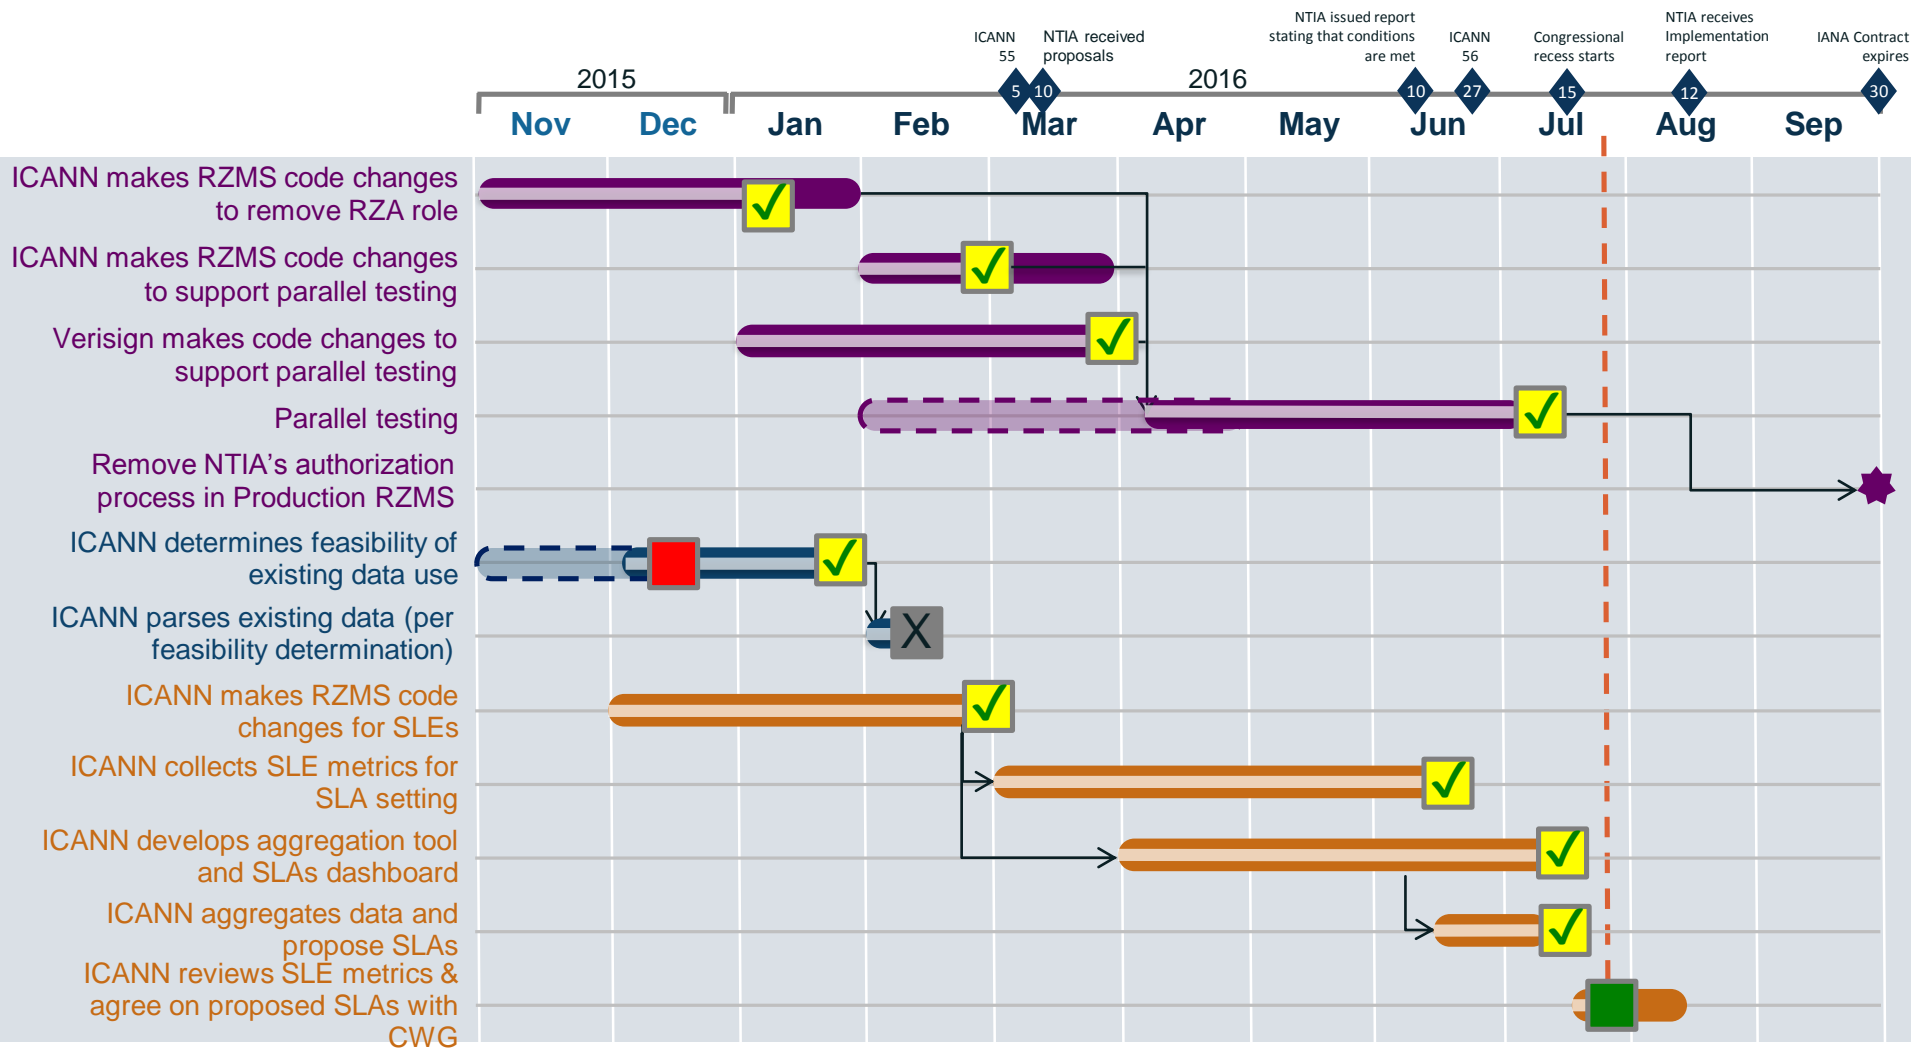


Project Updates:

- ✓ Shared proposed Name SLE performance targets with the CWG.
- ✓ Demo beta version of reporting dashboard to the CWG.

Upcoming Activities:

- Continue discussions with Names SLEs work group to finalize performance targets.


Open Items:

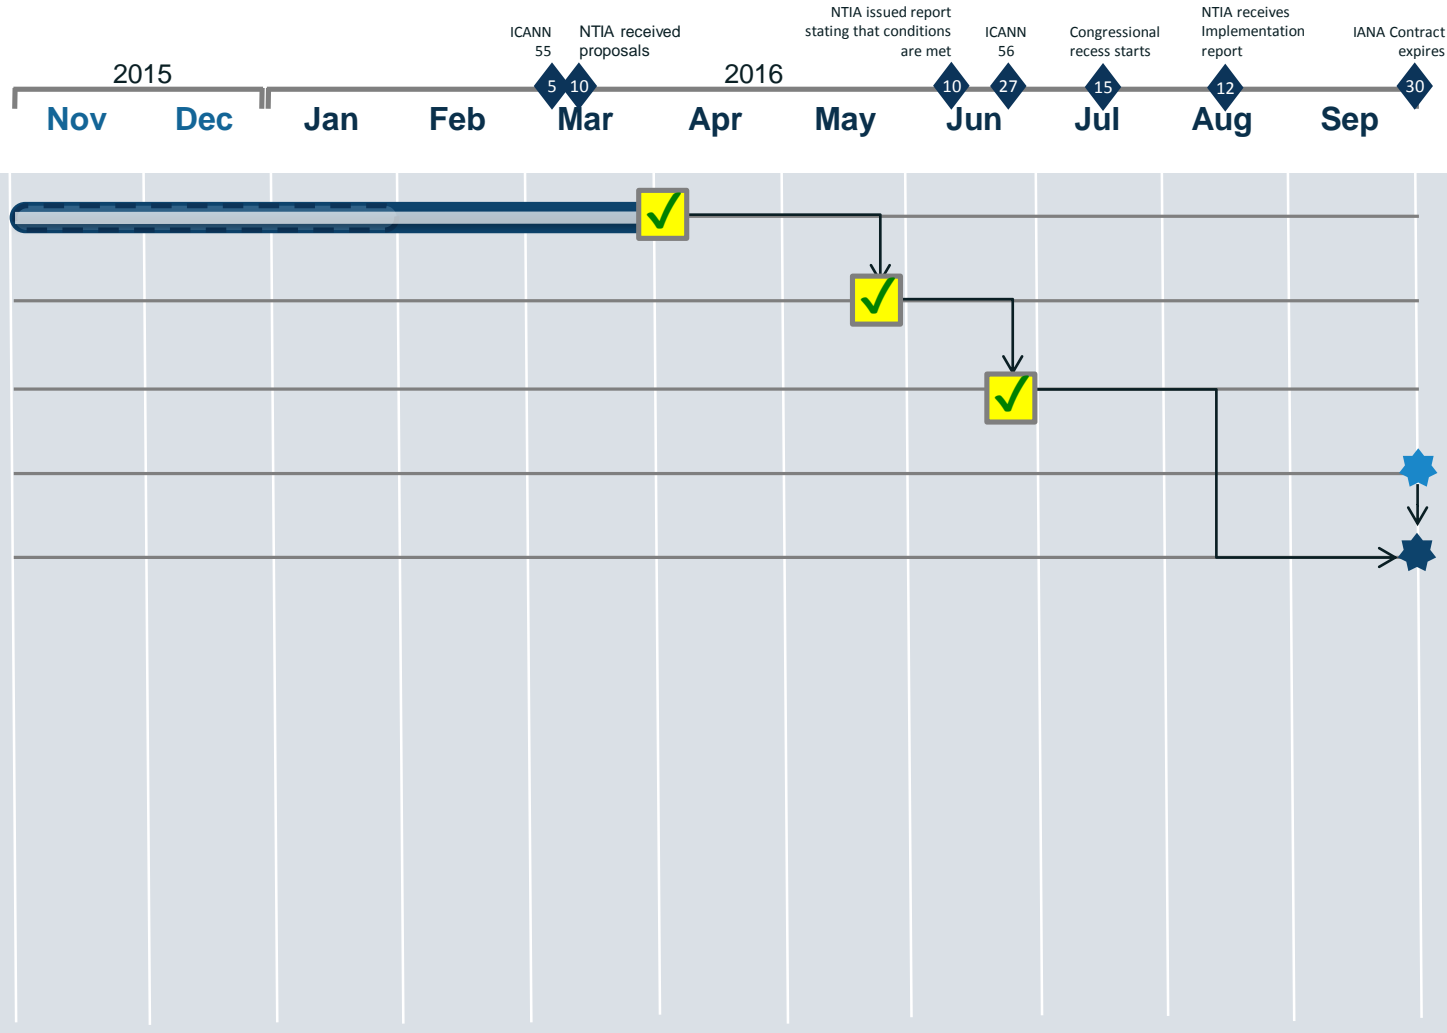

Project Updates:
 ✓ Signed the RIR SLA document.

Upcoming Activities:

Open Items:

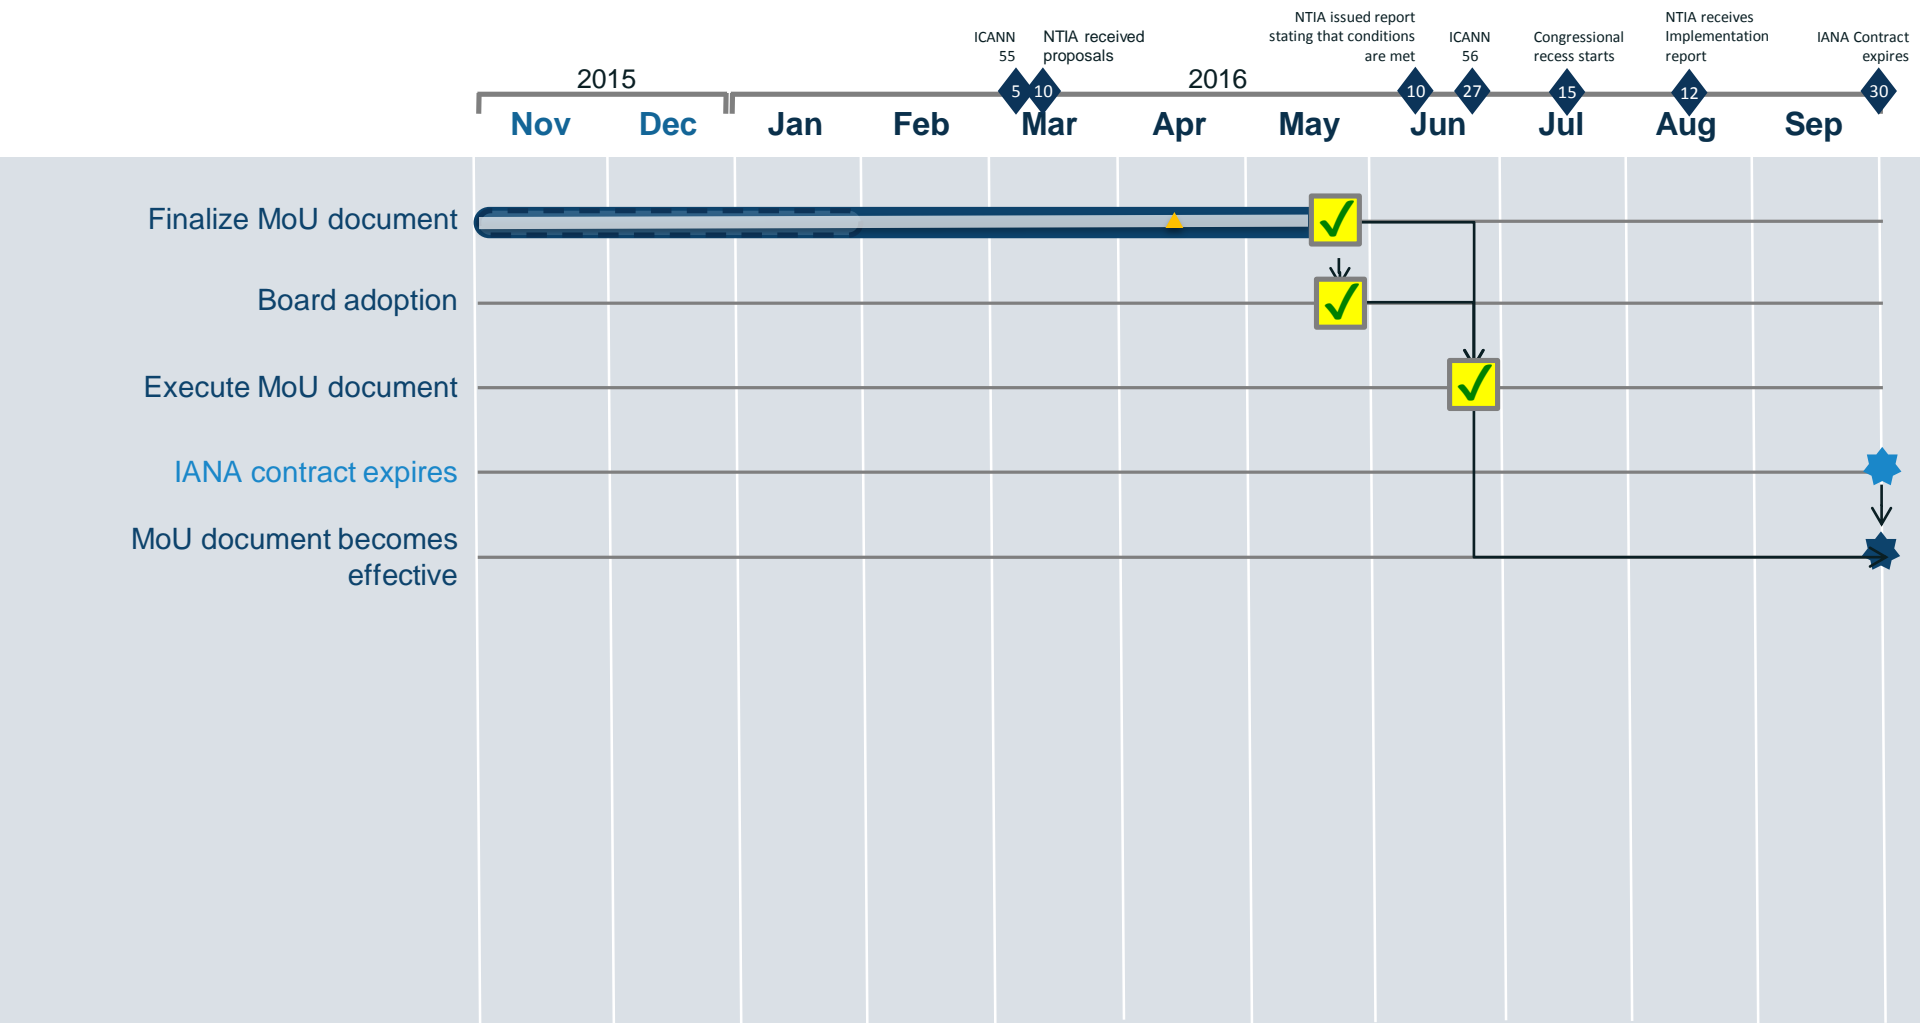

Project Updates:
 ✓ Signed the IETF MoU document.


Upcoming Activities:

Open Items:

Post-Transition IANA (PTI)

% Complete  60%

Status: on track

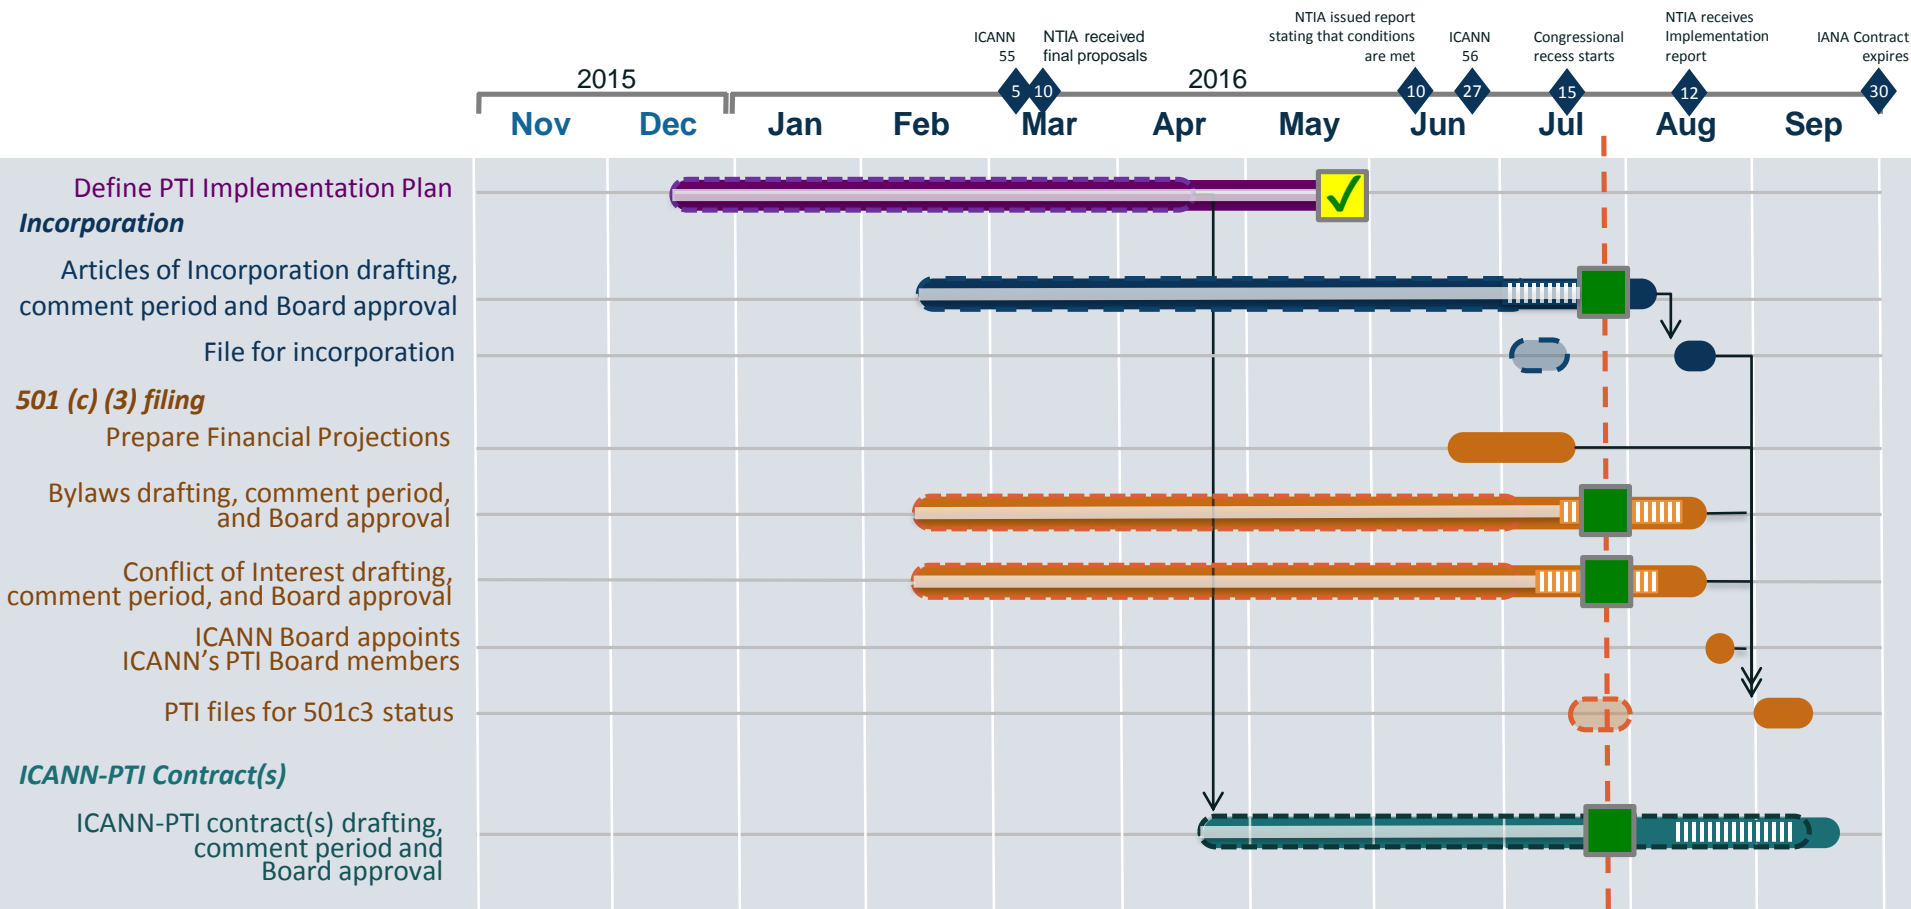

¹ Dependency on performance targets being defined by mid-July 2016 under Names SLEs project to finalize Names contract


Project Updates:

- ✓ Community reviewing Naming function agreement, Numbers and Protocol Parameters subcontracting agreement, and services agreement headers.
- ✓ CWG discussing PTI Bylaws, Articles of Incorporation and governance documents.

Upcoming Activities:

- Staff analysis of revised AoI public comments.
- Continue review of agreements with the community.
- Share 1st draft of services agreement with the community.

Open Items:

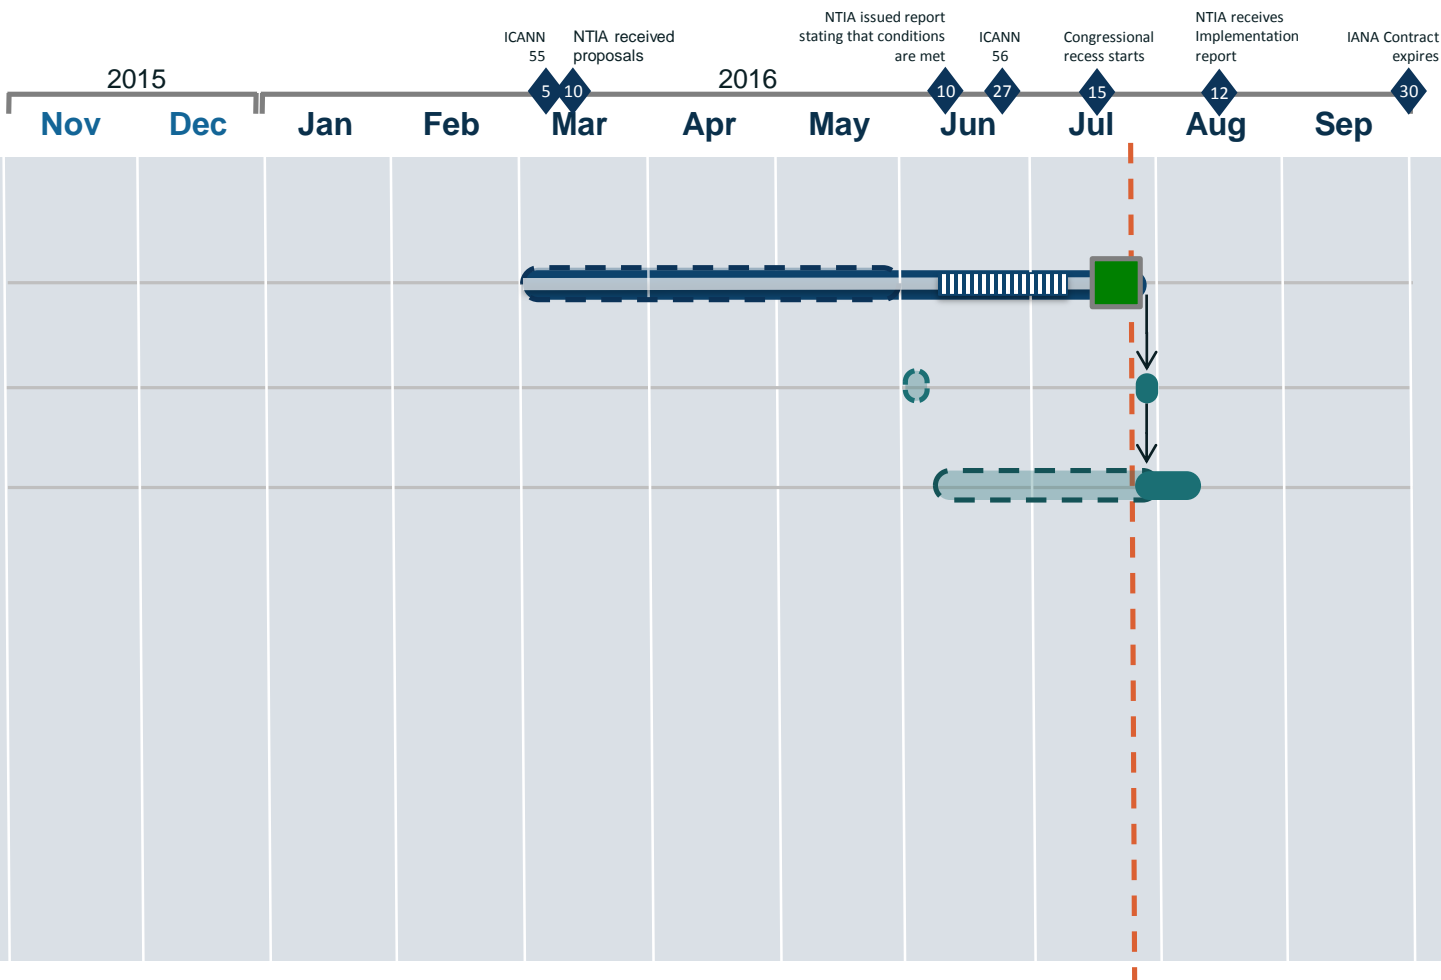



Project Updates:

- ✓ Finalizing analysis of public comments and revising RZERC charter.

Upcoming Activities:

- ICANN to send request for representatives to the RZERC to appointing organizations.
- ICANN Board approval of RZERC charter.

Open Items:

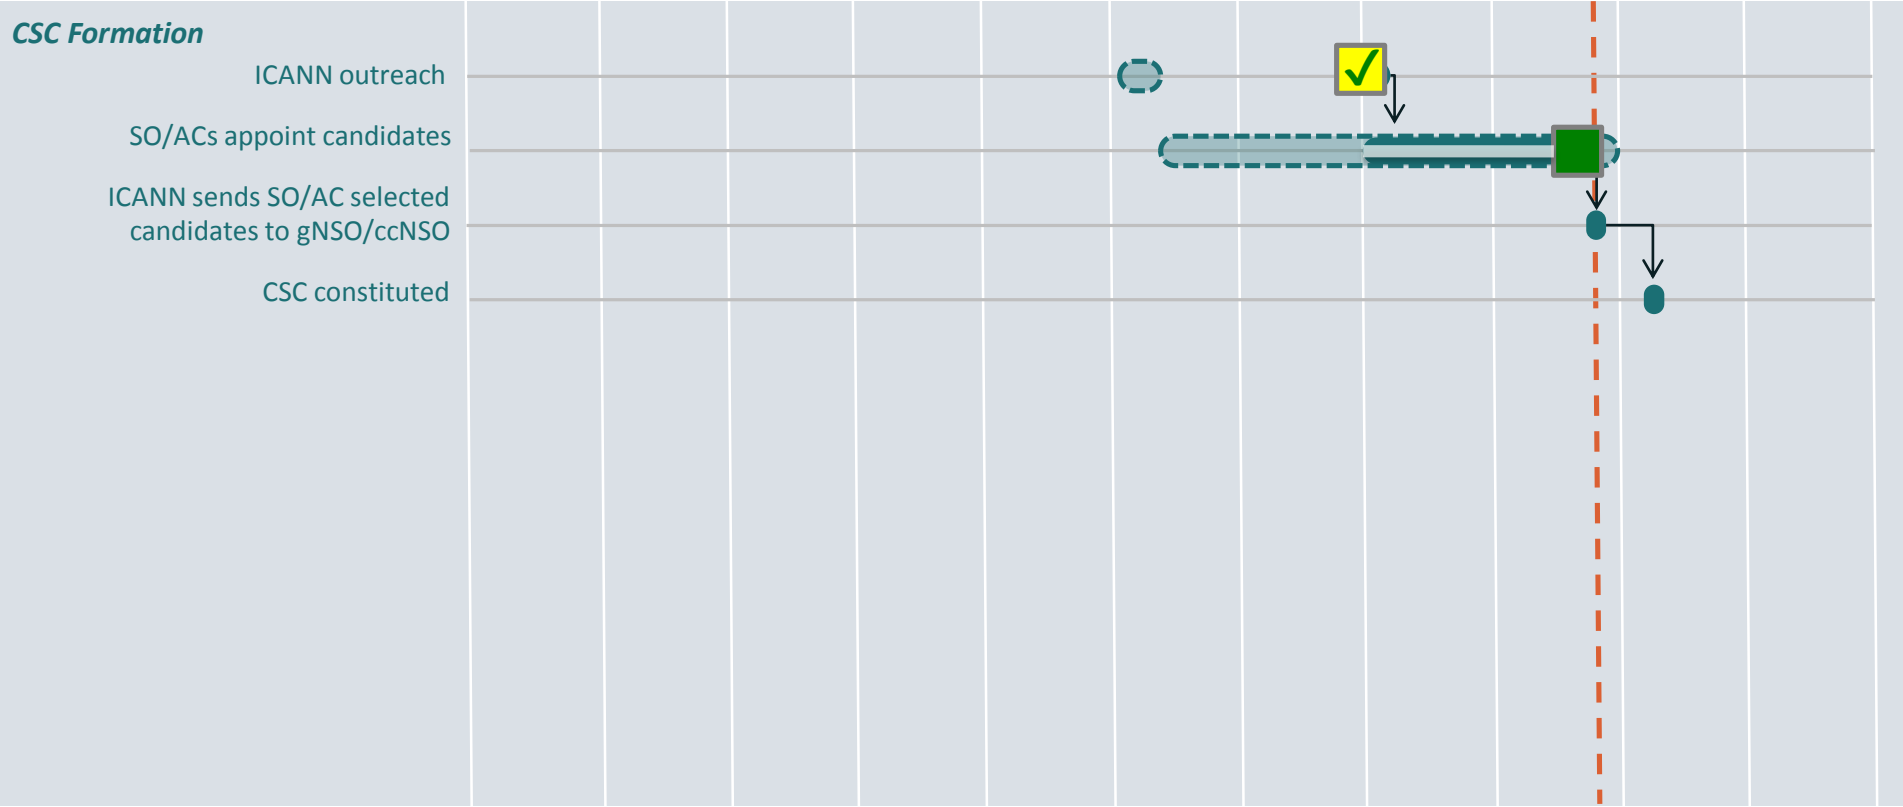

Project Updates:
 ✓ Appointing organizations submitted candidates.

Upcoming Activities:
 ▪ Send selected SO/AC candidates to gNSO/ccNSO.


Open Items:



DRAFT for Discussion

-  Baseline
-  Current Plan
-  CSC Charter activity
-  CSC Constitution activities
-  Operationalization activities

* Timeframes are estimates | 17

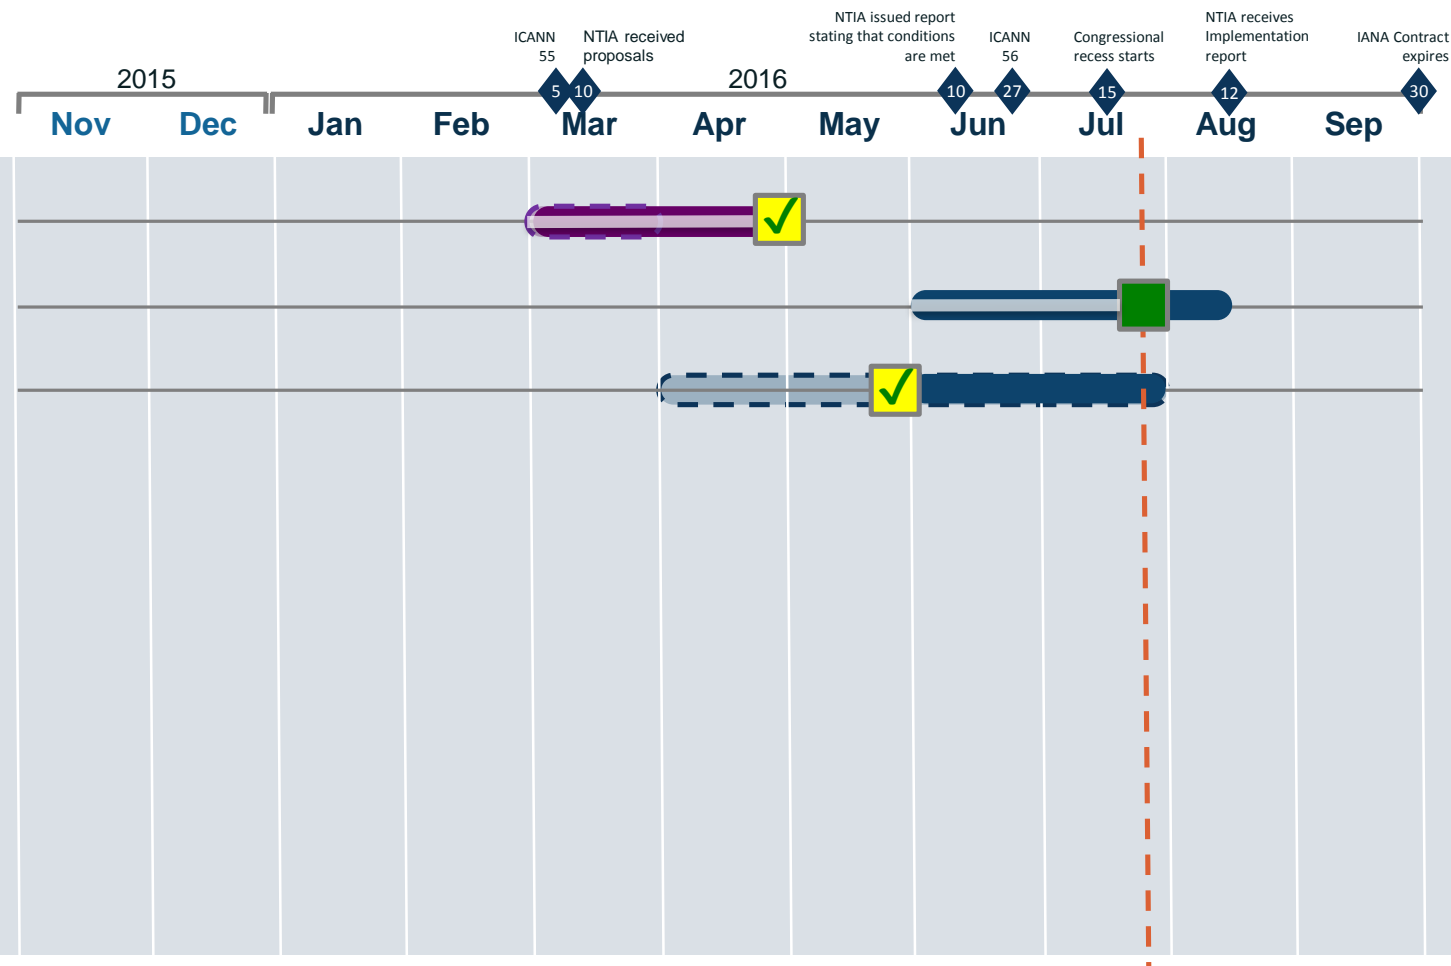


Project Updates:
 ✓ Escalation processes documentation being updated.

Upcoming Activities:

- Finalize escalation processes documentation.

Open Items:

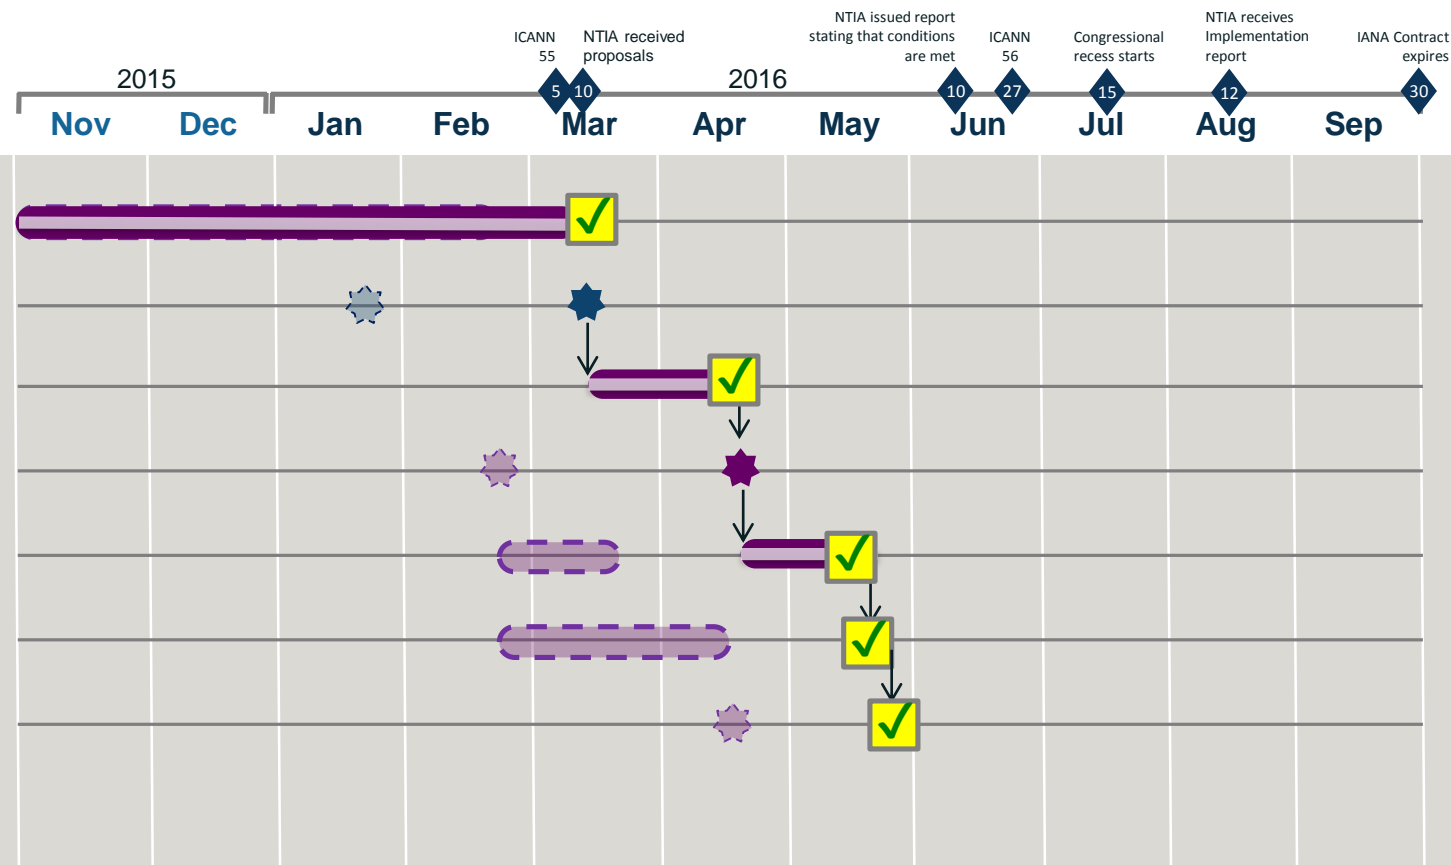

Project Updates:

Upcoming Activities:


Open Items:



DRAFT for Discussion

- Baseline
- Current Plan
- Bylaws activity
- USG activity

* Timeframes are estimates | 19

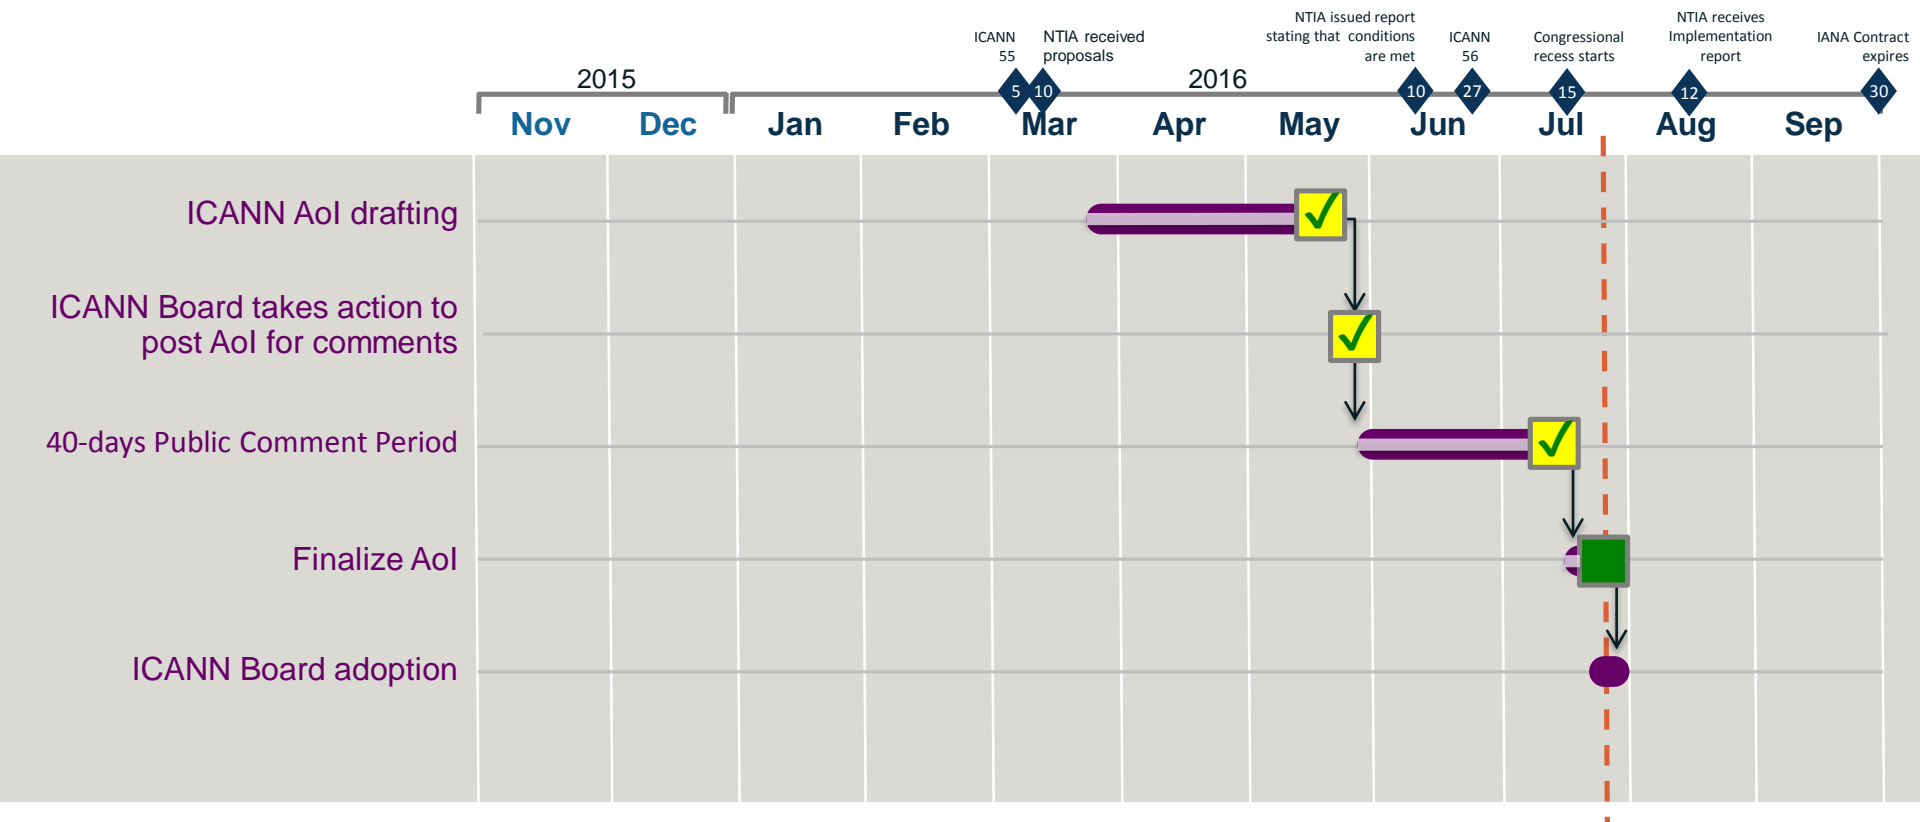

Project Updates:

- ✓ Finalizing analysis of public comments and revised Aol.

Upcoming Activities:


- Post staff analysis and revised Aol.
- ICANN board adoption of revised Aol.

Open Items:

Request For Reconsideration (RR) Enhancements

% Complete  50%

Status: **On-track**

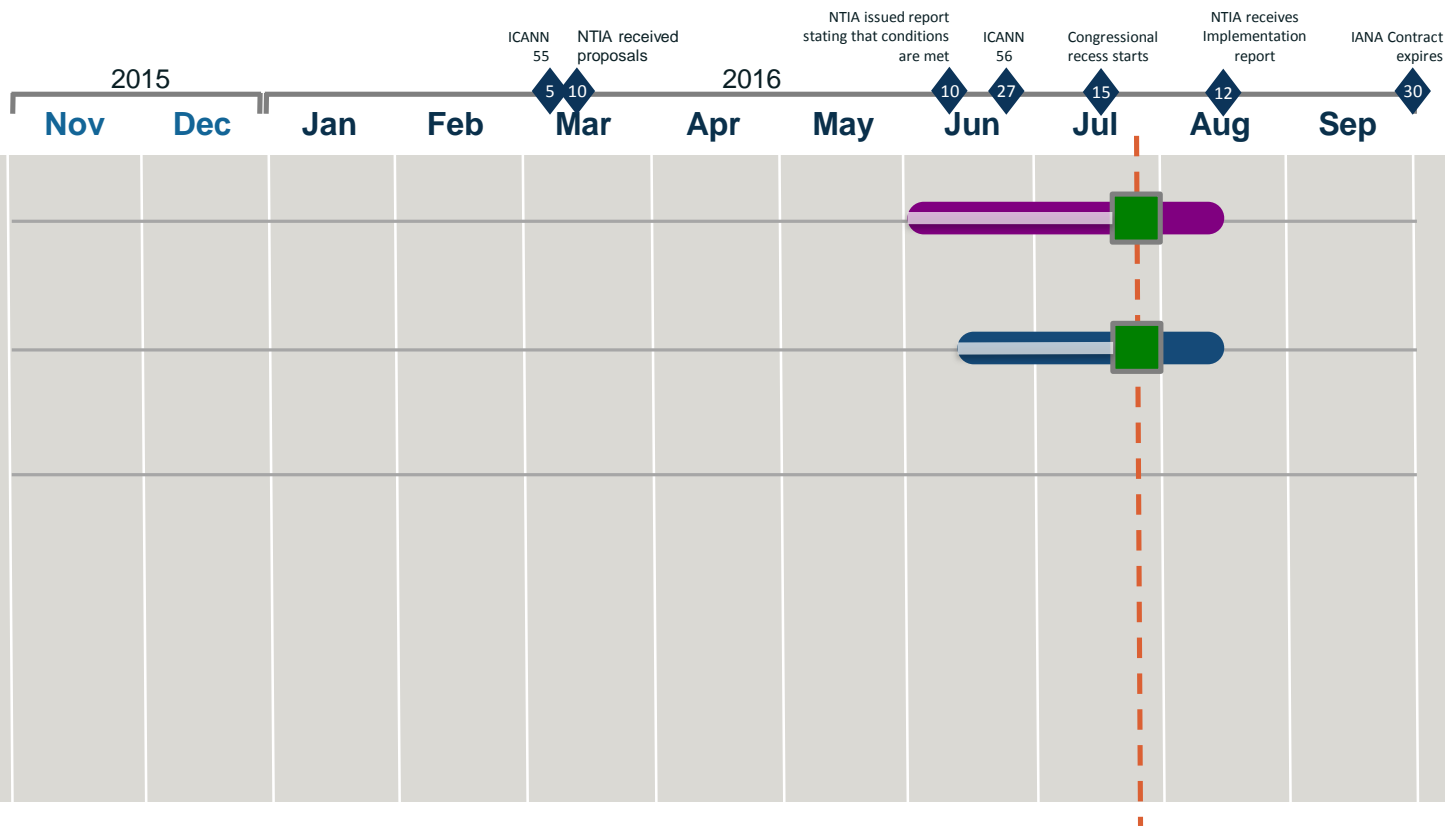

Project Updates:

- ✓ Updating Request for Reconsideration process documentation.

Upcoming Activities:

- Finalize Request for Reconsideration process documentation.

Open Items:




DRAFT for Discussion

--- Baseline
 — Current Plan

■ RR activities

* Timeframes are estimates | 21

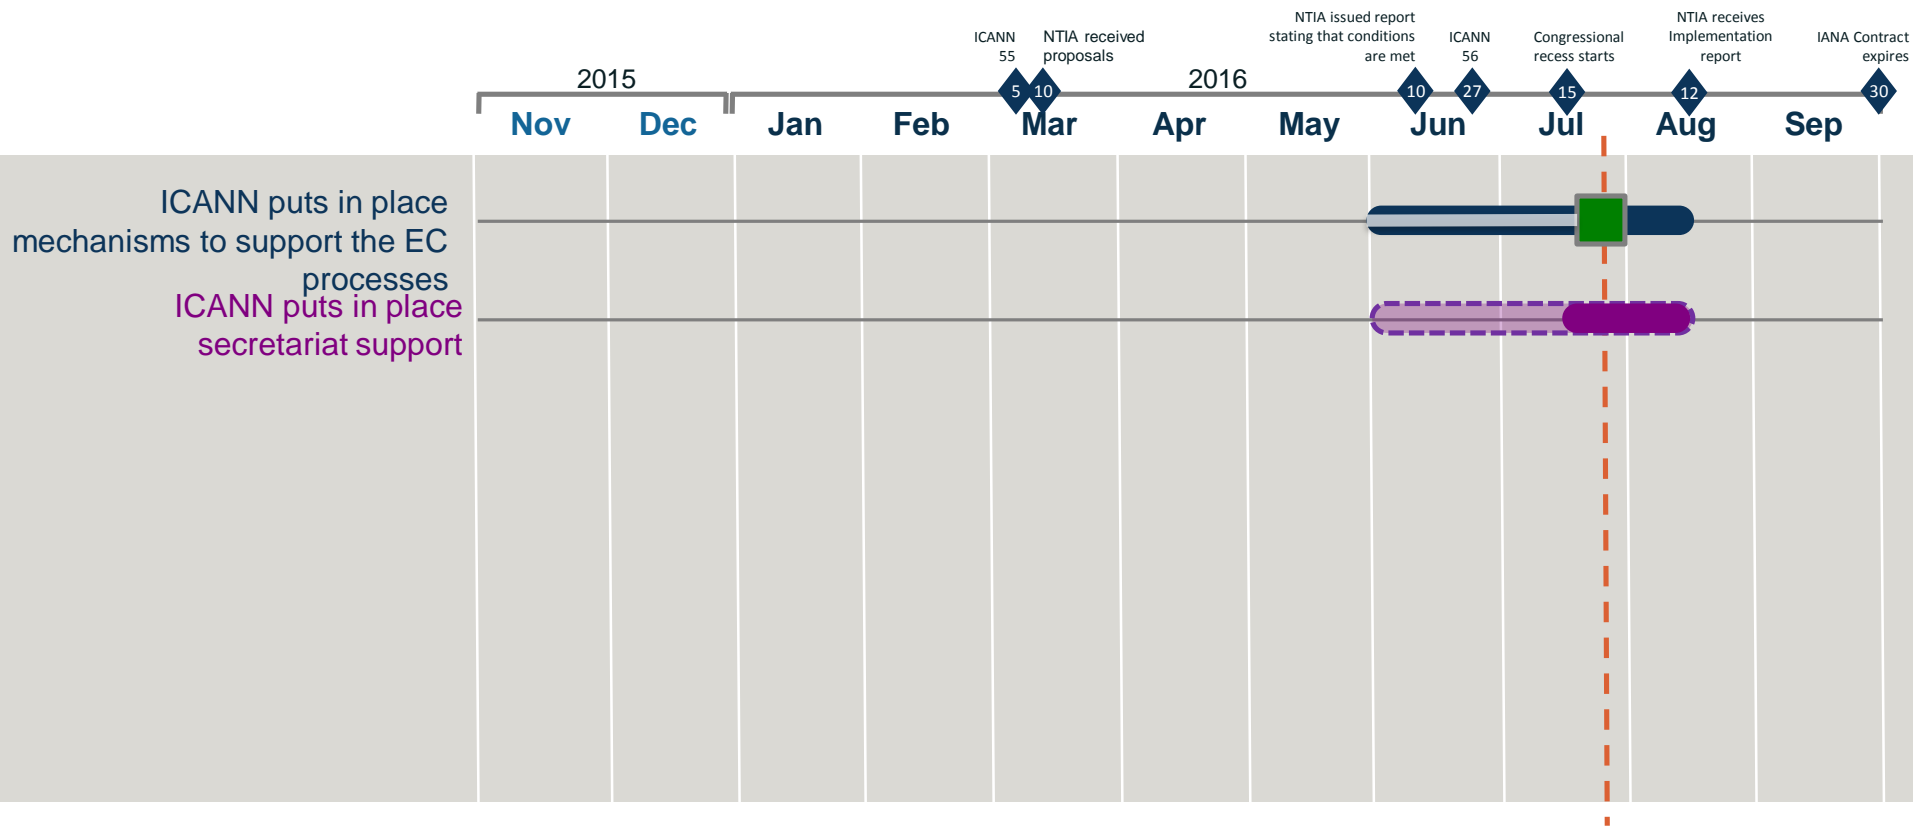


Project Updates:

- Identified items needed to support the Empowered Community.

Upcoming Activities:

Open Items:

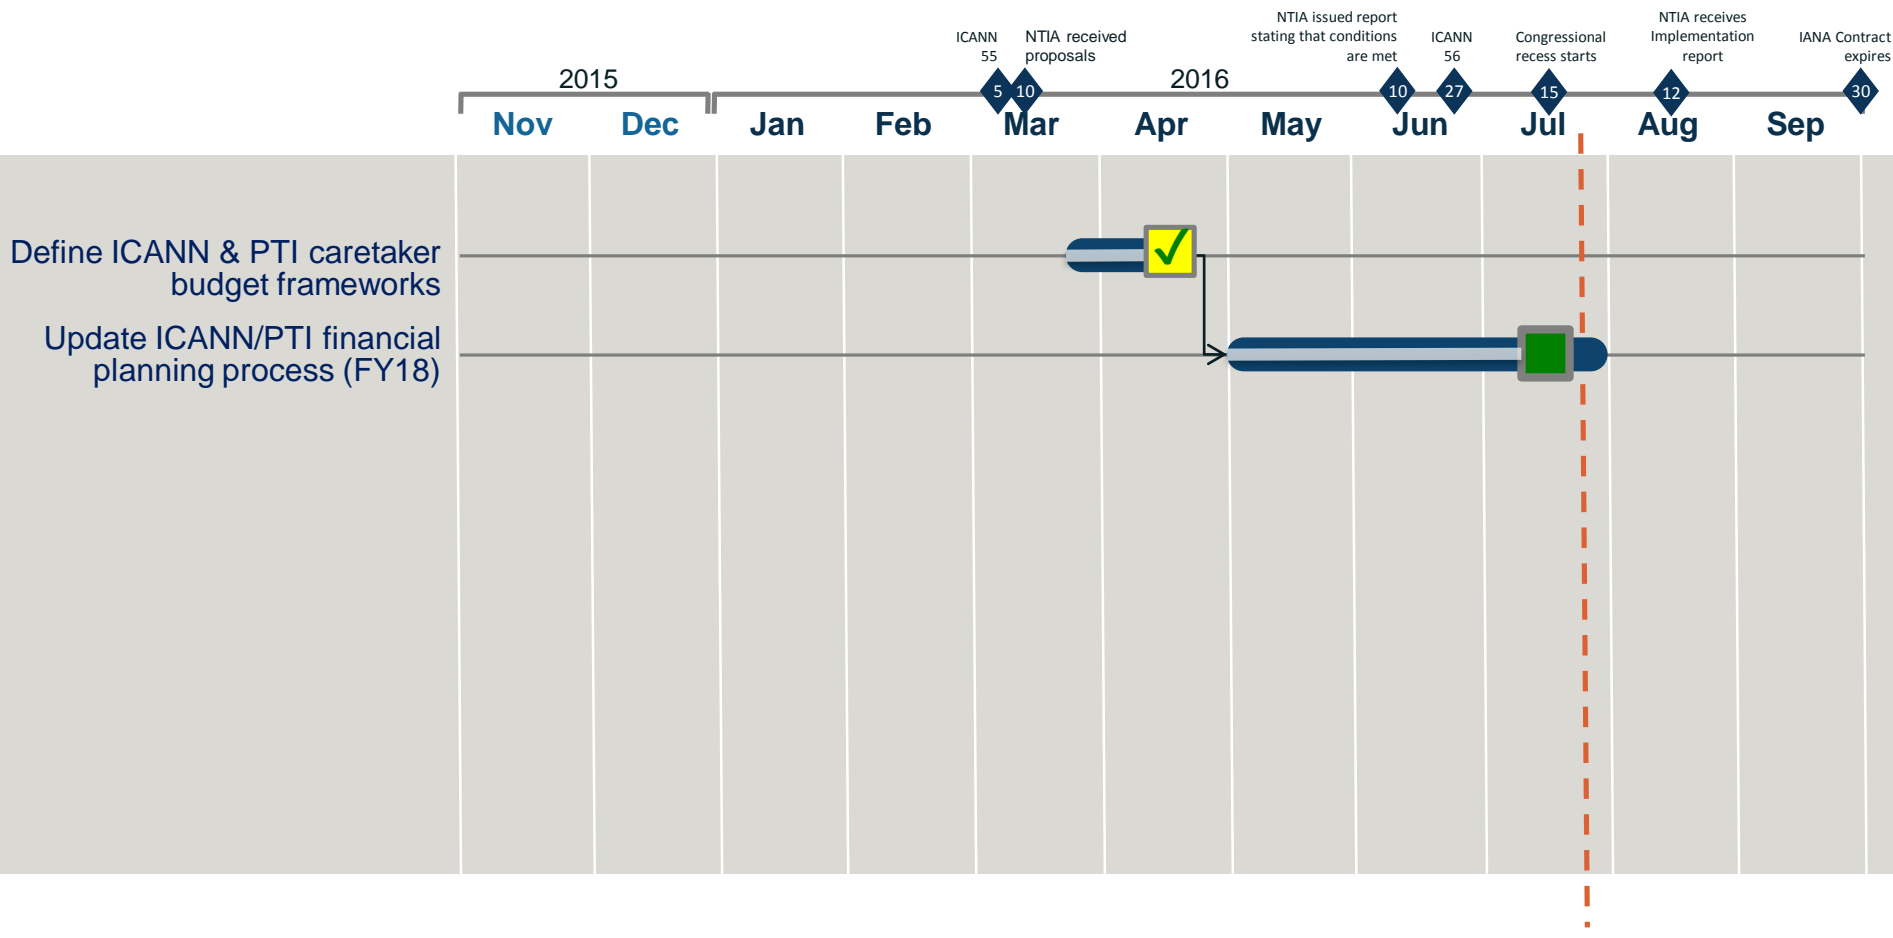

Project Updates:

- ✓ Consulted with the DT-O on a tentative financial planning process and timeline, including a community engagement plan.

Upcoming Activities:

- Finalize financial planning process.

Open Items:
