

EPDP - Temporary Specification for gTLD Registration Data

Fact sheet as of: 28-Feb-2019

Overview:

Following the adoption by the ICANN Board of a temporary specification on gTLD Registration Data to enable contracted parties to continue to comply with existing ICANN contractual requirements and with community-developed policies as they relate to WHOIS, while also complying with the European Union's General Data Protection Regulation (GDPR), a one-year policy development process is required to be initiated to confirm whether or not the temporary specification should become a consensus policy.

Wiki Page: [EPDP Wiki Home Page](#)
Email Archive: <https://mm.icann.org/pipermail/epdp-dt/>
EPDP Input Archive: NA

Chair: Kurt Prtiz
Vice-Chair(s): Rafik Dammak
Subteam Chair(s): N/A


EPDP Status

Start Date: 27-Jun-2018 **EPDP Duration to Date:** 8 Months
Expected Completion*: 24-May-2019 **Total Expected Duration:** 11 Months



*Note the Expected Completion date is based on the Temporary Specification expiry date of 24 May 2019. Milestones and scheduled meetings for this status report do not include, at this time, the second phase of the EPDP's charter requirement to also deliberate policy around access to non-public registration data. It's not expected to begin until gating questions have been answered and at least the delivery of the Initial Report for public comment.

Section I: Meeting Stats

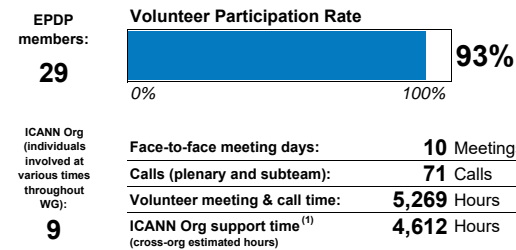

⁽¹⁾ Does not include time for Executives, Legal, IT Personnel and Other Organizational Support

Section II: Financial Resources

Direct Costs (1)	FY19 Approved Budget	FY19 Budget Spent to Date(3)	Committed FY19 Services(4)	Remaining FY19 Budget	Actual Expenses: WG to Date	Total Spent and Committed to Date
EPDP Professional Services	\$ 330,000	\$ 201,497	\$ 48,782	\$ 79,721	\$ 201,497	\$ 250,279
N/A	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
Travel, Facility, & Catering	\$ 260,000	\$ 181,027	\$ -	\$ 78,973	\$ 181,027	\$ 181,027
Total	\$ 590,000	\$ 382,523	\$ 48,782	\$ 158,695	\$ 382,523	\$ 431,305

⁽¹⁾ Excludes ICANN Organization and overhead allocation.

⁽³⁾ Based on the most recent month end financials (may not include recent expenditures). Represents expenses incurred since inception of work.

⁽²⁾ blank

⁽⁴⁾ Professional services includes services from signed contracts to be provided or invoiced; travel includes upcoming scheduled meetings.

Section III: Milestones

Project Management

10% of total effort



- Adopt charter
- Adopt work plan
- Assemble EPDP Team
- Prepare work products
- Confirm Project Plan
- Develop EPDP Fact Sheet

EPDP Deliberations

50% of total effort



- Temp Spec Triage
- Document Terms, Purposes, and Processing Activities
- Other Consensus Policies

Initial Report

20% of total effort



- Assemble initial conclusions
- Populate discussion papers with findings and potential recs.
- Consolidate interim recommendations and findings
- Build Draft Report for public comment
- Approve Draft Report for public comment
- Issue report for public comment

Final Report

20% of total effort



- Review public comment input received and incorporate as appropriate
- Determine consensus levels on interim recommendations
- Finalize Report
- Adopt final recommendations and report
- Send final report to GNSO Council

TOTAL:

100.00% Completed

