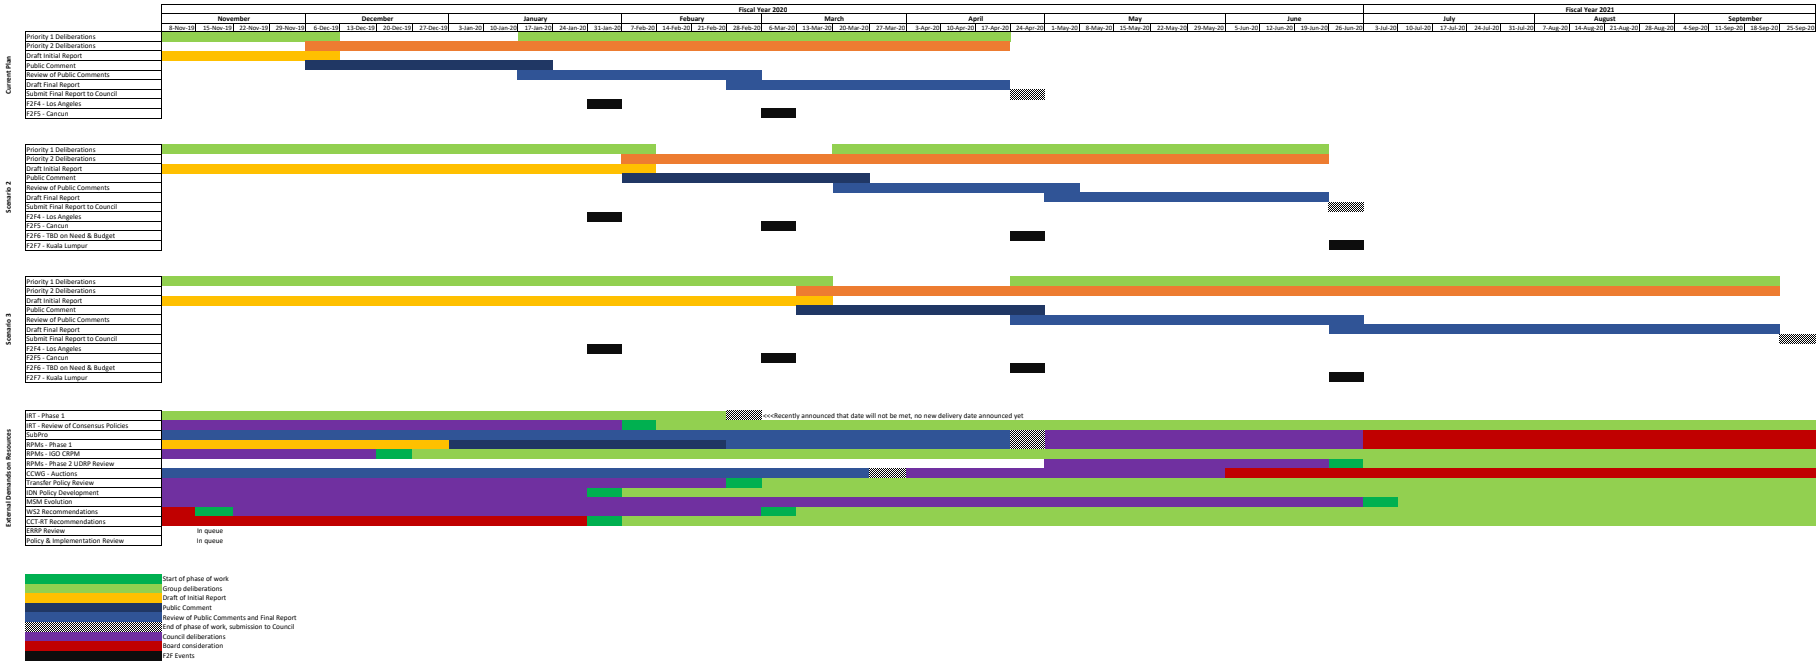
Fiscal Year 2020
Fiscal Year 2021
November
December
January
Febuary
March
April
May
June
July
August
September
8-Nov-19
15-Nov-19
22-Nov-19
29-Nov-19
6-Dec-19
13-Dec-19
20-Dec-19
27-Dec-19
3-Jan-20
10-Jan-20
17-Jan-20
24-Jan-20
31-Jan-20
7-Feb-20
14-Feb-20
21-Feb-20
28-Feb-20
6-Mar-20
13-Mar-20
20-Mar-20
27-Mar-20
3-Apr-20
10-Apr-20
17-Apr-20
24-Apr-20
1-May-20
8-May-20
15-May-20
22-May-20
29-May-20
5-Jun-20
12-Jun-20
19-Jun-20
26-Jun-20
3-Jul-20
10-Jul-20
17-Jul-20
24-Jul-20
31-Jul-20
7-Aug-20
14-Aug-20
21-Aug-20
28-Aug-20
4-Sep-20
11-Sep-20
18-Sep-20
25-Sep-20
Current Plan
Priority 1 Deliberations
Priority 2 Deliberations
Draft Initial Report
Public Comment
Review of Public Comments
Draft Final Report
Submit Final Report to Council
F2F4 - Los Angeles
F2F5 - Cancun
Scenario 2
Priority 1 Deliberations
Priority 2 Deliberations
Draft Initial Report
Public Comment
Review of Public Comments
Draft Final Report
Submit Final Report to Council
F2F4 - Los Angeles
F2F5 - Cancun
F2F6 - TBD on Need & Budget
F2F7 - Kuala Lumpur
Scenario 3
Priority 1 Deliberations
Priority 2 Deliberations
Draft Initial Report
Public Comment
Review of Public Comments
Draft Final Report
Submit Final Report to Council
F2F4 - Los Angeles
F2F5 - Cancun
F2F6 - TBD on Need & Budget
F2F7 - Kuala Lumpur
External Demands on Resources
IRT - Phase 1
<<Recently announced that date will not be met, no new delivery date announced yet
IRT - Review of Consensus Policies
SubPro
RPMs - Phase 1
RPMs - IGO CRPM
RPMs - Phase 2 UDRP Review
CCWG - Auctions
Transfer Policy Review
IDN Policy Development
MSM Evolution
WS2 Recommendations
CCT-RT Recommendations
ERRP Review
In queue
Policy & Implementation Review
In queue
Start of phase of work
Group deliberations
Draft of Initial Report
Public Comment
Review of Public Comments and Final Report
End of phase of work, submission to Council
Council deliberations
Board consideration
F2F Events
