	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
1	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
2	GNSO Portfolio Management Tool	3139d	03/04/19	03/13/31		34%		
3	RDDS - Program Track	2609d	03/04/19	03/01/29		44%		
4	EPDP: Standardized System for Access & Disclosure - Phase 2	2262d	07/01/20	03/01/29		34%		
17	EPDP: Legal vs. Natural + Feasibility of Unique Contacts of Registration Data - Phase 2A	890d	08/03/20	12/29/23		51%		
22	RDS2 Review Recommendations - Implementation	899d	07/23/20	01/02/24		100%		
30	IRT: Temporary Specification on gTLD Registration Data - Phase 1	1484d	03/04/19	11/07/24		58%		
35	Revised ICANN Procedure for Handling Whois Conflicts with Privacy Law	1330d	07/31/20	09/04/25		14%		
47	IRT: Privacy & Proxy Services Accreditation Issues	750d	08/16/21	06/28/24		50%		
49	IRT: Translation/Transliteration of gTLD Registration Data	750d	08/16/21	06/28/24		50%		
51	Registration Data Accuracy	1595d	07/12/21	08/20/27		32%		
62	RPM - Program Track	1677d	07/01/20	12/03/26		33%		
63	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 1 (URS, TMCH, Sunrise, Claims)	1043d	07/01/20	06/28/24		49%		
72	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 2 (UDRP)	1325d	11/05/21	12/03/26		21%		
79	gTLD - Program Track	1323d	07/01/20	07/25/25		47%		
80	CCWG: New gTLD Auction Proceeds	1043d	07/01/20	06/28/24		48%		
85	PDP: New gTLD Subsequent Procedures	1323d	07/01/20	07/25/25		51%		
91	GGP: Applicant Support (Placeholder awaiting plan)	352d	08/25/22	12/29/23		0%		
92	Closed Generics Facilitated Dialogue (Placeholder awaiting plan)	311d	04/22/22	06/30/23		0%		
93	Name Collision Analysis Project	783d	07/01/20	06/30/23		81%		
96	IDNs - Program Track	1803d	07/01/20	05/28/27		53%		
97	IDN Operational Working Group (Track 1)	480d	08/03/20	06/03/22		100%		
100	EPDP: IDNs (Track 2)	1723d	10/21/20	05/28/27		30%		
105	IDN GNSO Council Coordination w/ CCNSO Council (Track 3)	913d	07/01/20	12/29/23		70%		
107	Expiration - Program Track	1871d	10/01/20	12/02/27		10%		
108	PDP: Expired Domain Deletion Policy / Expired Registration Recovery Policy Policy Review	1871d	10/01/20	12/02/27		10%		
121	Transfers - Program Track	1912d	07/01/20	10/28/27		27%		
122	PDP: Transfer Policy Review	1912d	07/01/20	10/28/27		27%		
139	IGO - Program Track	992d	09/24/20	07/12/24		30%		
140	EPDP: Specific Curative Rights Protections for IGOs	992d	09/24/20	07/12/24		56%		
144	PDP: Curative Rights Protections for IGO/INGOs	442d	11/03/22	07/12/24		0%		
147	PDP: Protection of International Organization Names in All gTLDs (Remaining Acronyms)	442d	11/03/22	07/12/24		0%		
150	DNS_Abuse - Program Track	1195d	01/02/23	07/30/27		0%		
151	Track 2 - Issues that may benefit from education / communication / outreach	260d	01/02/23	12/29/23	342	0%		
152	Track 3 - Issues that may benefit from contractual negotiations between ICANN org and Contracted Parties	260d	01/01/24	12/27/24	151	0%	Planned	
153	Track 1 - Issues that may benefit from GNSO policy development	675d	12/27/24	07/30/27	124	0%	Planned	
162	Accountability - Program Track	1043d	07/01/20	06/28/24		42%		
163	Independent Review Process - Implementation Oversight Team	780d	07/01/20	06/27/23		50%		
166	Cross Community Working Group on Enhancing ICANN Accountability - WS2	550d	05/24/21	06/30/23		50%		
169	Geo Regions Review	783d	07/01/20	06/30/23		0%		
171	Multistakeholder Model Evolution	1043d	07/01/20	06/28/24		64%		
173	Reviews - Program Track	2792d	07/01/20	03/13/31		31%		
174	IANA Naming Function Review	226d	07/01/20	05/12/21		100%		
178	Registration Directory Service Review RT3	640d	09/29/28	03/13/31		0%		
183	Competition, Consumer Trust and Consumer Choice RT2	640d	08/09/27	01/18/30		0%		
188	Accountability and Transparency Review 3	1043d	07/01/20	06/28/24		64%		
191	Holistic Review - Pilot	1444d	11/30/20	06/11/26		37%		
198	Accountability and Transparency Review 4	620d	06/12/26	10/26/28		0%		
203	Security, Stability and Resiliency of the DNS #2	1044d	07/01/20	07/01/24		60%		
207	Security, Stability and Resiliency of the DNS #3	640d	09/29/28	03/13/31		0%		
212	CSC Effectiveness Review - 2021	525d	07/01/21	07/05/23		68%		
217	CSC Effectiveness Review - 2024	400d	08/01/24	02/11/26		0%		
222	GNSO Review RT3	680d	06/12/26	01/18/29		0%		
228	Operations - Program Track	1432d	06/01/20	11/25/25		50%		
229	Council Committee for Overseeing & Implementing Continuous Improvement	463d	06/16/21	03/24/23		61%		
234	Participant of Empowered Community	1382d	07/01/20	10/16/25		48%		
252	Participation on Customer Standing Committee	1394d	06/01/20	10/02/25		52%		
271	Participation on NomCom	1347d	09/01/20	10/29/25		46%		
281	Stakeholder Support - Registry Stakeholder Group	1304d	07/01/20	06/30/25		50%		
287	Stakeholder Support - Registrar Stakeholder Group	1304d	07/01/20	06/30/25		50%		
293	Stakeholder Support - NCSG/NCUC/NPOC	1304d	07/01/20	06/30/25		50%		
299	Stakeholder Support - CSG/BC/IPC/ISPCP	1304d	07/01/20	06/30/25		50%		
305	GNSO Council	1410d	07/01/20	11/25/25		48%		
306	GNSO Council - Monthly Meetings	1347d	09/01/20	10/29/25		46%		
312	GNSO Council - Leadership Meetings	1347d	09/01/20	10/29/25		46%		
318	GNSO Council - Action Items	1347d	09/01/20	10/29/25		46%		
324	GNSO Council - Small Teams	1385d	07/12/20	10/30/25		56%		
350	GNSO Standing Committee on Budget and Operations	1119d	11/02/20	02/13/25		40%		
371	GNSO Standing Selection Committee	1325d	10/28/20	11/25/25		42%		
407	GNSO Council - Strategic Planning Session	1163d	09/01/20	02/13/25		56%		
413	GNSO Elections - [PLACEHOLDER SECTION]							
417	ICANN Meeting Planning, Meeting, Respond to GAC Advice	1309d	07/01/20	07/07/25		48%		

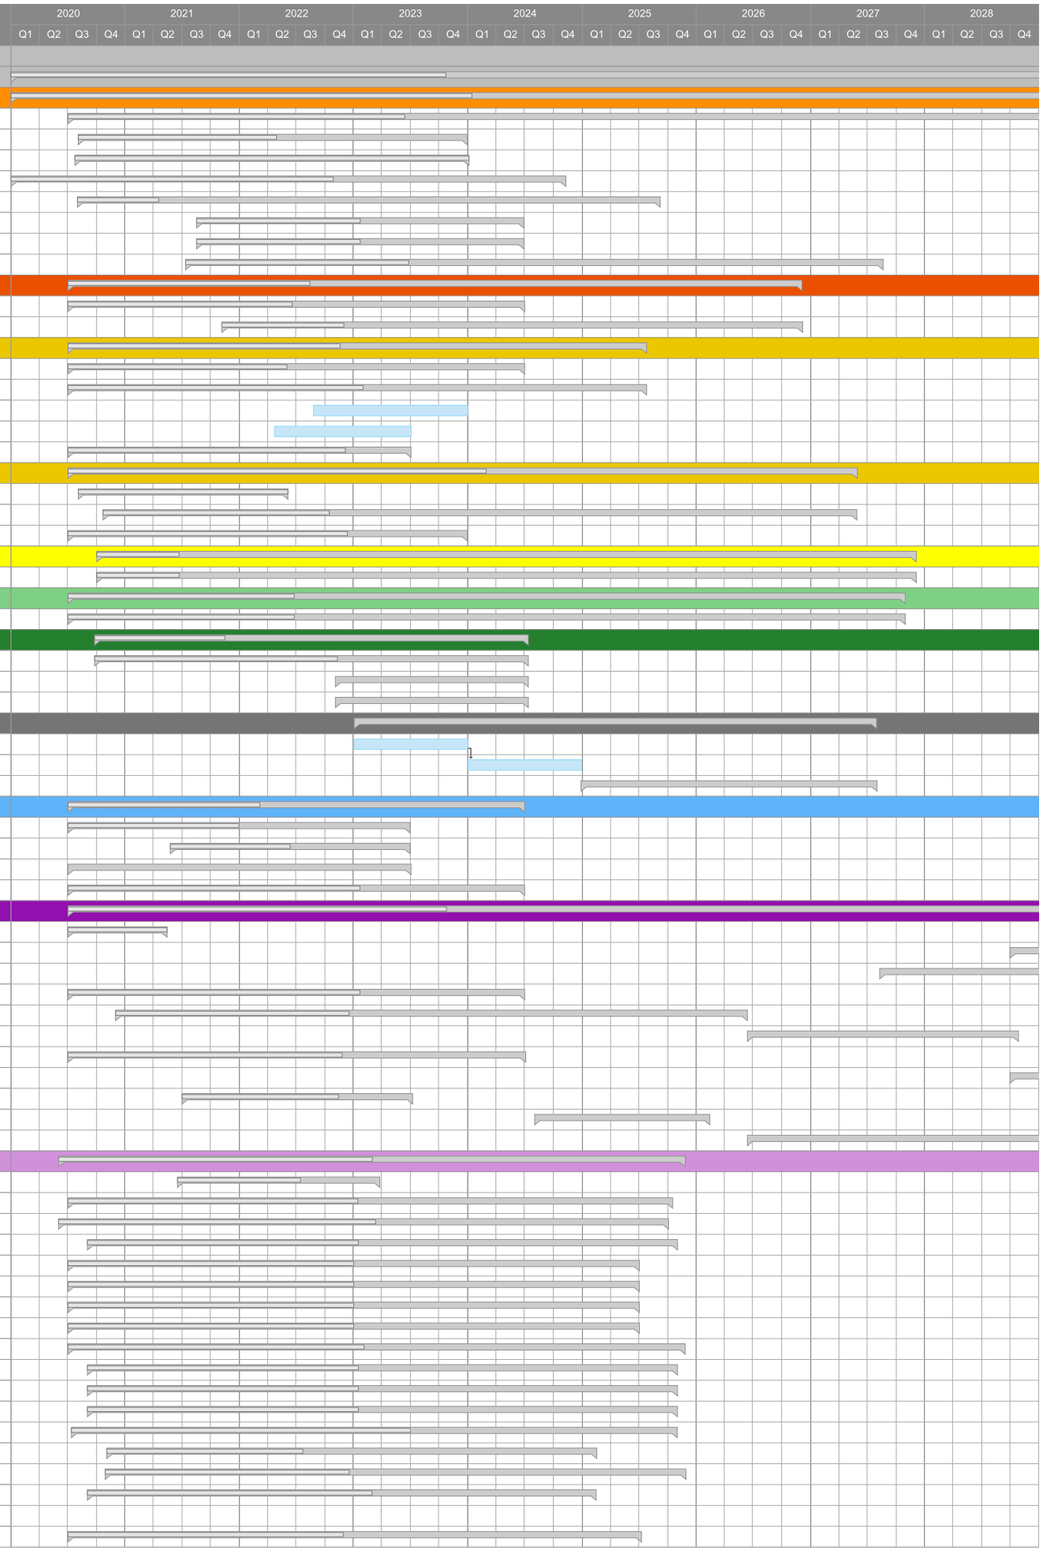

	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
1	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
2	GNSO Portfolio Management Tool	3139d	03/04/19	03/13/31		34%		
3	RDDS - Program Track	2609d	03/04/19	03/01/29		44%		
4	EPDP: Standardized System for Access & Disclosure - Phase 2	2262d	07/01/20	03/01/29		34%		
5	EPDP: Standardized System for Access & Disclosure - Phase 2	23d	07/01/20	07/31/20		100%		
6	Remaining EPDP-P2 Topics Track 1 (Legal vs. Natural + Feasability of Unique Contacts)	0	07/31/21	07/31/21		100%		
8	Remaining EPDP-P2 Topics Track 2 (Accuracy)	260d	08/03/20	07/31/21		100%		
9	Staff to produce Briefing Document on Accuracy	170d	08/03/20	03/26/21	5	100%		
10	Council to define scope of Accuracy Scoping Team	84d	03/29/21	07/22/21	9	100%		
11	Migrated to separate project	0	07/31/21	07/31/21		100%		
12	Board: Standardized System for Access & Disclosure - Phase 2 adopt consensus recommendations	852d	03/25/21	06/28/24		60%		
13	Board: Standardized System for Access & Disclosure Operational Design Phase	219d	03/25/21	01/25/22	5FS +168d	100%		
14	Board: Standardized System for Access & Disclosure - Phase 2 adopt consensus recommendations	852d	03/25/21	06/28/24	5FS +168d	50%	On-Hold	
15	IRT: Standardized System for Access & Disclosure - Phase 2	520d	07/01/24	06/26/26	14	0%	Planned	
16	SSAD Development and Implementation	699d	06/29/26	03/01/29	15	0%	Planned	
17	EPDP: Legal vs. Natural + Feasibility of Unique Contacts of Registration Data - Phase 2A	890d	08/03/20	12/29/23		51%		
18	Reset EPDP-P2A and elect new Chair	100d	08/03/20	12/18/20	5	100%		
19	EPDP: Registration Data - Phase 2A	225d	12/21/20	10/29/21	18	100%		
20	Board: Registration Data - Phase 2A adopt consensus recommendations	120d	11/01/21	04/15/22	19	100%		
21	IRT: Registration Data - Phase 2A	445d	04/18/22	12/29/23	20	1%		
22	RDS2 Review Recommendations - Implementation	899d	07/23/20	01/02/24		100%		
23	RDS2 Review - Recommendation CC.1 (suspension of domain due to incorrect RDS)	899d	07/23/20	01/02/24		100%		
27	RDS2 Review - Recommendation CC.4 (measure, audit, etc. of RDS Policies)	1d	07/23/20	07/23/20		100%		
30	IRT: Temporary Specification on gTLD Registration Data - Phase 1	1484d	03/04/19	11/07/24		58%		
31	IRT: Temporary Specification on gTLD Registration Data - Phase 1	1484d	03/04/19	11/07/24		59%	On-Schedule	On-Target
32	EPDP-P1 Rec27 Wave 1.5 & Wave 2 Other Policy Impacts	547d	03/01/21	04/04/23		57%		
33	Council to consider Wave 1.5 report and determine next steps	120d	03/01/21	08/13/21		100%		
34	Council to consider Wave Wave 2 reports and determine next steps	90d	11/30/22	04/04/23		0%	Planned	
35	Revised ICANN Procedure for Handling Whois Conflicts with Privacy Law	1330d	07/31/20	09/04/25		14%		
36	Council small scoping team to determine next steps and Council consideration	60d	07/31/20	10/22/20		100%		
37	Request ICANN org to develop revised proposal for invoking Procedure	270d	01/27/23	02/08/24		15%	On-Hold	On-Target
38	Council to deliberate findings and determine appropriate path	45d	02/09/24	04/11/24	37	0%	Planned	
39	IF required, review WPIAG Charter to determine if it's fit for purpose	30d	04/12/24	05/23/24	38	0%	Planned	
40	IF required, Council to approve charter and launch WPIAG	105d	05/24/24	10/17/24		0%		
41	Engage WPIAG	60d	05/24/24	08/15/24	39	0%	Planned	
42	Council to deliberate findings and determine appropriate path	45d	08/16/24	10/17/24	41	0%	Planned	
43	IF required, Council to approve launch of EPDP	230d	10/18/24	09/04/25		0%		
44	EPDP: Procedure for Handling Whois Conflicts with Privacy Law	90d	10/18/24	02/20/25	42	0%	Planned	
45	Board: Procedure for Handling Whois Conflicts with Privacy Law adopt consensus recommendations	50d	02/21/25	05/01/25	44	0%	Planned	
46	IRT: Procedure for Handling Whois Conflicts with Privacy Law	90d	05/02/25	09/04/25	45	0%	Planned	
47	IRT: Privacy & Proxy Services Accreditation Issues	750d	08/16/21	06/28/24		50%		
48	IRT: Privacy & Proxy Services Accreditation Issues	750d	08/16/21	06/28/24	33	50%	On-Hold	On-Target
49	IRT: Translation/Transliteration of gTLD Registration Data	750d	08/16/21	06/28/24		50%		
50	IRT: Translation/Transliteration of gTLD Registration Data	750d	08/16/21	06/28/24	33	50%	On-Hold	On-Target
51	Registration Data Accuracy	1595d	07/12/21	08/20/27		32%		
52	Registration Data Accuracy - Scoping Team	645d	07/12/21	12/29/23		78%	On-Hold	In-Trouble
53	Council: Decide to request Issue Report on Registration Data Accuracy	30d	01/01/24	02/09/24	52	0%	Planned	
54	Staff: Issue Report on Registration Data Accuracy	90d	02/12/24	06/14/24	53	0%	Planned	
55	Council: Approve PDP launch on Registration Data Accuracy	40d	06/17/24	08/09/24	54	0%	Planned	
56	Council: Approve charter on Registration Data Accuracy	40d	08/12/24	10/04/24	55	0%	Planned	
57	PDP: Registration Data Accuracy	400d	10/07/24	04/17/26		0%	Planned	
58	Restored Names Accuracy Policy (RNAP) Rec 27 Wave 1 Report	400d	10/07/24	04/17/26	56	0%	Planned	
59	Whois Data Reminder Policy (WDRP) Rec 27 Wave 1 Report	400d	10/07/24	04/17/26	56	0%	Planned	
60	Board: Registration Data Accuracy adopt consensus recommendations	50d	04/20/26	06/26/26	57	0%	Planned	
61	IRT: Registration Data Accuracy	300d	06/29/26	08/20/27	60	0%	Planned	
62	RPM - Program Track	1677d	07/01/20	12/03/26		33%		
63	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 1 (URS, TMCH, Sunrise, Claims)	1043d	07/01/20	06/28/24		49%		
64	PDP: RPM - Phase 1 Review of RPMs in All gTLDs (started 4 Mar 2016)	120d	07/01/20	12/15/20		100%		
65	EPDP-P1 Rec27 Wave 1 Other Policy Impacts	77d	07/01/20	10/15/20		100%		
70	Board: RPM - Phase 1 Review of RPMs in All gTLDs adopt consensus recommendations	283d	12/16/20	01/14/22	64	100%		
71	IRT: RPM - Phase 1 Review of RPMs in All gTLDs	550d	05/23/22	06/28/24	70FS +90d	5%		
72	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 2 (UDRP)	1325d	11/05/21	12/03/26		21%		
73	PSR: Policy Status Report on UDRP	185d	11/05/21	07/21/22		100%		
74	Council: Deliberate PSR and Confirm Start of PDP	135d	07/22/22	01/26/23	73	70%		
75	Drafting Team: Charter on Review of UDRP (incl. Items 2 through 11 of Rec27 Wave1)	150d	01/27/23	08/24/23	74	0%	Planned	
76	PDP: RPM - Phase 2 Review of UDRP	525d	08/25/23	08/28/25	75	0%	Planned	
77	Board: RPM - Phase 2 Review of UDRP adopt consensus recommendations	60d	08/29/25	11/20/25	76	0%	Planned	
78	IRT: RPM - Phase 2 Review of UDRP	270d	11/21/25	12/03/26	77	0%	Planned	
79	gTLD - Program Track	1323d	07/01/20	07/25/25		47%		
80	CCWG: New gTLD Auction Proceeds	1043d	07/01/20	06/28/24		48%		
81	CCWG: New gTLD Auction Proceeds (group completed 31 May 2020)	0	07/01/20	07/01/20		100%		
82	Council to deliberate and adopt CCWG recommendations	20d	08/03/20	08/28/20		100%		
83	Board: New gTLD Auction Proceeds - adopt consensus recommendations	466d	08/31/20	06/13/22	82	100%		
84	ICANN Org: Implement ICANN Org Grants Program	534d	06/14/22	06/28/24	83	0%		

	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
85	PDP: New gTLD Subsequent Procedures	1323d	07/01/20	07/25/25		51%		
86	PDP: New gTLD Subsequent Procedures (started 21 Jan 2016)	168d	07/01/20	02/19/21		100%		
87	Board: New gTLD Subsequent Procedures adopt consensus recommendations	615d	02/22/21	06/30/23		82%		
88	ICANN Org: New gTLD Subsequent Procedures Operational Design Phase	340d	09/13/21	12/30/22	86FS +145d	95%		
89	Board: New gTLD Subsequent Procedures adopt consensus recommendations	615d	02/22/21	06/30/23	86	75%		
90	IRT: New gTLD Subsequent Procedures	540d	07/03/23	07/25/25	87	0%	Planned	
91	GGP: Applicant Support (Placeholder awaiting plan)	352d	08/25/22	12/29/23		0%		
92	Closed Generics Facilitated Dialogue (Placeholder awaiting plan)	311d	04/22/22	06/30/23		0%		
93	Name Collision Analysis Project	783d	07/01/20	06/30/23		81%		
94	Name Collision Analysis Project - Phase 1 (14 Mar 2019 start)	192d	07/01/20	03/25/21		100%		
95	Name Collision Analysis Project - Phase 2	565d	05/03/21	06/30/23		75%		
96	**IDNs - Program Track**	**1803d**	**07/01/20**	**05/28/27**		**53%**		
97	IDN Operational Working Group (Track 1)	480d	08/03/20	06/03/22		100%		
100	EPDP: IDNs (Track 2)	1723d	10/21/20	05/28/27		30%		
101	Drafting Team: Charter on Internationalized Domain Names + EPDP Request	160d	10/21/20	06/01/21		100%		
102	EPDP: Internationalized Domain Names	1262d	05/20/21	03/20/26		28%	Revised Schedule	On-Target
103	Board: Internationalized Domain Names adopt consensus recommendations	60d	03/23/26	06/12/26	102	0%	Planned	
104	IRT: Internationalized Domain Names	250d	06/15/26	05/28/27	103	0%	Planned	
105	IDN GNSO Council Coordination w/ CCNSO Council (Track 3)	913d	07/01/20	12/29/23		70%		
106	GNSO Council to coordinate with the CCNSO regarding IDN policy developments	913d	07/01/20	12/29/23		70%		
107	**Expiration - Program Track**	**1871d**	**10/01/20**	**12/02/27**		**10%**		
108	PDP: Expired Domain Deletion Policy / Expired Registration Recovery Policy Policy Review	1871d	10/01/20	12/02/27		10%		
109	Council to extend PSR for 18 months or when bandwidth becomes available	45d	10/01/20	12/02/20		100%		
110	Council to Consider Request EDDP/ERRP Policy Status Report	136d	07/14/22	01/19/23	109FS +420d	75%		
111	Develop Expiration Policy Status Report (incl. Rec27 Wave1 EDDP Item 2 + ERRP Item3)	180d	01/20/23	09/28/23	110	0%	Planned	
112	Council to Request Expiration Policy Issue Report	45d	09/29/23	11/30/23	111	0%	Planned	
113	Expiration Policy Issue Report	150d	12/01/23	06/27/24		0%		
114	Develop Issues Report (incl. Rec27 Wave1 EDDP Item 2 + ERRP Item3)	150d	12/01/23	06/27/24	112	0%	Planned	
115	Council to approve PDP launch	10d	06/28/24	07/11/24	114	0%	Planned	
116	Council to approve scope and charter	25d	07/12/24	08/15/24	115	0%	Planned	
117	Expiration Policy Review	860d	08/16/24	12/02/27		0%		
118	PDP: Expiration Policy Review	400d	08/16/24	02/26/26	116	0%	Planned	
119	Board: Expiration Policy Review adopt consensus recommendations	60d	02/27/26	05/21/26	118	0%	Planned	
120	IRT: Expiration Policy Review	400d	05/22/26	12/02/27	119	0%	Planned	
121	**Transfers - Program Track**	**1912d**	**07/01/20**	**10/28/27**		**27%**		
122	PDP: Transfer Policy Review	1912d	07/01/20	10/28/27		27%		
123	Council to Request Transfer Policy Status Report	0	07/01/20	07/01/20		100%		
124	Develop Transfer Policy Status Report	0	07/01/20	07/01/20	123	100%		
125	Council to Request Transfer Policy Issue Report	0	07/01/20	07/01/20	124	100%		
126	Develop Transfer Issue Report	158d	07/01/20	02/05/21		100%		
129	Council to approve PDP launch	10d	02/05/21	02/18/21	127	100%		
130	Council to approve scope and charter	24d	02/19/21	03/24/21	129	100%		
131	Transfer Policy Review - Phase 1	1206d	02/18/21	10/02/25		37%		
132	PDP: Transfer Policy Review - Phase 1	746d	02/18/21	12/28/23		60%	On-Schedule	On-Target
133	Board: Transfer Policy Review - Phase 1 adopt consensus recommendations	60d	12/29/23	03/21/24	132	0%	Planned	
134	IRT: Transfer Policy Review - Phase 1	400d	03/22/24	10/02/25	133	0%	Planned	
135	Transfer Policy Review - Phase 2	1000d	12/29/23	10/28/27		0%		
136	PDP: Transfer Policy Review - Phase 2	540d	12/29/23	01/22/26	132	0%	Planned	
137	Board: Transfer Policy Review - Phase 2 adopt consensus recommendations	60d	01/23/26	04/16/26	136	0%	Planned	
138	IRT: Transfer Policy Review - Phase 2	400d	04/17/26	10/28/27	137	0%	Planned	
139	**IGO - Program Track**	**992d**	**09/24/20**	**07/12/24**		**30%**		
140	EPDP: Specific Curative Rights Protections for IGOs	992d	09/24/20	07/12/24		56%		
141	EPDP: Specific Curative Rights Protections for IGOs	550d	09/24/20	11/02/22		100%		
142	Board: Specific Curative Rights Protections for IGOs adopt consensus recommendations	172d	11/03/22	06/30/23	141	5%		
143	IRT: Specific Curative Rights Protections for IGOs	270d	07/03/23	07/12/24	142	0%	Planned	
144	PDP: Curative Rights Protections for IGO/INGOs	442d	11/03/22	07/12/24		0%		
145	Board: Curative Rights Protections for IGO/INGOs adopt consensus recommendations	172d	11/03/22	06/30/23	141	0%		
146	IRT: Curative Rights Protections for IGO/INGOs	270d	07/03/23	07/12/24	145	0%	Planned	
147	PDP: Protection of International Organization Names in All gTLDs (Remaining Acronyms)	442d	11/03/22	07/12/24		0%		
148	Board: Protection of International Organization Names in All gTLDs (Remaining Acronyms)	172d	11/03/22	06/30/23	141	0%		
149	IRT: PDP: Protection of International Organization Names in All gTLDs (Remaining Acronyms)	270d	07/03/23	07/12/24	148	0%	Planned	
150	**DNS_Abuse - Program Track**	**1195d**	**01/02/23**	**07/30/27**		**0%**		
151	Track 2 - Issues that may benefit from education / communication / outreach	260d	01/02/23	12/29/23	342	0%		
152	Track 3 - Issues that may benefit from contractual negotiations between ICANN org and Contracted Parties	260d	01/01/24	12/27/24	151	0%	Planned	
153	Track 1 - Issues that may benefit from GNSO policy development	675d	12/27/24	07/30/27	124	0%	Planned	
154	Council: Request Policy Issue Report	0	12/27/24	12/27/24	152	0%	Planned	
155	Staff: Develop Issue Report	45d	12/30/24	02/28/25	154	0%	Planned	
156	Council: Approve PDP launch	10d	03/03/25	03/14/25	155	0%	Planned	
157	Council: Approve scope and charter	20d	03/17/25	04/11/25	156	0%	Planned	
158	PDP: DNS Abuse - Malicious Registrations (tightly scoped)	600d	04/14/25	07/30/27		0%		
159	PDP: DNS Abuse - Malicious Registrations (tightly scoped)	270d	04/14/25	04/24/26	157	0%	Planned	
160	Board: DNS Abuse - Malicious Registrations (tightly scoped)	60d	04/27/26	07/17/26	159	0%	Planned	
161	IRT: DNS Abuse - Malicious Registrations (tightly scoped)	270d	07/20/26	07/30/27	160	0%	Planned	
162	**Accountability - Program Track**	**1043d**	**07/01/20**	**06/28/24**		**42%**		

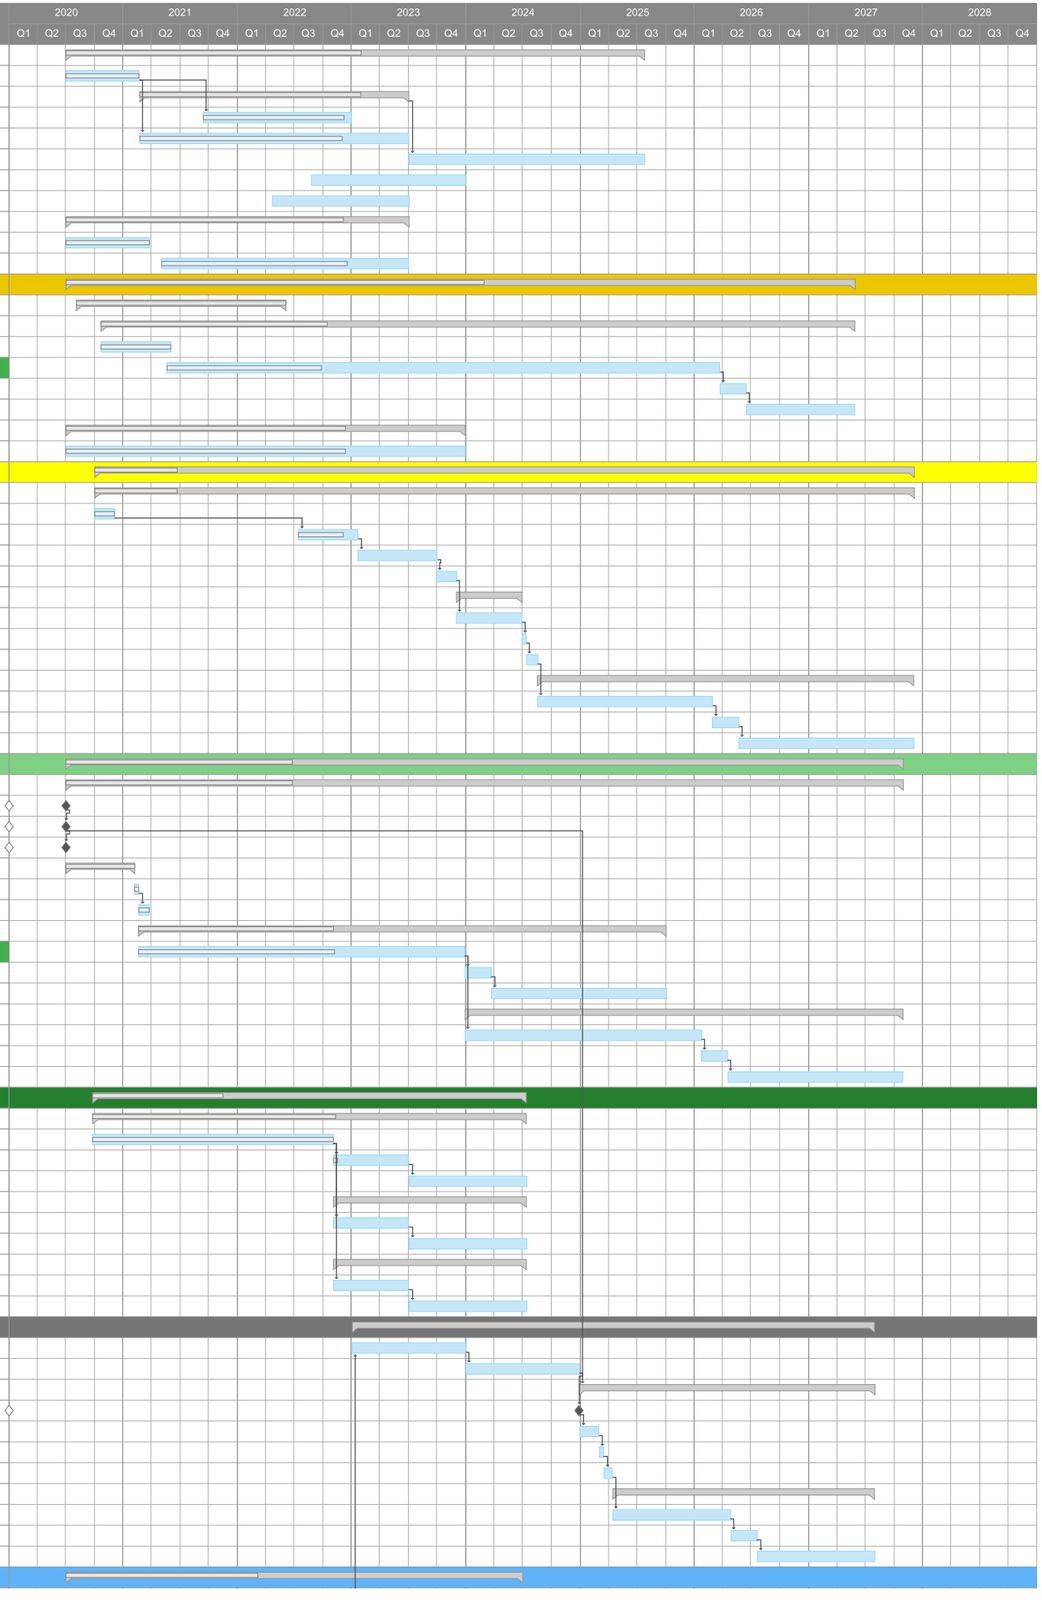

	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
163	Independent Review Process - Implementation Oversight Team	780d	07/01/20	06/27/23		50%		
164	IoT Oversight Team Group	780d	07/01/20	06/27/23		50%		
165	Establishment of Standing Panel for Independent Review Process	780d	07/01/20	06/27/23		50%		
166	Cross Community Working Group on Enhancing ICANN Accountability - WS2	550d	05/24/21	06/30/23		50%		
167	GNSO Council Implementation of WS2	550d	05/24/21	06/30/23		50%		
168	GNSO SG/C Implementation of WS2	550d	05/24/21	06/30/23		50%		
169	Geo Regions Review	783d	07/01/20	06/30/23		0%		
170	Geo Regions Review: Monitor for changes	783d	07/01/20	06/30/23		0%	On-Hold	
171	Multistakeholder Model Evolution	1043d	07/01/20	06/28/24		64%		
172	Monitor for MSM-Evo implementation assignments	1043d	07/01/20	06/28/24		64%		
173	**Reviews - Program Track**	**2792d**	**07/01/20**	**03/13/31**		**31%**		
174	IANA Naming Function Review	226d	07/01/20	05/12/21		100%		
178	Registration Directory Service Review RT3	640d	09/29/28	03/13/31		0%		
183	Competition, Consumer Trust and Consumer Choice RT2	640d	08/09/27	01/18/30		0%		
188	Accountability and Transparency Review 3	1043d	07/01/20	06/28/24		64%		
189	Council to form a small team to draft a public comment response to the ATRT3	22d	07/01/20	07/30/20		100%		
190	Monitor for ATRT3 implementation assignments	1043d	07/01/20	06/28/24		63%		
191	Holistic Review - Pilot	1444d	11/30/20	06/11/26		37%		
192	Holistic Review Pilot: Define Terms of Reference, Information Gaps, and Determine Prioritization to Start	674d	11/30/20	06/29/23		83%		
193	Council SSC to select GNSO representatives on Review Team	30d	06/30/23	08/10/23	192	0%	Planned	
194	Holistic Review Pilot	400d	08/11/23	02/20/25	193	0%	Planned	
195	Board: Holistic Review Pilot deliberate and adopt consensus recommendations	70d	02/21/25	05/29/25	194	0%	Planned	
196	Council to consider Holistic Review Pilot Results	60d	05/30/25	08/21/25	195	0%	Planned	
197	Holistic Review Pilot Implement Review recommendations	270d	05/30/25	06/11/26	195	0%	Planned	
198	Accountability and Transparency Review 4	620d	06/12/26	10/26/28		0%		
203	Security, Stability and Resiliency of the DNS #2	1044d	07/01/20	07/01/24		60%		
204	Security, Stability and Resiliency of the DNS #2	160d	07/01/20	02/09/21		100%		
205	Board: SSR#2 deliberate and adopt consensus recommendations	117d	02/10/21	07/22/21	204	100%		
206	Monitor for SSR#2 implementation assignments	767d	07/23/21	07/01/24	205	45%		
207	Security, Stability and Resiliency of the DNS #3	640d	09/29/28	03/13/31		0%		
212	CSC Effectiveness Review - 2021	525d	07/01/21	07/05/23		68%		
213	Council: establish terms of reference and determine is prior review recs were implemented	65d	07/01/21	09/29/21		100%		
214	CSC Effectiveness Review 2021	390d	09/30/21	03/29/23	213	85%		
215	Board: CSC Effectiveness Review deliberate and adopt consensus recommendations	70d	03/30/23	07/05/23	214	0%	Planned	
216	Consider CSC Effectiveness Review Results	60d	03/30/23	06/21/23	214	0%	Planned	
217	CSC Effectiveness Review - 2024	400d	08/01/24	02/11/26		0%		
222	GNSO Review RT3	680d	06/12/26	01/18/29		0%		
228	**Operations - Program Track**	**1432d**	**06/01/20**	**11/25/25**		**50%**		
229	Council Committee for Overseeing & Implementing Continuous Improvement	463d	06/16/21	03/24/23		61%		
230	CCOICI Assignment #4	398d	08/26/21	03/06/23		41%	On-Schedule	On-Target
231	CCOICI Assignment #6	340d	11/19/21	03/09/23		83%	On-Schedule	On-Target
232	CCOICI Assignment WS2	187d	03/30/22	12/15/22		100%		
233	CCOICI Pilot Program Assessment	463d	06/16/21	03/24/23		46%	On-Hold	On-Target
234	Participant of Empowered Community	1382d	07/01/20	10/16/25		48%		
235	Participant of Empowered Community - 2020	96d	07/01/20	11/11/20		100%		
238	Participant of Empowered Community - 2021	235d	11/12/20	10/06/21		100%		
241	Participant of Empowered Community - 2022	271d	10/07/21	10/20/22		100%		
244	Participant of Empowered Community - 2023	265d	10/21/22	10/26/23		24%		
245	Participant of Empowered Community - 2023	250d	10/21/22	10/05/23	243	25%		
246	Elect new participant to Empowered Community	15d	10/06/23	10/26/23	245	0%	Planned	
247	Participant of Empowered Community - 2024	265d	10/27/23	10/31/24		0%		
250	Participant of Empowered Community - 2025	250d	11/01/24	10/16/25		0%		
252	Participation on Customer Standing Committee	1394d	06/01/20	10/02/25		52%		
253	Customer Standing Committee - 2020	132d	07/01/20	12/31/20		100%		
256	Customer Standing Committee - 2021	349d	06/01/20	09/30/21		100%		
259	Customer Standing Committee - 2022	305d	08/01/21	09/29/22		100%		
262	Customer Standing Committee - 2023	307d	08/01/22	10/03/23		35%		
263	Council Approval - Customer Standing Committee slate - 2023	22d	08/01/22	08/30/22		100%		
264	Customer Standing Committee - 2023	261d	10/04/22	10/03/23	263FS +24d	30%		
265	Customer Standing Committee - 2024	307d	08/01/23	10/02/24				
268	Customer Standing Committee - 2025	306d	08/01/24	10/02/25				
271	Participation on NomCom	1347d	09/01/20	10/29/25		46%		
272	GNSO Participation on NomCom - 2020-2021	297d	09/01/20	10/20/21		100%		
273	GNSO Council to Confirm NomCom Job Description	1d	09/23/21	09/23/21		100%		
274	GNSO Participation on NomCom - 2021-2022	241d	10/20/21	09/21/22		100%		
275	GNSO Council to Confirm NomCom Job Description	1d	11/17/22	11/17/22		100%		
276	GNSO Participation on NomCom - 2022-2023	286d	09/21/22	10/25/23		30%		
277	GNSO Council to Confirm NomCom Job Description	1d	09/21/23	09/21/23		0%	Planned	
278	GNSO Participation on NomCom - 2023-2024	276d	10/25/23	11/13/24		0%	Planned	
279	GNSO Council to Confirm NomCom Job Description	1d	09/19/24	09/19/24		0%	Planned	
280	GNSO Participation on NomCom - 2024-2025	251d	11/13/24	10/29/25		0%	Planned	
281	Stakeholder Support - Registry Stakeholder Group	1304d	07/01/20	06/30/25		50%		
282	FY21 Stakeholder Support - Registry Stakeholder Group	261d	07/01/20	06/30/21		100%		
283	FY22 Stakeholder Support - Registry Stakeholder Group	261d	07/01/21	06/30/22		100%		

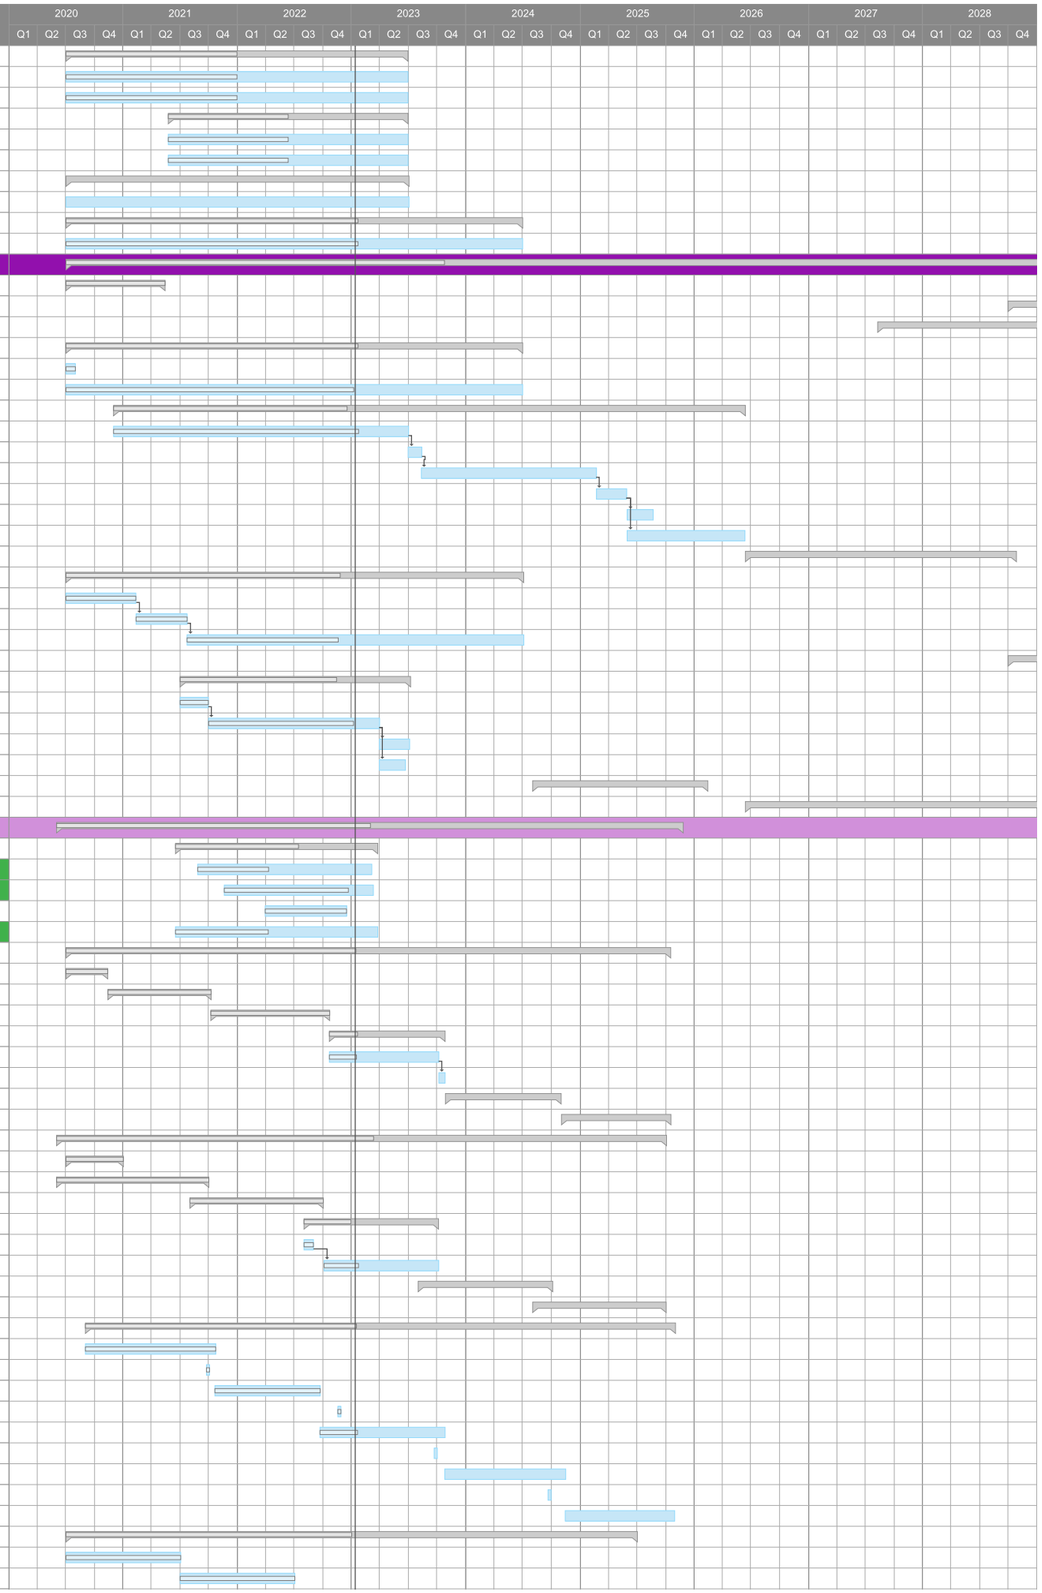

	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
284	FY23 Stakeholder Support - Registry Stakeholder Group	261d	07/01/22	06/30/23		50%		
285	FY24 Stakeholder Support - Registry Stakeholder Group	261d	07/01/23	06/28/24		0%	Planned	
286	FY25 Stakeholder Support - Registry Stakeholder Group	261d	07/01/24	06/30/25		0%	Planned	
287	Stakeholder Support - Registrar Stakeholder Group	1304d	07/01/20	06/30/25		50%		
288	FY21 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/20	06/30/21		100%		
289	FY22 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/21	06/30/22		100%		
290	FY23 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/22	06/30/23		50%		
291	FY24 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/23	06/28/24		0%	Planned	
292	FY25 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/24	06/30/25		0%	Planned	
293	Stakeholder Support - NCSG/NCUC/NPOC	1304d	07/01/20	06/30/25		50%		
294	FY21 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/20	06/30/21		100%		
295	FY22 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/21	06/30/22		100%		
296	FY23 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/22	06/30/23		50%		
297	FY24 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/23	06/28/24		0%	Planned	
298	FY25 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/24	06/30/25		0%	Planned	
299	Stakeholder Support - CSG/BC/IPC/ISPCP	1304d	07/01/20	06/30/25		50%		
300	FY21 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/20	06/30/21		100%		
301	FY22 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/21	06/30/22		100%		
302	FY23 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/22	06/30/23		50%		
303	FY24 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/23	06/28/24		0%	Planned	
304	FY25 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/24	06/30/25		0%	Planned	
305	GNSO Council	1410d	07/01/20	11/25/25		48%		
306	GNSO Council - Monthly Meetings	1347d	09/01/20	10/29/25		46%		
307	GNSO Council - Monthly Meetings 2020-2021	297d	09/01/20	10/20/21		100%		
308	GNSO Council - Monthly Meetings 2021-2022	241d	10/20/21	09/21/22		100%		
309	GNSO Council - Monthly Meetings 2022-2023	286d	09/21/22	10/25/23		30%	On-Schedule	On-Target
310	GNSO Council - Monthly Meetings 2023-2024	276d	10/25/23	11/13/24		0%	Planned	
311	GNSO Council - Monthly Meetings 2024-2025	251d	11/13/24	10/29/25		0%	Planned	
312	GNSO Council - Leadership Meetings	1347d	09/01/20	10/29/25		46%		
313	GNSO Council - Leadership Meetings 2020-2021	297d	09/01/20	10/20/21		100%		
314	GNSO Council - Leadership Meetings 2021-2022	241d	10/20/21	09/21/22		100%		
315	GNSO Council - Leadership Meetings 2022-2023	286d	09/21/22	10/25/23		30%	On-Schedule	On-Target
316	GNSO Council - Leadership Meetings 2023-2024	276d	10/25/23	11/13/24		0%	Planned	
317	GNSO Council - Leadership Meetings 2024-2025	251d	11/13/24	10/29/25		0%	Planned	
318	GNSO Council - Action Items	1347d	09/01/20	10/29/25		46%		
319	GNSO Council - Action Items 2020-2021	297d	09/01/20	10/20/21		100%		
320	GNSO Council - Action Items 2021-2022	241d	10/20/21	09/21/22		100%		
321	GNSO Council - Action Items 2022-2023	286d	09/21/22	10/25/23		30%	On-Schedule	On-Target
322	GNSO Council - Action Items 2023-2024	276d	10/25/23	11/13/24		0%	Planned	
323	GNSO Council - Action Items 2024-2025	251d	11/13/24	10/29/25		0%	Planned	
324	GNSO Council - Small Teams	1385d	07/12/20	10/30/25		56%		
325	GNSO Council - Small Teams - 2020-2021	270d	07/12/20	07/22/21		100%		
335	GNSO Council - Small Teams - 2021-2022	231d	11/03/21	09/21/22		100%		
341	GNSO Council - Small Teams - 2022-2023	430d	11/08/21	06/30/23		74%		
342	Next steps regarding DNS Abuse	300d	11/08/21	12/30/22		100%		
343	Collaborate with ICANN Board on Whois Disclosure System (EPDP_P2)	369d	02/01/22	06/30/23		70%	On-Schedule	On-Target
344	SubPro ODP Question & Answer Review Team	130d	06/24/22	12/22/22		90%	On-Schedule	On-Target
345	GNSO PDP Improvements (Staff + Council)	261d	07/01/22	06/30/23		40%	On-Schedule	On-Target
346	GNSO Council - Small Teams - 2023-2024	261d	11/01/23	10/30/24		0%		
348	GNSO Council - Small Teams - 2024-2025	260d	11/01/24	10/30/25		0%		
350	GNSO Standing Committee on Budget and Operations	1119d	11/02/20	02/13/25		40%		
351	GNSO Standing Committee on FY22 Budget and Operations 2020-2021	76d	11/02/20	02/15/21		100%		
355	GNSO Standing Committee on FY23 Budget and Operations 2021-2022	75d	11/01/21	02/11/22		100%		
359	GNSO Standing Committee on FY24 Budget and Operations 2022-2023	75d	11/01/22	02/13/23		0%	On-Schedule	On-Target
360	Refresh roster and confirm Chair	30d	11/01/22	12/12/22		0%		
361	Evaluate fiscal year budget and planning documents	35d	12/13/22	01/30/23	360	0%		
362	Complete draft of comments for Council consideration and submit	10d	01/31/23	02/13/23	361	0%		
363	GNSO Standing Committee on FY25 Budget and Operations 2023-2024	75d	11/01/23	02/13/24		0%	Planned	
367	GNSO Standing Committee on FY26 Budget and Operations 2024-2025	75d	11/01/24	02/13/25		0%	Planned	
371	GNSO Standing Selection Committee	1325d	10/28/20	11/25/25		42%		
372	GNSO Standing Selection Committee 2020-2021	260d	10/28/20	10/26/21		100%		
379	GNSO Standing Selection Committee 2021-2022	270d	10/27/21	11/08/22		100%		
386	GNSO Standing Selection Committee 2022-2023	290d	09/21/22	10/31/23		14%	On-Schedule	On-Target
387	Refresh roster and confirm Chair (within 3 weeks of AGM)	60d	09/21/22	12/13/22		50%		
388	Standing Selection Committee (SSC) 2022-2023	230d	12/14/22	10/31/23		5%		
389	Standing Selection Committee (SSC) fill positions as assigned	230d	12/14/22	10/31/23	387	8%		
390	Appoint GNSO Representative to Fellowship Program	30d	12/14/22	01/24/23	387	1%		
391	Obtain EOIs and Appoint CSC Liaison as Required	70d	05/31/23	09/05/23	387SS +180d			
392	Appoint GAC Liaison as Required (Not required til 2023-2024)	70d	06/28/23	10/03/23	387SS +200d			
393	GNSO Standing Selection Committee 2023-2024	270d	10/25/23	11/05/24			Planned	
400	GNSO Standing Selection Committee 2024-2025	270d	11/13/24	11/25/25			Planned	
407	GNSO Council - Strategic Planning Session	1163d	09/01/20	02/13/25		56%		
408	GNSO Council - Strategic Planning Session - 2020-2021	120d	09/01/20	02/15/21		100%		
409	GNSO Council - Strategic Planning Session - 2021-2022	120d	09/01/21	02/15/22		100%		

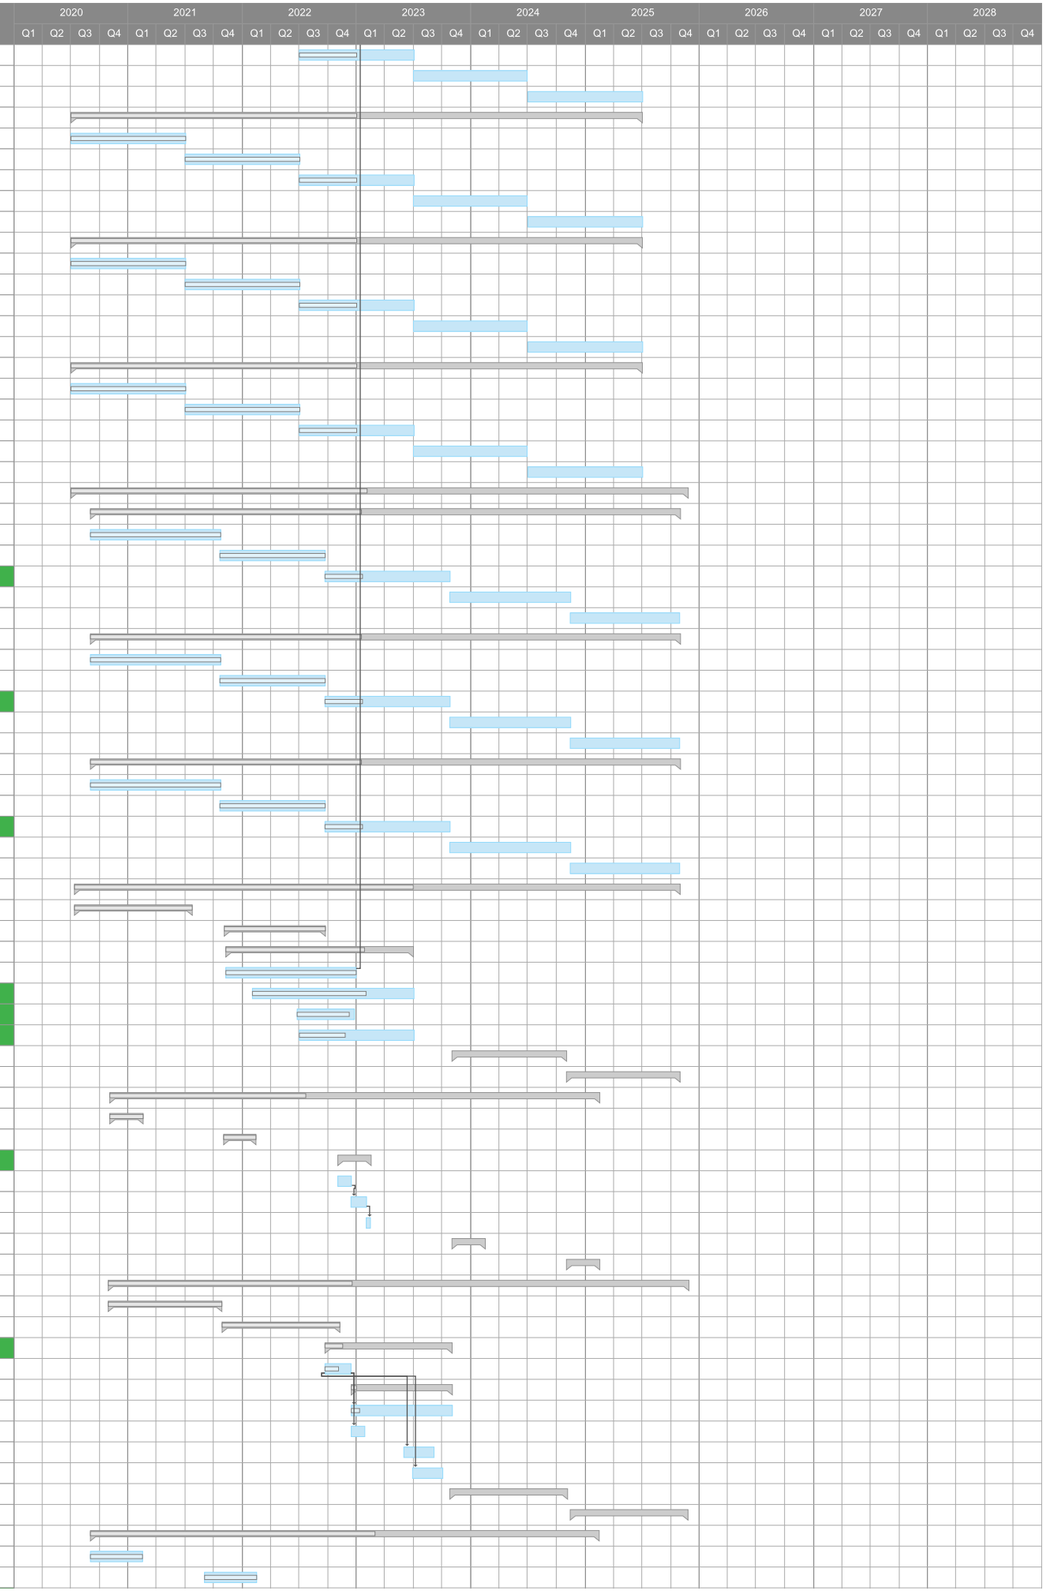
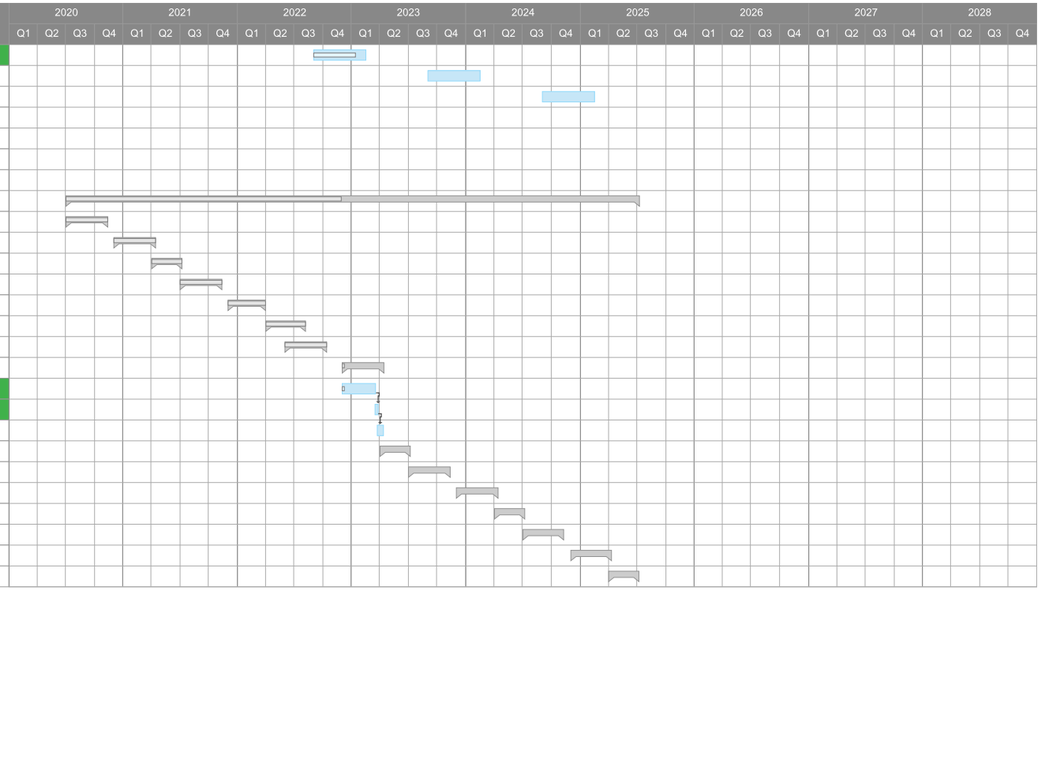
	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
410	GNSO Council - Strategic Planning Session - 2022-2023	120d	09/01/22	02/15/23		80%	On-Schedule	On-Target
411	GNSO Council - Strategic Planning Session - 2023-2024	120d	09/01/23	02/15/24		0%	Planned	
412	GNSO Council - Strategic Planning Session - 2024-2025	120d	09/01/24	02/13/25		0%	Planned	
413	⊟ GNSO Elections - [PLACEHOLDER SECTION]							
414	GNSO Council Chair							
415	GNSO - Board Seat 13							
416	GNSO - Board Seat 14							
417	⊟ ICANN Meeting Planning, Meeting, Respond to GAC Advice	1309d	07/01/20	07/07/25		48%		
418	⊞ ICANN69	95d	07/01/20	11/10/20		100%		
422	⊞ ICANN70	95d	12/01/20	04/12/21		100%		
426	⊞ ICANN71	70d	04/01/21	07/07/21		100%		
430	⊞ ICANN72	95d	07/01/21	11/10/21		100%		
434	⊞ ICANN73	87d	12/01/21	03/31/22		100%		
438	⊞ ICANN74	90d	04/01/22	08/04/22		100%		
442	⊞ ICANN75	95d	06/01/22	10/11/22		100%		
446	⊟ ICANN76	95d	12/01/22	04/12/23		4%		
447	ICANN76 Meeting Planning	75d	12/01/22	03/15/23		5%	On-Schedule	On-Target
448	ICANN76 ICANN Meeting	5d	03/16/23	03/22/23	447	0%	On-Schedule	On-Target
449	ICANN76 Respond to GAC Advice	15d	03/23/23	04/12/23	448	0%	Planned	
450	⊞ ICANN77	70d	04/01/23	07/06/23		0%		
454	⊞ ICANN78	95d	07/01/23	11/09/23		0%		
458	⊞ ICANN79	95d	12/01/23	04/11/24		0%		
462	⊞ ICANN80	70d	04/01/24	07/05/24		0%		
466	⊞ ICANN81	95d	07/01/24	11/08/24		0%		
470	⊞ ICANN82	95d	12/01/24	04/10/25		0%		
474	⊞ ICANN83	70d	04/01/25	07/07/25		0%
