	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
1	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
2	GNSO Portfolio Management Tool	3139d	03/04/19	03/13/31		39%		
3	RDDS - Program Track	2609d	03/04/19	03/01/29		47%		
4	EPDP: Standardized System for Access & Disclosure - Phase 2	2262d	07/01/20	03/01/29		39%		
18	EPDP: Legal vs. Natural + Feasibility of Unique Contacts of Reg Data - Phase 2A	890d	08/03/20	12/29/23		51%		
23	RDS2 Review Recommendations - Implementation	899d	07/23/20	01/02/24		100%		
31	IRT: Temporary Specification on gTLD Registration Data - Phase 1	1484d	03/04/19	11/07/24		70%		
36	Revised ICANN Procedure for Handling Whois Conflicts with Privacy Law	1423d	07/31/20	01/13/26		14%		
48	IRT: Privacy & Proxy Services Accreditation Issues	750d	08/16/21	06/28/24		50%		
50	IRT: Translation/Transliteration of gTLD Registration Data	750d	08/16/21	06/28/24		50%		
52	Registration Data Accuracy	1595d	07/12/21	08/20/27		32%		
63	RPM - Program Track	1711d	07/01/20	01/20/27		35%		
64	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 1 (URS, TMCH, Sunrise, Claims)	1043d	07/01/20	06/28/24		52%		
73	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 2 (UDRP)	1359d	11/05/21	01/20/27		22%		
80	gTLD - Program Track	1323d	07/01/20	07/25/25		52%		
81	CCWG: New gTLD Auction Proceeds (ICANN Org Grants Program)	1043d	07/01/20	06/28/24		48%		
86	PDP: New gTLD Subsequent Procedures	1323d	07/01/20	07/25/25		53%		
92	GGP: Applicant Support	429d	08/25/22	04/16/24		25%		
94	Closed Generics Facilitated Dialogue (Placeholder awaiting plan)	311d	04/22/22	06/30/23		10%	On-Schedule	On-Target
95	Name Collision Analysis Project	783d	07/01/20	06/30/23		85%		
98	IDNs - Program Track	1803d	07/01/20	05/28/27		47%		
99	IDN Operational Working Group (Track 1)	480d	08/03/20	06/03/22		100%		
102	EPDP: IDNs (Track 2)	1723d	10/21/20	05/28/27		33%		
107	IDN GNSO Council Coordination w/ CCNSO Council (Track 3)	1493d	07/01/20	03/20/26		45%		
109	Expiration - Program Track	1910d	10/01/20	01/26/28		12%		
110	PDP: Expired Domain Deletion Policy / Expired Registration Recovery Policy Policy Review	1910d	10/01/20	01/26/28		12%		
123	Transfers - Program Track	1912d	07/01/20	10/28/27		28%		
124	PDP: Transfer Policy Review	1912d	07/01/20	10/28/27		28%		
141	IGO - Program Track	992d	09/24/20	07/12/24		40%		
142	EPDP: Specific Curative Rights Protections for IGOs	992d	09/24/20	07/12/24		62%		
146	PDP: Curative Rights Protections for IGO/INGOs	442d	11/03/22	07/12/24		16%		
149	PDP: Protection of International Organization Names in All gTLDs (Remaining Acronyms)	442d	11/03/22	07/12/24		16%		
152	DNS_Abuse - Program Track	1195d	01/02/23	07/30/27		0%		
153	Track 2 - Issues that may benefit from education / communication / outreach	260d	01/02/23	12/29/23	360	0%	On-Schedule	On-Target
154	Track 3 - Issues that may benefit from contractual negotiations between ICANN org and Contracted Parties	260d	01/01/24	12/27/24	153	0%	Planned	
155	Track 1 - Issues that may benefit from GNSO policy development	675d	12/27/24	07/30/27		0%	Planned	
164	Accountability - Program Track	1043d	07/01/20	06/28/24		47%		
165	Independent Review Process - Implementation Oversight Team	780d	07/01/20	06/27/23		50%		
168	Cross Community Working Group on Enhancing ICANN Accountability - WS2	550d	05/24/21	06/30/23		71%		
171	Geo Regions Review	783d	07/01/20	06/30/23		0%		
173	Multistakeholder Model Evolution	1043d	07/01/20	06/28/24		66%		
175	Reviews - Program Track	2792d	07/01/20	03/13/31		32%		
176	IANA Naming Function Review	226d	07/01/20	05/12/21		100%		
180	Registration Directory Service Review RT3	640d	09/29/28	03/13/31		0%		
185	Competition, Consumer Trust and Consumer Choice RT2	640d	08/09/27	01/18/30		0%		
190	Accountability and Transparency Review 3	1043d	07/01/20	06/28/24		67%		
193	Holistic Review - Pilot	1444d	11/30/20	06/11/26		39%		
200	Accountability and Transparency Review 4	620d	06/12/26	10/26/28		0%		
205	Security, Stability and Resiliency of the DNS #2	1044d	07/01/20	07/01/24		65%		
209	Security, Stability and Resiliency of the DNS #3	640d	09/29/28	03/13/31		0%		
214	CSC Effectiveness Review - 2021	525d	07/01/21	07/05/23		68%		
219	CSC Effectiveness Review - 2024	400d	08/01/24	02/11/26		0%		
224	GNSO Review RT3	680d	06/12/26	01/18/29		0%		
230	Root_System - Program Track	870d	07/01/20	10/31/23		75%		
231	Root Server System Governance Working Group (GWG)	870d	07/01/20	10/31/23		75%	On-Schedule	On-Target
232	ICANN_Planning - Program Track	1163d	01/15/20	06/28/24		71%		
233	ICANN Planning - FY22	282d	01/15/20	02/11/21		100%		
236	ICANN Planning - FY23	359d	01/15/21	06/01/22		100%		
240	ICANN Planning - FY24	316d	01/15/22	03/31/23		97%		
245	ICANN Planning - FY25	381d	01/15/23	06/28/24		1%		
251	Operations - Program Track	1432d	06/01/20	11/25/25		51%		
252	Participant of Empowered Community	1382d	07/01/20	10/16/25		48%		
270	Participation on Customer Standing Committee	1394d	06/01/20	10/02/25		53%		
289	Participation on NomCom	1347d	09/01/20	10/29/25		47%		
299	Stakeholder Support - Registry Stakeholder Group	1304d	07/01/20	06/30/25		52%		
305	Stakeholder Support - Registrar Stakeholder Group	1304d	07/01/20	06/30/25		52%		
311	Stakeholder Support - NCSG/NCUC/NPOC	1304d	07/01/20	06/30/25		52%		
317	Stakeholder Support - CSG/BC/IPC/ISPCP	1304d	07/01/20	06/30/25		52%		
323	GNSO Council	1410d	07/01/20	11/25/25		54%		

	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
1	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
2	GNSO Portfolio Management Tool	3139d	03/04/19	03/13/31		39%		
3	RDDS - Program Track	2609d	03/04/19	03/01/29		47%		
4	EPDP: Standardized System for Access & Disclosure - Phase 2	2262d	07/01/20	03/01/29		39%		
5	EPDP: Standardized System for Access & Disclosure - Phase 2	23d	07/01/20	07/31/20		100%		
6	Remaining EPDP-P2 Topics Track 1 (Legal vs. Natural + Feasability of Unique Contacts)	0	07/31/21	07/31/21		100%		
8	Remaining EPDP-P2 Topics Track 2 (Accuracy)	260d	08/03/20	07/31/21		100%		
12	Board: Standardized System for Access & Disclosure - Phase 2 adopt consensus recommendations	852d	03/25/21	06/28/24		60%		
13	Board: Standardized System for Access & Disclosure Operational Design Phase	219d	03/25/21	01/25/22	5FS +168d	100%		
14	Board: Standardized System for Access & Disclosure - Phase 2 adopt consensus recommendations	852d	03/25/21	06/28/24	5FS +168d	50%		
15	EPDP_P2 Small Team - Collaborate with ICANN Board on Whois Disclosure System	369d	02/01/22	06/30/23		70%	On-Schedule	On-Target
16	IRT: Standardized System for Access & Disclosure - Phase 2	520d	07/01/24	06/26/26	14	0%	Planned	
17	SSAD Development and Implementation	699d	06/29/26	03/01/29	16	0%	Planned	
18	EPDP: Legal vs. Natural + Feasibility of Unique Contacts of Reg Data - Phase 2A	890d	08/03/20	12/29/23		51%		
19	Reset EPDP-P2A and elect new Chair	100d	08/03/20	12/18/20	5	100%		
20	EPDP: Registration Data - Phase 2A	225d	12/21/20	10/29/21	19	100%		
21	Board: Registration Data - Phase 2A adopt consensus recommendations	120d	11/01/21	04/15/22	20	100%		
22	IRT: Registration Data - Phase 2A	445d	04/18/22	12/29/23	21	1%	On-Schedule	On-Target
23	RDS2 Review Recommendations - Implementation	899d	07/23/20	01/02/24		100%		
31	IRT: Temporary Specification on gTLD Registration Data - Phase 1	1484d	03/04/19	11/07/24		69%		
32	IRT: Temporary Specification on gTLD Registration Data - Phase 1	1484d	03/04/19	11/07/24		75%	On-Schedule	On-Target
33	EPDP-P1 Rec27 Wave 1.5 & Wave 2 Other Policy Impacts	699d	03/01/21	11/02/23		57%		
34	Council to consider Wave 1.5 report and determine next steps	120d	03/01/21	08/13/21		100%		
35	Council to consider Wave Wave 2 reports and determine next steps	90d	07/01/23	11/02/23		0%	Planned	
36	Revised ICANN Procedure for Handling Whois Conflicts with Privacy Law	1423d	07/31/20	01/13/26		14%		
37	Council small scoping team to determine next steps and Council consideration	60d	07/31/20	10/22/20		100%		
38	Request ICANN org to develop revised proposal for invoking Procedure	270d	06/07/23	06/18/24		15%	On-Hold	On-Target
39	Council to deliberate findings and determine appropriate path	45d	06/19/24	08/20/24	38	0%	Planned	
40	IF required, review WPIAG Charter to determine if it's fit for purpose	30d	08/21/24	10/01/24	39	0%	Planned	
41	IF required, Council to approve charter and launch WPIAG	105d	10/02/24	02/25/25		0%		
44	IF required, Council to approve launch of EPDP	230d	02/26/25	01/13/26		0%		
48	IRT: Privacy & Proxy Services Accreditation Issues	750d	08/16/21	06/28/24		50%		
49	IRT: Privacy & Proxy Services Accreditation Issues	750d	08/16/21	06/28/24	34	50%	On-Hold	On-Target
50	IRT: Translation/Transliteration of gTLD Registration Data	750d	08/16/21	06/28/24		50%		
51	IRT: Translation/Transliteration of gTLD Registration Data	750d	08/16/21	06/28/24	34	50%	On-Hold	On-Target
52	Registration Data Accuracy	1595d	07/12/21	08/20/27		32%		
53	Registration Data Accuracy - Scoping Team	645d	07/12/21	12/29/23		78%	On-Hold	In-Trouble
54	Council: Decide to request Issue Report on Registration Data Accuracy	30d	01/01/24	02/09/24	53	0%	Planned	
55	Staff: Issue Report on Registration Data Accuracy	90d	02/12/24	06/14/24	54	0%	Planned	
56	Council: Approve PDP launch on Registration Data Accuracy	40d	06/17/24	08/09/24	55	0%	Planned	
57	Council: Approve charter on Registration Data Accuracy	40d	08/12/24	10/04/24	56	0%	Planned	
58	PDP: Registration Data Accuracy	400d	10/07/24	04/17/26		0%	Planned	
61	Board: Registration Data Accuracy adopt consensus recommendations	50d	04/20/26	06/26/26	58	0%	Planned	
62	IRT: Registration Data Accuracy	300d	06/29/26	08/20/27	61	0%	Planned	
63	RPM - Program Track	1711d	07/01/20	01/20/27		35%		
64	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 1 (URS, TMCH, Sunrise, Claims)	1043d	07/01/20	06/28/24		52%		
65	PDP: RPM - Phase 1 Review of RPMs in All gTLDs (started 4 Mar 2016)	120d	07/01/20	12/15/20		100%		
66	EPDP-P1 Rec27 Wave 1 Other Policy Impacts	77d	07/01/20	10/15/20		100%		
71	Board: RPM - Phase 1 Review of RPMs in All gTLDs adopt consensus recommendations	283d	12/16/20	01/14/22	65	100%		
72	IRT: RPM - Phase 1 Review of RPMs in All gTLDs	550d	05/23/22	06/28/24	71FS +90d	10%		
73	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 2 (UDRP)	1359d	11/05/21	01/20/27		22%		
74	PSR: Policy Status Report on UDRP	185d	11/05/21	07/21/22		100%		
75	Council: Deliberate PSR and Confirm Start of PDP	169d	07/22/22	03/15/23	74	70%		
76	Drafting Team: Charter on Review of UDRP (incl. Items 2 through 11 of Rec27 Wave1)	150d	03/16/23	10/11/23	75	0%	Planned	
77	PDP: RPM - Phase 2 Review of UDRP	525d	10/12/23	10/15/25	76	0%	Planned	
78	Board: RPM - Phase 2 Review of UDRP adopt consensus recommendations	60d	10/16/25	01/07/26	77	0%	Planned	
79	IRT: RPM - Phase 2 Review of UDRP	270d	01/08/26	01/20/27	78	0%	Planned	
80	gTLD - Program Track	1323d	07/01/20	07/25/25		52%		
81	CCWG: New gTLD Auction Proceeds (ICANN Org Grants Program)	1043d	07/01/20	06/28/24		50%		
82	CCWG: New gTLD Auction Proceeds (group completed 31 May 2020)	0	07/01/20	07/01/20		100%		
83	Council to deliberate and adopt CCWG recommendations	20d	08/03/20	08/28/20		100%		
84	Board: New gTLD Auction Proceeds - adopt consensus recommendations	466d	08/31/20	06/13/22	83	100%		
85	ICANN Org: Implement ICANN Org Grants Program	534d	06/14/22	06/28/24	84	5%		
86	PDP: New gTLD Subsequent Procedures	1323d	07/01/20	07/25/25		53%		
87	PDP: New gTLD Subsequent Procedures (started 21 Jan 2016)	168d	07/01/20	02/19/21		100%		
88	Board: New gTLD Subsequent Procedures adopt consensus recommendations	615d	02/22/21	06/30/23		87%		
89	ICANN Org: New gTLD Subsequent Procedures Operational Design Phase	340d	09/13/21	12/30/22	87FS +145d	100%		
90	Board: New gTLD Subsequent Procedures adopt consensus recommendations	615d	02/22/21	06/30/23	87	80%		
91	IRT: New gTLD Subsequent Procedures	540d	07/03/23	07/25/25	88	0%	Planned	
92	GGP: Applicant Support	429d	08/25/22	04/16/24		25%		
93	GGP: New gTLD Subsequent Procedures - Applicant Support (SubPro_GGP)	429d	08/25/22	04/16/24		25%	On-Schedule	On-Target
94	Closed Generics Facilitated Dialogue (Placeholder awaiting plan)	311d	04/22/22	06/30/23		10%	On-Schedule	On-Target
95	Name Collision Analysis Project	783d	07/01/20	06/30/23		85%		
96	Name Collision Analysis Project - Phase 1 (14 Mar 2019 start)	192d	07/01/20	03/25/21		100%		

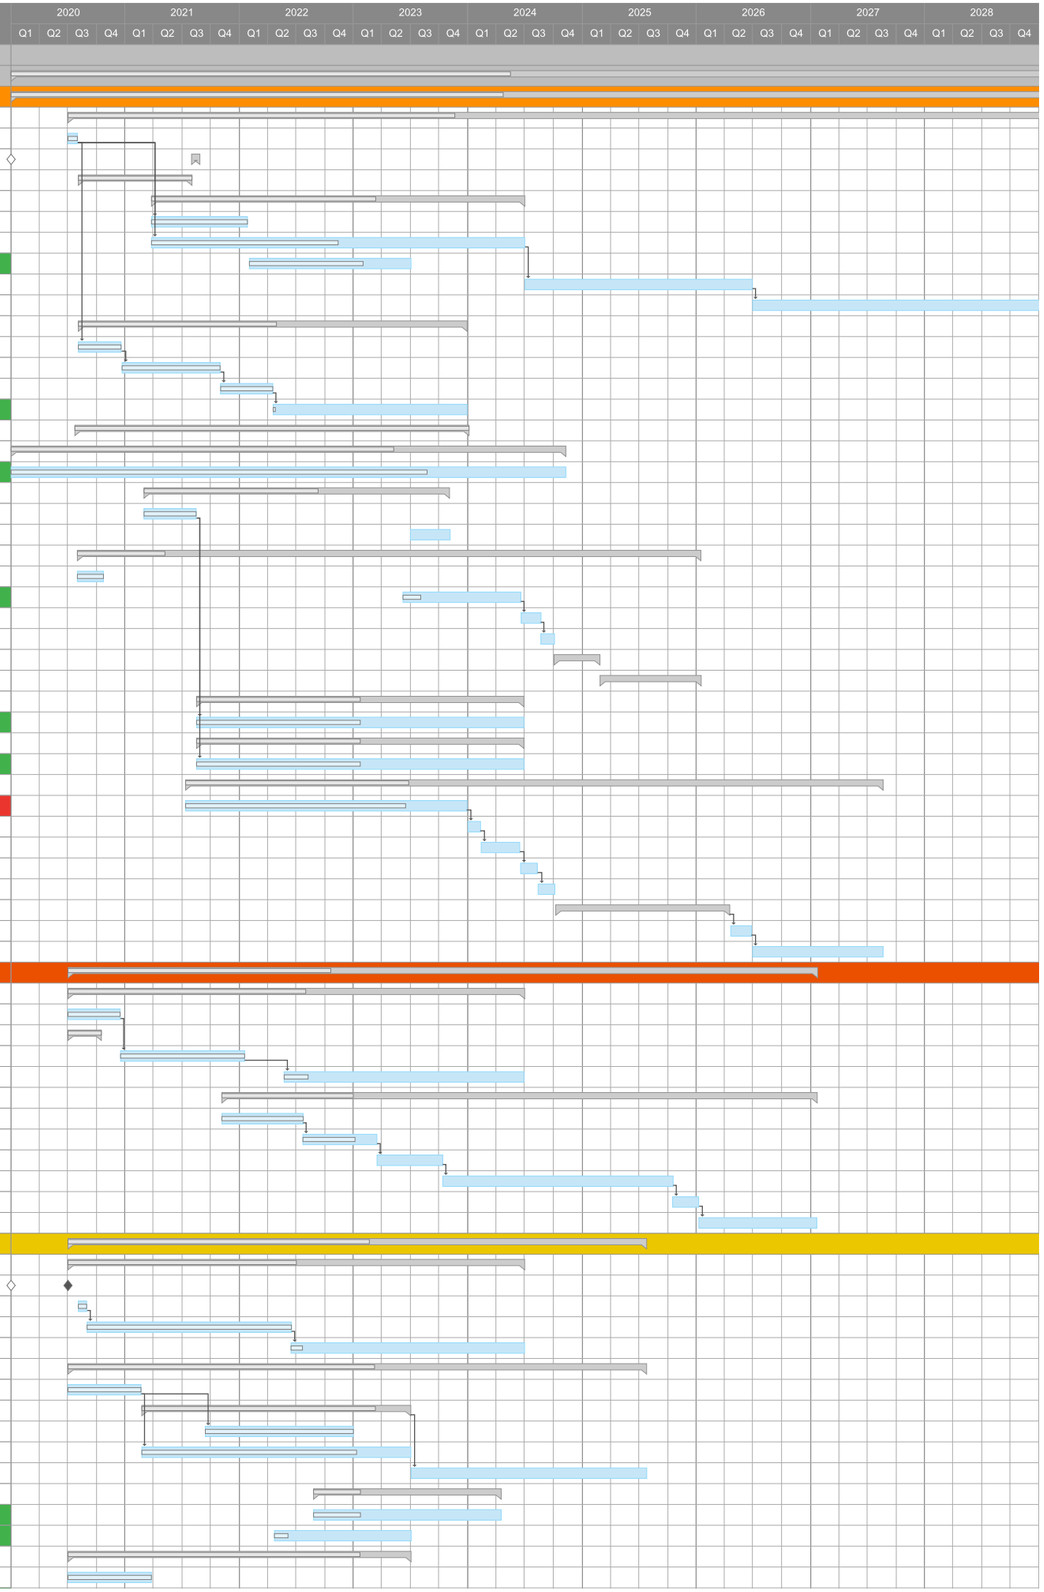

	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
97	Name Collision Analysis Project - Phase 2	565d	05/03/21	06/30/23		80%	On-Schedule	On-Target
98	**IDNs - Program Track**	**1803d**	**07/01/20**	**05/28/27**		**47%**		
99	IDN Operational Working Group (Track 1)	480d	08/03/20	06/03/22		100%		
102	EPDP: IDNs (Track 2)	1723d	10/21/20	05/28/27		33%		
103	Drafting Team: Charter on Internationalized Domain Names + EPDP Request	160d	10/21/20	06/01/21		100%		
104	EPDP: Internationalized Domain Names	1262d	05/20/21	03/20/26		32%	Revised Schedule	On-Target
105	Board: Internationalized Domain Names adopt consensus recommendations	60d	03/23/26	06/12/26	104	0%	Planned	
106	IRT: Internationalized Domain Names	250d	06/15/26	05/28/27	105	0%	Planned	
107	IDN GNSO Council Coordination w/ CCNSO Council (Track 3)	1493d	07/01/20	03/20/26		45%		
108	GNSO Council to coordinate with the CCNSO regarding IDN policy developments	1493d	07/01/20	03/20/26		45%		
109	**Expiration - Program Track**	**1910d**	**10/01/20**	**01/26/28**		**12%**		
110	PDP: Expired Domain Deletion Policy / Expired Registration Recovery Policy Policy Review	1910d	10/01/20	01/26/28		12%		
111	Council to extend PSR for 18 months or when bandwidth becomes available	45d	10/01/20	12/02/20		100%		
112	Council to Consider Request EDDP/ERRP Policy Status Report	175d	07/14/22	03/15/23	111FS +420d	75%		
113	Develop Expiration Policy Status Report (incl. Rec27 Wave1 EDDP Item 2 + ERRP Item3)	180d	03/16/23	11/22/23	112	0%	Planned	
114	Council to Request Expiration Policy Issue Report	45d	11/23/23	01/24/24	113	0%	Planned	
115	Expiration Policy Issue Report	150d	01/25/24	08/21/24		0%		
117	Council to approve PDP launch	10d	08/22/24	09/04/24	116	0%	Planned	
118	Council to approve scope and charter	25d	09/05/24	10/09/24	117	0%	Planned	
119	Expiration Policy Review	860d	10/10/24	01/26/28		0%		
120	PDP: Expiration Policy Review	400d	10/10/24	04/22/26	118	0%	Planned	
121	Board: Expiration Policy Review adopt consensus recommendations	60d	04/23/26	07/15/26	120	0%	Planned	
122	IRT: Expiration Policy Review	400d	07/16/26	01/26/28	121	0%	Planned	
123	**Transfers - Program Track**	**1912d**	**07/01/20**	**10/28/27**		**28%**		
124	PDP: Transfer Policy Review	1912d	07/01/20	10/28/27		28%		
125	Council to Request Transfer Policy Status Report	0	07/01/20	07/01/20		100%		
126	Develop Transfer Policy Status Report	0	07/01/20	07/01/20	125	100%		
127	Council to Request Transfer Policy Issue Report	0	07/01/20	07/01/20	126	100%		
128	Develop Transfer Issue Report	158d	07/01/20	02/05/21		100%		
131	Council to approve PDP launch	10d	02/05/21	02/18/21	129	100%		
132	Council to approve scope and charter	24d	02/19/21	03/24/21	131	100%		
133	Transfer Policy Review - Phase 1	1206d	02/18/21	10/02/25		39%		
134	PDP: Transfer Policy Review - Phase 1	746d	02/18/21	12/28/23		63%	Behind Schedule	At-Risk
135	Board: Transfer Policy Review - Phase 1 adopt consensus recommendations	60d	12/29/23	03/21/24	134	0%	Planned	
136	IRT: Transfer Policy Review - Phase 1	400d	03/22/24	10/02/25	135	0%	Planned	
137	Transfer Policy Review - Phase 2	1000d	12/29/23	10/28/27		0%		
138	PDP: Transfer Policy Review - Phase 2	540d	12/29/23	01/22/26	134	0%	Planned	
139	Board: Transfer Policy Review - Phase 2 adopt consensus recommendations	60d	01/23/26	04/16/26	138	0%	Planned	
140	IRT: Transfer Policy Review - Phase 2	400d	04/17/26	10/28/27	139	0%	Planned	
141	**IGO - Program Track**	**992d**	**09/24/20**	**07/12/24**		**40%**		
142	EPDP: Specific Curative Rights Protections for IGOs	992d	09/24/20	07/12/24		62%		
143	EPDP: Specific Curative Rights Protections for IGOs	550d	09/24/20	11/02/22		100%		
144	Board: Specific Curative Rights Protections for IGOs adopt consensus recommendations	172d	11/03/22	06/30/23	143	40%		
145	IRT: Specific Curative Rights Protections for IGOs	270d	07/03/23	07/12/24	144	0%	Planned	
146	PDP: Curative Rights Protections for IGO/INGOs	442d	11/03/22	07/12/24		16%		
147	Board: Curative Rights Protections for IGO/INGOs adopt consensus recommendations	172d	11/03/22	06/30/23	143	40%		
148	IRT: Curative Rights Protections for IGO/INGOs	270d	07/03/23	07/12/24	147	0%	Planned	
149	PDP: Protection of International Organization Names in All gTLDs (Remaining Acronyms)	442d	11/03/22	07/12/24		16%		
150	Board: Protection of International Organization Names in All gTLDs (Remaining Acronyms)	172d	11/03/22	06/30/23	143	40%		
151	IRT: PDP: Protection of International Organization Names in All gTLDs (Remaining Acronyms)	270d	07/03/23	07/12/24	150	0%	Planned	
152	**DNS_Abuse - Program Track**	**1195d**	**01/02/23**	**07/30/27**		**0%**		
153	Track 2 - Issues that may benefit from education / communication / outreach	260d	01/02/23	12/29/23	360	0%	On-Schedule	On-Target
154	Track 3 - Issues that may benefit from contractual negotiations between ICANN org and Contracted Parties	260d	01/01/24	12/27/24	153	0%	Planned	
155	Track 1 - Issues that may benefit from GNSO policy development	675d	12/27/24	07/30/27		0%	Planned	
164	**Accountability - Program Track**	**1043d**	**07/01/20**	**06/28/24**		**47%**		
165	Independent Review Process - Implementation Oversight Team	780d	07/01/20	06/27/23		50%		
166	IoT Oversight Team Group	780d	07/01/20	06/27/23		50%		
167	Establishment of Standing Panel for Independent Review Process	780d	07/01/20	06/27/23		50%		
168	Cross Community Working Group on Enhancing ICANN Accountability - WS2	550d	05/24/21	06/30/23		71%		
169	GNSO Council Implementation of WS2	409d	05/24/21	12/15/22		100%		
170	GNSO SG/C Implementation of WS2	550d	05/24/21	06/30/23		50%		
171	Geo Regions Review	783d	07/01/20	06/30/23		0%		
172	Geo Regions Review: Monitor for changes	783d	07/01/20	06/30/23		0%	On-Hold	
173	Multistakeholder Model Evolution	1043d	07/01/20	06/28/24		66%		
174	Monitor for MSM-Evo implementation assignments	1043d	07/01/20	06/28/24		66%		
175	**Reviews - Program Track**	**2792d**	**07/01/20**	**03/13/31**		**32%**		
176	IANA Naming Function Review	226d	07/01/20	05/12/21		100%		
180	Registration Directory Service Review RT3	640d	09/29/28	03/13/31		0%		
185	Competition, Consumer Trust and Consumer Choice RT2	640d	08/09/27	01/18/30		0%		
190	Accountability and Transparency Review 3	1043d	07/01/20	06/28/24		67%		
191	Council to form a small team to draft a public comment response to the ATRT3	22d	07/01/20	07/30/20		100%		
192	Monitor for ATRT3 implementation assignments	1043d	07/01/20	06/28/24		66%		
193	Holistic Review - Pilot	1444d	11/30/20	06/11/26		39%		
194	Holistic Review Pilot: Define Terms of Reference, Information Gaps, and Determine Prioritization to Start	674d	11/30/20	06/29/23		86%		

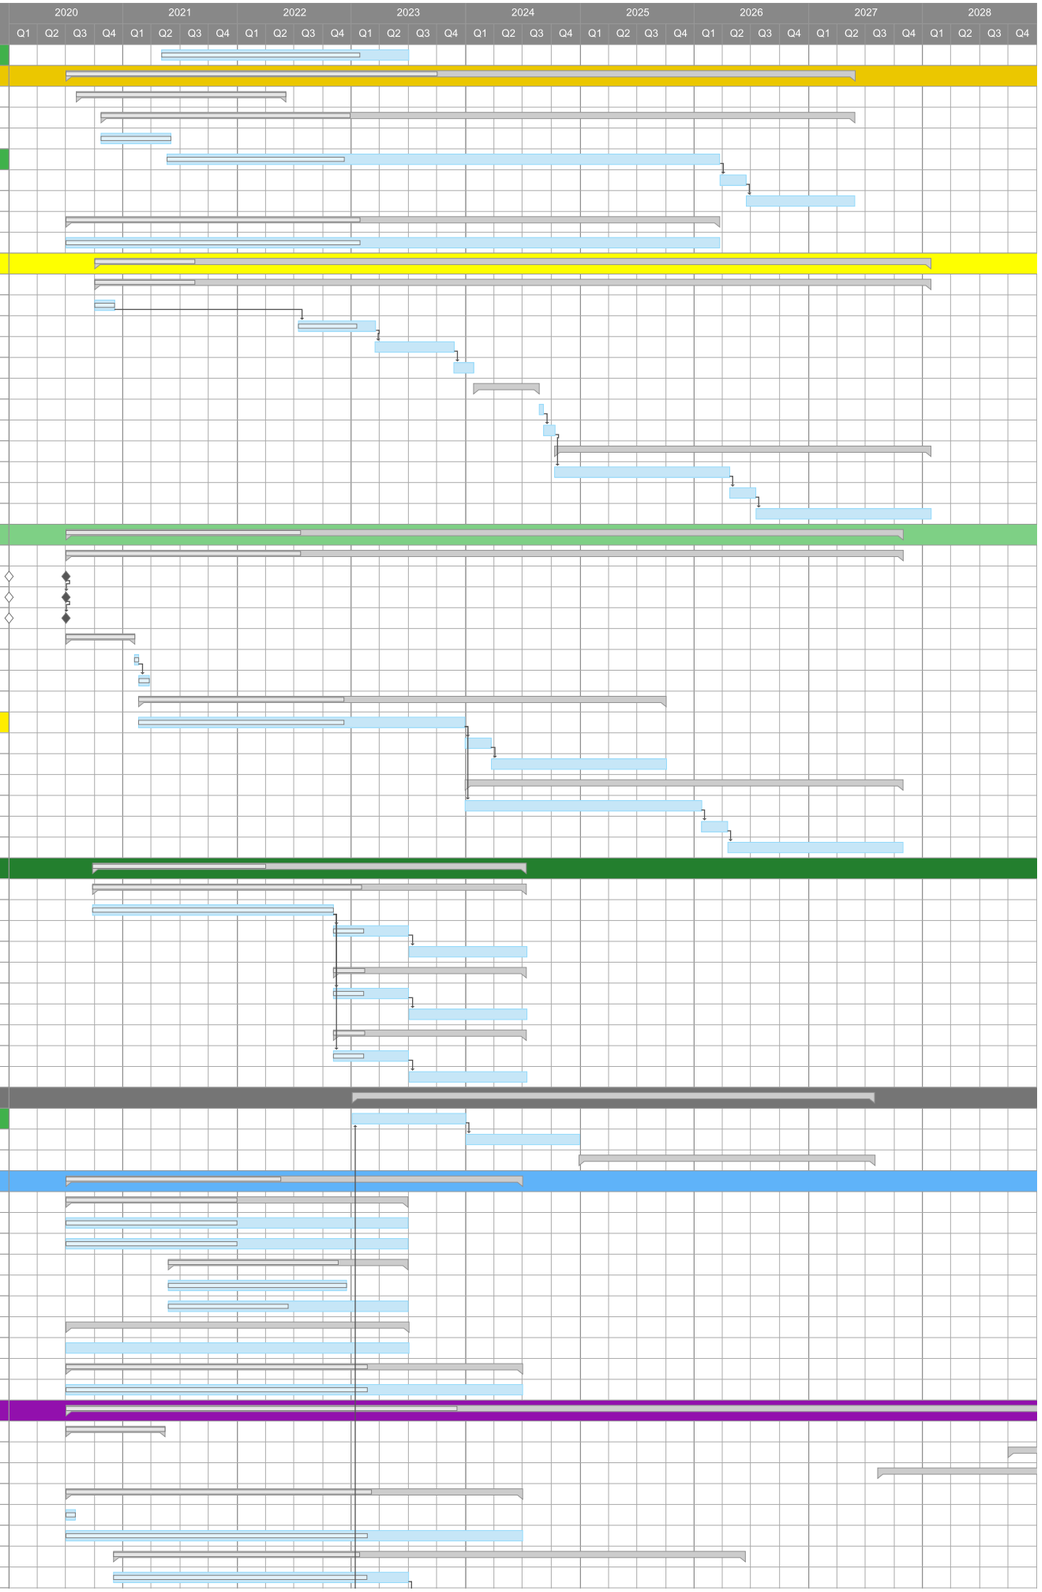

	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
195	Council SSC to select GNSO representatives on Review Team	30d	06/30/23	08/10/23	194	0%	Planned	
196	Holistic Review Pilot	400d	08/11/23	02/20/25	195	0%	Planned	
197	Board: Holistic Review Pilot deliberate and adopt consensus recommendations	70d	02/21/25	05/29/25	196	0%	Planned	
198	Council to consider Holistic Review Pilot Results	60d	05/30/25	08/21/25	197	0%	Planned	
199	Holistic Review Pilot Implement Review recommendations	270d	05/30/25	06/11/26	197	0%	Planned	
200	Accountability and Transparency Review 4	620d	06/12/26	10/26/28		0%		
201	Council SSC to select GNSO representatives on Review Team	30d	06/12/26	07/23/26	199	0%	Planned	
202	Accountability and Transparency Review 4	250d	07/24/26	07/08/27	201	0%	Planned	
203	Board: ATRT#4 deliberate and adopt consensus recommendations	70d	07/09/27	10/14/27	202	0%	Planned	
204	ATRT#4 Implement Review recommendations	270d	10/15/27	10/26/28	203	0%	Planned	
205	Security, Stability and Resiliency of the DNS #2	1044d	07/01/20	07/01/24		65%		
206	Security, Stability and Resiliency of the DNS #2	160d	07/01/20	02/09/21		100%		
207	Board: SSR#2 deliberate and adopt consensus recommendations	117d	02/10/21	07/22/21	206	100%		
208	Monitor for SSR#2 implementation assignments	767d	07/23/21	07/01/24	207	53%		
209	Security, Stability and Resiliency of the DNS #3	640d	09/29/28	03/13/31		0%		
214	CSC Effectiveness Review - 2021	525d	07/01/21	07/05/23		68%		
215	Council: establish terms of reference and determine is prior review recs were implemented	65d	07/01/21	09/29/21		100%		
216	CSC Effectiveness Review 2021	390d	09/30/21	03/29/23	215	85%		
217	Board: CSC Effectiveness Review deliberate and adopt consensus recommendations	70d	03/30/23	07/05/23	216	0%	Planned	
218	Consider CSC Effectiveness Review Results	60d	03/30/23	06/21/23	216	0%	Planned	
219	CSC Effectiveness Review - 2024	400d	08/01/24	02/11/26		0%		
224	GNSO Review RT3	680d	06/12/26	01/18/29		0%		
230	**Root_System - Program Track**	**870d**	**07/01/20**	**10/31/23**		**75%**		
231	Root Server System Governance Working Group (GWG)	870d	07/01/20	10/31/23		75%	On-Schedule	On-Target
232	**ICANN_Planning - Program Track**	**1163d**	**01/15/20**	**06/28/24**		**71%**		
233	ICANN Planning - FY22	282d	01/15/20	02/11/21		100%		
236	ICANN Planning - FY23	359d	01/15/21	06/01/22		100%		
240	ICANN Planning - FY24	316d	01/15/22	03/31/23		97%		
241	Trend Identification - FY24	56d	01/15/22	04/01/22		100%		
242	ICANN Planning Prioritization Framework FY24	44d	10/01/22	11/30/22		100%		
243	IANA & ICANN Budget & OPs Plan for Public Comment - FY24	96d	10/01/22	02/10/23		90%		
244	GNSO Standing Committee on FY24 Budget and Operations 2022-2023	131d	10/01/22	03/31/23		100%		
245	ICANN Planning - FY25	381d	01/15/23	06/28/24		1%		
246	Trend Identification - FY25	56d	01/15/23	03/31/23		1%		
247	ICANN Planning Prioritization Framework FY25	44d	04/01/23	05/31/23		0%	Planned	
248	IANA & ICANN Budget & OPs Plan for Public Comment - FY25	96d	10/01/23	02/09/24		0%	Planned	
249	IANA & ICANN 5 Year Strategic Planning - FY26-FY30	250d	05/01/23	04/12/24		0%	Planned	
250	GNSO Budget & OPs Townhall on FY25 Budget and Operations 2023-2024	357d	02/16/23	06/28/24		1%		
251	**Operations - Program Track**	**1432d**	**06/01/20**	**11/25/25**		**51%**		
252	Participant of Empowered Community	1382d	07/01/20	10/16/25		48%		
253	Participant of Empowered Community - 2020	96d	07/01/20	11/11/20		100%		
256	Participant of Empowered Community - 2021	235d	11/12/20	10/06/21		100%		
259	Participant of Empowered Community - 2022	271d	10/07/21	10/20/22		100%		
262	Participant of Empowered Community - 2023	265d	10/21/22	10/26/23		24%		
263	Participant of Empowered Community - 2023	250d	10/21/22	10/05/23	261	25%		
264	Elect new participant to Empowered Community	15d	10/06/23	10/26/23	263	0%	Planned	
265	Participant of Empowered Community - 2024	265d	10/27/23	10/31/24		0%		
268	Participant of Empowered Community - 2025	250d	11/01/24	10/16/25		0%		
270	Participation on Customer Standing Committee	1394d	06/01/20	10/02/25		53%		
271	Customer Standing Committee - 2020	132d	07/01/20	12/31/20		100%		
274	Customer Standing Committee - 2021	349d	06/01/20	09/30/21		100%		
277	Customer Standing Committee - 2022	305d	08/01/21	09/29/22		100%		
280	Customer Standing Committee - 2023	307d	08/01/22	10/03/23		40%		
281	Council Approval - Customer Standing Committee slate - 2023	22d	08/01/22	08/30/22		100%		
282	Customer Standing Committee - 2023	261d	10/04/22	10/03/23	281FS +24d	35%		
283	Customer Standing Committee - 2024	307d	08/01/23	10/02/24				
286	Customer Standing Committee - 2025	306d	08/01/24	10/02/25				
289	Participation on NomCom	1347d	09/01/20	10/29/25		47%		
290	GNSO Participation on NomCom - 2020-2021	297d	09/01/20	10/20/21		100%		
291	GNSO Council to Confirm NomCom Job Description	1d	09/23/21	09/23/21		100%		
292	GNSO Participation on NomCom - 2021-2022	241d	10/20/21	09/21/22		100%		
293	GNSO Council to Confirm NomCom Job Description	1d	11/17/22	11/17/22		100%		
294	GNSO Participation on NomCom - 2022-2023	286d	09/21/22	10/25/23		35%		
295	GNSO Council to Confirm NomCom Job Description	1d	09/21/23	09/21/23		0%	Planned	
296	GNSO Participation on NomCom - 2023-2024	276d	10/25/23	11/13/24		0%	Planned	
297	GNSO Council to Confirm NomCom Job Description	1d	09/19/24	09/19/24		0%	Planned	
298	GNSO Participation on NomCom - 2024-2025	251d	11/13/24	10/29/25		0%	Planned	
299	Stakeholder Support - Registry Stakeholder Group	1304d	07/01/20	06/30/25		52%		
300	FY21 Stakeholder Support - Registry Stakeholder Group	261d	07/01/20	06/30/21		100%		
301	FY22 Stakeholder Support - Registry Stakeholder Group	261d	07/01/21	06/30/22		100%		
302	FY23 Stakeholder Support - Registry Stakeholder Group	261d	07/01/22	06/30/23		60%		
303	FY24 Stakeholder Support - Registry Stakeholder Group	261d	07/01/23	06/28/24		0%	Planned	
304	FY25 Stakeholder Support - Registry Stakeholder Group	261d	07/01/24	06/30/25		0%	Planned	
305	Stakeholder Support - Registrar Stakeholder Group	1304d	07/01/20	06/30/25		52%		

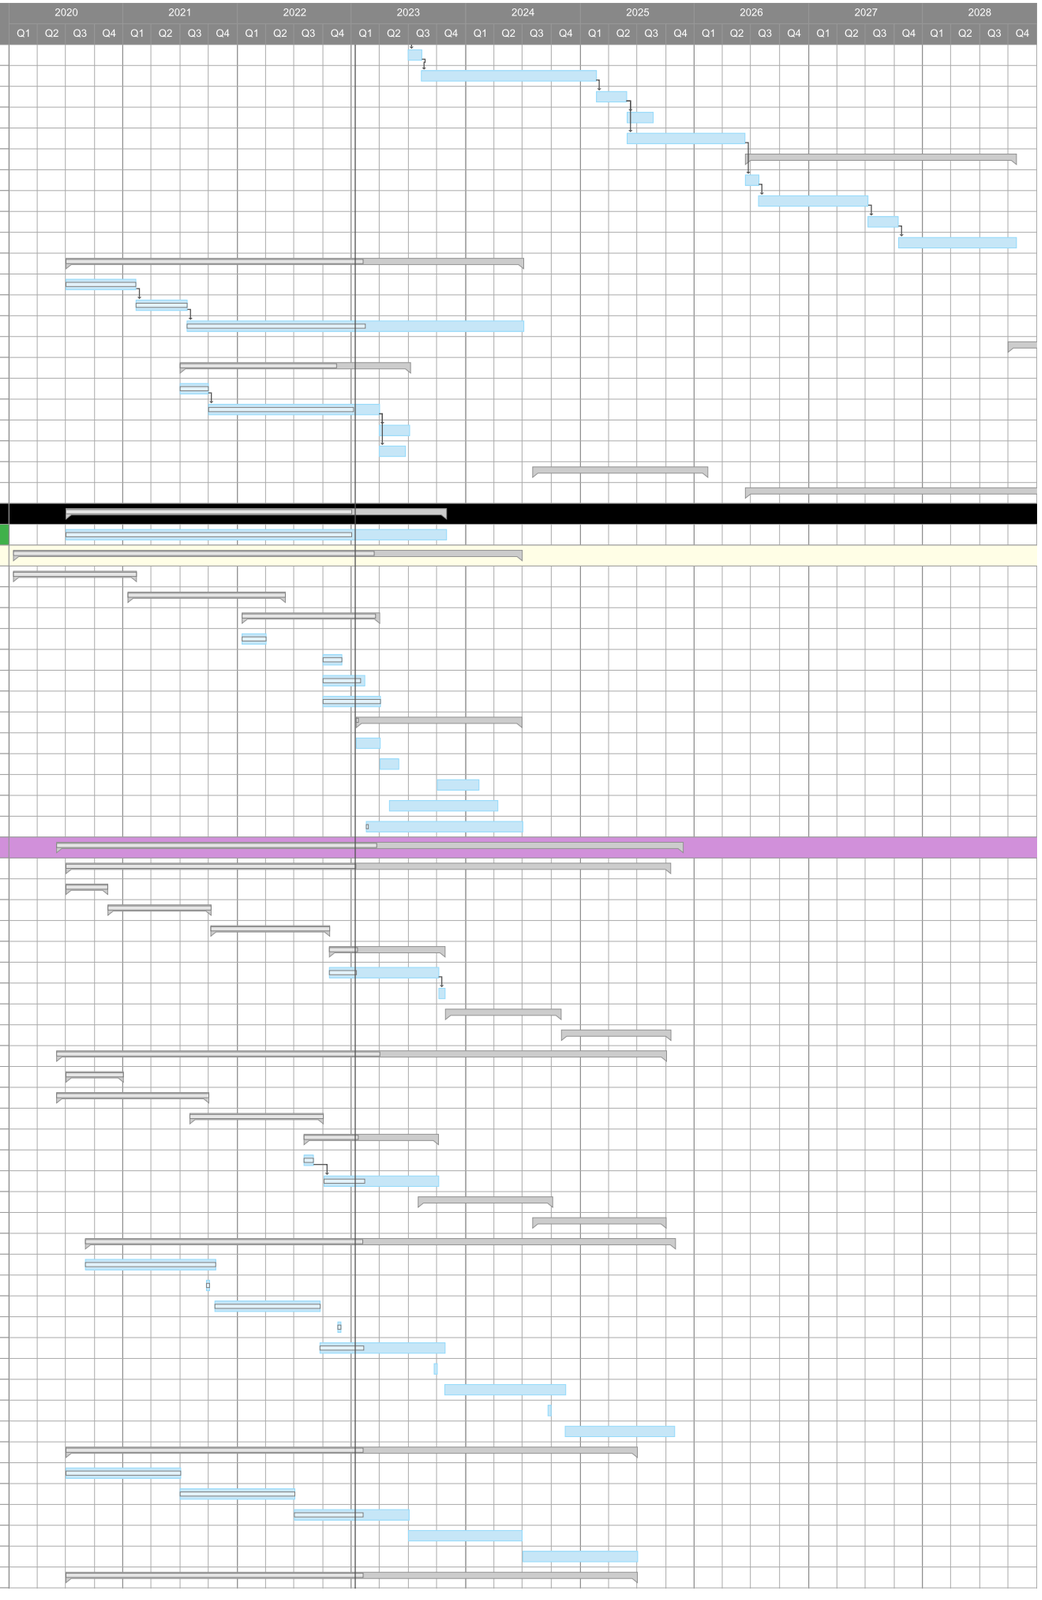

	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
306	FY21 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/20	06/30/21		100%		
307	FY22 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/21	06/30/22		100%		
308	FY23 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/22	06/30/23		60%		
309	FY24 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/23	06/28/24		0%	Planned	
310	FY25 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/24	06/30/25		0%	Planned	
311	Stakeholder Support - NCSG/NCUC/NPOC	1304d	07/01/20	06/30/25		52%		
312	FY21 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/20	06/30/21		100%		
313	FY22 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/21	06/30/22		100%		
314	FY23 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/22	06/30/23		60%		
315	FY24 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/23	06/28/24		0%	Planned	
316	FY25 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/24	06/30/25		0%	Planned	
317	Stakeholder Support - CSG/BC/IPC/ISPCP	1304d	07/01/20	06/30/25		52%		
318	FY21 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/20	06/30/21		100%		
319	FY22 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/21	06/30/22		100%		
320	FY23 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/22	06/30/23		60%		
321	FY24 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/23	06/28/24		0%	Planned	
322	FY25 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/24	06/30/25		0%	Planned	
323	GNSO Council	1410d	07/01/20	11/25/25		54%		
324	GNSO Council - Monthly Meetings	1347d	09/01/20	10/29/25		47%		
325	GNSO Council - Monthly Meetings 2020-2021	297d	09/01/20	10/20/21		100%		
326	GNSO Council - Monthly Meetings 2021-2022	241d	10/20/21	09/21/22		100%		
327	GNSO Council - Monthly Meetings 2022-2023	286d	09/21/22	10/25/23		35%	On-Schedule	On-Target
328	GNSO Council - Monthly Meetings 2023-2024	276d	10/25/23	11/13/24		0%	Planned	
329	GNSO Council - Monthly Meetings 2024-2025	251d	11/13/24	10/29/25		0%	Planned	
330	GNSO Council - Leadership Meetings	1347d	09/01/20	10/29/25		47%		
331	GNSO Council - Leadership Meetings 2020-2021	297d	09/01/20	10/20/21		100%		
332	GNSO Council - Leadership Meetings 2021-2022	241d	10/20/21	09/21/22		100%		
333	GNSO Council - Leadership Meetings 2022-2023	286d	09/21/22	10/25/23		35%	On-Schedule	On-Target
334	GNSO Council - Leadership Meetings 2023-2024	276d	10/25/23	11/13/24		0%	Planned	
335	GNSO Council - Leadership Meetings 2024-2025	251d	11/13/24	10/29/25		0%	Planned	
336	GNSO Council - Action Items	1347d	09/01/20	10/29/25		47%		
337	GNSO Council - Action Items 2020-2021	297d	09/01/20	10/20/21		100%		
338	GNSO Council - Action Items 2021-2022	241d	10/20/21	09/21/22		100%		
339	GNSO Council - Action Items 2022-2023	286d	09/21/22	10/25/23		35%	On-Schedule	On-Target
340	GNSO Council - Action Items 2023-2024	276d	10/25/23	11/13/24		0%	Planned	
341	GNSO Council - Action Items 2024-2025	251d	11/13/24	10/29/25		0%	Planned	
342	GNSO Council - Small Teams	1385d	07/12/20	10/30/25		57%		
343	GNSO Council - Small Teams - 2020-2021	270d	07/12/20	07/22/21		100%		
353	GNSO Council - Small Teams - 2021-2022	231d	11/03/21	09/21/22		100%		
359	GNSO Council - Small Teams - 2022-2023	430d	11/08/21	06/30/23		77%		
360	Next steps regarding DNS Abuse	300d	11/08/21	12/30/22		100%		
361	SubPro ODP Question & Answer Review Team	130d	06/24/22	12/22/22		100%		
362	GNSO PDP Improvements (Staff + Council)	261d	07/01/22	06/30/23		40%	On-Schedule	On-Target
363	GNSO Council - Small Teams - 2023-2024	261d	11/01/23	10/30/24		0%		
365	GNSO Council - Small Teams - 2024-2025	260d	11/01/24	10/30/25		0%		
367	GNSO Standing Committee on Budget and Operations	335d	11/02/20	02/11/22		100%		
376	Council Committee for Overseeing & Implementing Continuous Improvement	463d	06/16/21	03/24/23		66%		
377	CCOICI Assignment #4	398d	08/26/21	03/06/23		55%	On-Schedule	On-Target
378	CCOICI Assignment #6	340d	11/19/21	03/09/23		88%	On-Schedule	On-Target
379	CCOICI Assignment WS2	187d	03/30/22	12/15/22		100%		
380	CCOICI Pilot Program Assessment	463d	06/16/21	03/24/23		46%	On-Hold	On-Target
381	GNSO Standing Selection Committee	1325d	10/28/20	11/25/25		54%		
382	GNSO Standing Selection Committee 2020-2021	260d	10/28/20	10/26/21		100%		
389	GNSO Standing Selection Committee 2021-2022	270d	10/27/21	11/08/22		100%		
396	GNSO Standing Selection Committee 2022-2023	290d	09/21/22	10/31/23		72%		
397	Refresh roster and confirm Chair (within 3 weeks of AGM)	60d	09/21/22	12/13/22		100%		
398	Standing Selection Committee (SSC) 2022-2023	230d	12/14/22	10/31/23		65%		
399	Standing Selection Committee (SSC) fill positions as assigned	230d	12/14/22	10/31/23	397	100%		
400	Appoint GNSO Representative to Fellowship Program	30d	12/14/22	01/24/23	397	100%		
401	Obtain EOIs and Appoint CSC Liaison as Required	70d	05/31/23	09/05/23	397SS +180d			
402	Appoint GAC Liaison as Required (Not required til 2023-2024)	70d	06/28/23	10/03/23	397SS +200d			
403	GNSO Standing Selection Committee 2023-2024	270d	10/25/23	11/05/24			Planned	
410	GNSO Standing Selection Committee 2024-2025	270d	11/13/24	11/25/25			Planned	
417	GNSO Council - Strategic Planning Session	1163d	09/01/20	02/13/25		60%		
418	GNSO Council - Strategic Planning Session - 2020-2021	120d	09/01/20	02/15/21		100%		
419	GNSO Council - Strategic Planning Session - 2021-2022	120d	09/01/21	02/15/22		100%		
420	GNSO Council - Strategic Planning Session - 2022-2023	120d	09/01/22	02/15/23		100%		
421	GNSO Council - Strategic Planning Session - 2023-2024	120d	09/01/23	02/15/24		0%	Planned	
422	GNSO Council - Strategic Planning Session - 2024-2025	120d	09/01/24	02/13/25		0%	Planned	
423	GNSO Elections - [PLACEHOLDER SECTION]							
427	ICANN Meeting Planning, Meeting, Respond to GAC Advice	1309d	07/01/20	07/07/25		52%		
428	ICANN69	95d	07/01/20	11/10/20		100%		
432	ICANN70	95d	12/01/20	04/12/21		100%		
436	ICANN71	70d	04/01/21	07/07/21		100%		

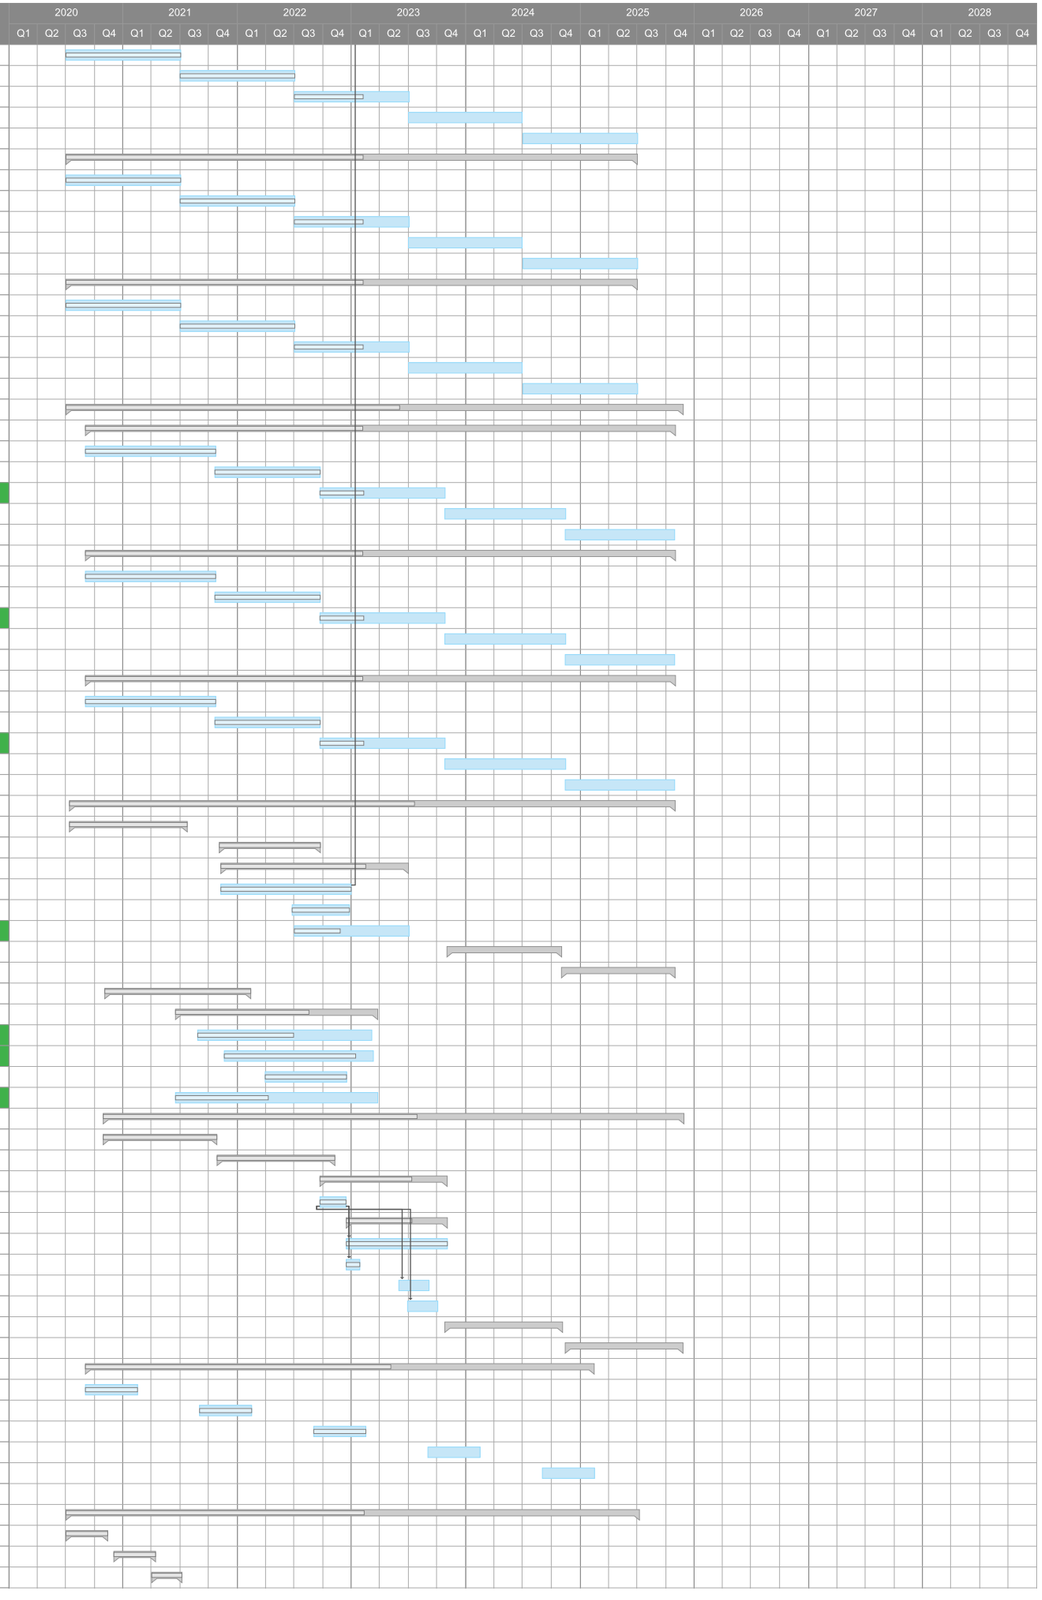
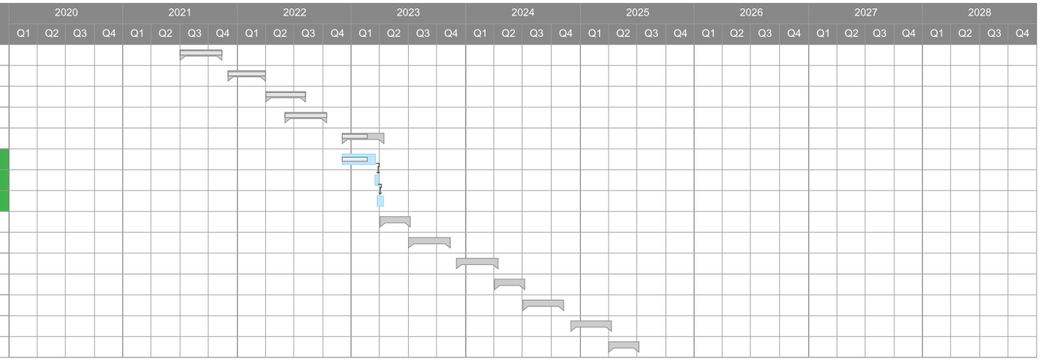
	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
440	ICANN72	95d	07/01/21	11/10/21		100%		
444	ICANN73	87d	12/01/21	03/31/22		100%		
448	ICANN74	90d	04/01/22	08/04/22		100%		
452	ICANN75	95d	06/01/22	10/11/22		100%		
456	ICANN76	95d	12/01/22	04/12/23		59%		
457	ICANN76 Meeting Planning	75d	12/01/22	03/15/23		75%	On-Schedule	On-Target
458	ICANN76 ICANN Meeting	5d	03/16/23	03/22/23	457	0%	On-Schedule	On-Target
459	ICANN76 Respond to GAC Advice	15d	03/23/23	04/12/23	458	0%	On-Schedule	On-Target
460	ICANN77	70d	04/01/23	07/06/23		0%		
464	ICANN78	95d	07/01/23	11/09/23		0%		
468	ICANN79	95d	12/01/23	04/11/24		0%		
472	ICANN80	70d	04/01/24	07/05/24		0%		
476	ICANN81	95d	07/01/24	11/08/24		0%		
480	ICANN82	95d	12/01/24	04/10/25		0%		
484	ICANN83	70d	04/01/25	07/07/25		0%
