	WBS	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
1		Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
2		GNSO Portfolio Management Tool	3270d	03/04/19	09/12/31		41%		
3	1	RDDS - Program Track	2609d	03/04/19	03/01/29		47%		
4	1.1	EPDP: Standardized System for Access & Disclosure - Phase 2	2262d	07/01/20	03/01/29		38%		
19	1.2	EPDP: Legal vs. Natural + Feasibility of Unique Contacts of Reg Data - Phase 2A	890d	08/03/20	12/29/23		51%		
24	1.3	RDS2 Review Recommendations - Implementation	899d	07/23/20	01/02/24		100%		
32	1.4	IRT: Temporary Specification on gTLD Registration Data - Phase 1	1539d	03/04/19	01/23/25		69%		
37	1.5	Revised ICANN Procedure for Handling Whois Conflicts with Privacy Law	1432d	07/31/20	01/26/26		14%		
49	1.6	IRT: Privacy & Proxy Services Accreditation Issues	751d	08/16/21	07/01/24		50%		
51	1.7	IRT: Translation/Transliteration of gTLD Registration Data	751d	08/16/21	07/01/24		50%		
53	1.8	Registration Data Accuracy	1595d	07/12/21	08/20/27		32%		
64	2	RPM - Program Track	2283d	07/01/20	03/30/29		33%		
65	2.1	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 1 (URS, TMCH, Sunrise, Claims)	1175d	07/01/20	12/31/24		47%		
74	2.2	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 2 (UDRP)	1931d	11/05/21	03/30/29		24%		
82	3	gTLD - Program Track	1175d	07/01/20	12/31/24		58%		
83	3.1	CCWG: New gTLD Auction Proceeds (ICANN Org Grants Program)	1043d	07/01/20	06/28/24		50%		
88	3.2	PDP: New gTLD Subsequent Procedures	1175d	07/01/20	12/31/24		46%		
95	3.3	GGP: Applicant Support	429d	08/25/22	04/16/24		37%		
97	3.4	Closed Generics Facilitated Dialogue	311d	04/22/22	06/30/23		80%	On-Schedule	On-Target
98	3.5	Name Collision Analysis Project	870d	07/01/20	10/31/23		85%		
101	4	IDNs - Program Track	1803d	07/01/20	05/28/27		50%		
102	4.1	IDN Operational Working Group (Track 1)	480d	08/03/20	06/03/22		100%		
105	4.2	EPDP: IDNs (Track 2)	1723d	10/21/20	05/28/27		38%		
110	4.3	IDN GNSO Council Coordination w/ CCNSO Council (Track 3)	1493d	07/01/20	03/20/26		49%		
112	5	Expiration - Program Track	2182d	10/01/20	02/09/29		14%		
113	5.1	PDP: Expired Domain Deletion Policy / Expired Registration Recovery Policy Policy Review	2182d	10/01/20	02/09/29		14%		
126	6	Transfers - Program Track	1757d	07/01/20	03/25/27		41%		
127	6.1	PDP: Transfer Policy Review	1757d	07/01/20	03/25/27		41%		
140	7	IGO - Program Track	1137d	09/24/20	01/31/25		38%		
141	7.1	EPDP: Specific Curative Rights Protections for IGOs	1137d	09/24/20	01/31/25		58%		
145	7.2	PDP: Curative Rights Protections for IGO/INGOs	587d	11/03/22	01/31/25		18%		
148	7.3	PDP: Protection of International Organization Names in All gTLDs (Remaining Acronyms)	587d	11/03/22	01/31/25		18%		
151	8	DNS_Abuse - Program Track	1273d	03/15/23	01/28/28		0%		
152	8.1	Next steps regarding DNS Abuse (Council small team reconvened)	78d	03/15/23	06/30/23		1%	On-Schedule	On-Target
153	8.2	Track 2 - Issues that may benefit from education / communication / outreach	260d	07/03/23	06/28/24	152	0%	On-Schedule	On-Target
154	8.3	Track 3 - Issues that may benefit from contractual negotiations between ICANN org and Contracted Parties	260d	07/01/24	06/27/25	153	0%	Planned	
155	8.4	Track 1 - Issues that may benefit from GNSO policy development	675d	06/27/25	01/28/28		0%	Planned	
164	9	Accountability - Program Track	1043d	07/01/20	06/28/24		52%		
165	9.1	Independent Review Process - Implementation Oversight Team	1042d	07/01/20	06/27/24		70%		
168	9.2	Cross Community Working Group on Enhancing ICANN Accountability - WS2	810d	05/24/21	06/28/24		73%		
171	9.3	Geo Regions Review	1043d	07/01/20	06/28/24		0%		
173	9.4	Multistakeholder Model Evolution	1043d	07/01/20	06/28/24		70%		
175	10	Reviews - Program Track	2923d	07/01/20	09/12/31		33%		
176	10.1	IANA Naming Function Review	226d	07/01/20	05/12/21		100%		
180	10.2	Registration Directory Service Review RT3	640d	04/02/29	09/12/31		0%		
185	10.3	Competition, Consumer Trust and Consumer Choice RT2	640d	01/13/27	06/26/29		0%		
190	10.4	Accountability and Transparency Review 3	1043d	07/01/20	06/28/24		71%		
193	10.5	Holistic Review - Pilot	1575d	11/30/20	12/11/26		37%		
200	10.6	Accountability and Transparency Review 4	620d	12/14/26	04/27/29		0%		
205	10.7	Security, Stability and Resiliency of the DNS #2	1044d	07/01/20	07/01/24		69%		
209	10.8	Security, Stability and Resiliency of the DNS #3	640d	04/02/29	09/12/31		0%		
214	10.9	CSC Effectiveness Review - 2021	543d	07/01/21	07/31/23		75%		
219	10.10	CSC Effectiveness Review - 2024	400d	08/01/24	02/11/26		0%		
224	10.11	GNSO Review RT3	680d	12/14/26	07/20/29		0%		
230	11	Root_System - Program Track	870d	07/01/20	10/31/23		82%		
231	11.1	Root Server System Governance Working Group (GWG)	870d	07/01/20	10/31/23		82%	On-Schedule	On-Target
232	12	ICANN_Planning - Program Track	1163d	01/15/20	06/28/24		74%		
233	12.1	ICANN Planning - FY22	282d	01/15/20	02/11/21		100%		
236	12.2	ICANN Planning - FY23	359d	01/15/21	06/01/22		100%		
240	12.3	ICANN Planning - FY24	285d	01/15/22	02/16/23		100%		
245	12.4	ICANN Planning - FY25	358d	02/15/23	06/28/24		5%		
251	13	Operations - Program Track	1432d	06/01/20	11/25/25		55%		
252	13.1	Participant of Empowered Community	1382d	07/01/20	10/16/25		53%		
270	13.2	Participation on Customer Standing Committee	1394d	06/01/20	10/02/25		56%		
289	13.3	Participation on NomCom	1347d	09/01/20	10/29/25		50%		
299	13.4	Stakeholder Support - Registry Stakeholder Group	1304d	07/01/20	06/30/25		56%		
305	13.5	Stakeholder Support - Registrar Stakeholder Group	1304d	07/01/20	06/30/25		56%		
311	13.6	Stakeholder Support - NCSG/NCUC/NPOC	1304d	07/01/20	06/30/25		56%		
317	13.7	Stakeholder Support - CSG/BC/IPC/ISPCP	1304d	07/01/20	06/30/25		56%		
323	13.8	GNSO Council	1410d	07/01/20	11/25/25		57%		

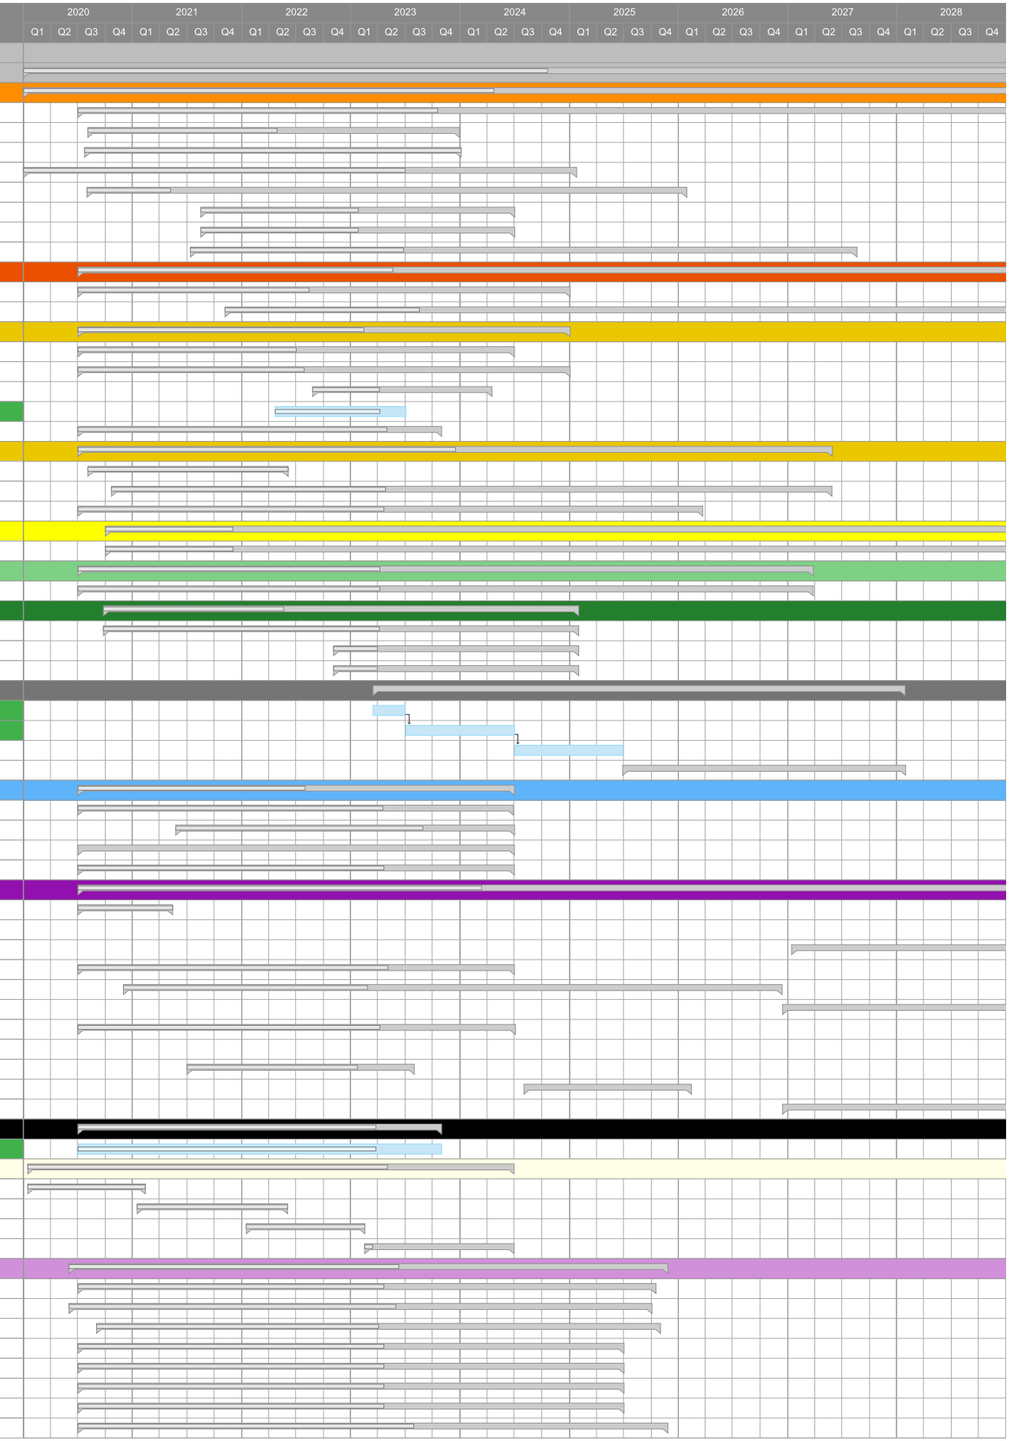

	WBS	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
1		Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
2		GNSO Portfolio Management Tool	3270d	03/04/19	09/12/31		41%		
3	1	RDDS - Program Track	2609d	03/04/19	03/01/29		47%		
4	1.1	EPDP: Standardized System for Access & Disclosure - Phase 2	2262d	07/01/20	03/01/29		38%		
5	1.1.1	EPDP: Standardized System for Access & Disclosure - Phase 2	23d	07/01/20	07/31/20		100%		
6	1.1.2	Remaining EPDP-P2 Topics Track 1 (Legal vs. Natural + Feasability of Unique Contacts)	0	07/31/21	07/31/21		100%		
8	1.1.3	Remaining EPDP-P2 Topics Track 2 (Accuracy)	260d	08/03/20	07/31/21		100%		
12	1.1.4	Board: Standardized System for Access & Disclosure - Phase 2 adopt consensus recommendations	852d	03/25/21	06/28/24		60%		
13	1.1.4.1	Board: Standardized System for Access & Disclosure Operational Design Phase	219d	03/25/21	01/25/22	5FS +168d	100%		
14	1.1.4.2	Board: Standardized System for Access & Disclosure - Phase 2 adopt consensus recommendations	852d	03/25/21	06/28/24	5FS +168d	50%		
15	1.1.5	EPDP_P2 Small Team - Collaborate with ICANN Board on Whois Disclosure System	478d	02/01/22	11/30/23		70%	On-Schedule	On-Target
16	1.1.6	ICANN Org: Build RDRS System and launch into Production	206d	02/16/23	11/30/23		10%	On-Schedule	On-Target
17	1.1.7	IRT: Standardized System for Access & Disclosure - Phase 2	520d	07/01/24	06/26/26	14	0%	Planned	
18	1.1.8	SSAD Development and Implementation	699d	06/29/26	03/01/29	17	0%	Planned	
19	1.2	EPDP: Legal vs. Natural + Feasibility of Unique Contacts of Reg Data - Phase 2A	890d	08/03/20	12/29/23		51%		
20	1.2.1	Reset EPDP-P2A and elect new Chair	100d	08/03/20	12/18/20	5	100%		
21	1.2.2	EPDP: Registration Data - Phase 2A	225d	12/21/20	10/29/21	20	100%		
22	1.2.3	Board: Registration Data - Phase 2A adopt consensus recommendations	120d	11/01/21	04/15/22	21	100%		
23	1.2.4	IRT: Registration Data - Phase 2A	445d	04/18/22	12/29/23	22	1%	On-Hold	
24	1.3	RDS2 Review Recommendations - Implementation	899d	07/23/20	01/02/24		100%		
32	1.4	IRT: Temporary Specification on gTLD Registration Data - Phase 1	1539d	03/04/19	01/23/25		69%		
33	1.4.1	IRT: Temporary Specification on gTLD Registration Data - Phase 1	1539d	03/04/19	01/23/25		74%	On-Schedule	On-Target
34	1.4.2	EPDP-P1 Rec27 Wave 1.5 & Wave 2 Other Policy Impacts	699d	03/01/21	11/02/23		57%		
37	1.5	Revised ICANN Procedure for Handling Whois Conflicts with Privacy Law	1432d	07/31/20	01/26/26		14%		
38	1.5.1	Council small scoping team to determine next steps and Council consideration	60d	07/31/20	10/22/20		100%		
39	1.5.2	Request ICANN org to develop revised proposal for invoking Procedure	279d	06/07/23	07/01/24		15%	On-Hold	On-Target
40	1.5.3	Council to deliberate findings and determine appropriate path	45d	07/02/24	09/02/24	39	0%	Planned	
41	1.5.4	IF required, review WPIAG Charter to determine if it's fit for purpose	30d	09/03/24	10/14/24	40	0%	Planned	
42	1.5.5	IF required, Council to approve charter and launch WPIAG	105d	10/15/24	03/10/25		0%		
45	1.5.6	IF required, Council to approve launch of EPDP	230d	03/11/25	01/26/26		0%		
49	1.6	IRT: Privacy & Proxy Services Accreditation Issues	751d	08/16/21	07/01/24		50%		
50	1.6.1	IRT: Privacy & Proxy Services Accreditation Issues	751d	08/16/21	07/01/24	35	50%	On-Hold	On-Target
51	1.7	IRT: Translation/Transliteration of gTLD Registration Data	751d	08/16/21	07/01/24		50%		
52	1.7.1	IRT: Translation/Transliteration of gTLD Registration Data	751d	08/16/21	07/01/24	35	50%	On-Hold	On-Target
53	1.8	Registration Data Accuracy	1595d	07/12/21	08/20/27		32%		
54	1.8.1	Registration Data Accuracy - Scoping Team	645d	07/12/21	12/29/23		78%	On-Hold	In-Trouble
55	1.8.2	Council: Decide to request Issue Report on Registration Data Accuracy	30d	01/01/24	02/09/24	54	0%	Planned	
56	1.8.3	Staff: Issue Report on Registration Data Accuracy	90d	02/12/24	06/14/24	55	0%	Planned	
57	1.8.4	Council: Approve PDP launch on Registration Data Accuracy	40d	06/17/24	08/09/24	56	0%	Planned	
58	1.8.5	Council: Approve charter on Registration Data Accuracy	40d	08/12/24	10/04/24	57	0%	Planned	
59	1.8.6	PDP: Registration Data Accuracy	400d	10/07/24	04/17/26		0%	Planned	
62	1.8.7	Board: Registration Data Accuracy adopt consensus recommendations	50d	04/20/26	06/26/26	59	0%	Planned	
63	1.8.8	IRT: Registration Data Accuracy	300d	06/29/26	08/20/27	62	0%	Planned	
64	2	RPM - Program Track	2283d	07/01/20	03/30/29		33%		
65	2.1	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 1 (URS, TMCH, Sunrise, Claims)	1175d	07/01/20	12/31/24		47%		
66	2.1.1	PDP: RPM - Phase 1 Review of RPMs in All gTLDs (started 4 Mar 2016)	120d	07/01/20	12/15/20		100%		
67	2.1.2	EPDP-P1 Rec27 Wave 1 Other Policy Impacts	77d	07/01/20	10/15/20		100%		
72	2.1.3	Board: RPM - Phase 1 Review of RPMs in All gTLDs adopt consensus recommendations	283d	12/16/20	01/14/22	66	100%		
73	2.1.4	IRT: RPM - Phase 1 Review of RPMs in All gTLDs	682d	05/23/22	12/31/24	72FS +90d	10%		
74	2.2	PDP: Review of All Rights Protection Mechanisms in All gTLDs - Phase 2 (UDRP)	1931d	11/05/21	03/30/29		24%		
75	2.2.1	PSR: Policy Status Report on UDRP	185d	11/05/21	07/21/22		100%		
76	2.2.2	Council: Deliberate PSR and Confirm Start of PDP (resolved 18 month delay to complete RPM_P1)	195d	07/22/22	04/20/23	75	100%		
77	2.2.3	Council: Deliberate PSR and Confirm Start of PDP	169d	10/01/24	05/23/25		0%	Planned	
78	2.2.4	Drafting Team: Charter on Review of UDRP (incl. Items 2 through 11 of Rec27 Wave1)	150d	05/26/25	12/19/25	77	0%	Planned	
79	2.2.5	PDP: RPM - Phase 2 Review of UDRP	525d	12/22/25	12/24/27	78	0%	Planned	
80	2.2.6	Board: RPM - Phase 2 Review of UDRP adopt consensus recommendations	60d	12/27/27	03/17/28	79	0%	Planned	
81	2.2.7	IRT: RPM - Phase 2 Review of UDRP	270d	03/20/28	03/30/29	80	0%	Planned	
82	3	gTLD - Program Track	1175d	07/01/20	12/31/24		61%		
83	3.1	CCWG: New gTLD Auction Proceeds (ICANN Org Grants Program)	1043d	07/01/20	06/28/24		61%		
84	3.1.1	CCWG: New gTLD Auction Proceeds (group completed 31 May 2020)	0	07/01/20	07/01/20		100%		
85	3.1.2	Council to deliberate and adopt CCWG recommendations	20d	08/03/20	08/28/20		100%		
86	3.1.3	Board: New gTLD Auction Proceeds - adopt consensus recommendations	466d	08/31/20	06/13/22	85	100%		
87	3.1.4	ICANN Org: Implement ICANN Org Grants Program	534d	06/14/22	06/28/24	86	25%		
88	3.2	PDP: New gTLD Subsequent Procedures	1175d	07/01/20	12/31/24		46%		
89	3.2.1	PDP: New gTLD Subsequent Procedures (started 21 Jan 2016)	168d	07/01/20	02/19/21		100%		
90	3.2.2	Board: New gTLD Subsequent Procedures adopt consensus recommendations	875d	02/22/21	06/28/24		73%		
91	3.2.2.1	ICANN Org: New gTLD Subsequent Procedures Operational Design Phase	340d	09/13/21	12/30/22	89FS +145d	100%		
92	3.2.2.2	Board: New gTLD Subsequent Procedures adopt consensus recommendations	875d	02/22/21	06/28/24	89	63%		
93	3.2.3	IRT: New gTLD Subsequent Procedures	468d	03/17/23	12/31/24		2%	On-Schedule	On-Target
94	3.2.4	GNSO Council Small Team on remaining SubPro Recommendations	271d	03/17/23	03/29/24		2%	On-Schedule	On-Target
95	3.3	GGP: Applicant Support	429d	08/25/22	04/16/24		37%		
96	3.3.1	GGP: New gTLD Subsequent Procedures - Applicant Support (SubPro_GGP)	429d	08/25/22	04/16/24		37%	On-Schedule	On-Target
97	3.4	Closed Generics Facilitated Dialogue	311d	04/22/22	06/30/23		80%	On-Schedule	On-Target
98	3.5	Name Collision Analysis Project	870d	07/01/20	10/31/23		85%		
99	3.5.1	Name Collision Analysis Project - Phase 1 (14 Mar 2019 start)	192d	07/01/20	03/25/21		100%		
100	3.5.2	Name Collision Analysis Project - Phase 2	652d	05/03/21	10/31/23		80%	On-Schedule	On-Target
101	4	IDNs - Program Track	1803d	07/01/20	05/28/27		50%		

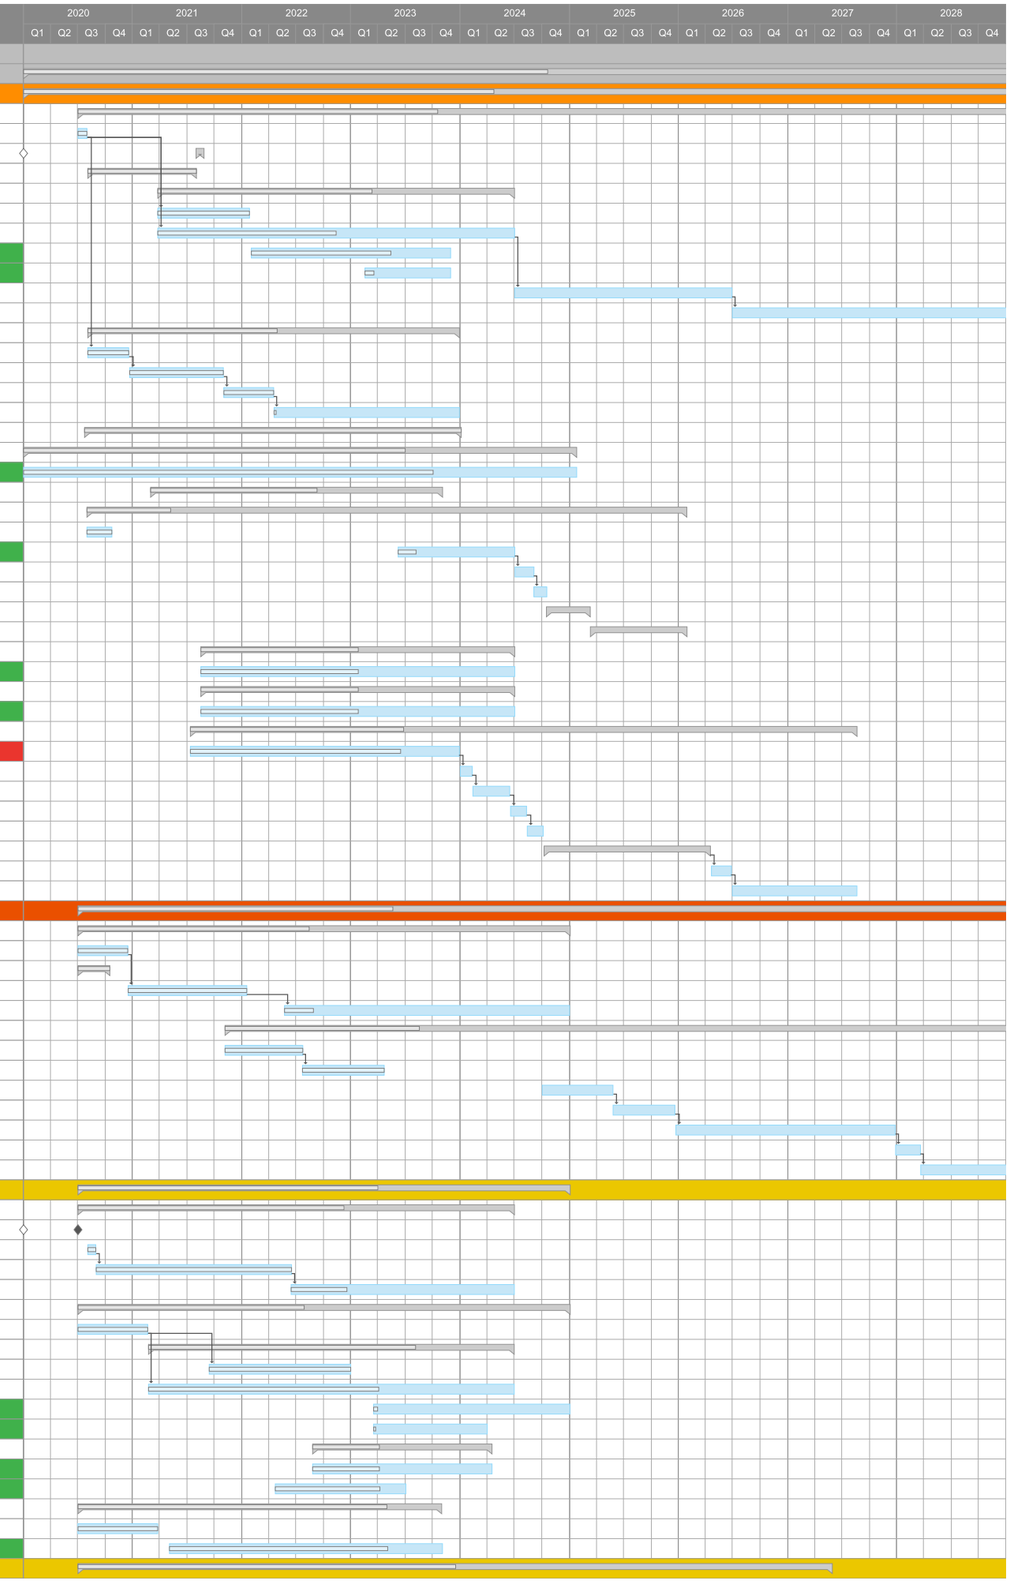

	WBS	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
102	4.1	IDN Operational Working Group (Track 1)	480d	08/03/20	06/03/22		100%		
103	4.1.1	Determine scope of Track 1 working group	30d	08/03/20	09/11/20		100%		
104	4.1.2	Engage Operational Track 1 expert group	450d	09/14/20	06/03/22	103	100%		
105	4.2	EPDP: IDNs (Track 2)	1723d	10/21/20	05/28/27		38%		
106	4.2.1	Drafting Team: Charter on Internationalized Domain Names + EPDP Request	160d	10/21/20	06/01/21		100%		
107	4.2.2	EPDP: Internationalized Domain Names	1262d	05/20/21	03/20/26		39%	Revised Schedule	On-Target
108	4.2.3	Board: Internationalized Domain Names adopt consensus recommendations	60d	03/23/26	06/12/26	107	0%	Planned	
109	4.2.4	IRT: Internationalized Domain Names	250d	06/15/26	05/28/27	108	0%	Planned	
110	4.3	IDN GNSO Council Coordination w/ CCNSO Council (Track 3)	1493d	07/01/20	03/20/26		49%		
111	4.3.1	GNSO Council to coordinate with the CCNSO regarding IDN policy developments	1493d	07/01/20	03/20/26		49%		
112	5	Expiration - Program Track	2182d	10/01/20	02/09/29		14%		
113	5.1	PDP: Expired Domain Deletion Policy / Expired Registration Recovery Policy Policy Review	2182d	10/01/20	02/09/29		14%		
114	5.1.1	Council to extend PSR for 18 months or when bandwidth becomes available	45d	10/01/20	12/02/20		100%		
115	5.1.2	Council to Consider Request EDDP/ERRP Policy Status Report	447d	07/14/22	03/29/24	114FS +420d	45%		
116	5.1.3	Develop Expiration Policy Status Report (incl. Rec27 Wave1 EDDP Item 2 + ERRP Item3)	180d	04/01/24	12/06/24	115	0%	Planned	
117	5.1.4	Council to Request Expiration Policy Issue Report	45d	12/09/24	02/07/25	116	0%	Planned	
118	5.1.5	Expiration Policy Issue Report	150d	02/10/25	09/05/25		0%		
120	5.1.6	Council to approve PDP launch	10d	09/08/25	09/19/25	119	0%	Planned	
121	5.1.7	Council to approve scope and charter	25d	09/22/25	10/24/25	120	0%	Planned	
122	5.1.8	Expiration Policy Review	860d	10/27/25	02/09/29		0%		
123	5.1.8.1	PDP: Expiration Policy Review	400d	10/27/25	05/07/27	121	0%	Planned	
124	5.1.8.2	Board: Expiration Policy Review adopt consensus recommendations	60d	05/10/27	07/30/27	123	0%	Planned	
125	5.1.8.3	IRT: Expiration Policy Review	400d	08/02/27	02/09/29	124	0%	Planned	
126	6	Transfers - Program Track	1757d	07/01/20	03/25/27		41%		
127	6.1	PDP: Transfer Policy Review	1757d	07/01/20	03/25/27		41%		
128	6.1.1	Council to Request Transfer Policy Status Report	0	07/01/20	07/01/20		100%		
129	6.1.2	Develop Transfer Policy Status Report	0	07/01/20	07/01/20	128	100%		
130	6.1.3	Council to Request Transfer Policy Issue Report	0	07/01/20	07/01/20	129	100%		
131	6.1.4	Develop Transfer Issue Report	158d	07/01/20	02/05/21		100%		
134	6.1.5	Council to approve PDP launch	10d	02/05/21	02/18/21	132	100%		
135	6.1.6	Council to approve scope and charter	24d	02/19/21	03/24/21	134	100%		
136	6.1.7	Transfer Policy Review	1591d	02/18/21	03/25/27		34%		
137	6.1.7.1	PDP: Transfer Policy Review	1131d	02/18/21	06/19/25		48%	Revised Schedule	On-Target
138	6.1.7.2	Board: Transfer Policy Review - adopt consensus recommendations	60d	06/20/25	09/11/25	137	0%	Planned	
139	6.1.7.3	IRT: Transfer Policy Review	400d	09/12/25	03/25/27	138	0%	Planned	
140	7	IGO - Program Track	1137d	09/24/20	01/31/25		38%		
141	7.1	EPDP: Specific Curative Rights Protections for IGOs	1137d	09/24/20	01/31/25		58%		
142	7.1.1	EPDP: Specific Curative Rights Protections for IGOs	550d	09/24/20	11/02/22		100%		
143	7.1.2	Board: Specific Curative Rights Protections for IGOs adopt consensus recommendations	237d	11/03/22	09/29/23	142	45%		
144	7.1.3	IRT: Specific Curative Rights Protections for IGOs	350d	10/02/23	01/31/25	143	0%	Planned	
145	7.2	PDP: Curative Rights Protections for IGO/INGOs	587d	11/03/22	01/31/25		18%		
146	7.2.1	Board: Curative Rights Protections for IGO/INGOs adopt consensus recommendations	237d	11/03/22	09/29/23	142	45%		
147	7.2.2	IRT: Curative Rights Protections for IGO/INGOs	350d	10/02/23	01/31/25	146	0%	Planned	
148	7.3	PDP: Protection of International Organization Names in All gTLDs (Remaining Acronyms)	587d	11/03/22	01/31/25		18%		
149	7.3.1	Board: Protection of International Organization Names in All gTLDs (Remaining Acronyms)	237d	11/03/22	09/29/23	142	45%		
150	7.3.2	IRT: PDP: Protection of International Organization Names in All gTLDs (Remaining Acronyms)	350d	10/02/23	01/31/25	149	0%	Planned	
151	8	DNS_Abuse - Program Track	1273d	03/15/23	01/28/28		0%		
152	8.1	Next steps regarding DNS Abuse (Council small team reconvened)	78d	03/15/23	06/30/23		1%	On-Schedule	On-Target
153	8.2	Track 2 - Issues that may benefit from education / communication / outreach	260d	07/03/23	06/28/24	152	0%	On-Schedule	On-Target
154	8.3	Track 3 - Issues that may benefit from contractual negotiations between ICANN org and Contracted Parties	260d	07/01/24	06/27/25	153	0%	Planned	
155	8.4	Track 1 - Issues that may benefit from GNSO policy development	675d	06/27/25	01/28/28		0%	Planned	
156	8.4.1	Council: Request Policy Issue Report	0	06/27/25	06/27/25	154	0%	Planned	
157	8.4.2	Staff: Develop Issue Report	45d	06/30/25	08/29/25	156	0%	Planned	
158	8.4.3	Council: Approve PDP launch	10d	09/01/25	09/12/25	157	0%	Planned	
159	8.4.4	Council: Approve scope and charter	20d	09/15/25	10/10/25	158	0%	Planned	
160	8.4.5	PDP: DNS Abuse - Malicious Registrations (tightly scoped)	600d	10/13/25	01/28/28		0%		
164	9	Accountability - Program Track	1043d	07/01/20	06/28/24		52%		
165	9.1	Independent Review Process - Implementation Oversight Team	1042d	07/01/20	06/27/24		70%		
166	9.1.1	IoT Oversight Team Group	1042d	07/01/20	06/27/24		70%		
167	9.1.2	Establishment of Standing Panel for Independent Review Process	1042d	07/01/20	06/27/24		70%		
168	9.2	Cross Community Working Group on Enhancing ICANN Accountability - WS2	810d	05/24/21	06/28/24		73%		
169	9.2.1	GNSO Council Implementation of WS2	409d	05/24/21	12/15/22		100%		
170	9.2.2	GNSO SG/C Implementation of WS2	810d	05/24/21	06/28/24		60%		
171	9.3	Geo Regions Review	1043d	07/01/20	06/28/24		0%		
172	9.3.1	Geo Regions Review: Monitor for changes	1043d	07/01/20	06/28/24		0%	On-Hold	
173	9.4	Multistakeholder Model Evolution	1043d	07/01/20	06/28/24		70%		
174	9.4.1	Monitor for MSM-Evo implementation assignments	1043d	07/01/20	06/28/24		70%		
175	10	Reviews - Program Track	2923d	07/01/20	09/12/31		33%		
176	10.1	IANA Naming Function Review	226d	07/01/20	05/12/21		100%		
180	10.2	Registration Directory Service Review RT3	640d	04/02/29	09/12/31		0%		
185	10.3	Competition, Consumer Trust and Consumer Choice RT2	640d	01/13/27	06/26/29		0%		
190	10.4	Accountability and Transparency Review 3	1043d	07/01/20	06/28/24		71%		
193	10.5	Holistic Review - Pilot	1575d	11/30/20	12/11/26		37%		
194	10.5.1	Holistic Review Pilot: Define Terms of Reference, Information Gaps, and Determine Prioritization to Start	805d	11/30/20	12/29/23		75%		
195	10.5.2	Council SSC to select GNSO representatives on Review Team	30d	01/01/24	02/09/24	194	0%	Planned	
196	10.5.3	Holistic Review Pilot	400d	02/12/24	08/22/25	195	0%	Planned	
197	10.5.4	Board: Holistic Review Pilot deliberate and adopt consensus recommendations	70d	08/25/25	11/28/25	196	0%	Planned	

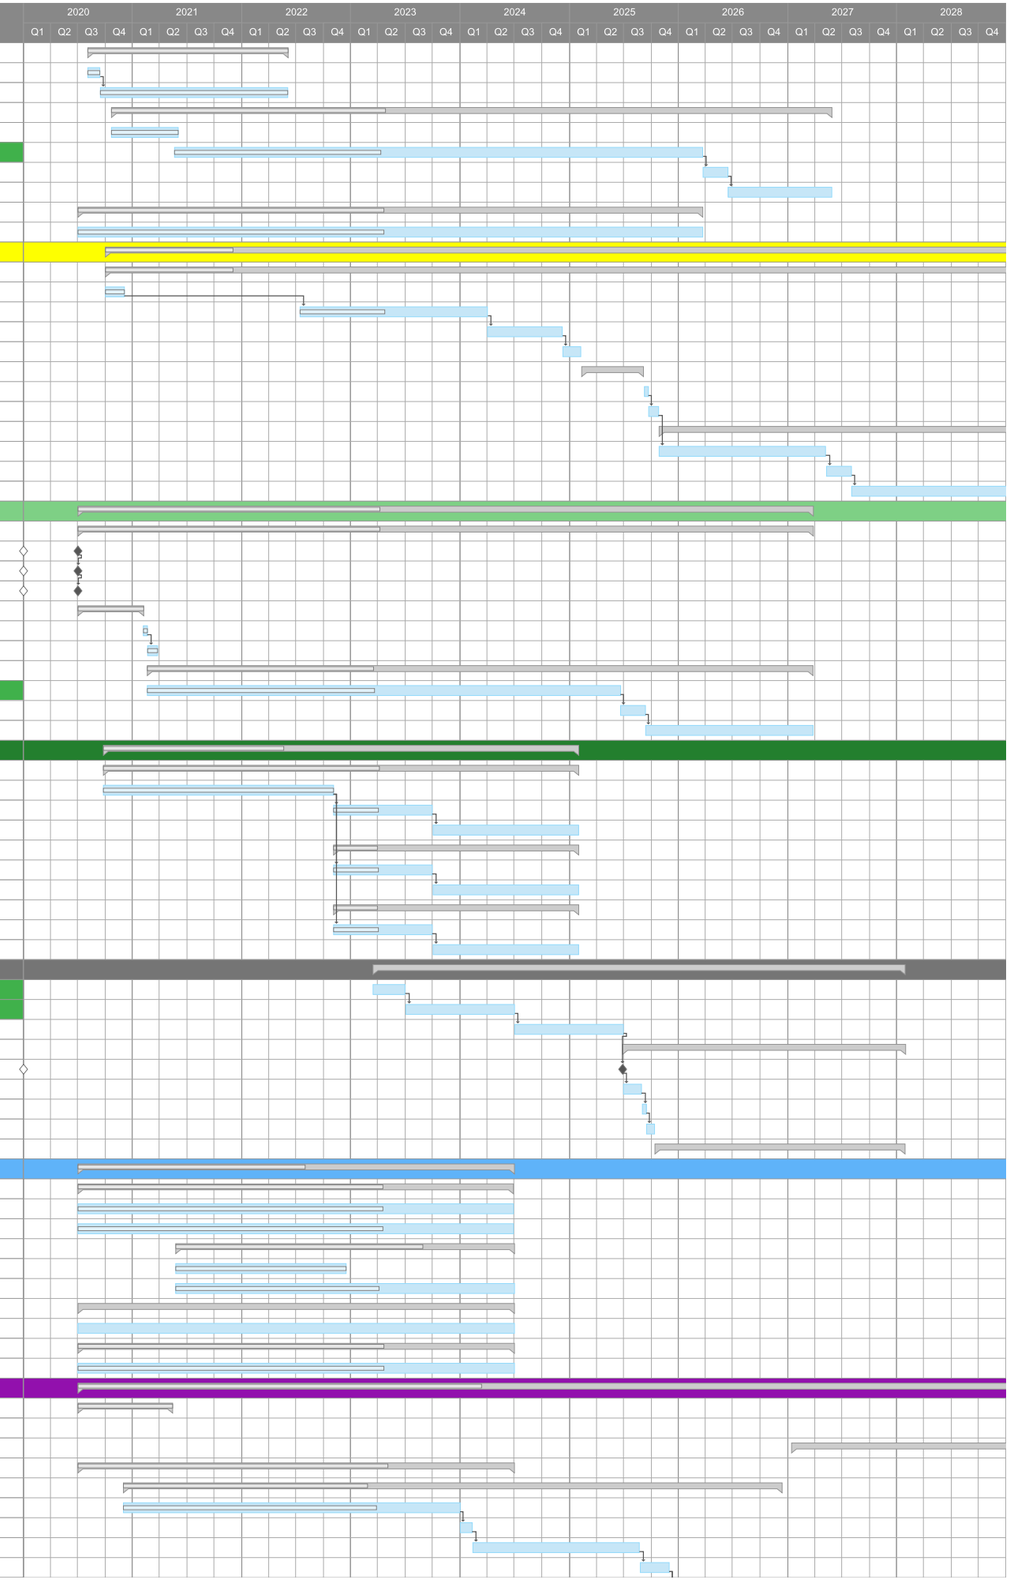

	WBS	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
198	10.5.5	Council to consider Holistic Review Pilot Results	60d	12/01/25	02/20/26	197	0%	Planned	
199	10.5.6	Holistic Review Pilot Implement Review recommendations	270d	12/01/25	12/11/26	197	0%	Planned	
200	10.6	Accountability and Transparency Review 4	620d	12/14/26	04/27/29		0%		
205	10.7	Security, Stability and Resiliency of the DNS #2	1044d	07/01/20	07/01/24		69%		
206	10.7.1	Security, Stability and Resiliency of the DNS #2	160d	07/01/20	02/09/21		100%		
207	10.7.2	Board: SSR#2 deliberate and adopt consensus recommendations	117d	02/10/21	07/22/21	206	100%		
208	10.7.3	Monitor for SSR#2 implementation assignments	767d	07/23/21	07/01/24	207	58%		
209	10.8	Security, Stability and Resiliency of the DNS #3	640d	04/02/29	09/12/31		0%		
214	10.9	CSC Effectiveness Review - 2021	543d	07/01/21	07/31/23		75%		
215	10.9.1	Council: establish terms of reference and determine is prior review recs were implemented	65d	07/01/21	09/29/21		100%		
216	10.9.2	CSC Effectiveness Review 2021	390d	09/30/21	03/29/23	215	100%		
217	10.9.3	Board: CSC Effectiveness Review deliberate and adopt consensus recommendations	88d	03/30/23	07/31/23	216	1%		
218	10.9.4	Consider CSC Effectiveness Review Results	67d	03/30/23	06/30/23	216	1%		
219	10.10	CSC Effectiveness Review - 2024	400d	08/01/24	02/11/26		0%		
224	10.11	GNSO Review RT3	680d	12/14/26	07/20/29		0%		
230	11	Root_System - Program Track	870d	07/01/20	10/31/23		82%		
231	11.1	Root Server System Governance Working Group (GWG)	870d	07/01/20	10/31/23		82%	On-Schedule	On-Target
232	12	ICANN_Planning - Program Track	1163d	01/15/20	06/28/24		74%		
233	12.1	ICANN Planning - FY22	282d	01/15/20	02/11/21		100%		
236	12.2	ICANN Planning - FY23	359d	01/15/21	06/01/22		100%		
240	12.3	ICANN Planning - FY24	285d	01/15/22	02/16/23		100%		
245	12.4	ICANN Planning - FY25	358d	02/15/23	06/28/24		5%		
246	12.4.1	Trend Identification - FY25	163d	02/15/23	09/29/23		20%	On-Schedule	
247	12.4.2	ICANN Planning Prioritization Framework FY25	44d	04/01/23	05/31/23		10%	On-Schedule	
248	12.4.3	IANA & ICANN Budget & OPs Plan for Public Comment - FY25	96d	10/01/23	02/09/24		0%	Planned	
249	12.4.4	IANA & ICANN 5 Year Strategic Planning - FY26-FY30	250d	05/01/23	04/12/24		0%	Planned	
250	12.4.5	GNSO Budget & OPs Townhall on FY25 Budget and Operations 2023-2024	261d	07/01/23	06/28/24		0%	Planned	
251	13	Operations - Program Track	1432d	06/01/20	11/25/25		55%		
252	13.1	Participant of Empowered Community	1382d	07/01/20	10/16/25		53%		
253	13.1.1	Participant of Empowered Community - 2020	96d	07/01/20	11/11/20		100%		
256	13.1.2	Participant of Empowered Community - 2021	235d	11/12/20	10/06/21		100%		
259	13.1.3	Participant of Empowered Community - 2022	271d	10/07/21	10/20/22		100%		
262	13.1.4	Participant of Empowered Community - 2023	265d	10/21/22	10/26/23		47%		
263	13.1.4.1	Participant of Empowered Community - 2023	250d	10/21/22	10/05/23	261	50%		
264	13.1.4.2	Elect new participant to Empowered Community	15d	10/06/23	10/26/23	263	0%	Planned	
265	13.1.5	Participant of Empowered Community - 2024	265d	10/27/23	10/31/24		0%		
268	13.1.6	Participant of Empowered Community - 2025	250d	11/01/24	10/16/25		0%		
270	13.2	Participation on Customer Standing Committee	1394d	06/01/20	10/02/25		56%		
271	13.2.1	Customer Standing Committee - 2020	132d	07/01/20	12/31/20		100%		
274	13.2.2	Customer Standing Committee - 2021	349d	06/01/20	09/30/21		100%		
277	13.2.3	Customer Standing Committee - 2022	305d	08/01/21	09/29/22		100%		
280	13.2.4	Customer Standing Committee - 2023	307d	08/01/22	10/03/23		54%		
281	13.2.4.1	Council Approval - Customer Standing Committee slate - 2023	22d	08/01/22	08/30/22		100%		
282	13.2.4.2	Customer Standing Committee - 2023	261d	10/04/22	10/03/23	281FS +24d	50%		
283	13.2.5	Customer Standing Committee - 2024	307d	08/01/23	10/02/24		0%		
284	13.2.5.1	Council Approval - Customer Standing Committee slate - 2024	22d	08/01/23	08/30/23		0%		
285	13.2.5.2	Customer Standing Committee - 2024	261d	10/04/23	10/02/24	284FS +24d		Planned	
286	13.2.6	Customer Standing Committee - 2025	306d	08/01/24	10/02/25				
289	13.3	Participation on NomCom	1347d	09/01/20	10/29/25		50%		
290	13.3.1	GNSO Participation on NomCom - 2020-2021	297d	09/01/20	10/20/21		100%		
291	13.3.2	GNSO Council to Confirm NomCom Job Description	1d	09/23/21	09/23/21		100%		
292	13.3.3	GNSO Participation on NomCom - 2021-2022	241d	10/20/21	09/21/22		100%		
293	13.3.4	GNSO Council to Confirm NomCom Job Description	1d	11/17/22	11/17/22		100%		
294	13.3.5	GNSO Participation on NomCom - 2022-2023	286d	09/21/22	10/25/23		50%		
295	13.3.6	GNSO Council to Confirm NomCom Job Description	1d	09/21/23	09/21/23		0%	Planned	
296	13.3.7	GNSO Participation on NomCom - 2023-2024	276d	10/25/23	11/13/24		0%	Planned	
297	13.3.8	GNSO Council to Confirm NomCom Job Description	1d	09/19/24	09/19/24		0%	Planned	
298	13.3.9	GNSO Participation on NomCom - 2024-2025	251d	11/13/24	10/29/25		0%	Planned	
299	13.4	Stakeholder Support - Registry Stakeholder Group	1304d	07/01/20	06/30/25		56%		
300	13.4.1	FY21 Stakeholder Support - Registry Stakeholder Group	261d	07/01/20	06/30/21		100%		
301	13.4.2	FY22 Stakeholder Support - Registry Stakeholder Group	261d	07/01/21	06/30/22		100%		
302	13.4.3	FY23 Stakeholder Support - Registry Stakeholder Group	261d	07/01/22	06/30/23		78%		
303	13.4.4	FY24 Stakeholder Support - Registry Stakeholder Group	261d	07/01/23	06/28/24		0%	Planned	
304	13.4.5	FY25 Stakeholder Support - Registry Stakeholder Group	261d	07/01/24	06/30/25		0%	Planned	
305	13.5	Stakeholder Support - Registrar Stakeholder Group	1304d	07/01/20	06/30/25		56%		
306	13.5.1	FY21 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/20	06/30/21		100%		
307	13.5.2	FY22 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/21	06/30/22		100%		
308	13.5.3	FY23 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/22	06/30/23		78%		
309	13.5.4	FY24 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/23	06/28/24		0%	Planned	
310	13.5.5	FY25 Stakeholder Support - Registrar Stakeholder Group	261d	07/01/24	06/30/25		0%	Planned	
311	13.6	Stakeholder Support - NCSG/NCUC/NPOC	1304d	07/01/20	06/30/25		56%		
312	13.6.1	FY21 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/20	06/30/21		100%		
313	13.6.2	FY22 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/21	06/30/22		100%		
314	13.6.3	FY23 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/22	06/30/23		78%		
315	13.6.4	FY24 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/23	06/28/24		0%	Planned	
316	13.6.5	FY25 Stakeholder Support - NCSG/NCUC/NPOC	261d	07/01/24	06/30/25		0%	Planned	
317	13.7	Stakeholder Support - CSG/BC/IPC/ISPCP	1304d	07/01/20	06/30/25		56%		

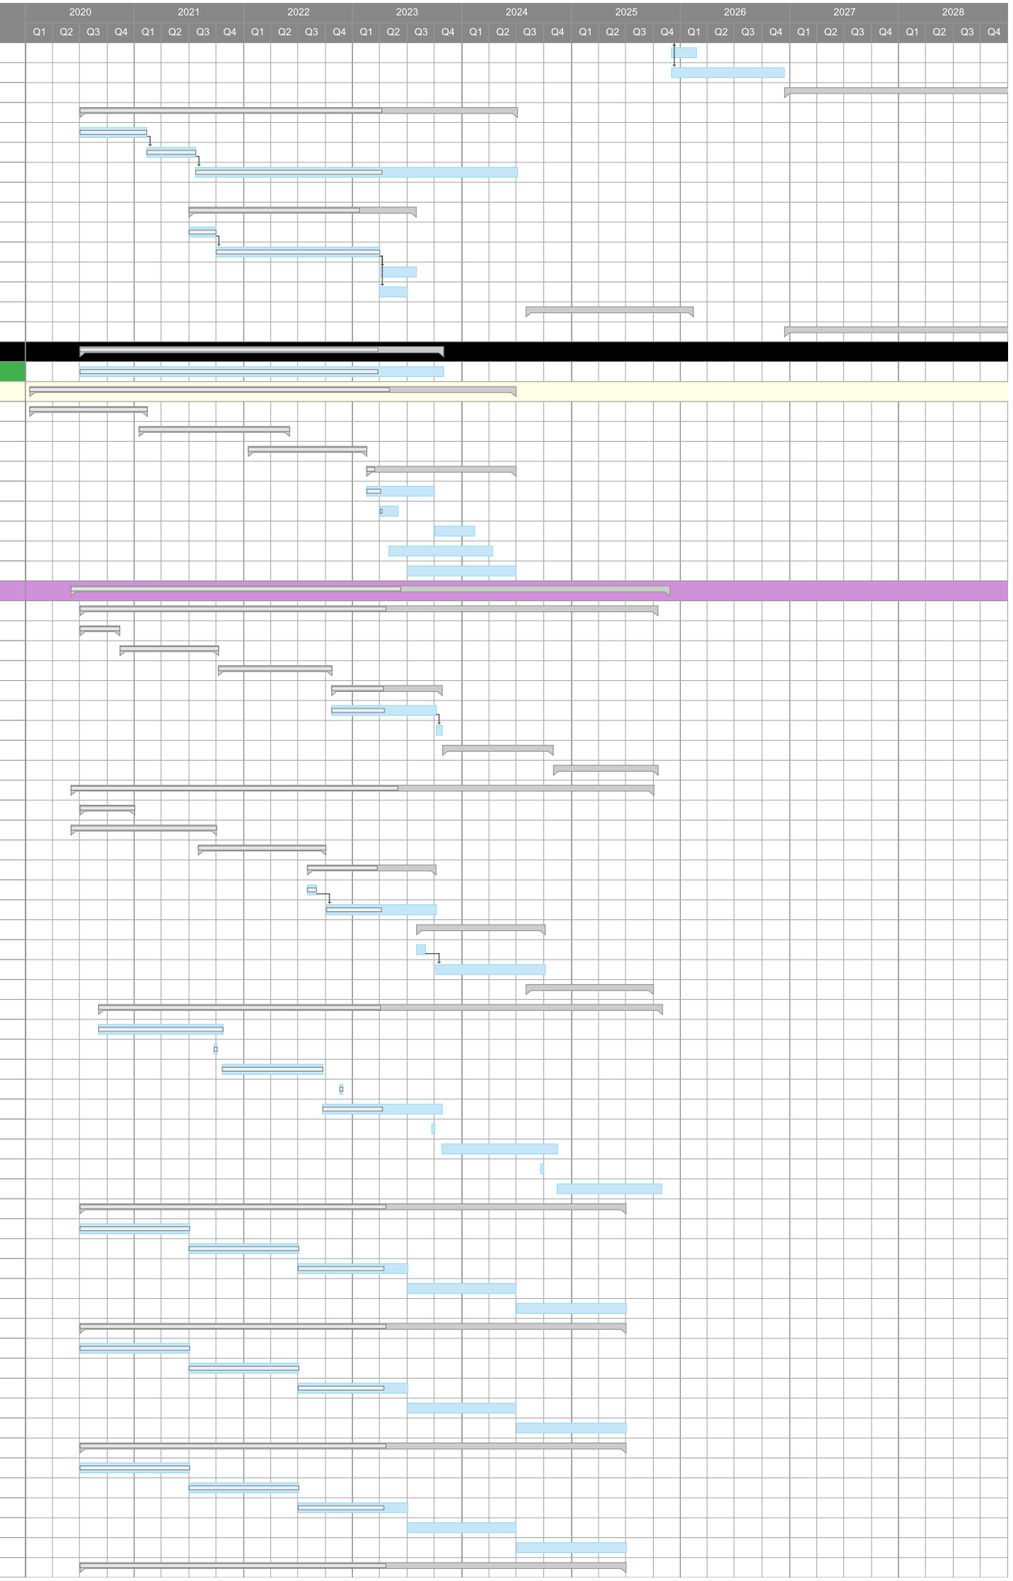
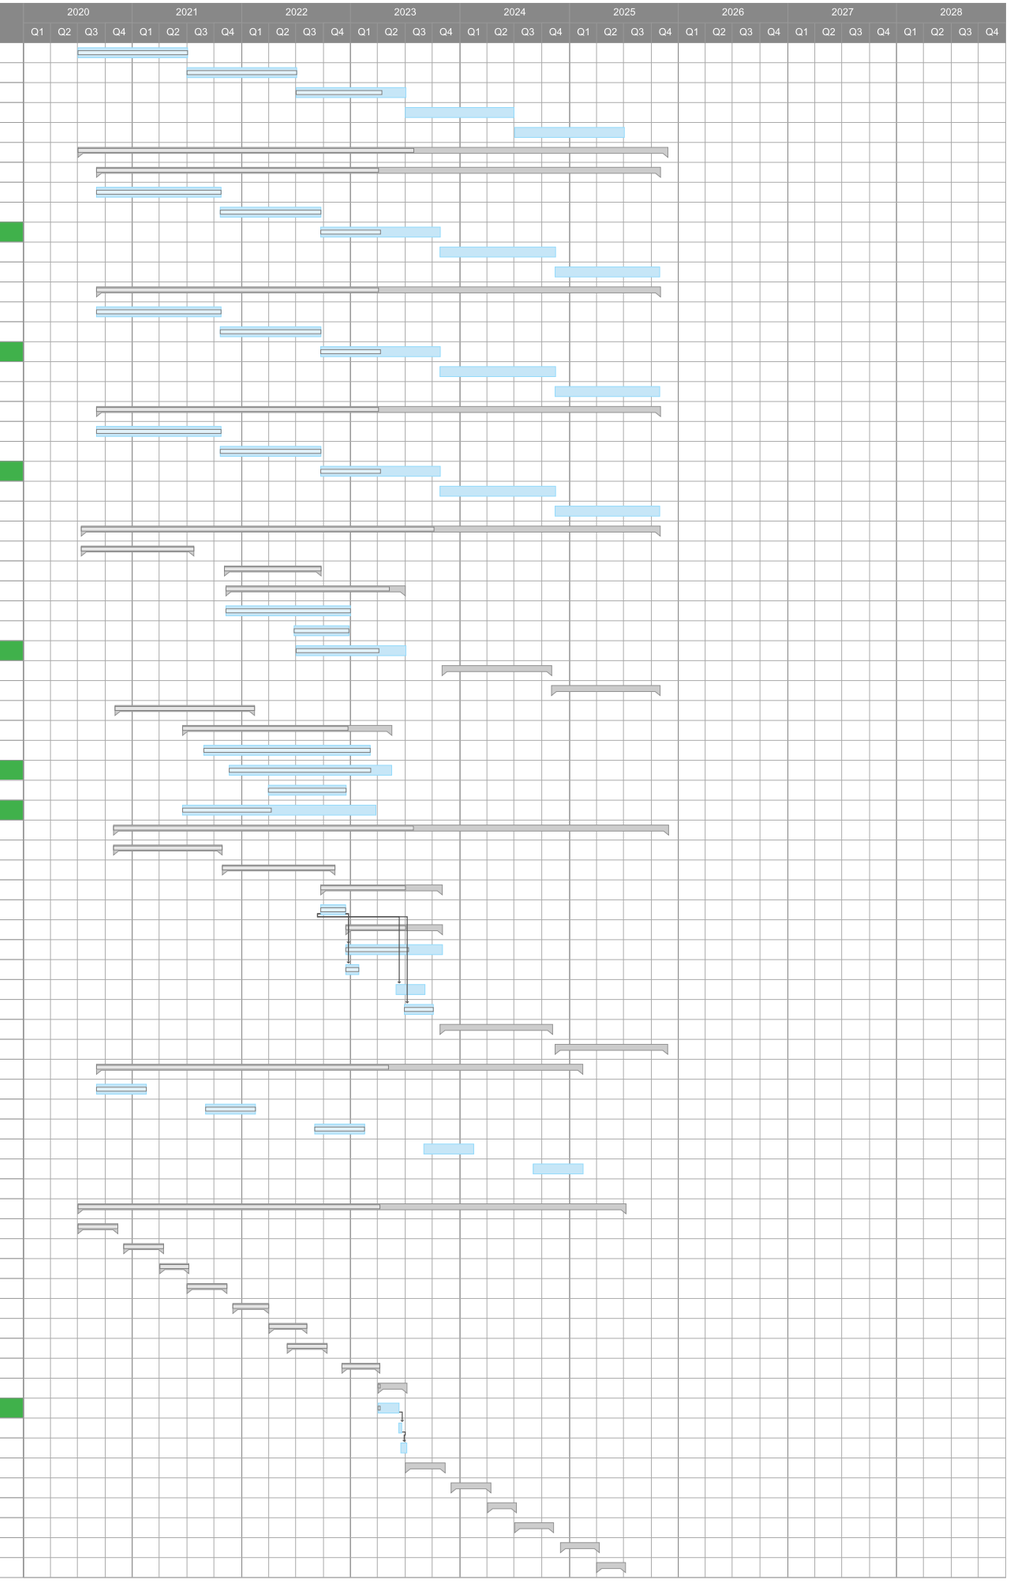
	WBS	Program_Project	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Project_Status	Project_Health
318	13.7.1	FY21 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/20	06/30/21		100%		
319	13.7.2	FY22 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/21	06/30/22		100%		
320	13.7.3	FY23 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/22	06/30/23		78%		
321	13.7.4	FY24 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/23	06/28/24		0%	Planned	
322	13.7.5	FY25 Stakeholder Support - CSG/BC/IPC/ISPCP	261d	07/01/24	06/30/25		0%	Planned	
323	13.8	GNSO Council	1410d	07/01/20	11/25/25		57%		
324	13.8.1	GNSO Council - Monthly Meetings	1347d	09/01/20	10/29/25		50%		
325	13.8.1.1	GNSO Council - Monthly Meetings 2020-2021	297d	09/01/20	10/20/21		100%		
326	13.8.1.2	GNSO Council - Monthly Meetings 2021-2022	241d	10/20/21	09/21/22		100%		
327	13.8.1.3	GNSO Council - Monthly Meetings 2022-2023	286d	09/21/22	10/25/23		50%	On-Schedule	On-Target
328	13.8.1.4	GNSO Council - Monthly Meetings 2023-2024	276d	10/25/23	11/13/24		0%	Planned	
329	13.8.1.5	GNSO Council - Monthly Meetings 2024-2025	251d	11/13/24	10/29/25		0%	Planned	
330	13.8.2	GNSO Council - Leadership Meetings	1347d	09/01/20	10/29/25		50%		
331	13.8.2.1	GNSO Council - Leadership Meetings 2020-2021	297d	09/01/20	10/20/21		100%		
332	13.8.2.2	GNSO Council - Leadership Meetings 2021-2022	241d	10/20/21	09/21/22		100%		
333	13.8.2.3	GNSO Council - Leadership Meetings 2022-2023	286d	09/21/22	10/25/23		50%	On-Schedule	On-Target
334	13.8.2.4	GNSO Council - Leadership Meetings 2023-2024	276d	10/25/23	11/13/24		0%	Planned	
335	13.8.2.5	GNSO Council - Leadership Meetings 2024-2025	251d	11/13/24	10/29/25		0%	Planned	
336	13.8.3	GNSO Council - Action Items	1347d	09/01/20	10/29/25		50%		
337	13.8.3.1	GNSO Council - Action Items 2020-2021	297d	09/01/20	10/20/21		100%		
338	13.8.3.2	GNSO Council - Action Items 2021-2022	241d	10/20/21	09/21/22		100%		
339	13.8.3.3	GNSO Council - Action Items 2022-2023	286d	09/21/22	10/25/23		50%	On-Schedule	On-Target
340	13.8.3.4	GNSO Council - Action Items 2023-2024	276d	10/25/23	11/13/24		0%	Planned	
341	13.8.3.5	GNSO Council - Action Items 2024-2025	251d	11/13/24	10/29/25		0%	Planned	
342	13.8.4	GNSO Council - Small Teams	1385d	07/12/20	10/30/25		61%		
343	13.8.4.1	GNSO Council - Small Teams - 2020-2021	270d	07/12/20	07/22/21		100%		
353	13.8.4.2	GNSO Council - Small Teams - 2021-2022	231d	11/03/21	09/21/22		100%		
359	13.8.4.3	GNSO Council - Small Teams - 2022-2023	430d	11/08/21	06/30/23		91%		
360	13.8.4.3.1	Next steps regarding DNS Abuse	300d	11/08/21	12/30/22		100%		
361	13.8.4.3.2	SubPro ODP Question & Answer Review Team	130d	06/24/22	12/22/22		100%		
362	13.8.4.3.3	GNSO PDP Improvements (Staff + Council)	261d	07/01/22	06/30/23		75%	On-Schedule	On-Target
363	13.8.4.4	GNSO Council - Small Teams - 2023-2024	261d	11/01/23	10/30/24		0%		
365	13.8.4.5	GNSO Council - Small Teams - 2024-2025	260d	11/01/24	10/30/25		0%		
367	13.8.5	GNSO Standing Committee on Budget and Operations (closed Feb 2023)	335d	11/02/20	02/11/22		100%		
376	13.8.6	Council Committee for Overseeing & Implementing Continuous Improvement	499d	06/16/21	05/15/23		79%		
377	13.8.6.1	CCOICI Assignment #4	398d	08/26/21	03/06/23		100%		
378	13.8.6.2	CCOICI Assignment #6	387d	11/19/21	05/15/23		87%	Behind Schedule	On-Target
379	13.8.6.3	CCOICI Assignment WS2	187d	03/30/22	12/15/22		100%		
380	13.8.6.4	CCOICI Pilot Program Assessment	463d	06/16/21	03/24/23		46%	On-Hold	On-Target
381	13.8.7	GNSO Standing Selection Committee	1325d	10/28/20	11/25/25		54%		
382	13.8.7.1	GNSO Standing Selection Committee 2020-2021	260d	10/28/20	10/26/21		100%		
389	13.8.7.2	GNSO Standing Selection Committee 2021-2022	270d	10/27/21	11/08/22		100%		
396	13.8.7.3	GNSO Standing Selection Committee 2022-2023	290d	09/21/22	10/31/23		70%		
397	13.8.7.3.1	Refresh roster and confirm Chair (within 3 weeks of AGM)	60d	09/21/22	12/13/22		100%		
398	13.8.7.3.2	Standing Selection Committee (SSC) 2022-2023	230d	12/14/22	10/31/23		62%		
399	13.8.7.3.2.1	Standing Selection Committee (SSC) fill positions as assigned	230d	12/14/22	10/31/23	397	65%		
400	13.8.7.3.2.2	Appoint GNSO Representative to Fellowship Program	30d	12/14/22	01/24/23	397	100%		
401	13.8.7.3.2.3	Obtain EOIs and Appoint CSC Liaison as Required	70d	05/31/23	09/05/23	397SS +180d	0%	On-Schedule	
402	13.8.7.3.2.4	Appoint GAC Liaison as Required (Not required til 2023-2024)	70d	06/28/23	10/03/23	397SS +200d	100%		
403	13.8.7.4	GNSO Standing Selection Committee 2023-2024	270d	10/25/23	11/05/24			Planned	
410	13.8.7.5	GNSO Standing Selection Committee 2024-2025	270d	11/13/24	11/25/25			Planned	
417	13.8.8	GNSO Council - Strategic Planning Session	1163d	09/01/20	02/13/25		60%		
418	13.8.8.1	GNSO Council - Strategic Planning Session - 2020-2021	120d	09/01/20	02/15/21		100%		
419	13.8.8.2	GNSO Council - Strategic Planning Session - 2021-2022	120d	09/01/21	02/15/22		100%		
420	13.8.8.3	GNSO Council - Strategic Planning Session - 2022-2023	120d	09/01/22	02/15/23		100%		
421	13.8.8.4	GNSO Council - Strategic Planning Session - 2023-2024	120d	09/01/23	02/15/24		0%	Planned	
422	13.8.8.5	GNSO Council - Strategic Planning Session - 2024-2025	120d	09/01/24	02/13/25		0%	Planned	
423	13.8.9	GNSO Elections - [PLACEHOLDER SECTION]							
427	13.8.10	ICANN Meeting Planning, Meeting, Respond to GAC Advice	1309d	07/01/20	07/07/25		55%		
428	13.8.10.1	ICANN69	95d	07/01/20	11/10/20		100%		
432	13.8.10.2	ICANN70	95d	12/01/20	04/12/21		100%		
436	13.8.10.3	ICANN71	70d	04/01/21	07/07/21		100%		
440	13.8.10.4	ICANN72	95d	07/01/21	11/10/21		100%		
444	13.8.10.5	ICANN73	87d	12/01/21	03/31/22		100%		
448	13.8.10.6	ICANN74	90d	04/01/22	08/04/22		100%		
452	13.8.10.7	ICANN75	95d	06/01/22	10/11/22		100%		
456	13.8.10.8	ICANN76	91d	12/01/22	04/06/23		100%		
460	13.8.10.9	ICANN77	70d	04/01/23	07/06/23		7%		
461	13.8.10.9.1	ICANN77 Meeting Planning	50d	04/01/23	06/08/23		10%	On-Schedule	On-Target
462	13.8.10.9.2	ICANN77 ICANN Meeting	5d	06/09/23	06/15/23	461	0%	Planned	
463	13.8.10.9.3	ICANN77 Respond to GAC Advice	15d	06/16/23	07/06/23	462	0%	Planned	
464	13.8.10.10	ICANN78	95d	07/01/23	11/09/23		0%		
468	13.8.10.11	ICANN79	95d	12/01/23	04/11/24		0%		
472	13.8.10.12	ICANN80	70d	04/01/24	07/05/24		0%		
476	13.8.10.13	ICANN81	95d	07/01/24	11/08/24		0%		
480	13.8.10.14	ICANN82	95d	12/01/24	04/10/25		0%		
484	13.8.10.15	ICANN83	70d	04/01/25	07/07/25		0%
