#	Name		Planned Duration	Start Date	Completion Date	%	Pre dec
1	Announce Request for Volunteers for Charter Drafting Team	✓	5 days	7/1/14 8:00 AM	7/8/14 5:00	100.	
2	Form Charter Drafting Team and Announce 1st Meeting	✓	1 days	7/8/14 8:00 AM	7/8/14 5:00	100.	1
3	Create and Deploy Project Tools (mail list, AC, conference line, etc)	✓	1 days	7/9/14 8:00 AM	7/9/14 5:00	100.	1
4	**Support Charter Drafting Team Meetings**	✓	21 days	7/14/14 8:00 AM	8/11/14 5:00	100.	
5	DT Call #01 - 14 Jul	✓	1 days	7/14/14 8:00 AM	7/14/14 5:00	100.	2,
6	DT Call #02 - 21 Jul	✓	1 days	7/21/14 8:00 AM	7/21/14 5:00	100.	
7	DT Call #03 - 28 Jul	✓	1 days	7/28/14 8:00 AM	7/28/14 5:00	100.	
8	DT Call #04 - 11 Aug	✓	1 days	8/11/14 8:00 AM	8/11/14 5:00	100.	
9	Develop Draft Charter and Approve within DT	✓	20 days	7/14/14 8:00 AM	8/8/14 5:00	100.	4
10	Deliver Charter to all SOs/ACs for Approval	✓	25 days	8/11/14 8:00 AM	9/15/14 5:00	100.	9
11	Announce Request for Volunteers for Cross-Community Working Group	✓	10 days	9/16/14 8:00 AM	9/29/14 5:00	100.	10
12	Form Cross-Community Working Group and Announce 1st Meeting	✓	1 days	9/30/14 8:00 AM	9/30/14 5:00	100.	11
13	List of CWG Meetings and Sub-team meetings can be found at the bottom of the project	✓	1 days	7/1/14 8:00 AM	7/1/14 5:00	100.	
14	Review CWG Principles	✓	21 days	10/23/14 8:00 AM	11/20/14	100.	86
15	**Establish sub-teams to develop Draft Proposal**	✓	106 days	10/23/14 8:00 AM	4/3/15 5:00	100.	
16	**CWG RFP1 - Description of Community's Use of IANA Functions**	✓	6 days	10/23/14 8:00 AM	10/30/14	100.	
17	Sub-team deliberations	✓	6 days	10/23/14 8:00 AM	10/30/14	100.	86
18	Develop draft RFP1	✓	6 days	10/23/14 8:00 AM	10/30/14	100.	86
19	**CWG RFP2 - Existing, Pre-Transition Arrangements**	✓	8 days	10/23/14 8:00 AM	11/3/14 6:00	100.	
20	**CWG RFP2A - Existing, Pre-Transition Arrangements – Policy Sources**	✓	8 days	10/23/14 8:00 AM	11/3/14 6:00	100.	
21	Sub-team deliberations	✓	8 days	10/23/14 8:00 AM	11/3/14 6:00	100.	86
22	Develop draft RFP2A	✓	8 days	10/23/14 8:00 AM	11/3/14 6:00	100.	86
23	**CWG RFP2B - Existing, Pre-Transition Arrangements – Oversight & Accountability**	✓	8 days	10/23/14 8:00 AM	11/3/14 6:00	100.	
24	Sub-team deliberations	✓	8 days	10/23/14 8:00 AM	11/3/14 6:00	100.	86
25	Develop draft RFP2B	✓	8 days	10/23/14 8:00 AM	11/3/14 6:00	100.	86
26	**CWG RFP2C - Existing, Pre-Transition Arrangements, NTIA IANA Functions Contract Triage**	✓	8 days	10/23/14 8:00 AM	11/3/14 6:00	100.	
27	Sub-team deliberations	✓	8 days	10/23/14 8:00 AM	11/3/14 6:00	100.	86
28	Develop draft RFP2C	✓	8 days	10/23/14 8:00 AM	11/3/14 6:00	100.	86
29	**CWG RFP3 - Proposed Post-Transition Oversight and Accountability Arrangements**	✓	95 days	11/4/14 9:00 AM	3/31/15 5:00	100.	
30	Sub-team deliberations - Replacement of NTIA's role as IANA Functions Contract Administrator	✓	95 days	11/4/14 9:00 AM	3/31/15 5:00	100.	23,
31	Sub-team deliberations - Replacement of NTIA's role as Root Zone Management Process Administrator	✓	95 days	11/4/14 9:00 AM	3/31/15 5:00	100.	23,
32	Sub-team RFP3B deliberations - Internal Option	✓	54 days	1/14/15 8:00 AM	3/31/15 5:00	100.	
33	Develop draft RFP3	✓	95 days	11/4/14 9:00 AM	3/31/15 5:00	100.	20,
34	**CWG RFP4 - Transition Implications**	✓	93 days	11/11/14 8:00 AM	4/3/15 5:00	100.	
35	Sub-team deliberations	✓	93 days	11/11/14 8:00 AM	4/3/15 5:00	100.	
36	Develop draft RFP4	✓	93 days	11/11/14 8:00 AM	4/3/15 5:00	100.	
37	**CWG RFP5 - NTIA Requirements (validation of)**	✓	72 days	12/12/14 8:00 AM	4/3/15 5:00	100.	
38	Sub-team deliberations	✓	72 days	12/12/14 8:00 AM	4/3/15 5:00	100.	
39	Develop draft RFP5	✓	72 days	12/12/14 8:00 AM	4/3/15 5:00	100.	
40	**CWG RFP6 - Community Process (summary of)**	✓	26 days	2/27/15 8:00 AM	4/3/15 5:00	100.	
41	Sub-team deliberations	✓	26 days	2/27/15 8:00 AM	4/3/15 5:00	100.	
42	Develop draft RFP6	✓	26 days	2/27/15 8:00 AM	4/3/15 5:00	100.	
43	Consolidate & Refine 1st Draft Proposal	✓	26 days	10/23/14 8:00 AM	12/1/14 6:00	100.	
44	Deliver Draft Proposal to Chartering Organizations	✓	1 days	12/1/14 8:00 AM	12/1/14 6:00	100.	43
45	Publish Draft Proposal for Public Comment - 1 Dec (21 days)	✓	16 days	12/1/14 8:00 AM	12/22/14	100.	43
46	**Conduct Webinars for Draft Proposal**	✓	2 days	12/2/14 8:00 AM	12/3/14 6:00	100.	43
47	Webinar #1	✓	1 days	12/2/14 8:00 AM	12/2/14 6:00	100.	
48	Webinar #2	✓	1 days	12/3/14 8:00 AM	12/3/14 6:00	100.	
49	Webinar #3	✓	1 days	12/3/14 8:00 AM	12/3/14 6:00	100.	
50	Review Public Comments and other feedback	✓	7 days	12/14/14 12:00 AM	12/23/14	100.	45
51	Create Summary Report of Public Comments	✓	20 days	12/23/14 9:00 AM	1/30/15 6:00	100.	45
52	Identify and contract with independent legal advice	✓	33 days	1/26/15 8:00 AM	3/11/15 5:00	100.	
53	Conduct legal analysis against proposal options		57 days	3/12/15 8:00 AM	6/1/15 5:00	65.0	52
54	**CWG Design Teams**	✓	42 days	2/12/15 8:00 AM	4/10/15 5:00	100.	
55	Create Design Team Framework & Process Step	✓	14 days	2/12/15 8:00 AM	3/3/15 6:00	100.	
56	Design Team A - IANA Service Level Expectations	✓	29 days	3/3/15 8:00 AM	4/10/15 5:00	100.	
57	Design Team B - Appeal Mechanism for ccTLD Delegations / Redelegations	✓	29 days	3/3/15 8:00 AM	4/10/15 5:00	100.	
58	Design Team C - CSC	✓	29 days	3/3/15 8:00 AM	4/10/15 5:00	100.	
59	Design Team D - Authorization Function	✓	24 days	3/10/15 8:00 AM	4/10/15 5:00	100.	
60	Design Team E - SAC 69	✓	24 days	3/10/15 8:00 AM	4/10/15 5:00	100.	
61	Design Team F - Relationship between the NTIA, IANA and the Root Zone Maintainer	✓	24 days	3/10/15 8:00 AM	4/10/15 5:00	100.	
62	Design Team G - IANA Intellectual Property Rights, including the IANA Trademark and Domain Name	✓	1 days	4/10/15 8:00 AM	4/10/15 5:00	100.	
63	Design Team H - .INT Operations	✓	1 days	4/10/15 8:00 AM	4/10/15 5:00	100.	
64	Design Team I - Competition policy and Conflicts of Interest	✓	1 days	4/10/15 8:00 AM	4/10/15 5:00	100.	
65	Design Team J - CSC/MRT confidentiality and the perception of conflicts of interest	✓	1 days	4/10/15 8:00 AM	4/10/15 5:00	100.	
66	Design Team K - OFAC Licensing	✓	1 days	4/10/15 8:00 AM	4/10/15 5:00	100.	
67	Design Team L - IANA Function Separation Mechanism	✓	19 days	3/17/15 8:00 AM	4/10/15 5:00	100.	
68	Design Team M - Escalation Mechanisms beyond CSC	✓	19 days	3/17/15 8:00 AM	4/10/15 5:00	100.	
69	Design Team N - Periodic Review of the IANA Functions	✓	19 days	3/17/15 8:00 AM	4/10/15 5:00	100.	
70	Design Team O - IANA Budget	✓	16 days	3/20/15 8:00 AM	4/10/15 5:00	100.	
71	Red Team (SAC069, Stress Test)	✓	11 days	3/27/15 8:00 AM	4/10/15 5:00	100.	
72	Consolidate & Refine 2nd Draft Proposal		48 days	2/16/15 8:00 AM	4/22/15 5:00	80.0	
73	Deliver 2nd Draft Proposal to Chartering Organizations		1 days	4/23/15 8:00 AM	4/23/15 5:00	0.0	72
74	Publish Draft Proposal for Public Comment (28 days)		21 days	4/23/15 8:00 AM	5/21/15 5:00	0.0	72
75	Review Public Comments		10 days	5/22/15 8:00 AM	6/5/15 5:00	0.0	74
76	Create Summary Report of Public Comments		10 days	5/22/15 8:00 AM	6/5/15 5:00	0.0	74
77	Develop Final Proposal and Approve within CWG		12 days	5/22/15 8:00 AM	6/9/15 5:00	0.0	74
78	Submit Final Proposal to Chartering Organizations		1 days	6/8/15 8:00 AM	6/8/15 5:00	0.0	77
79	Chartering Organizations Approve Final Proposal		13 days	6/9/15 8:00 AM	6/25/15 5:00	0.0	78
80	Submit Final Proposal to ICG		1 days	6/25/15 8:00 AM	6/25/15 5:00	78.3	79
81	blank	✓	0 days	6/25/15 8:00 AM	6/25/15 8:00	100.	
82	blank	✓	0 days	6/25/15 8:00 AM	6/25/15 8:00	100.	
83	**Support Cross-Community Working Group Meetings**		159 days	10/6/14 8:00 AM	6/1/15 5:00	91.2	
84	CWG Call #01 - Introductions, Charter Review - 6 Oct	✓	1 days	10/6/14 8:00 AM	10/6/14 5:00	100.	12
85	CWG Call #02 - Discuss Workplan & Deliverables- 13 Oct	✓	1 days	10/13/14 8:00 AM	10/13/14	100.	
86	CWG Call #03 - 22 Oct	✓	1 days	10/22/14 8:00 AM	10/22/14	100.	
87	CWG Call #04 - 30 Oct	✓	1 days	10/30/14 8:00 AM	10/30/14	100.	
88	CWG Call #05 - 04 Nov	✓	1 days	11/4/14 8:00 AM	11/4/14 6:00	100.	
89	RFP3 Subgroup Call - 6 Nov	✓	1 days	11/6/14 8:00 AM	11/6/14 6:00	100.	
90	RFP3 Subgroup Call - 12 Nov	✓	1 days	11/12/14 8:00 AM	11/12/14	100.	
91	CWG Call #06 - 13 Nov	✓	1 days	11/13/14 8:00 AM	11/13/14	100.	
92	RFP3B Subgroup Call - 13 Nov	✓	1 days	11/13/14 8:00 AM	11/13/14	100.	
93	CWG Call #07 - 19 Nov - Frankfurt	✓	1 days	11/19/14 8:00 AM	11/19/14	100.	
94	CWG Call #08 - 20 Nov - Frankfurt	✓	1 days	11/20/14 8:00 AM	11/20/14	100.	
95	RFP4 Subgroup Call - 25 Nov	✓	1 days	11/25/14 8:00 AM	11/25/14	100.	
96	CWG Call #09 - 27 Nov	✓	1 days	11/27/14 12:00 AM	12/1/14 6:00	100.	
97	RFP4 Subgroup Call - 28 Nov	✓	1 days	11/28/14 12:00 AM	12/1/14 6:00	100.	
98	CWG Call #11 - 11 Dec	✓	1 days	12/11/14 8:00 AM	12/11/14	100.	
99	RFP5 Subgroup Call - 12 Dec	✓	1 days	12/12/14 8:00 AM	12/12/14	100.	
100	RFP3 Subgroup Call - 15 Dec	✓	1 days	12/15/14 8:00 AM	12/15/14	100.	
101	RFP4 Subgroup Call - 16 Dec	✓	1 days	12/16/14 8:00 AM	12/16/14	100.	
102	RFP5 Subgroup Call - 17 Dec	✓	1 days	12/17/14 8:00 AM	12/17/14	100.	
103	CWG Call #12 - 18 Dec	✓	1 days	12/18/14 8:00 AM	12/18/14	100.	
104	RFP3 Subgroup Call - 19 Dec	✓	1 days	12/19/14 8:00 AM	12/19/14	100.	
105	RFP3 Subgroup Call - 22 Dec	✓	1 days	12/22/14 8:00 AM	12/22/14	100.	
106	RFP4 Subgroup Call - 23 Dec	✓	1 days	12/23/14 8:00 AM	12/23/14	100.	
107	RFP3 Subgroup Call - 29 Dec	✓	1 days	12/29/14 12:00 AM	1/5/15 6:00	100.	
108	RFP4 Subgroup Call - 29 Dec	✓	1 days	12/29/14 12:00 AM	1/5/15 6:00	100.	
109	CWG Call #13 - 30 Dec	✓	1 days	12/30/14 12:00 AM	1/5/15 6:00	100.	
110	RFP5 Subgroup Call - 30 Dec	✓	1 days	12/30/14 12:00 AM	1/5/15 6:00	100.	
111	RFP3 Subgroup Call - 2 Jan	✓	1 days	1/2/15 12:00 AM	1/5/15 6:00	100.	
112	RFP4 Subgroup Call - 6 Jan	✓	1 days	1/6/15 8:00 AM	1/6/15 6:00	100.	
113	RFP3 Subgroup Call - 7 Jan	✓	1 days	1/7/15 8:00 AM	1/7/15 6:00	100.	
114	RFP5 Subgroup Call - 7 Jan	✓	1 days	1/7/15 8:00 AM	1/7/15 6:00	100.	
115	CWG Call #14 - 08 Jan	✓	1 days	1/8/15 8:00 AM	1/8/15 6:00	100.	
116	CWG Call #15 - 10 Jan	✓	1 days	1/10/15 12:00 AM	1/12/15 6:00	100.	
117	CWG Call #16 - 10 Jan	✓	1 days	1/10/15 12:00 AM	1/12/15 6:00	100.	
118	CWG Call #17 - 11 Jan	✓	1 days	1/11/15 12:00 AM	1/12/15 6:00	100.	
119	CWG Call #18 - 11 Jan	✓	1 days	1/11/15 12:00 AM	1/12/15 6:00	100.	
120	RFP3B Subgroup Call - 14 Jan	✓	1 days	1/14/15 8:00 AM	1/14/15 6:00	100.	
121	CWG Call #18 - 15 Jan	✓	1 days	1/15/15 8:00 AM	1/15/15 6:00	100.	
122	RFP3 Subgroup Call - 16 Jan	✓	1 days	1/16/15 8:00 AM	1/16/15 6:00	100.	
123	RFP3 Subgroup Call - 19 Jan	✓	1 days	1/19/15 12:00 AM	1/20/15 6:00	100.	
124	CWG Call #19 - 22 Jan	✓	1 days	1/22/15 8:00 AM	1/22/15 6:00	100.	
125	RFP3B Subgfroup Call - 23 Jan	✓	1 days	1/23/15 8:00 AM	1/23/15 6:00	100.	
126	RFP3 Subgroup Call - 26 Jan	✓	1 days	1/26/15 8:00 AM	1/26/15 6:00	100.	
127	RFP4 Subgroup Call - 28 Jan	✓	1 days	1/28/15 8:00 AM	1/28/15 6:00	100.	
128	RFP3B Subgroup Call - 27 Jan	✓	1 days	1/27/15 8:00 AM	1/27/15 6:00	100.	
129	CWG Call #20 - 29 Jan	✓	1 days	1/29/15 8:00 AM	1/29/15 6:00	100.	
130	RFP3 Subgroup Call - 30 Jan	✓	1 days	1/30/15 8:00 AM	1/30/15 6:00	100.	
131	RFP3 Subgroup Call - 2 Feb	✓	1 days	2/2/15 8:00 AM	2/2/15 6:00	100.	
132	CWG Webinar for Singapore Meeting - 3 Feb	✓	1 days	2/3/15 8:00 AM	2/3/15 6:00	100.	
133	CWG Singapore Session - 11 Feb	✓	1 days	2/11/15 8:00 AM	2/11/15 6:00	100.	
134	CWG Singapore Session - 12 Feb	✓	1 days	2/12/15 8:00 AM	2/12/15 6:00	100.	
135	CWG Call - 19 Feb	✓	1 days	2/19/15 8:00 AM	2/19/15 6:00	100.	
136	CWG Call - 24 Feb	✓	1 days	2/24/15 8:00 AM	2/24/15 6:00	100.	
137	CWG Call - 26 Feb	✓	1 days	2/26/15 8:00 AM	2/26/15 6:00	100.	
138	CWG Call - 3 Mar	✓	1 days	3/3/15 8:00 AM	3/3/15 6:00	100.	
139	CWG Call - 5 Mar	✓	1 days	3/5/15 8:00 AM	3/5/15 6:00	100.	
140	Client Committee Call - 9 Mar	✓	1 days	3/9/15 8:00 AM	3/9/15 5:00	100.	
141	CWG Call - 10 Mar	✓	1 days	3/10/15 8:00 AM	3/10/15 5:00	100.	
142	Client Committee Call - 11 Mar	✓	1 days	3/11/15 8:00 AM	3/11/15 5:00	100.	
143	CWG Call - 12 Mar	✓	1 days	3/12/15 8:00 AM	3/12/15 5:00	100.	
144	Client Committee Call - 12 Mar	✓	1 days	3/12/15 8:00 AM	3/12/15 5:00	100.	
145	DT-C Call - 13 Mar	✓	1 days	3/13/15 8:00 AM	3/13/15 5:00	100.	
146	DT-C Call - 16 Mar	✓	1 days	3/16/15 8:00 AM	3/16/15 5:00	100.	
147	CWG Call - 17 Mar	✓	1 days	3/17/15 8:00 AM	3/17/15 5:00	100.	
148	DT-M Call - 18 Mar	✓	1 days	3/18/15 8:00 AM	3/18/15 5:00	100.	
149	Client Committee Call - 19 Mar	✓	1 days	3/19/15 8:00 AM	3/19/15 5:00	100.	
150	CWG Call - 19 Mar	✓	1 days	3/19/15 8:00 AM	3/19/15 5:00	100.	
151	DT-M Call - 19 Mar	✓	1 days	3/19/15 8:00 AM	3/19/15 5:00	100.	
152	DT-C Call - 20 Mar	✓	1 days	3/20/15 8:00 AM	3/20/15 5:00	100.	
153	DT-C Call - 23 Mar	✓	1 days	3/23/15 8:00 AM	3/23/15 5:00	100.	
154	DT-M Call - 23 Mar	✓	1 days	4/23/15 8:00 AM	4/23/15 5:00	100.	
155	CWG - Face to Face - 26 Mar	✓	1 days	3/26/15 8:00 AM	3/26/15 5:00	100.	
156	CWG - Face to Face - 27 Mar	✓	1 days	3/27/15 8:00 AM	3/27/15 5:00	100.	
157	DT-M Call - 31 Mar	✓	1 days	3/31/15 8:00 AM	3/31/15 5:00	100.	
158	DT-O Call - 1 Apr	✓	1 days	4/1/15 8:00 AM	4/1/15 5:00	100.	
159	CWG Call - 2 Apr	✓	1 days	4/2/15 8:00 AM	4/2/15 5:00	100.	
160	Client Committee Call - 2 Apr	✓	1 days	4/2/15 8:00 AM	4/2/15 5:00	100.	
161	DT-C Call - 2 Apr	✓	1 days	4/2/15 8:00 AM	4/2/15 5:00	100.	
162	DT-M Call - 2 Apr	✓	1 days	4/2/15 8:00 AM	4/2/15 5:00	100.	
163	DT-O Call - 3 Apr	✓	1 days	4/3/15 8:00 AM	4/3/15 5:00	100.	
164	DT-O Call - 6 Apr	✓	1 days	4/6/15 8:00 AM	4/6/15 5:00	100.	
165	CWG Call - 7 Apr	✓	1 days	4/7/15 8:00 AM	4/7/15 5:00	100.	
166	DT-A Call - 7 Apr	✓	1 days	4/7/15 8:00 AM	4/7/15 5:00	100.	
167	DT-M Call - 7 Apr	✓	1 days	4/7/15 8:00 AM	4/7/15 5:00	100.	
168	DT-C Call - 8 Apr	✓	1 days	4/8/15 8:00 AM	4/8/15 5:00	100.	
169	DT-L Call - 8 Apr	✓	1 days	4/8/15 8:00 AM	4/8/15 5:00	100.	
170	DT-N Call - 8 Apr	✓	1 days	4/8/15 8:00 AM	4/8/15 5:00	100.	
171	Client Committee Call - 9 Apr	✓	1 days	4/9/15 8:00 AM	4/9/15 5:00	100.	
172	DT-B Call - 9 Apr	✓	1 days	4/9/15 8:00 AM	4/9/15 5:00	100.	
173	DT-O Call - 9 Apr	✓	1 days	4/9/15 8:00 AM	4/9/15 5:00	100.	
174	Client Committee Call - 10 Apr	✓	1 days	4/10/15 8:00 AM	4/10/15 5:00	100.	
175	DT-C Call - 10 Apr	✓	1 days	4/10/15 8:00 AM	4/10/15 5:00	100.	
176	DT-M Call - 10 Apr	✓	1 days	4/10/15 8:00 AM	4/10/15 5:00	100.	
177	DT-N Call - 10 Apr	✓	1 days	4/10/15 8:00 AM	4/10/15 5:00	100.	
178	High Intensity Session - 13 Apr	✓	1 days	4/13/15 8:00 AM	4/13/15 5:00	100.	
179	DT-A Call - 13 Apr	✓	1 days	4/13/15 8:00 AM	4/13/15 5:00	100.	
180	DT-F Call - 13 Apr	✓	1 days	4/13/15 8:00 AM	4/13/15 5:00	100.	
181	High Intensity Session - 14 Apr	✓	1 days	4/14/15 8:00 AM	4/14/15 5:00	100.	
182	DT-F Call - 15 Apr	✓	1 days	4/15/15 8:00 AM	4/15/15 5:00	100.	
183	CWG Call - 16 Apr	✓	1 days	4/16/15 8:00 AM	4/16/15 5:00	100.	
184	Client Committee Call - 16 Apr	✓	1 days	4/16/15 8:00 AM	4/16/15 5:00	100.	
185	CWG Call - 21 Apr	✓	1 days	4/21/15 8:00 AM	4/21/15 5:00	100.	
186	CWG Call - 23 Apr	✓	1 days	4/23/15 8:00 AM	4/23/15 5:00	100.	
187	Client Committee Call - 23 Apr	✓	1 days	4/23/15 8:00 AM	4/23/15 5:00	100.	
188	CWG Call - 28 Apr		1 days	4/28/15 8:00 AM	4/28/15 5:00	0.0	
189	CWG Call - 30 Apr		1 days	4/30/15 8:00 AM	4/30/15 5:00	0.0	
190	CWG Call - 5 May		1 days	5/5/15 8:00 AM	5/5/15 5:00	0.0	
191	CWG Call - 7 May		1 days	5/7/15 8:00 AM	5/7/15 5:00	0.0	
192	CWG Call - 12 May		1 days	5/12/15 8:00 AM	5/12/15 5:00	0.0	
193	CWG Call - 14 May		1 days	5/14/15 8:00 AM	5/14/15 5:00	0.0	
194	CWG Call - 19 May		1 days	5/19/15 8:00 AM	5/19/15 5:00	0.0	
195	CWG Call - 21 May		1 days	5/21/15 8:00 AM	5/21/15 5:00	0.0	
196	High Intensity Session - 30 May		1 days	5/30/15 12:00 AM	6/1/15 5:00	0.0	
197	High Intensity Session - 31 May		1 days	5/31/15 12:00 AM	6/1/15 5:00	0.0	

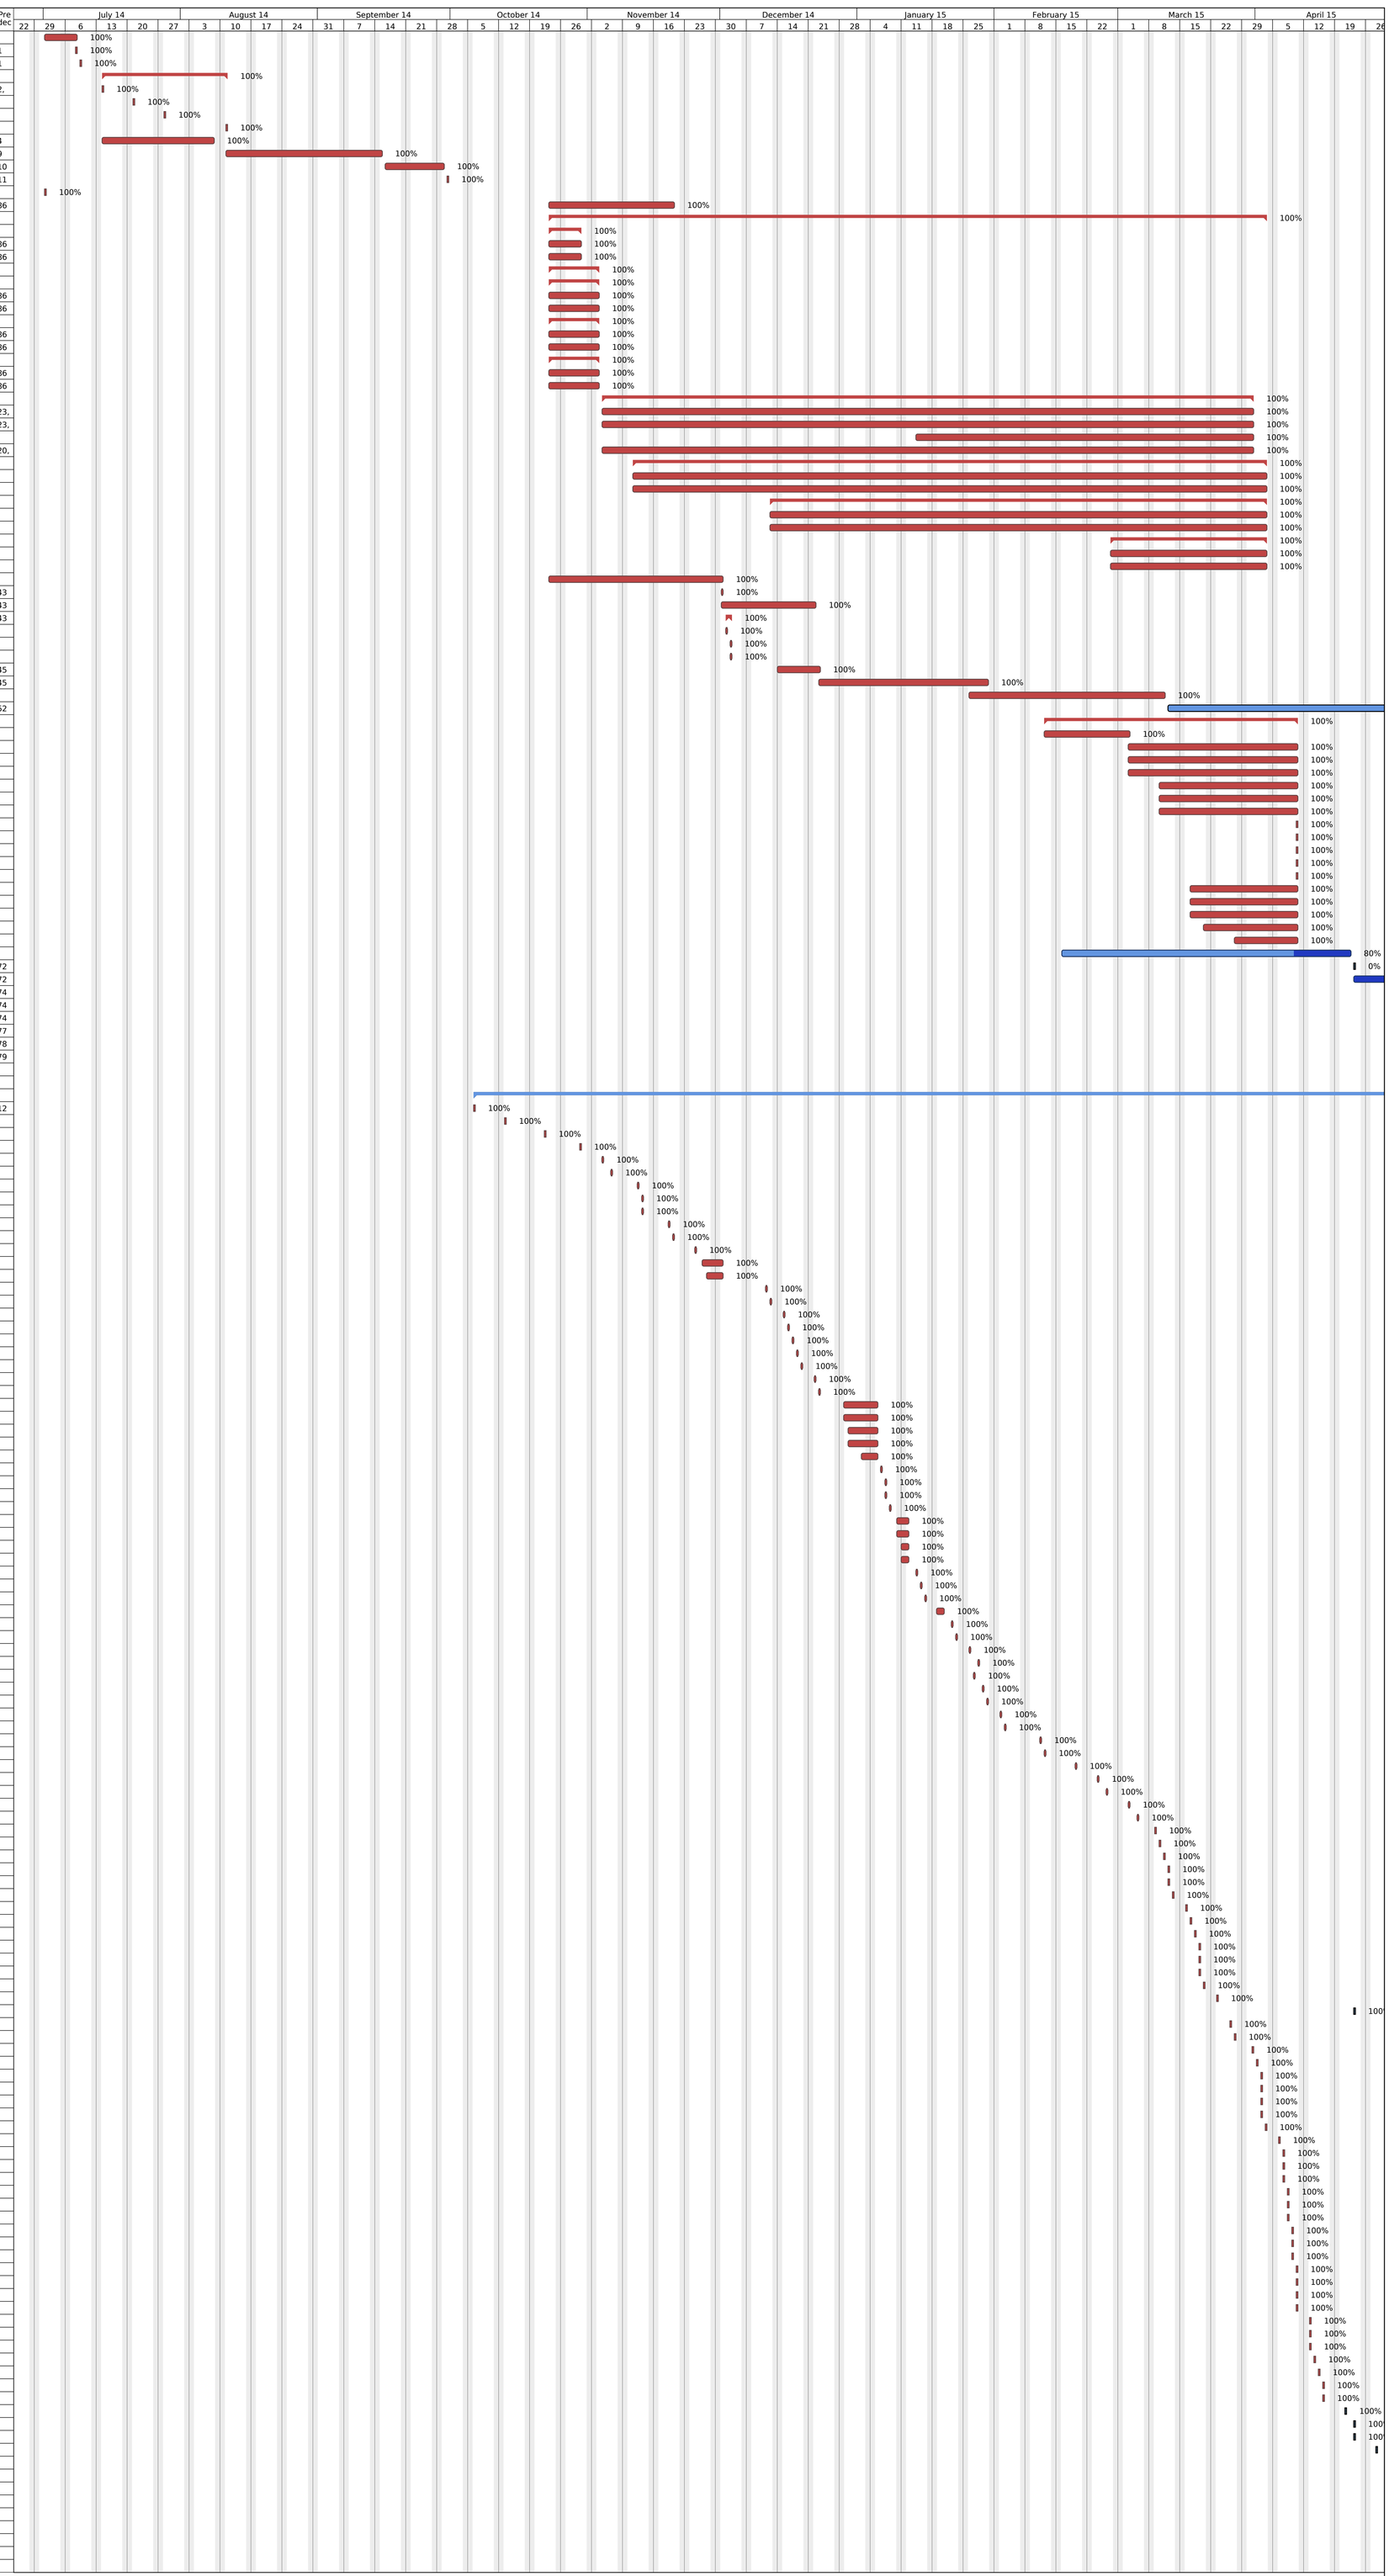

©2000-2015 Licensed Copyright by Workfront, Inc. All rights reserved.

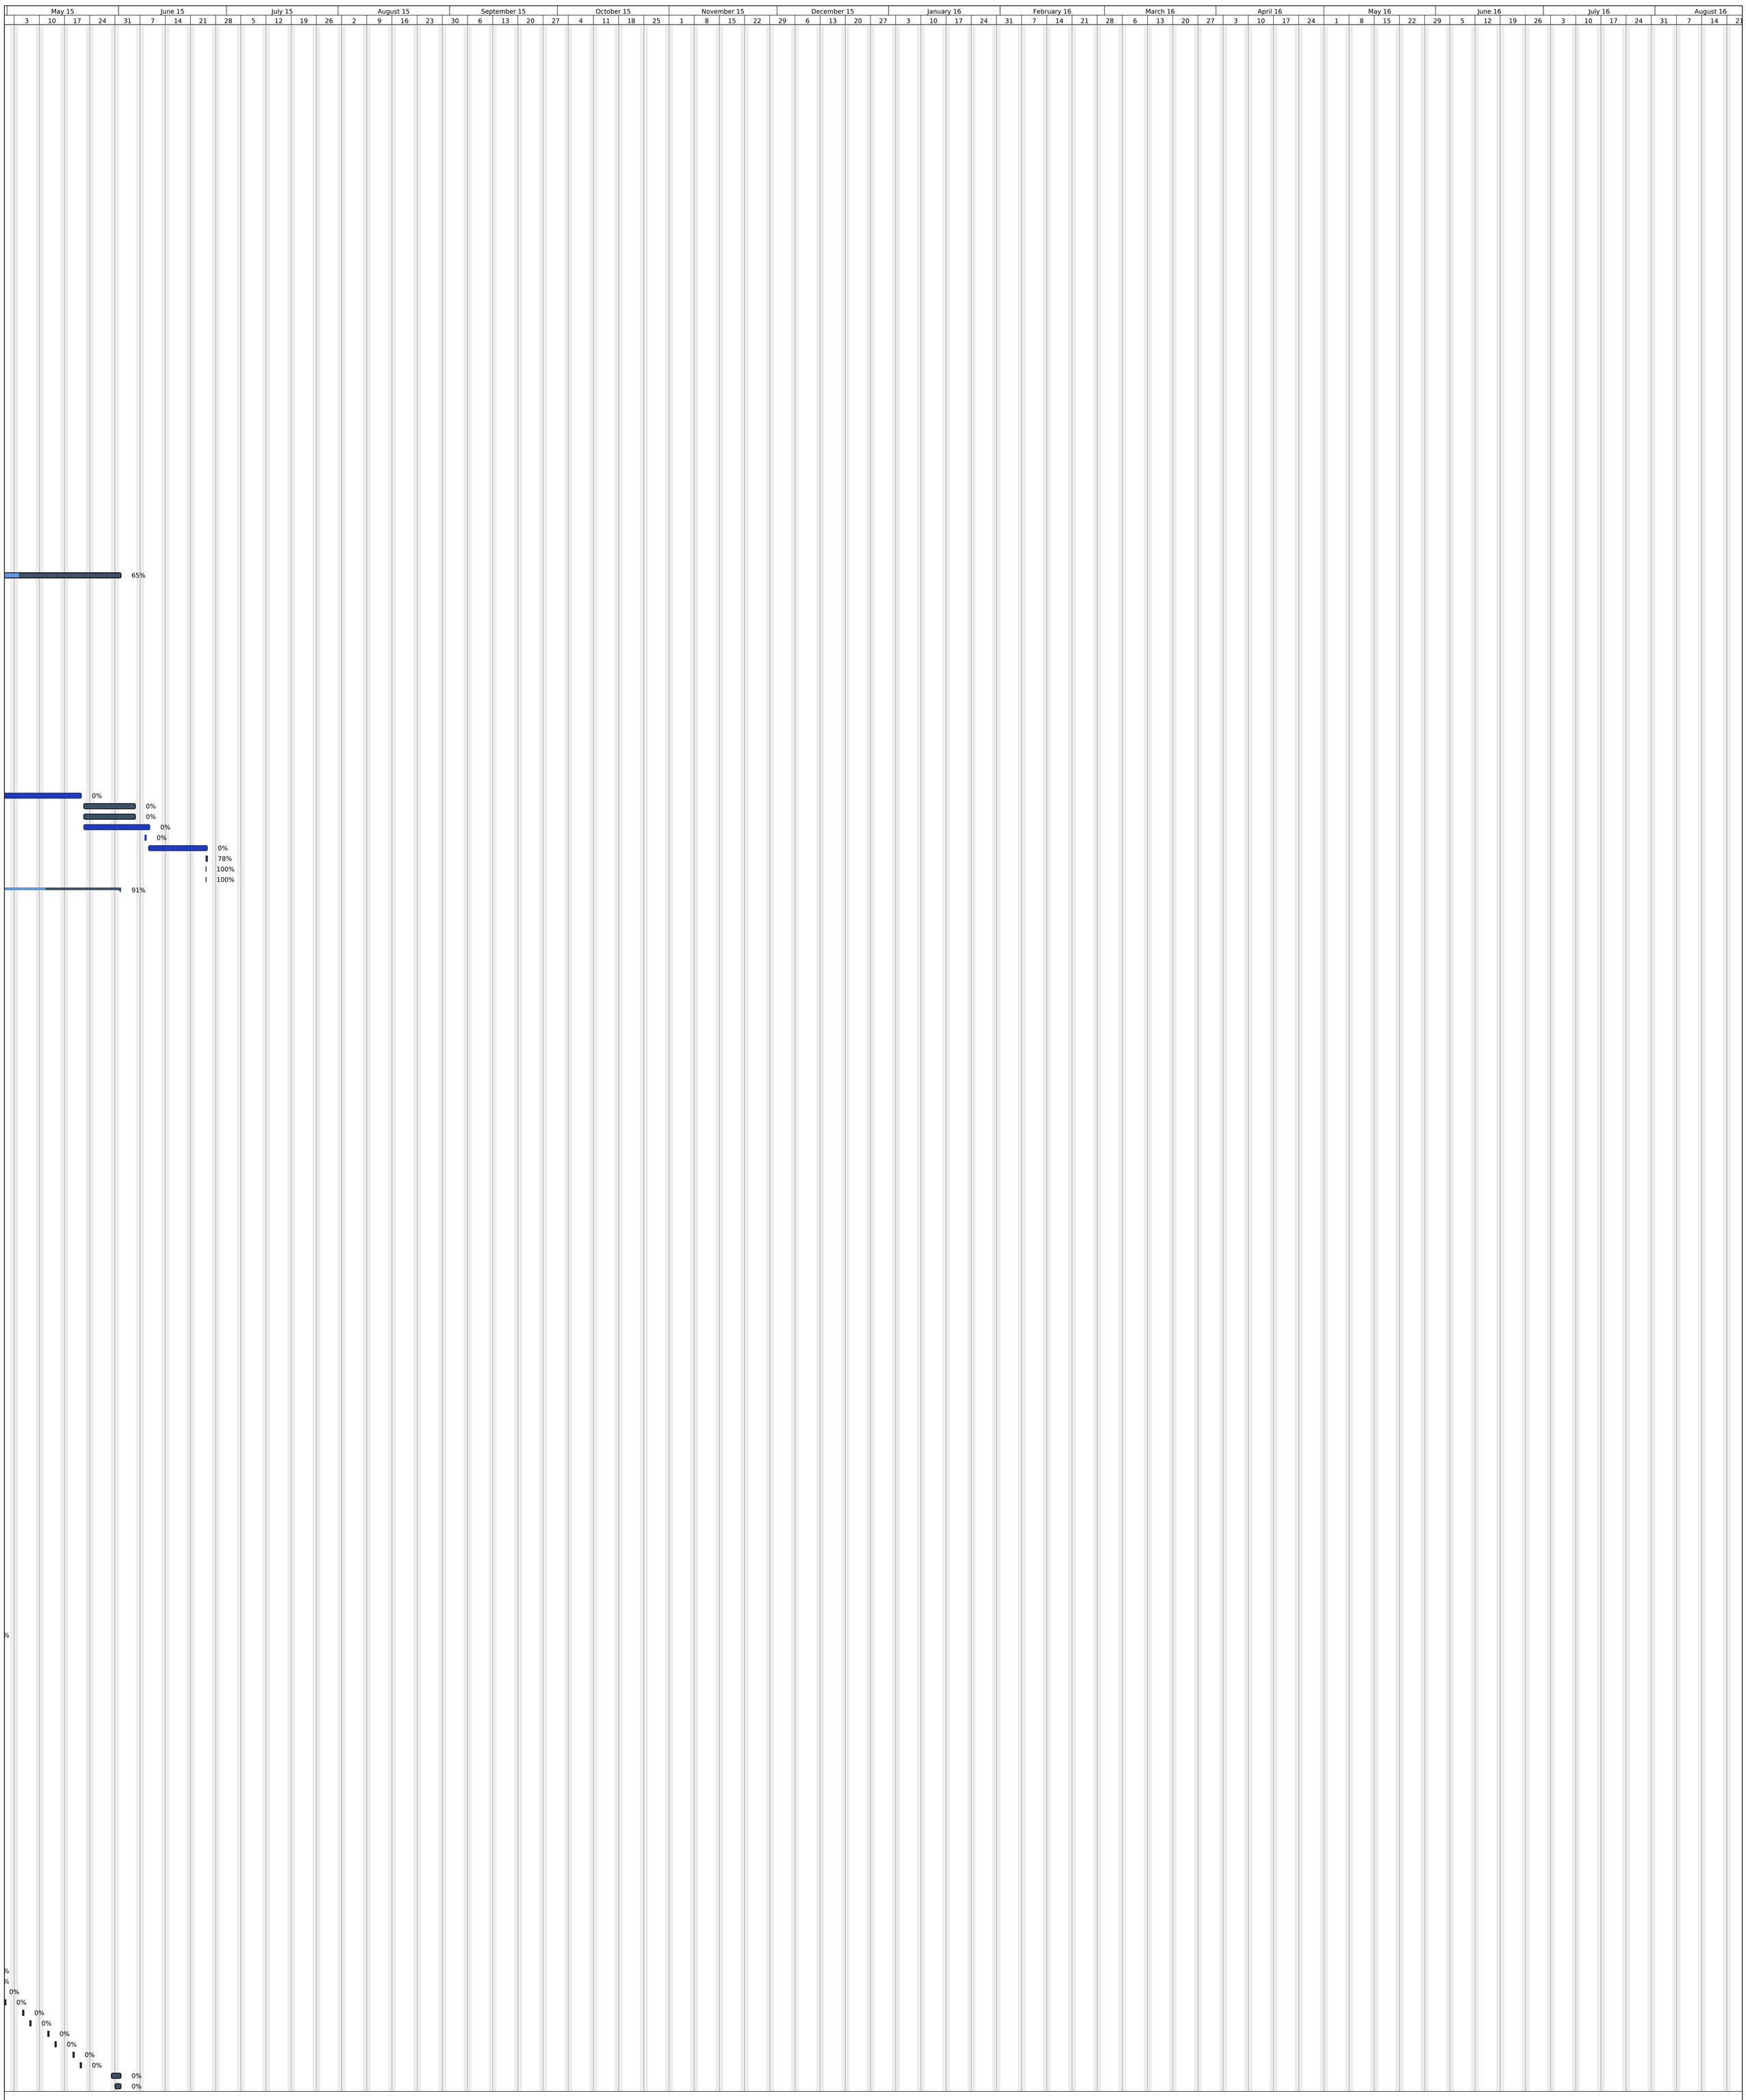

©2000-2015 Licensed Copyright by Workfront, Inc. All rights reserved.
