| # | Name | Duration | Start Date | Completion Date | % | Predecessors |
|---|---|---|---|---|---|---|
| 1 | **Prepare Issue Report** | 132 days | 7/29/15 8:00 AM | 2/12/16 5:00 PM | 100.0% | |
| 2 | Prepare Preliminary Issue Report | 18 days | 7/29/15 8:00 AM | 8/21/15 5:00 PM | 100.0% | |
| 3 | Legal Review of Preliminary Issue Report and Amend Report | 5 days | 8/24/15 8:00 AM | 8/28/15 5:00 PM | 100.0% | 2 |
| 4 | Publish Preliminary Issue Report for Public Comment | 44 days | 8/31/15 8:00 AM | 10/30/15 5:00 PM | 100.0% | 3 |
| 5 | Publish Public Comment Summary and Analysis | 17 days | 11/2/15 8:00 AM | 11/24/15 5:00 PM | 100.0% | 4 |
| 6 | Complete Issue Report | 24 days | 11/2/15 8:00 AM | 12/7/15 5:00 PM | 100.0% | 4 |
| 7 | Initiate PDP on New gTLD Subsequent Procedures | 1 days | 12/17/15 8:00 AM | 12/17/15 5:00 PM | 100.0% | |
| 8 | Adopt New gTLD Subsequent Procedures Charter | 1 days | 1/21/16 8:00 AM | 1/21/16 5:00 PM | 100.0% | |
| 9 | Publish Call For Volunteers | 15 days | 1/25/16 8:00 AM | 2/12/16 5:00 PM | 100.0% | |
| 10 | **Initiate PDP Operations** | 53 days | 2/22/16 8:00 AM | 5/4/16 5:00 PM | 100.0% | |
| 11 | Elect WG Chairs | 12 days | 2/22/16 8:00 AM | 3/8/16 5:00 PM | 100.0% | |
| 12 | Develop Work Organization | 35 days | 3/10/16 8:00 AM | 4/27/16 5:00 PM | 100.0% | |
| 13 | Develop Work Plan | 5 days | 4/28/16 8:00 AM | 5/4/16 5:00 PM | 100.0% | 12 |
| 14 | **Misc WG Activities** | 145 days | 4/4/16 8:00 AM | 10/26/16 5:00 PM | 90.41% | |
| 15 | Review Existing Principles/Recommendations | 14 days | 4/4/16 8:00 AM | 4/21/16 5:00 PM | 100.0% | |
| 16 | Send outreach to SO/AC/SG/C for Statements/Advice | 10 days | 5/2/16 8:00 AM | 5/13/16 5:00 PM | 100.0% | |
| 17 | Select liaison for RPMs PDP | 21 days | 4/18/16 8:00 AM | 5/16/16 5:00 PM | 100.0% | |
| 18 | ICANN56 - Helsinki Meeting Planning | 14 days | 5/23/16 8:00 AM | 6/10/16 5:00 PM | 100.0% | |
| 19 | ICANN57 - Hyderabad Meeting Planning | 14 days | 10/7/16 8:00 AM | 10/26/16 5:00 PM | 50.0% | |
| 20 | **Overarching Issues/Topics** | 194 days | 4/11/16 8:00 AM | 1/23/17 5:00 PM | 68.14% | |
| 21 | Draft Request for Constituency Comment 1 | 33 days | 4/25/16 8:00 AM | 6/9/16 5:00 PM | 100.0% | |
| 22 | Seek Input From SO/AC/SG/Cs | 31 days | 6/10/16 8:00 AM | 7/25/16 5:00 PM | 100.0% | 21 |
| 23 | Consider Input from SO/AC/SG/Cs | 80 days | 7/26/16 8:00 AM | 11/15/16 5:00 PM | 50.0% | 22 |
| 24 | Conclude deliberations 4.2.1: Cancelling Subsequent Procedures | 40 days | 11/16/16 8:00 AM | 1/23/17 5:00 PM | 25.0% | 23 |
| 25 | Conclude deliberations 4.2.15: Different TLD Types | 40 days | 11/16/16 8:00 AM | 1/23/17 5:00 PM | 25.0% | 23 |
| 26 | Conclude deliberations 4.2.7: Applications Assessed in Rounds | 40 days | 11/16/16 8:00 AM | 1/23/17 5:00 PM | 25.0% | 23 |
| 27 | Conclude deliberations 4.2.2: Predictability | 40 days | 11/16/16 8:00 AM | 1/23/17 5:00 PM | 0.0% | 23 |
| 28 | Conclude deliberations 4.2.4: Community Engagement | 40 days | 11/16/16 8:00 AM | 1/23/17 5:00 PM | 0.0% | 23 |
| 29 | Conclude deliberations 4.2.16: Application Submission Limits | 40 days | 11/16/16 8:00 AM | 1/23/17 5:00 PM | 0.0% | 23 |
| 30 | **4.2.1: Cancelling Subsequent Procedures** | 184 days | 4/11/16 8:00 AM | 1/9/17 5:00 PM | 76.92% | |
| 31 | 4.2.1: Preliminary deliberations | 100 days | 4/11/16 8:00 AM | 8/30/16 5:00 PM | 100.0% | |
| 32 | Consider preliminary inputs from CCT-RT. Conclude in Phase 2. | 30 days | 11/16/16 8:00 AM | 1/9/17 5:00 PM | 0.0% | |
| 33 | 4.2.15: Different TLD Types | 80 days | 4/18/16 8:00 AM | 8/9/16 5:00 PM | 100.0% | |
| 34 | 4.2.7: Applications Assessed in Round (Application Order) | 120 days | 4/25/16 8:00 AM | 10/12/16 5:00 PM | 100.0% | |
| 35 | 4.2.2: Predictability | 50 days | 5/9/16 8:00 AM | 7/19/16 5:00 PM | 100.0% | |
| 36 | 4.2.4: Community Engagement | 50 days | 5/9/16 8:00 AM | 7/19/16 5:00 PM | 100.0% | |
| 37 | 4.2.16: Application Submission Limits | 50 days | 5/16/16 8:00 AM | 7/26/16 5:00 PM | 100.0% | |
| 38 | **Track 1 - Overall Process** | 125 days | 8/15/16 8:00 AM | 2/17/17 5:00 PM | 11.21% | |
| 39 | 4.2.8: Accreditation Programs | 84 days | 8/15/16 8:00 AM | 12/13/16 5:00 PM | 25.0% | |
| 40 | **4.2.14: Support for Applicants from Developing Countries** | 125 days | 8/15/16 8:00 AM | 2/17/17 5:00 PM | 20.16% | |
| 41 | 4.2.14: Preliminary deliberations | 125 days | 8/15/16 8:00 AM | 2/17/17 5:00 PM | 25.0% | |
| 42 | Consider preliminary inputs from CCT-RT. Conclude in Phase 2. | 30 days | 11/1/16 8:00 AM | 12/14/16 5:00 PM | 0.0% | |
| 43 | 4.2.6: Clarity of Application Process | 29 days | 11/2/16 8:00 AM | 12/14/16 5:00 PM | 0.0% | |
| 44 | 4.2.10: Application Fees | 29 days | 11/2/16 8:00 AM | 12/14/16 5:00 PM | 0.0% | |
| 45 | 4.2.17: Variable Fees | 29 days | 11/2/16 8:00 AM | 12/14/16 5:00 PM | 0.0% | |
| 46 | 4.2.12: Application Queuing | 18 days | 11/29/16 8:00 AM | 12/22/16 5:00 PM | 0.0% | |
| 47 | 4.2.13: Application Submission Period | 11 days | 11/29/16 8:00 AM | 12/13/16 5:00 PM | 0.0% | |
| 48 | 4.2.9: Systems | 23 days | 12/5/16 8:00 AM | 1/13/17 5:00 PM | 0.0% | |
| 49 | 4.2.5: Applicant Guidebook | 41 days | 12/5/16 8:00 AM | 2/8/17 5:00 PM | 0.0% | |
| 50 | 4.2.11: Communications | 23 days | 12/5/16 8:00 AM | 1/13/17 5:00 PM | 0.0% | |
| 51 | **Track 2 - Legal/Contractual/Regulatory** | 180 days | 8/8/16 8:00 AM | 4/28/17 5:00 PM | 0.95% | |
| 52 | **4.3.2: Base Registry Agreement/Differentiation** | 148 days | 9/22/16 8:00 AM | 4/28/17 5:00 PM | 0.0% | |
| 53 | 4.3.2: Preliminary deliberations | 148 days | 9/22/16 8:00 AM | 4/28/17 5:00 PM | 0.0% | |
| 54 | Consider preliminary inputs from CCT-RT. Conclude in Phase 2. | 30 days | 11/1/16 8:00 AM | 12/14/16 5:00 PM | 0.0% | |
| 55 | **4.3.7: Second-level RPMs** | 139 days | 8/8/16 8:00 AM | 3/2/17 5:00 PM | 6.25% | |
| 56 | Liaise with RPMs PDP, determine what, if any, RPMs related work is within scope | 10 days | 8/8/16 8:00 AM | 8/19/16 5:00 PM | 100.0% | |
| 57 | 4.3.7: Preliminary deliberations | 120 days | 9/2/16 8:00 AM | 3/2/17 5:00 PM | 0.0% | |
| 58 | Consider preliminary inputs from CCT-RT. Conclude in Phase 2. | 30 days | 11/1/16 8:00 AM | 12/14/16 5:00 PM | 0.0% | |
| 59 | 4.3.1: Reserved Names List (Top-level, second-level, string requirements) | 73 days | 10/20/16 8:00 | 2/10/17 5:00 PM | 0.0% | |
| 60 | 4.3.3: Registrant Protections | 47 days | 11/3/16 8:00 AM | 1/19/17 5:00 PM | 0.0% | |
| 61 | 4.3.10: IGO/INGO Protections | 6 days | 11/18/16 8:00 AM | 11/29/16 5:00 PM | 0.0% | |
| 62 | 4.3.11: Closed Generics | 49 days | 12/1/16 8:00 AM | 2/16/17 5:00 PM | 0.0% | |
| 63 | Applicant Terms and Conditions | 49 days | 12/15/16 8:00 AM | 3/2/17 5:00 PM | 0.0% | |
| 64 | **4.3.5: Registrar Non-Discrimination** | 79 days | 11/1/16 8:00 AM | 3/2/17 5:00 PM | 0.0% | |
| 65 | 4.3.5: Preliminary deliberations | 49 days | 12/15/16 8:00 AM | 3/2/17 5:00 PM | 0.0% | |
| 66 | Consider preliminary inputs from CCT-RT. Conclude in Phase 2. | 50 days | 11/1/16 8:00 AM | 1/20/17 5:00 PM | 0.0% | |
| 67 | **4.3.8: Registry/Registrar Standardization (Separation)** | 99 days | 11/1/16 8:00 AM | 3/30/17 5:00 PM | 0.0% | |
| 68 | 4.3.8: Preliminary deliberations | 61 days | 1/5/17 8:00 AM | 3/30/17 5:00 PM | 0.0% | |
| 69 | Consider preliminary inputs from CCT-RT. Conclude in Phase 2. | 30 days | 11/1/16 8:00 AM | 12/14/16 5:00 PM | 0.0% | |
| 70 | 4.3.6: TLD Rollout | 51 days | 1/19/17 8:00 AM | 3/30/17 5:00 PM | 0.0% | |
| 71 | 4.3.4: Contractual Compliance | 51 days | 1/19/17 8:00 AM | 3/30/17 5:00 PM | 0.0% | |
| 72 | **4.3.9: Global Public Interest (GAC Advice/Safeguards)** | 120 days | 11/1/16 8:00 AM | 4/28/17 5:00 PM | 0.0% | |
| 73 | 4.3.9: Preliminary deliberations | 63 days | 2/1/17 8:00 AM | 4/28/17 5:00 PM | 0.0% | |
| 74 | Consider preliminary inputs from CCT-RT. Conclude in Phase 2. | 30 days | 11/1/16 8:00 AM | 12/14/16 5:00 PM | 0.0% | |
| 75 | **Track 3 - String Contention, Objections & Disputes** | 175 days | 8/15/16 8:00 AM | 4/28/17 5:00 PM | 0.0% | |
| 76 | **4.4.3: Objections (Role of Independent Objector)** | 105 days | 8/29/16 8:00 AM | 2/3/17 5:00 PM | 0.0% | |
| 77 | Look at all the objections that were filed, how they turned out, consistency. Look at the role of | 82 days | 9/27/16 8:00 AM | 1/31/17 5:00 PM | 0.0% | |
| 78 | Look at role of the Independent Objector | 37 days | 12/1/16 8:00 AM | 1/31/17 5:00 PM | 0.0% | |
| 79 | 4.4.3: Preliminary deliberations | 105 days | 8/29/16 8:00 AM | 2/3/17 5:00 PM | 0.0% | |
| 80 | Consider preliminary inputs from CCT-RT. Conclude in Phase 2. | 30 days | 11/1/16 8:00 AM | 12/14/16 5:00 PM | 0.0% | |
| 81 | 4.4.1: New gTLD Applicant Freedom of Expression | 32 days | 1/16/17 8:00 AM | 2/28/17 5:00 PM | 0.0% | |
| 82 | **4.4.5: Community Applications (Community Priority Evaluations)** | 101 days | 11/1/16 8:00 AM | 4/3/17 5:00 PM | 0.0% | |
| 83 | 4.4.5: Preliminary deliberations | 25 days | 2/28/17 8:00 AM | 4/3/17 5:00 PM | 0.0% | |
| 84 | Consider preliminary inputs from CCT-RT. Conclude in Phase 2. | 30 days | 11/1/16 8:00 AM | 12/14/16 5:00 PM | 0.0% | |

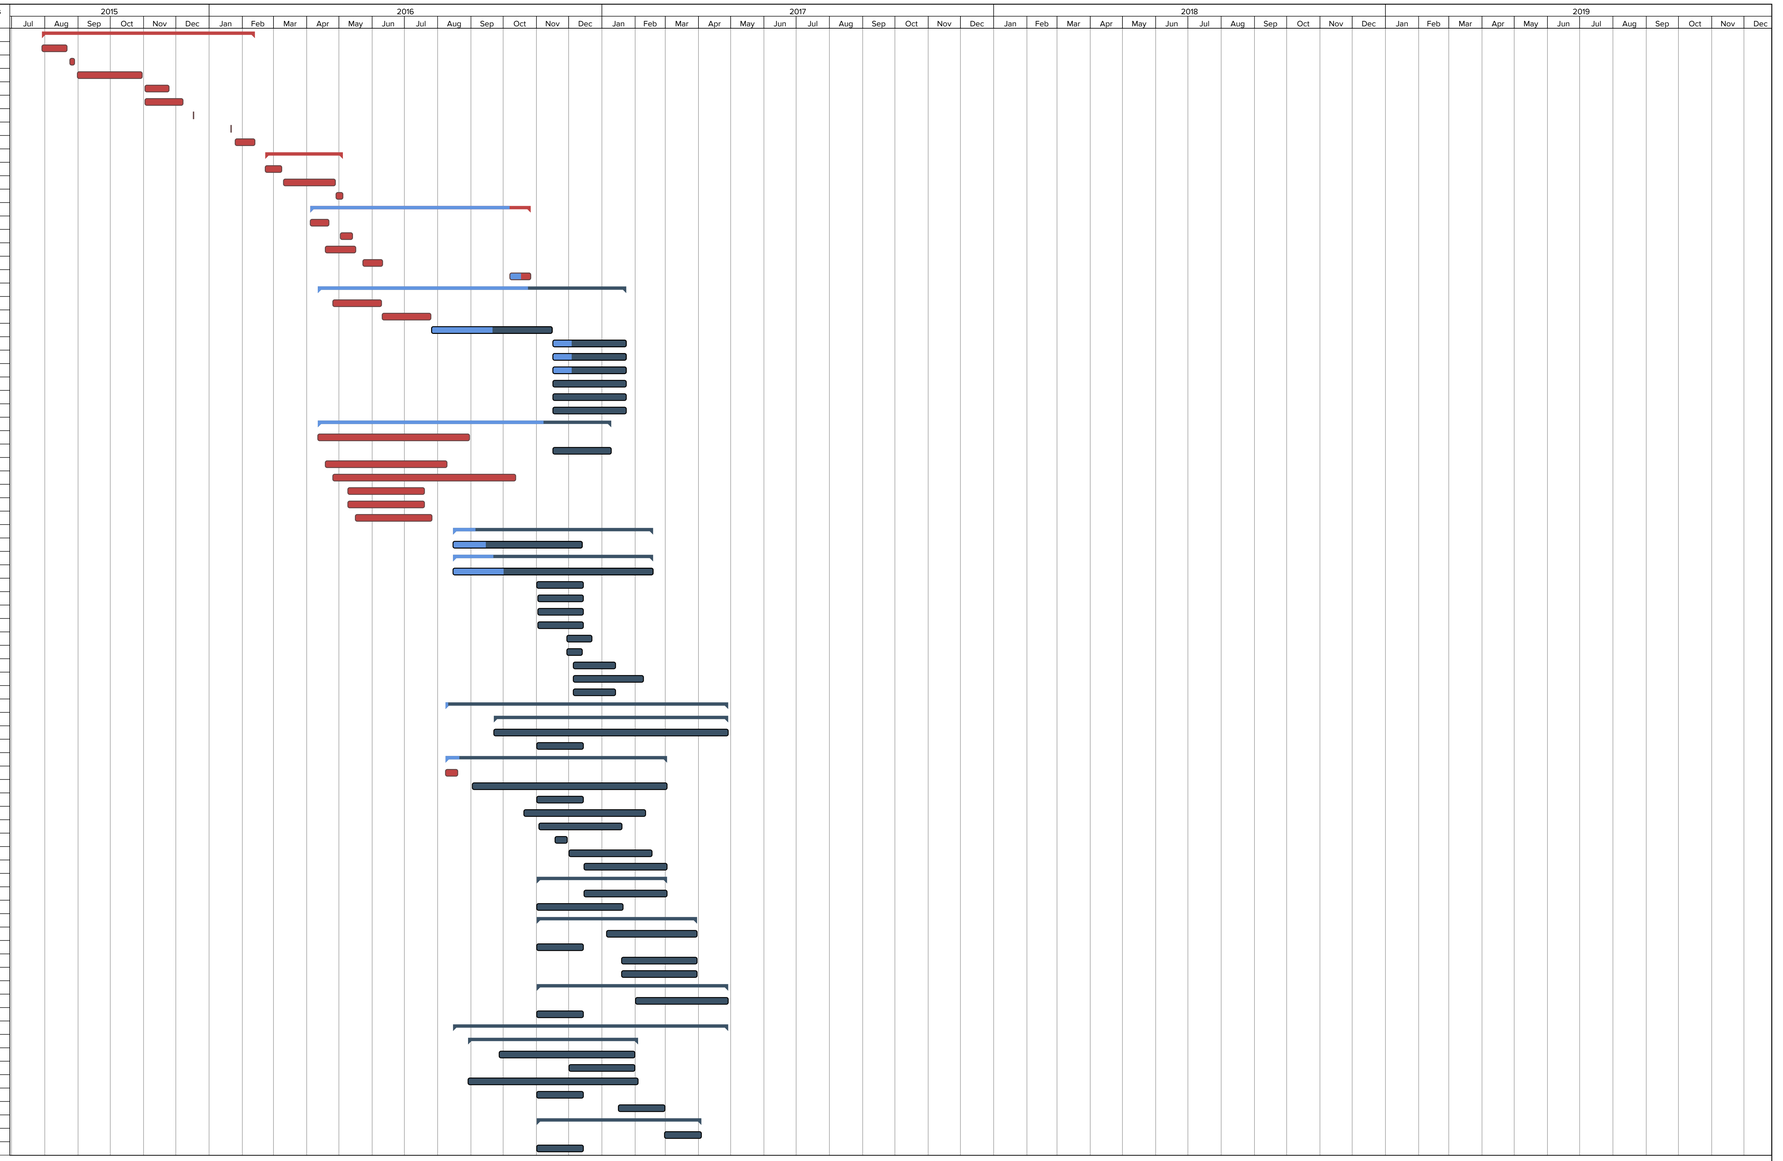


Project: Policy Development Next Phase New gTLD - FY16-FY17
Planned Start: 7/1/15
Planned Completion: 7/10/18
Printed On: 10/28/16

Projected Start: 7/8/15
Projected Completion: 8/16/18



Policy Development Next Phase New gTLD

This effort is intended to analyze subjects that may lead to changes or adjustments for subsequent New gTLD Procedures by preparing a Preliminary Issue Report, seeking public comment, and then preparing a final Issue Report for GNSO Council consideration.

Planned
Summary
In Progress
Milestone

©2000-2016 Licensed Copyright by Workfront, Inc. All rights reserved.

| # | Name | Duration | Start Date | Completion Date | % | Predecessors |
|---|---|---|---|---|---|---|
| 85 | **4.4.2: String Similarity (Evaluations)** | 175 days | 8/15/16 8:00 AM | 4/28/17 5:00 PM | 0.0% | |
| 86 | Develop list of string similarity outcomes (e.g., plurals). Include auctions, indirect contention, | 29 days | 3/21/17 8:00 AM | 4/28/17 5:00 PM | 0.0% | |
| 87 | 4.4.2: Preliminary deliberations | 70 days | 8/15/16 8:00 AM | 11/21/16 5:00 PM | 0.0% | |
| 88 | Consider preliminary inputs from CCT-RT. Conclude in Phase 2. | 30 days | 11/1/16 8:00 AM | 12/14/16 5:00 PM | 0.0% | |
| 89 | 4.4.4: Accountability Mechanisms | 19 days | 4/4/17 8:00 AM | 4/28/17 5:00 PM | 0.0% | |
| 90 | **Track 4 - IDNs & Universal Acceptance/SSR and Technical/Operational/Financial** | 109 days | 10/31/16 8:00 AM | 4/12/17 5:00 PM | 0.0% | |
| 91 | 4.5.1: Internationalized Domain Names | 60 days | 11/3/16 8:00 AM | 2/7/17 5:00 PM | 0.0% | |
| 92 | Universal Acceptance | 40 days | 11/11/16 8:00 AM | 1/18/17 5:00 PM | 0.0% | |
| 93 | 4.6.2: Applicant Reviews | 100 days | 11/11/16 8:00 AM | 4/12/17 5:00 PM | 0.0% | |
| 94 | 4.6.3: Name Collisions | 80 days | 10/31/16 8:00 AM | 3/2/17 5:00 PM | 0.0% | |
| 95 | **4.6.1: Security and Stability** | 80 days | 11/1/16 8:00 AM | 3/3/17 5:00 PM | 0.0% | |
| 96 | 4.6.1:Preliminary deliberations | 70 days | 11/15/16 8:00 AM | 3/3/17 5:00 PM | 0.0% | |
| 97 | Consider preliminary inputs from CCT-RT. Conclude in Phase 2. | 30 days | 11/1/16 8:00 AM | 12/14/16 5:00 PM | 0.0% | |
| 98 | **Community Comment 2 (CC2)** | 157 days | 11/21/16 8:00 AM | 7/10/17 5:00 PM | 0.0% | |
| 99 | Draft Request for Constituency Comment 2 | 50 days | 11/21/16 8:00 AM | 2/9/17 5:00 PM | 0.0% | |
| 100 | Seek Input From SO/AC/SG/Cs | 30 days | 2/10/17 8:00 AM | 3/23/17 5:00 PM | 0.0% | 99 |
| 101 | Consider Input from SO/AC/SG/Cs | 30 days | 3/24/17 8:00 AM | 5/4/17 5:00 PM | 0.0% | 100 |
| 102 | Consolidate and Organize Input | 7 days | 5/5/17 8:00 AM | 5/15/17 5:00 PM | 0.0% | 101 |
| 103 | Conclude deliberations 4.2.8: Accreditation Programs | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 104 | Conclude deliberations 4.2.14: Support for Applicants from Developing Countries | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 105 | Conclude deliberations 4.2.6: Clarity of Application Process | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 106 | Conclude deliberations 4.2.10: Application Fees | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 107 | Conclude deliberations 4.2.17: Variable Fees | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 108 | Conclude deliberations 4.2.12: Application Queuing | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 109 | Conclude deliberations 4.2.13: Application Submission Period | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 110 | Conclude deliberations 4.2.9: Systems | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 111 | Conclude deliberations 4.2.5: Applicant Guidebook | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 112 | Conclude deliberations 4.2.11: Communications | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 113 | Conclude deliberations 4.3.2: Base Registry Agreement/Differentiation | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 114 | Conclude deliberations 4.3.7: Second-level RPMs | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 115 | Conclude deliberations 4.3.1: Reserved Names List | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 116 | Conclude deliberations 4.3.3: Registrant Protections | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 117 | Conclude deliberations 4.3.10: IGO/INGO Protections | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 118 | Conclude deliberations 4.3.11: Closed Generics | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 119 | Conclude deliberations Applicant T&Cs | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 120 | Conclude deliberations 4.3.5: Registrar Non-Discrimination | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 121 | Conclude deliberations 4.3.8: Registry/Registrar Standardization (Separation) | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 122 | Conclude deliberations 4.3.6: TLD Rollout | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 123 | Conclude deliberations 4.3.4: Contractual Compliance | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 124 | Conclude deliberations 4.3.9: Global Public Interest (GAC Advice/Safeguards) | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 125 | Conclude deliberations 4.4.3: Objections (Role of Independent Objector) | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 126 | Conclude deliberations 4.4.1: New gTLD Applicant Freedom of Expression | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 127 | Conclude deliberations 4.4.5: Community Applications (Community Priority Evaluations) | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 128 | Conclude deliberations 4.4.2: String Similarity (Evaluations) | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 129 | Conclude deliberations 4.4.2: String Similarity | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 130 | Conclude deliberations 4.5.1: Internationalized Domain Names | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 131 | Conclude deliberations Univeral Acceptance | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 132 | Conclude deliberations 4.6.2: Applicant Reviews | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 133 | Conclude deliberations 4.6.3: Name Collisions | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 134 | Conclude deliberations 4.6.1: Security and Stability | 40 days | 5/16/17 8:00 AM | 7/10/17 5:00 PM | 0.0% | 102 |
| 135 | **Phase 2: Continued Work on Dependency Driven Subjects (CCT-RT, external efforts)** | 45 days | 5/1/17 8:00 AM | 6/30/17 5:00 PM | 0.0% | 90, 38, 75, 51 |
| 136 | 4.2.3: Competition, Consumer Trust & Consumer Choice | 45 days | 5/1/17 8:00 AM | 6/30/17 5:00 PM | 0.0% | |
| 137 | 4.2.14: Support for Applicants from Developing Countries, cont. | 45 days | 5/1/17 8:00 AM | 6/30/17 5:00 PM | 0.0% | |
| 138 | 4.3.9: Global Public Interest (GAC Advice/Safeguards), cont. | 45 days | 5/1/17 8:00 AM | 6/30/17 5:00 PM | 0.0% | |
| 139 | 4.3.7: Second-level RPMs, cont. | 45 days | 5/1/17 8:00 AM | 6/30/17 5:00 PM | 0.0% | |
| 140 | 4.3.5: Registrar Non-Discrimination, cont. | 45 days | 5/1/17 8:00 AM | 6/30/17 5:00 PM | 0.0% | |
| 141 | 4.3.8: Registry/Registrar Standardization (Separation), cont. | 45 days | 5/1/17 8:00 AM | 6/30/17 5:00 PM | 0.0% | |
| 142 | 4.3.2: Base Registry Agreement/Differentiation, cont. | 45 days | 5/1/17 8:00 AM | 6/30/17 5:00 PM | 0.0% | |
| 143 | 4.4.2: String Similarity (Evaluations), cont. | 45 days | 5/1/17 8:00 AM | 6/30/17 5:00 PM | 0.0% | |
| 144 | 4.4.3: Objections (Role of Independent Objector), cont. | 45 days | 5/1/17 8:00 AM | 6/30/17 5:00 PM | 0.0% | |
| 145 | 4.4.5: Communuty Applications (Community Priority Evaluations), cont. | 45 days | 5/1/17 8:00 AM | 6/30/17 5:00 PM | 0.0% | |
| 146 | 4.6.1: Security and Stability, cont. | 45 days | 5/1/17 8:00 AM | 6/30/17 5:00 PM | 0.0% | |
| 147 | 4.2.8: Accreditation Programs, cont. | 45 days | 5/1/17 8:00 AM | 6/30/17 5:00 PM | 0.0% | |
| 148 | **Initial Report** | 127 days | 7/3/17 8:00 AM | 1/3/18 5:00 PM | 0.0% | |
| 149 | Prepare Draft Initial Report | 45 days | 7/3/17 8:00 AM | 9/1/17 5:00 PM | 0.0% | 135 |
| 150 | WG Agreement on Initial Report | 14 days | 9/4/17 8:00 AM | 9/21/17 5:00 PM | 0.0% | 149 |
| 151 | Publish Initial Report for Public Comment | 40 days | 9/22/17 8:00 AM | 11/16/17 5:00 PM | 0.0% | 150 |
| 152 | Publish Summary of Public Comment | 28 days | 11/17/17 8:00 AM | 1/3/18 5:00 PM | 0.0% | 151 |
| 153 | **Final Report** | 162 days | 11/17/17 8:00 AM | 7/10/18 5:00 PM | 0.0% | |
| 154 | Consider Public Comment | 28 days | 11/17/17 8:00 AM | 1/3/18 5:00 PM | 0.0% | 151 |
| 155 | Revise Report | 120 days | 1/4/18 8:00 AM | 6/20/18 5:00 PM | 0.0% | 154 |
| 156 | WG Agreement on Final Report | 14 days | 6/21/18 8:00 AM | 7/10/18 5:00 PM | 0.0% | 155 |

Project: Policy Development Next Phase New gTLD - FY16-FY17
Planned Start: 7/1/15
Planned Completion: 7/10/18
Printed On: 10/28/16

Projected Start: 7/8/15
Projected Completion: 8/16/18



Policy Development Next Phase New gTLD

This effort is intended to analyze subjects that may lead to changes or adjustments for subsequent New gTLD Procedures by preparing a Preliminary Issue Report, seeking public comment, and then preparing a final Issue Report for GNSO Council consideration.

Planned
Summary
In Progress
Milestone

©2000-2016 Licensed Copyright by Workfront, Inc. All rights reserved.
